


Mary E. Britton Middle School

➤ **Completed Work:**

- Continue ACM Panels at East Wall of Gym. Finished at Mechanical Mezzanine Wall and North Walls of Area F
- Storm Shelter Roof Poured on 5/16
- Continue Interior CMU Chase Walls at Area A and C 1st Floor
- CMU at Restroom Walls at C 2nd Floor
- Continue Brick Veneer at Courtyard Area Between Area C and E
- Kitchen Cooler Delivered on 5/21
- Continue decking and Perimeter angle at Area E Corridor F100A
- Continue Setting Structural Steel at Area E/F G301 Mechanical Platform ahead of Decking
- Continue Tying in Structural Steel at Gym Lobby Entrance (Check Elevations of Embeds)
- Start Roofing at Area B Platform Low Roof on 5/20
- Continue Exterior Framing at Platform of C Gable End as well as Exterior Framing around Windows

➤ **Upcoming Work/Look Ahead:**

- Finish Decking Area E and Structural Steel and Decking at Gym Entrance as well as E/F Platform
- Finish CMU at Plumbing Chase Walls C 2nd Floor
- Continue Brick Veneer at Courtyard between C and E as well as Area A South Wall
- Continue ACM Panel at Area F East Gym Wall
- Start Roofing at Main Flat Roof of B and D, Roofing Area A Standing Seam (Trim out)
- Start Standing Seam Panels at Area A
- Continue Kitchen Cooler Installation
- Continue Painting Area A (Prime and First Coat at Classrooms 2nd Floor)
- Continue Terrazzo Area 1st Floor A then move to 2nd Floor
- Finish Mud and Sanding Area A 2nd Floor
- Exterior Wall Furring/Framing Continuing at C Platform as well as Storm Shelter Parapet Walls
- Start Installing Sheetrock Area C First Floor
- Finish Lighting Panel Wire Pulls Throughout Building
- Finish Sprinkler Area A Second Floor (Roughly 70% as of 5/22)
- Mechanical and Plumbing Rough In Continuing at Area E and Area D

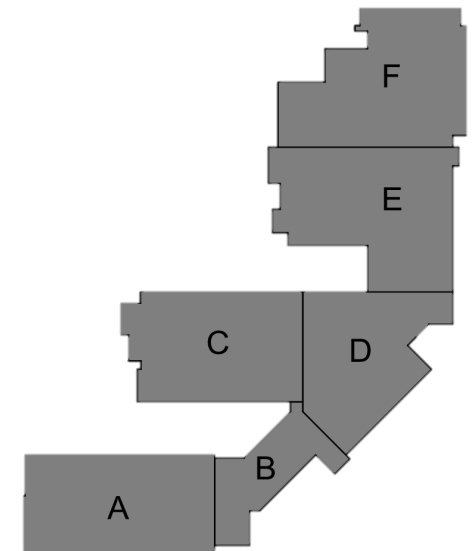

Mary E. Britton Middle School



Area A – Brick at Classroom Wing



Week Ending May 24, 2024



Mary E. Britton Middle School

Area B – MEP Above Ceiling Rough In



Week Ending May 24, 2024

Mary E. Britton Middle School

Area B – Roofing Prep



Week Ending May 24, 2024

Mary E. Britton Middle School




Area C – Furring for ACM Panels



Week Ending May 24, 2024

Mary E. Britton Middle School



Area E Brick at Cafeteria




Week Ending May 24, 2024

Mary E. Britton Middle School



Area E – Corridor Roof Decking

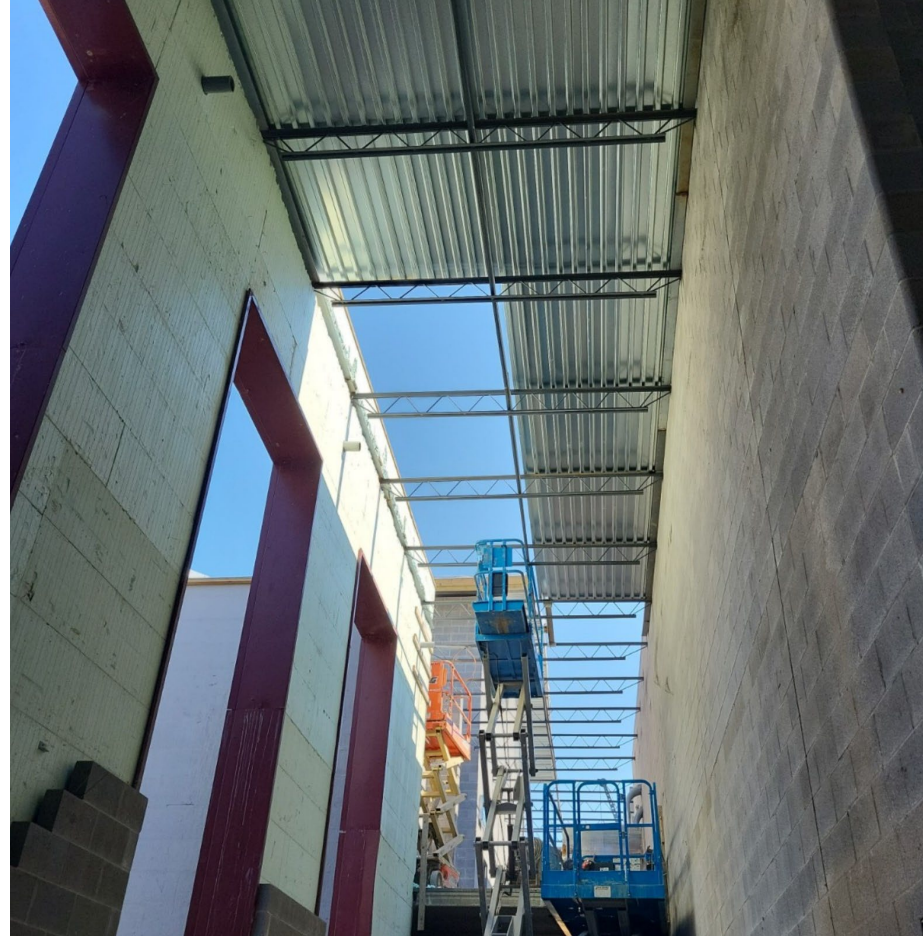

Week Ending May 24, 2024



Mary E. Britton Middle School

Area F – Gym ACM Panels Continue



Week Ending May 24, 2024

Mary E. Britton Middle School



Area F – Gym ACM Panels



Week Ending May 24, 2024
