


# Phase 1.1 - June 2015 - August 2015

Site Setup, Abatement, Demolition, Permanent Busway & Parking Established

Parking Changes		
• South Building Parking Lots Prepped for Construction	Parking Spaces Lost	- 35 Spaces
• Temporary Parking Lots Under Construction		
• Permanent Parking Lot Under Construction		
		<b>-35</b>
Classroom Changes		
• Partial Demolition South Building	Program Space Lost	- 30 Classrooms
• Reconsolidation of Existing Space	Program Space Added	+ 17 Classrooms
		<b>-13</b>

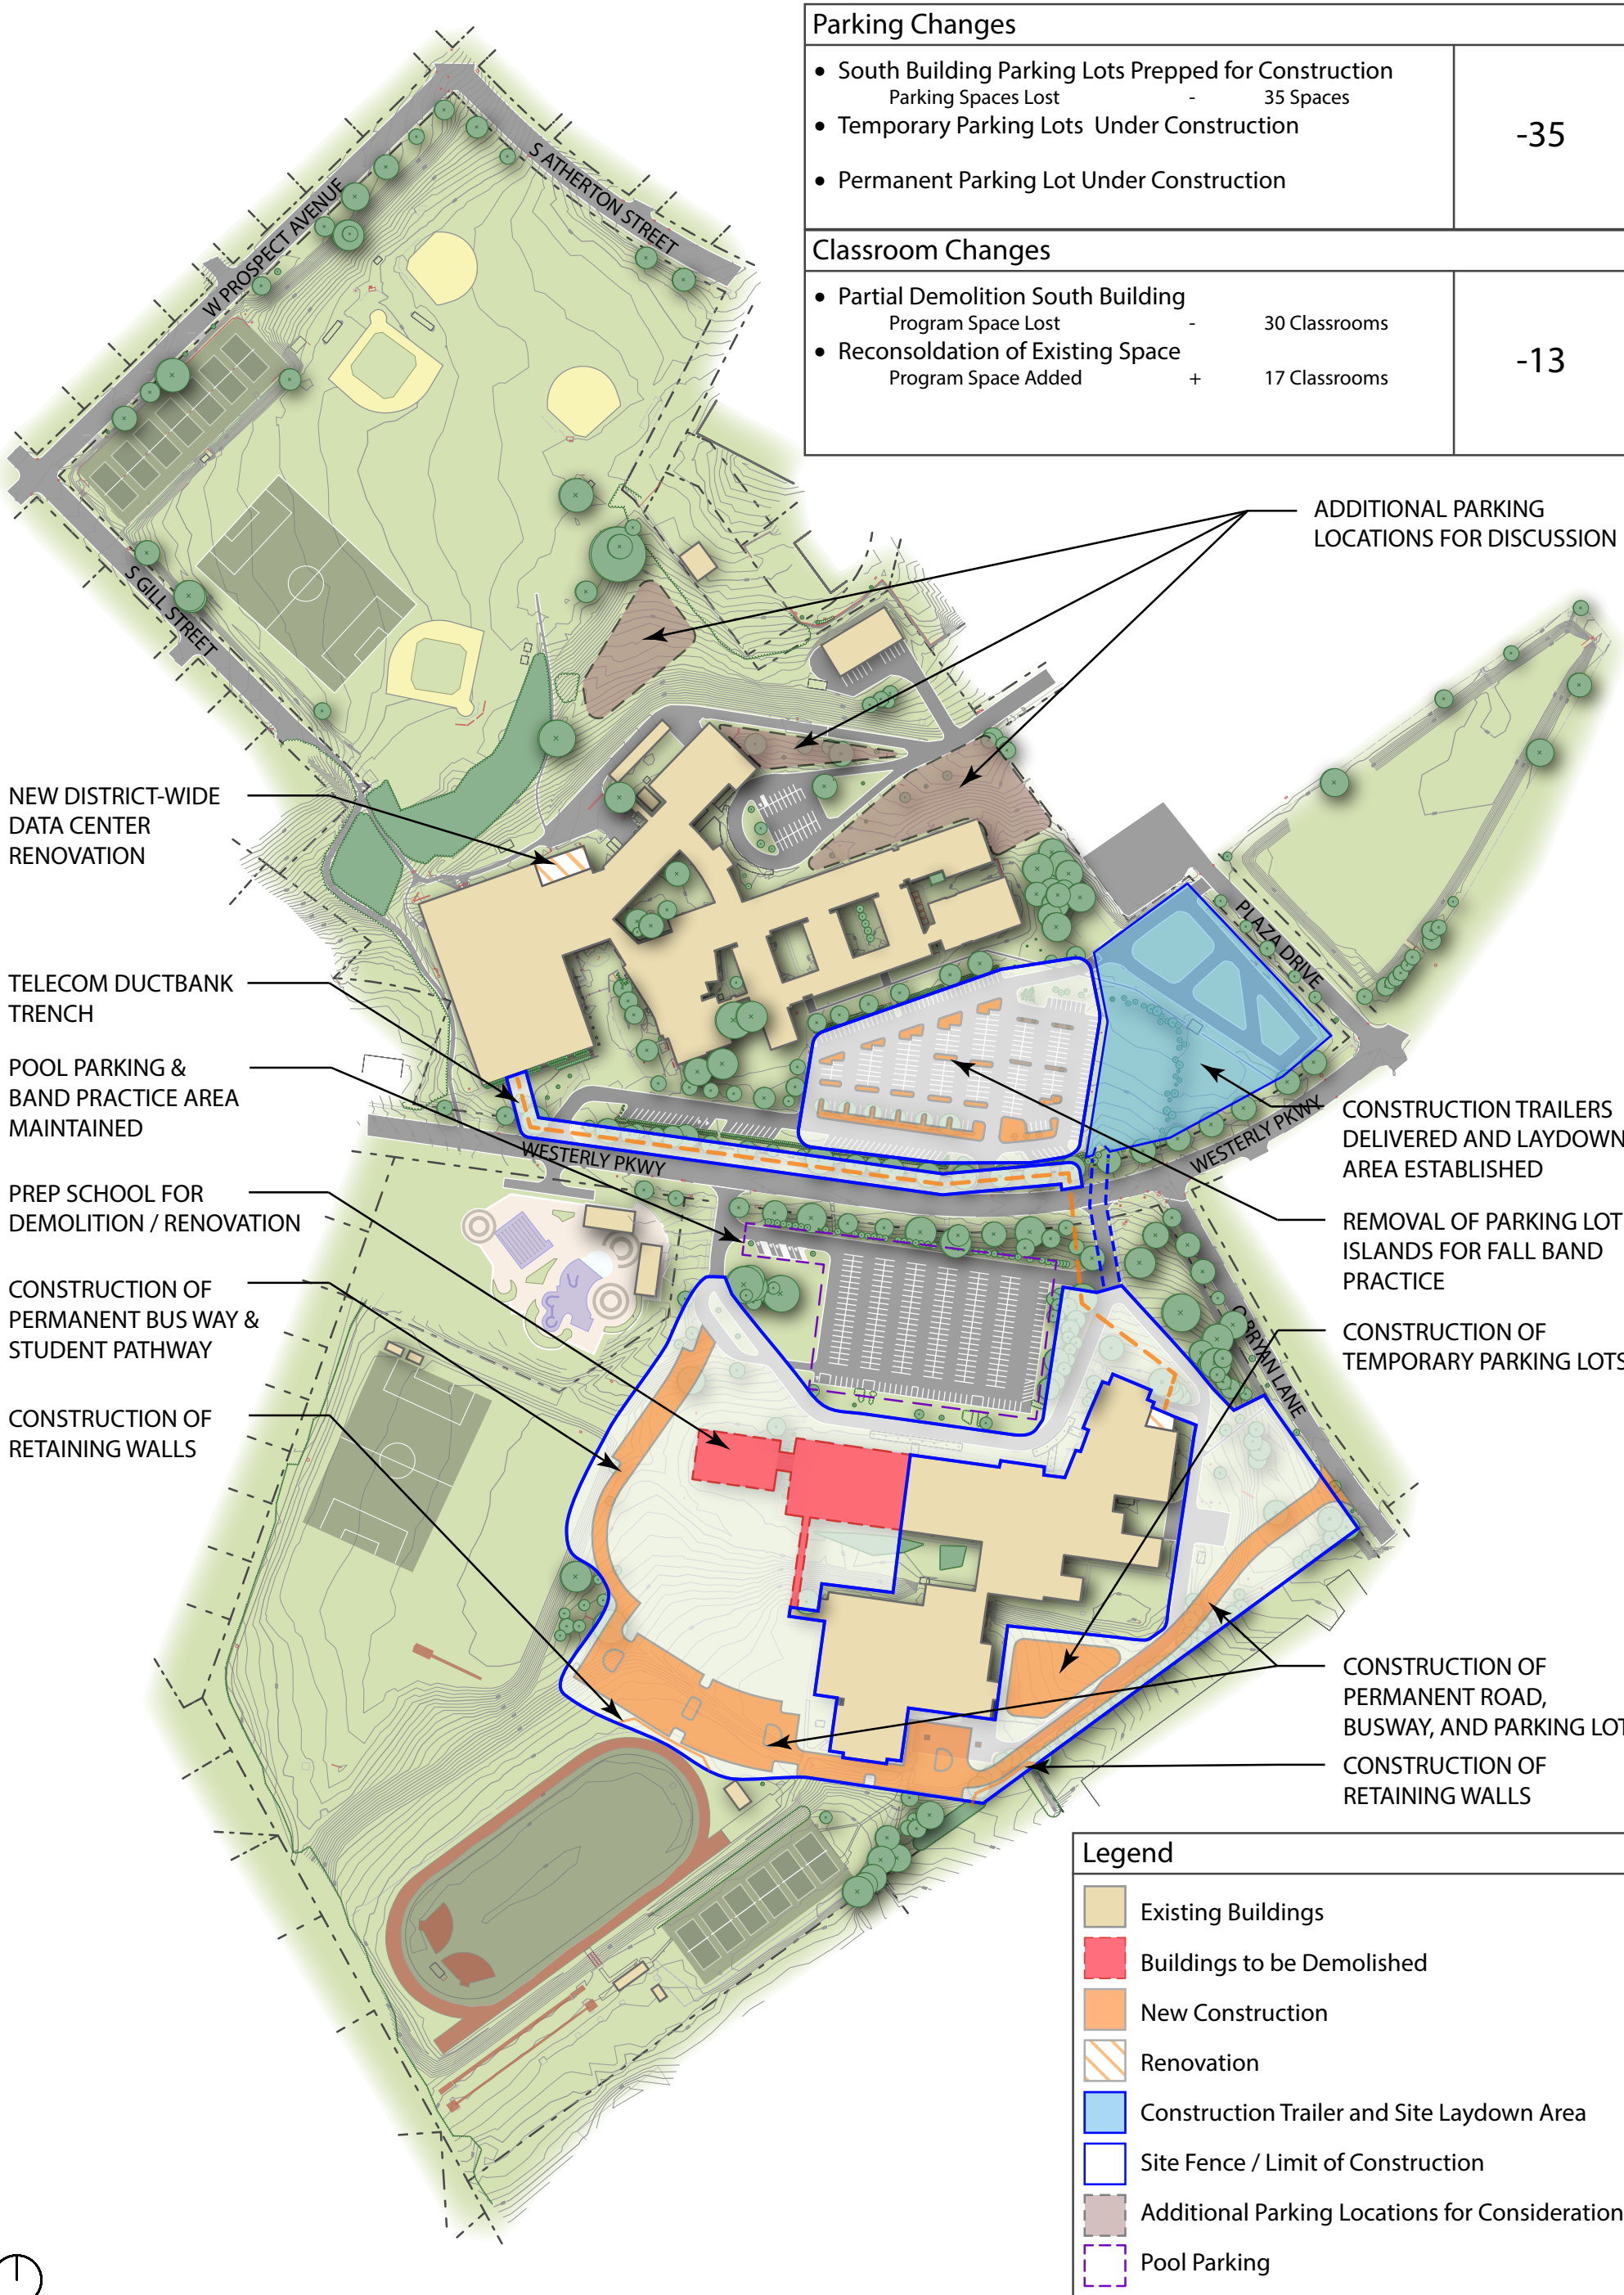

NEW DISTRICT-WIDE DATA CENTER RENOVATION

TELECOM DUCTBANK TRENCH

POOL PARKING & BAND PRACTICE AREA MAINTAINED

PREP SCHOOL FOR DEMOLITION / RENOVATION

CONSTRUCTION OF PERMANENT BUS WAY & STUDENT PATHWAY

CONSTRUCTION OF RETAINING WALLS

ADDITIONAL PARKING LOCATIONS FOR DISCUSSION

CONSTRUCTION TRAILERS DELIVERED AND LAYDOWN AREA ESTABLISHED

REMOVAL OF PARKING LOT ISLANDS FOR FALL BAND PRACTICE

CONSTRUCTION OF TEMPORARY PARKING LOTS

CONSTRUCTION OF PERMANENT ROAD, BUSWAY, AND PARKING LOT

CONSTRUCTION OF RETAINING WALLS

Legend	
	Existing Buildings
	Buildings to be Demolished
	New Construction
	Renovation
	Construction Trailer and Site Laydown Area
	Site Fence / Limit of Construction
	Additional Parking Locations for Consideration
	Pool Parking



# Phase 1.2 - September 2015 - January 2017


## Construction of 4 Education Units and Mechanical Room of New Building & Renovation of Kitchen

### Parking Changes

• South Building Parking Lots Demolished	Parking Spaces Lost	-	290 Spaces	<b>-43</b>
• Temporary Parking Lots Constructed	Parking Spaces Provided	+	50 Spaces	
• Permanent Parking Lot Constructed	Parking Spaces Added	+	197 Spaces	

### Classroom Changes

• Partial Demolition South Building	Program Space Lost	-	33 Classrooms	<b>-16</b>
• Reconsolidation of Existing Space	Program Space Added	+	17 Classrooms	

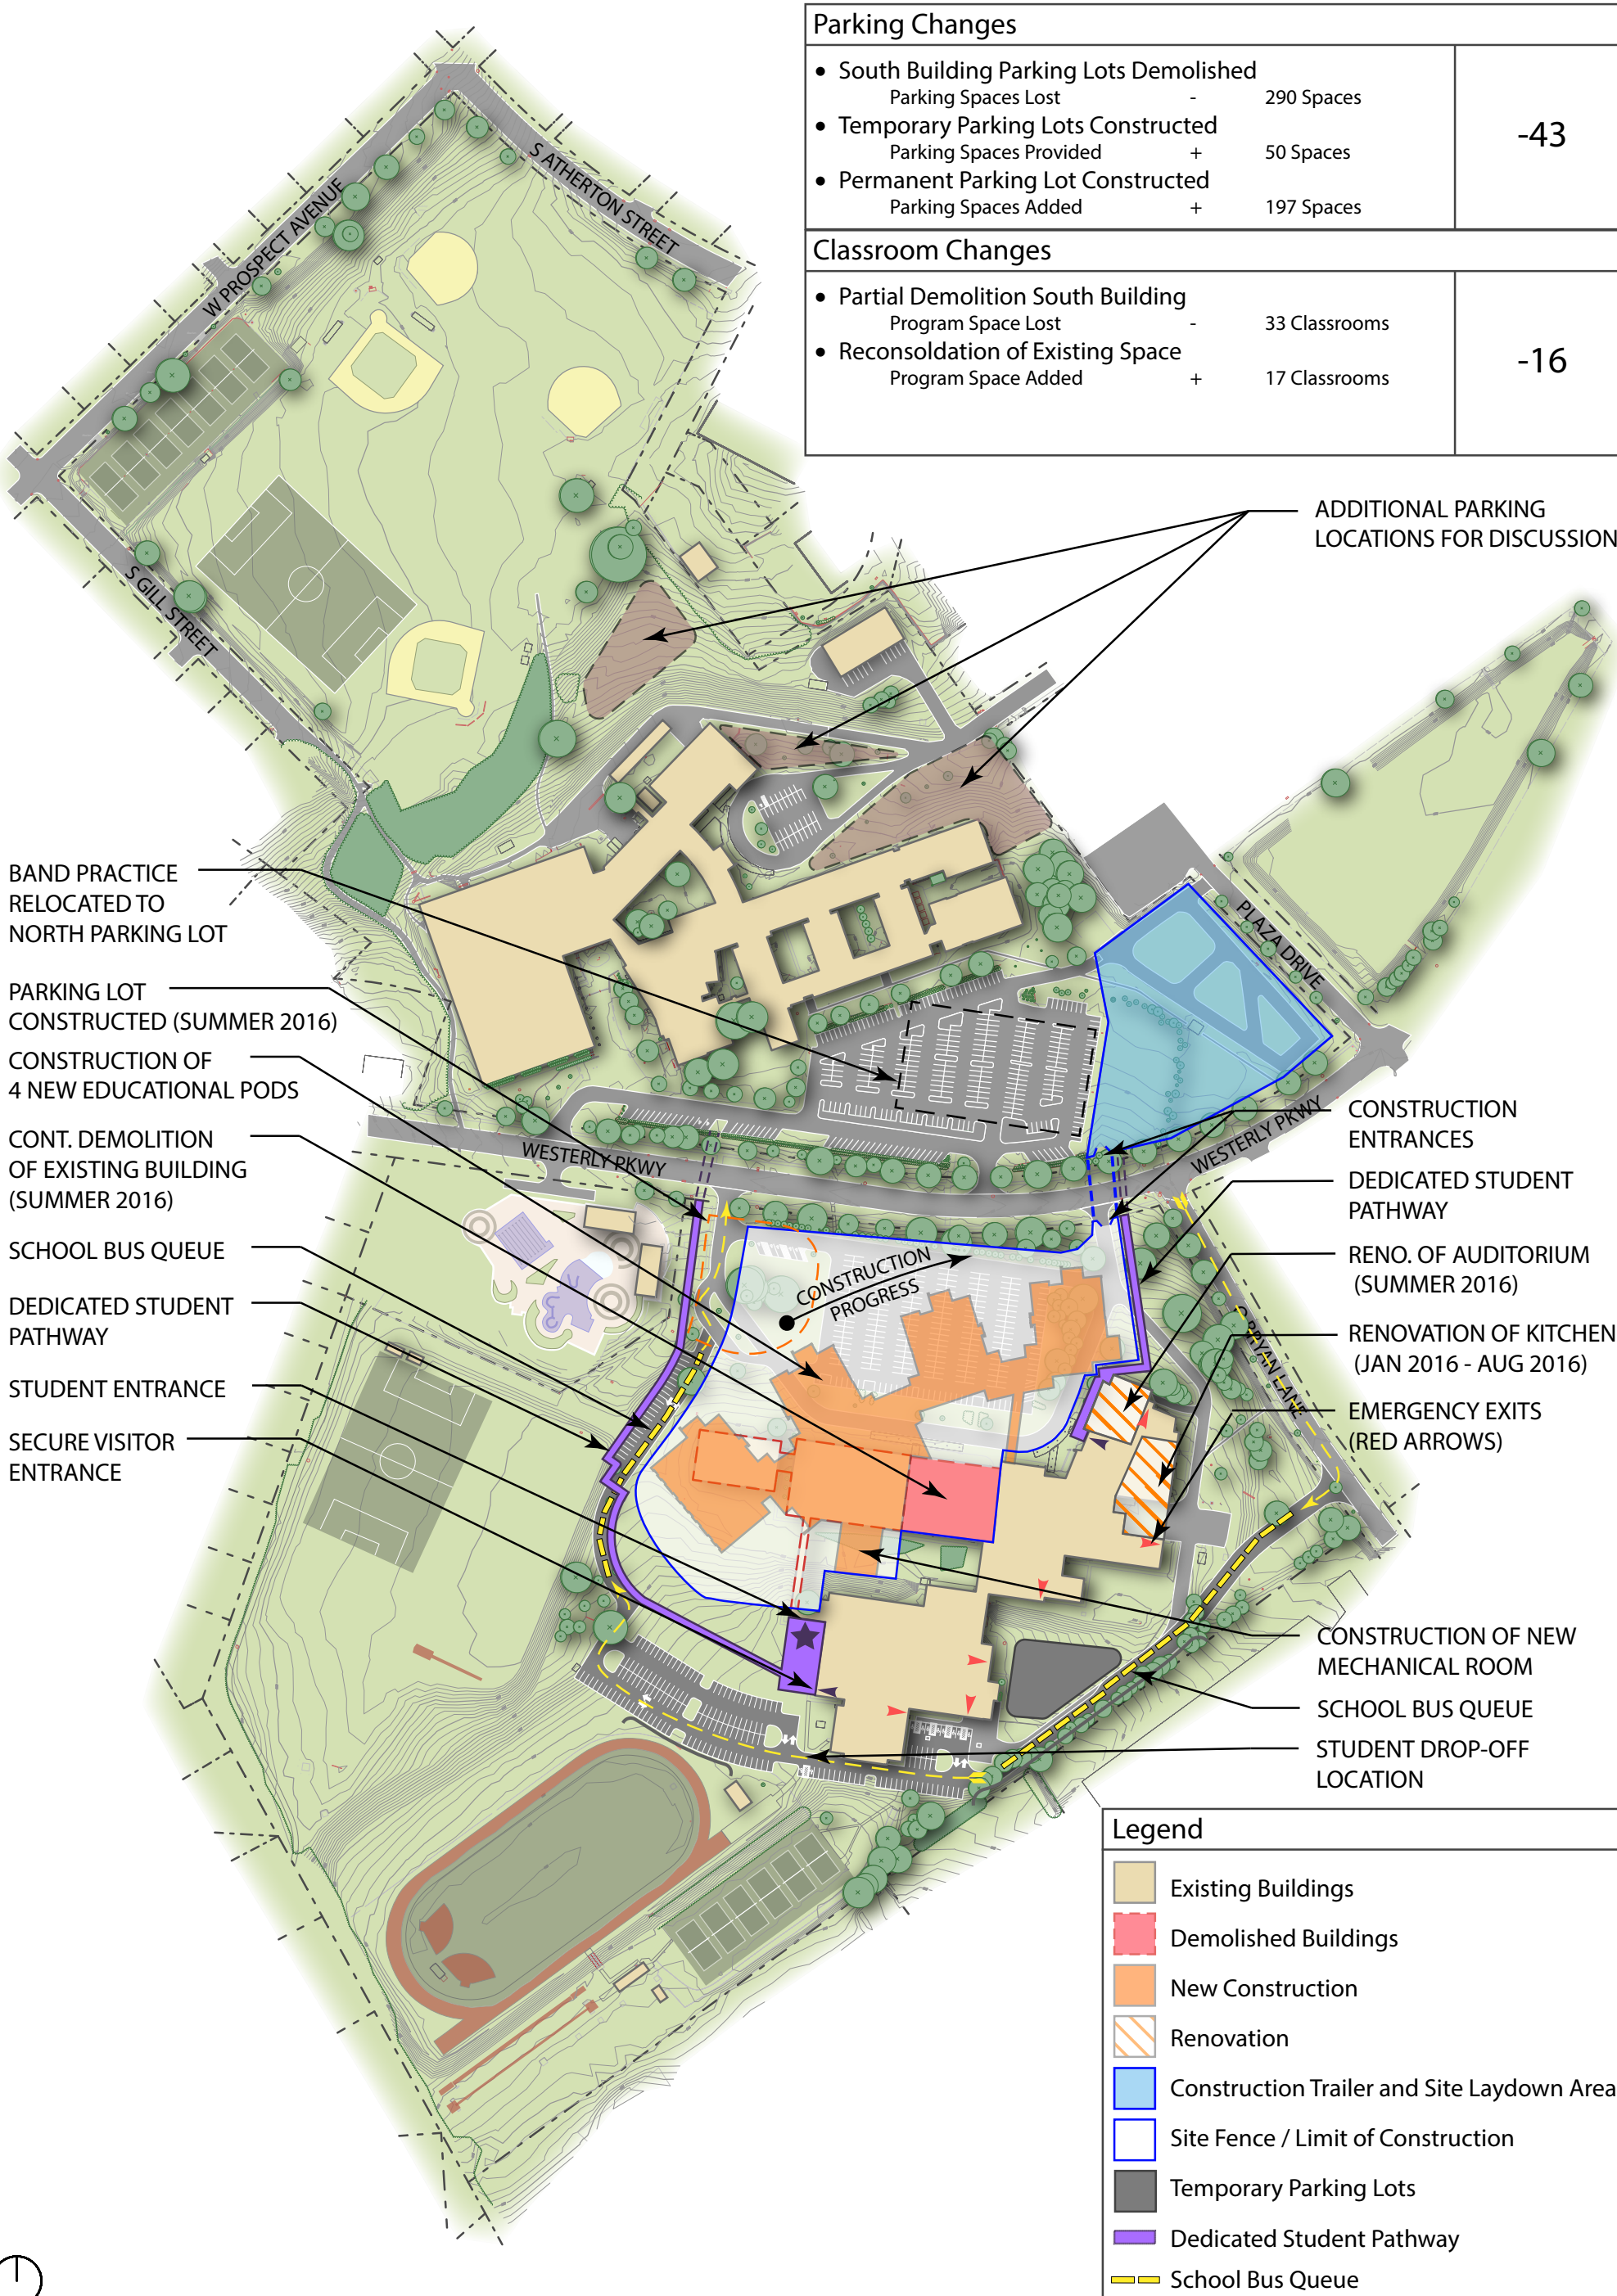

ADDITIONAL PARKING LOCATIONS FOR DISCUSSION

- BAND PRACTICE RELOCATED TO NORTH PARKING LOT
- PARKING LOT CONSTRUCTED (SUMMER 2016)
- CONSTRUCTION OF 4 NEW EDUCATIONAL PODS
- CONT. DEMOLITION OF EXISTING BUILDING (SUMMER 2016)
- SCHOOL BUS QUEUE
- DEDICATED STUDENT PATHWAY
- STUDENT ENTRANCE
- SECURE VISITOR ENTRANCE

- CONSTRUCTION ENTRANCES
- DEDICATED STUDENT PATHWAY
- RENO. OF AUDITORIUM (SUMMER 2016)
- RENOVATION OF KITCHEN (JAN 2016 - AUG 2016)
- EMERGENCY EXITS (RED ARROWS)
- CONSTRUCTION OF NEW MECHANICAL ROOM
- SCHOOL BUS QUEUE
- STUDENT DROP-OFF LOCATION

### Legend


	Existing Buildings
	Demolished Buildings
	New Construction
	Renovation
	Construction Trailer and Site Laydown Area
	Site Fence / Limit of Construction
	Temporary Parking Lots
	Dedicated Student Pathway
	School Bus Queue



# Phase 2.1 - January 2017 - May 2017

## Continued Construction of New Building / Renovation of South Building

Parking Changes			
• South Parking Lots Demolished			
Parking Spaces Lost	-	290 Spaces	
• South Parking Lots Constructed			
Parking Spaces Provided	+	197 Spaces	<b>-64</b>
• Pool Parking Lot Constructed			
Parking Spaces Added	+	29 Spaces	
Classroom Changes			
• Remaining Demolition of South Building			
Program Space Lost	-	73 Classrooms	<b>-36</b>
• Partial Demolition of North Building			
Program Space Lost	-	44 Classrooms	
• Educational Unit A & B Completed			
Program Space Added	+	81 Classrooms	

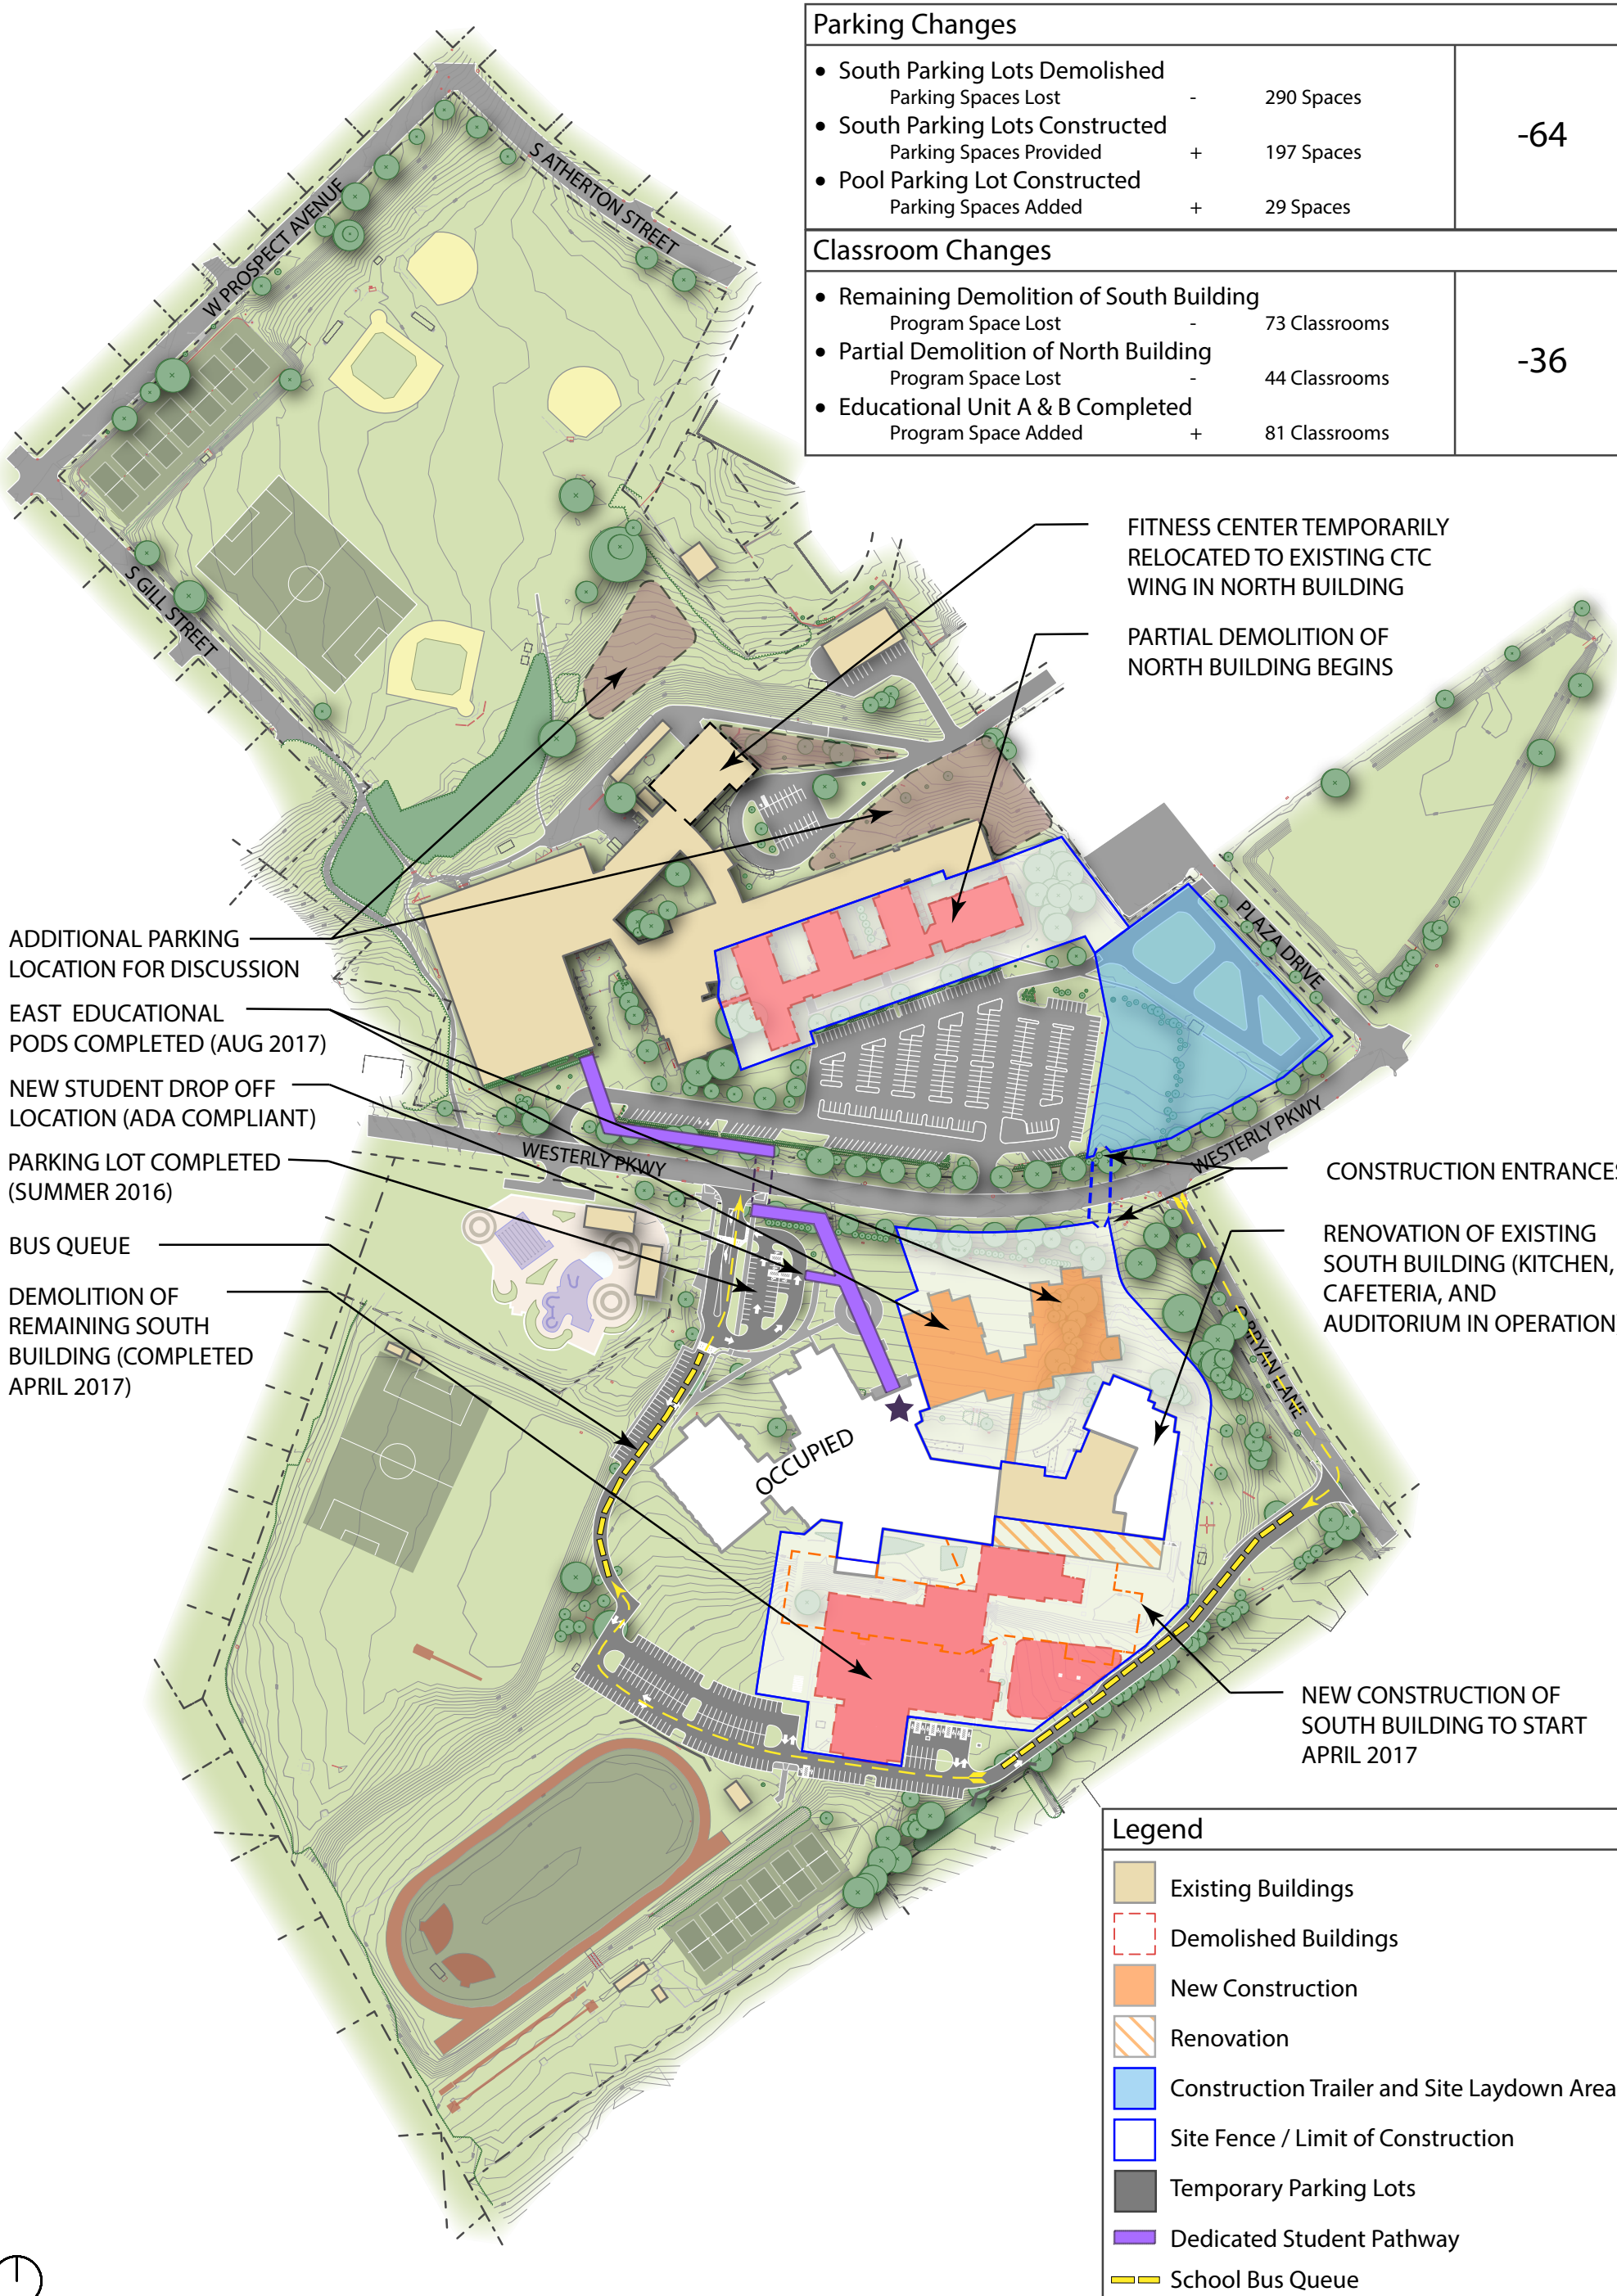

ADDITIONAL PARKING LOCATION FOR DISCUSSION

EAST EDUCATIONAL PODS COMPLETED (AUG 2017)

NEW STUDENT DROP OFF LOCATION (ADA COMPLIANT)

PARKING LOT COMPLETED (SUMMER 2016)

BUS QUEUE

DEMOLITION OF REMAINING SOUTH BUILDING (COMPLETED APRIL 2017)

FITNESS CENTER TEMPORARILY RELOCATED TO EXISTING CTC WING IN NORTH BUILDING

PARTIAL DEMOLITION OF NORTH BUILDING BEGINS

CONSTRUCTION ENTRANCES

RENOVATION OF EXISTING SOUTH BUILDING (KITCHEN, CAFETERIA, AND AUDITORIUM IN OPERATION)


NEW CONSTRUCTION OF SOUTH BUILDING TO START APRIL 2017

Legend	
<span style="display: inline-block; width: 15px; height: 10px; background-color: #d2b48c; border: 1px solid black;"></span>	Existing Buildings
<span style="display: inline-block; width: 15px; height: 10px; border: 2px dashed red;"></span>	Demolished Buildings
<span style="display: inline-block; width: 15px; height: 10px; background-color: #ff8c00;"></span>	New Construction
<span style="display: inline-block; width: 15px; height: 10px; background: repeating-linear-gradient(45deg, transparent, transparent 2px, #ff8c00 2px, #ff8c00 4px);"></span>	Renovation
<span style="display: inline-block; width: 15px; height: 10px; background-color: #add8e6;"></span>	Construction Trailer and Site Laydown Area
<span style="display: inline-block; width: 15px; height: 10px; border: 2px solid blue;"></span>	Site Fence / Limit of Construction
<span style="display: inline-block; width: 15px; height: 10px; background-color: #696969;"></span>	Temporary Parking Lots
<span style="display: inline-block; width: 15px; height: 10px; background-color: #800080;"></span>	Dedicated Student Pathway
<span style="display: inline-block; width: 15px; height: 10px; border-bottom: 2px dashed yellow;"></span>	School Bus Queue



# Phase 2.2 - June 2017 - August 2017

## Continued Construction of New Building / Demolition of North Building

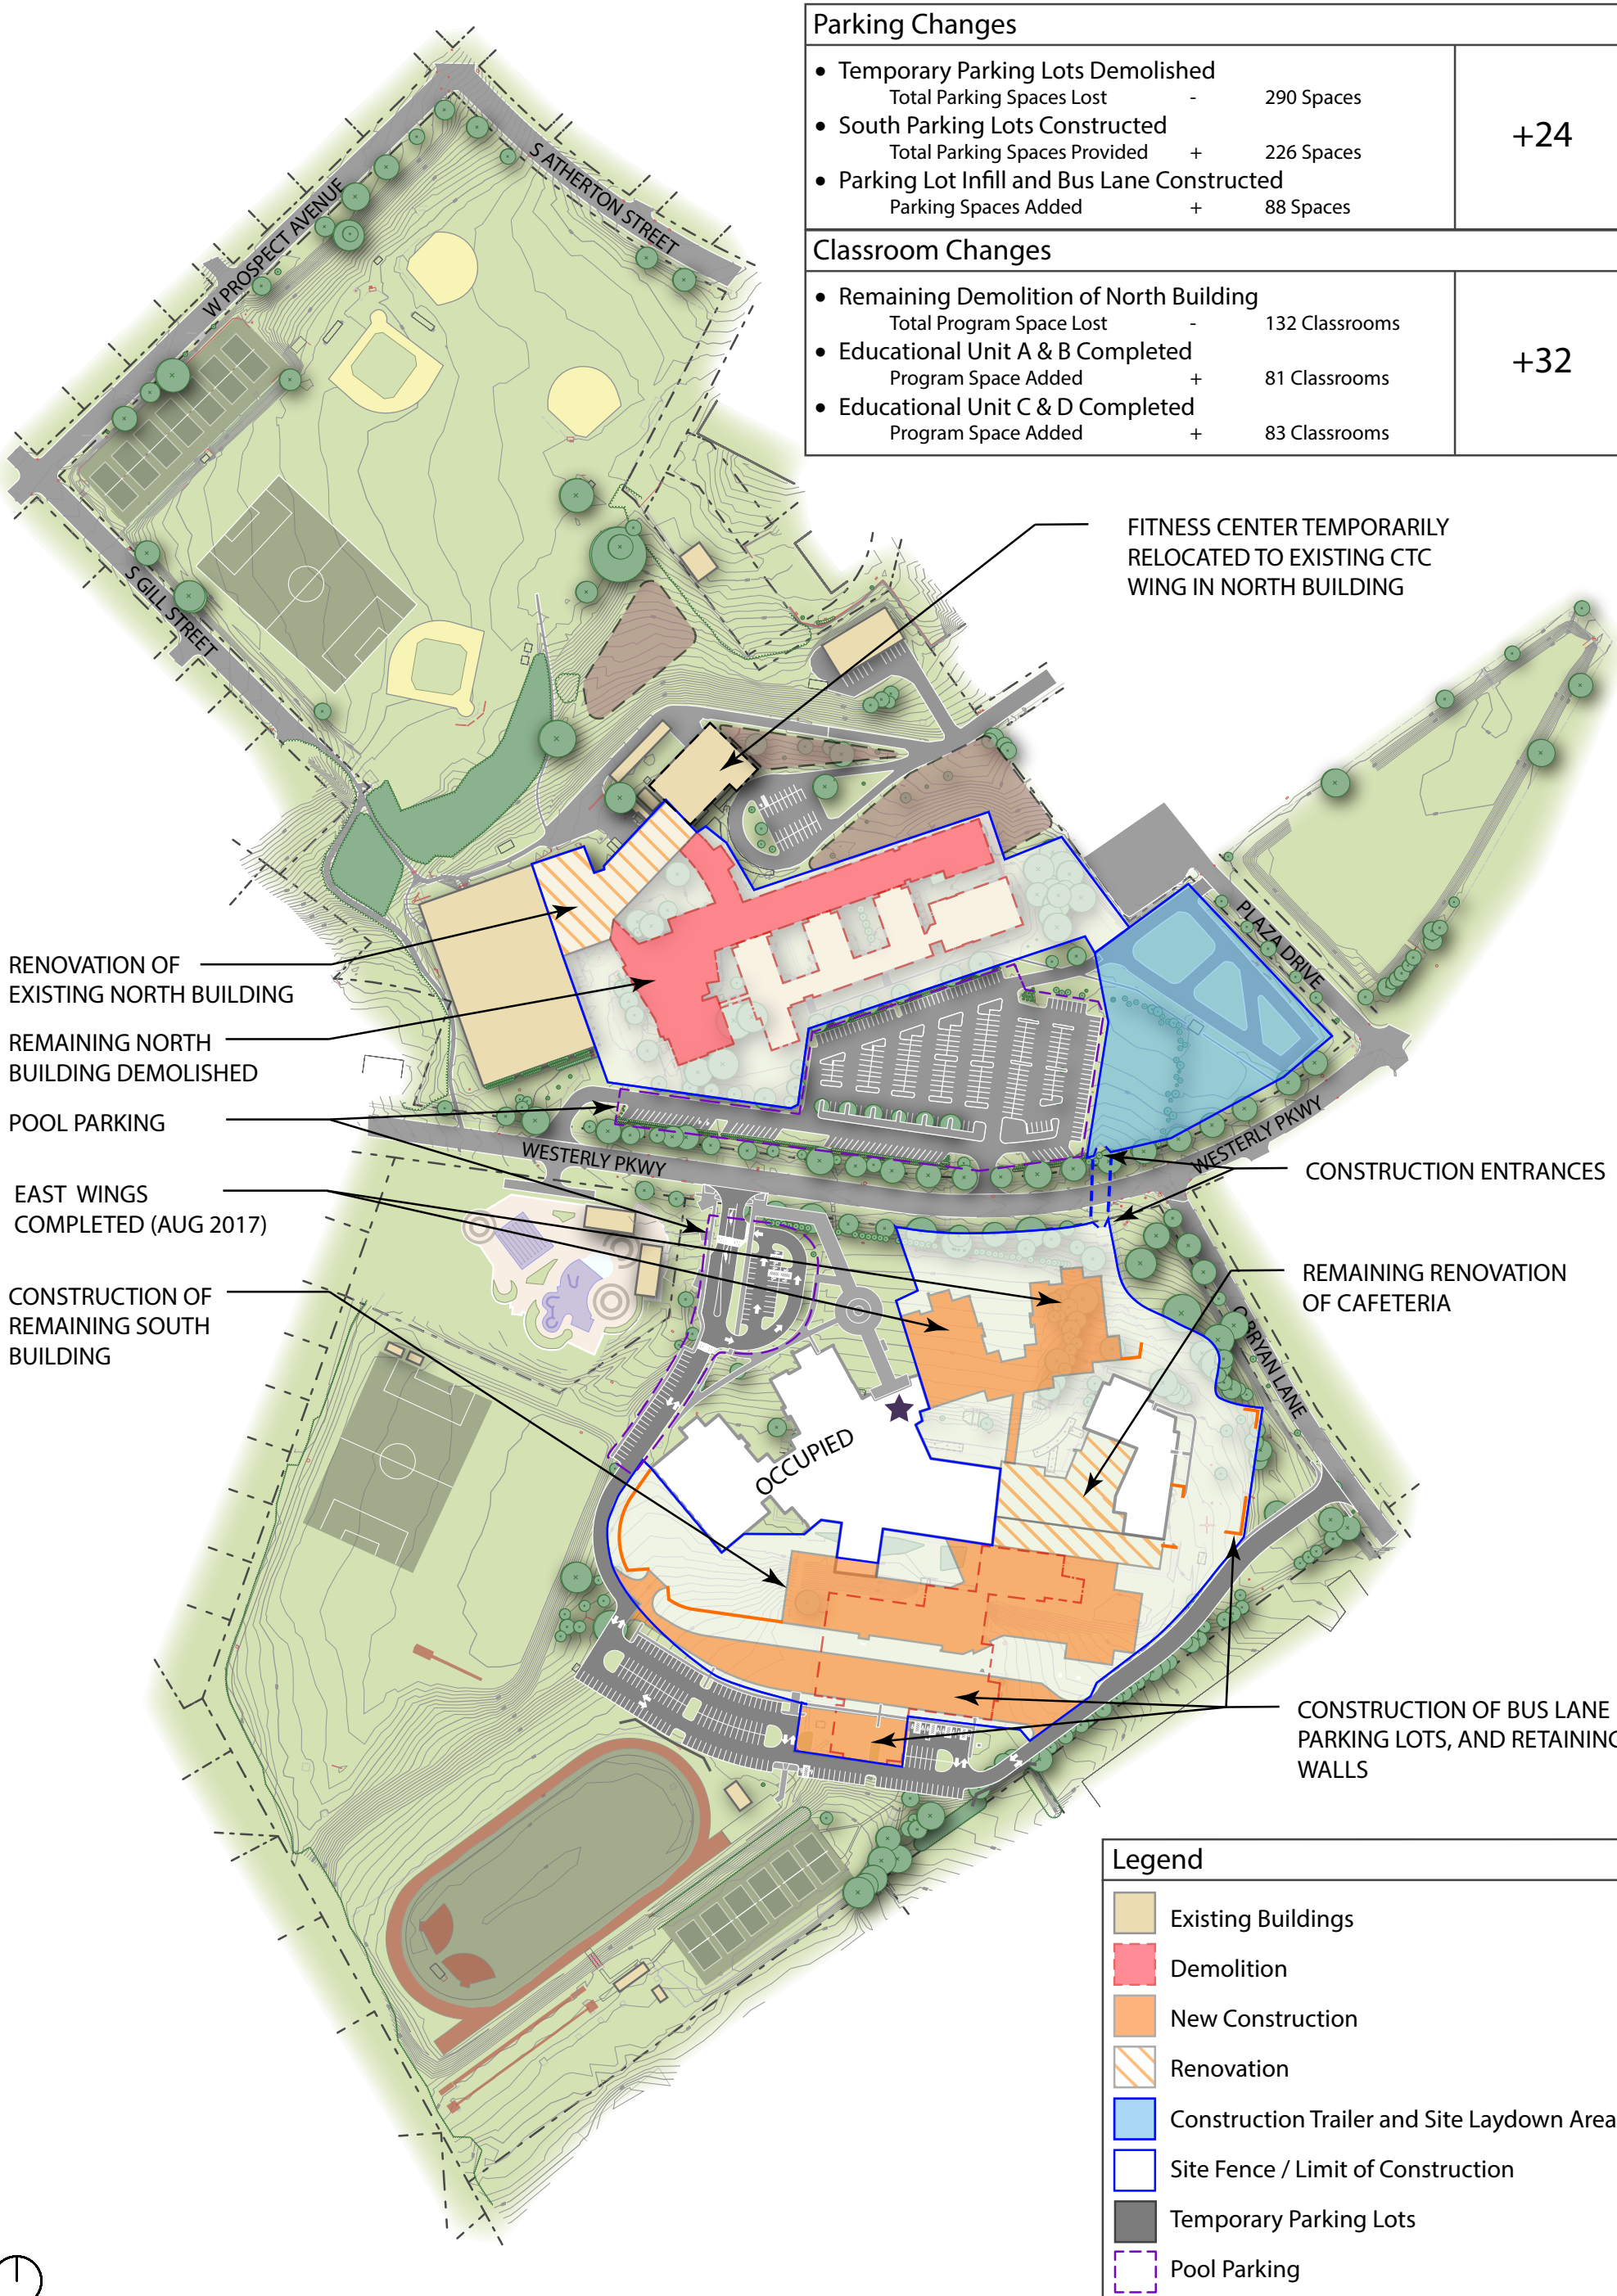

Parking Changes			
• Temporary Parking Lots Demolished			
Total Parking Spaces Lost	-	290 Spaces	
• South Parking Lots Constructed			<b>+24</b>
Total Parking Spaces Provided	+	226 Spaces	
• Parking Lot Infill and Bus Lane Constructed			
Parking Spaces Added	+	88 Spaces	
Classroom Changes			
• Remaining Demolition of North Building			
Total Program Space Lost	-	132 Classrooms	
• Educational Unit A & B Completed			<b>+32</b>
Program Space Added	+	81 Classrooms	
• Educational Unit C & D Completed			
Program Space Added	+	83 Classrooms	

RENOVATION OF EXISTING NORTH BUILDING

REMAINING NORTH BUILDING DEMOLISHED

POOL PARKING

EAST WINGS COMPLETED (AUG 2017)

CONSTRUCTION OF REMAINING SOUTH BUILDING

FITNESS CENTER TEMPORARILY RELOCATED TO EXISTING CTC WING IN NORTH BUILDING

CONSTRUCTION ENTRANCES

REMAINING RENOVATION OF CAFETERIA


CONSTRUCTION OF BUS LANE PARKING LOTS, AND RETAINING WALLS

Legend	
	Existing Buildings
	Demolition
	New Construction
	Renovation
	Construction Trailer and Site Laydown Area
	Site Fence / Limit of Construction
	Temporary Parking Lots
	Pool Parking



# Phase 3.1 - September 2017 - May 2018

## Renovation and Addition to North Building

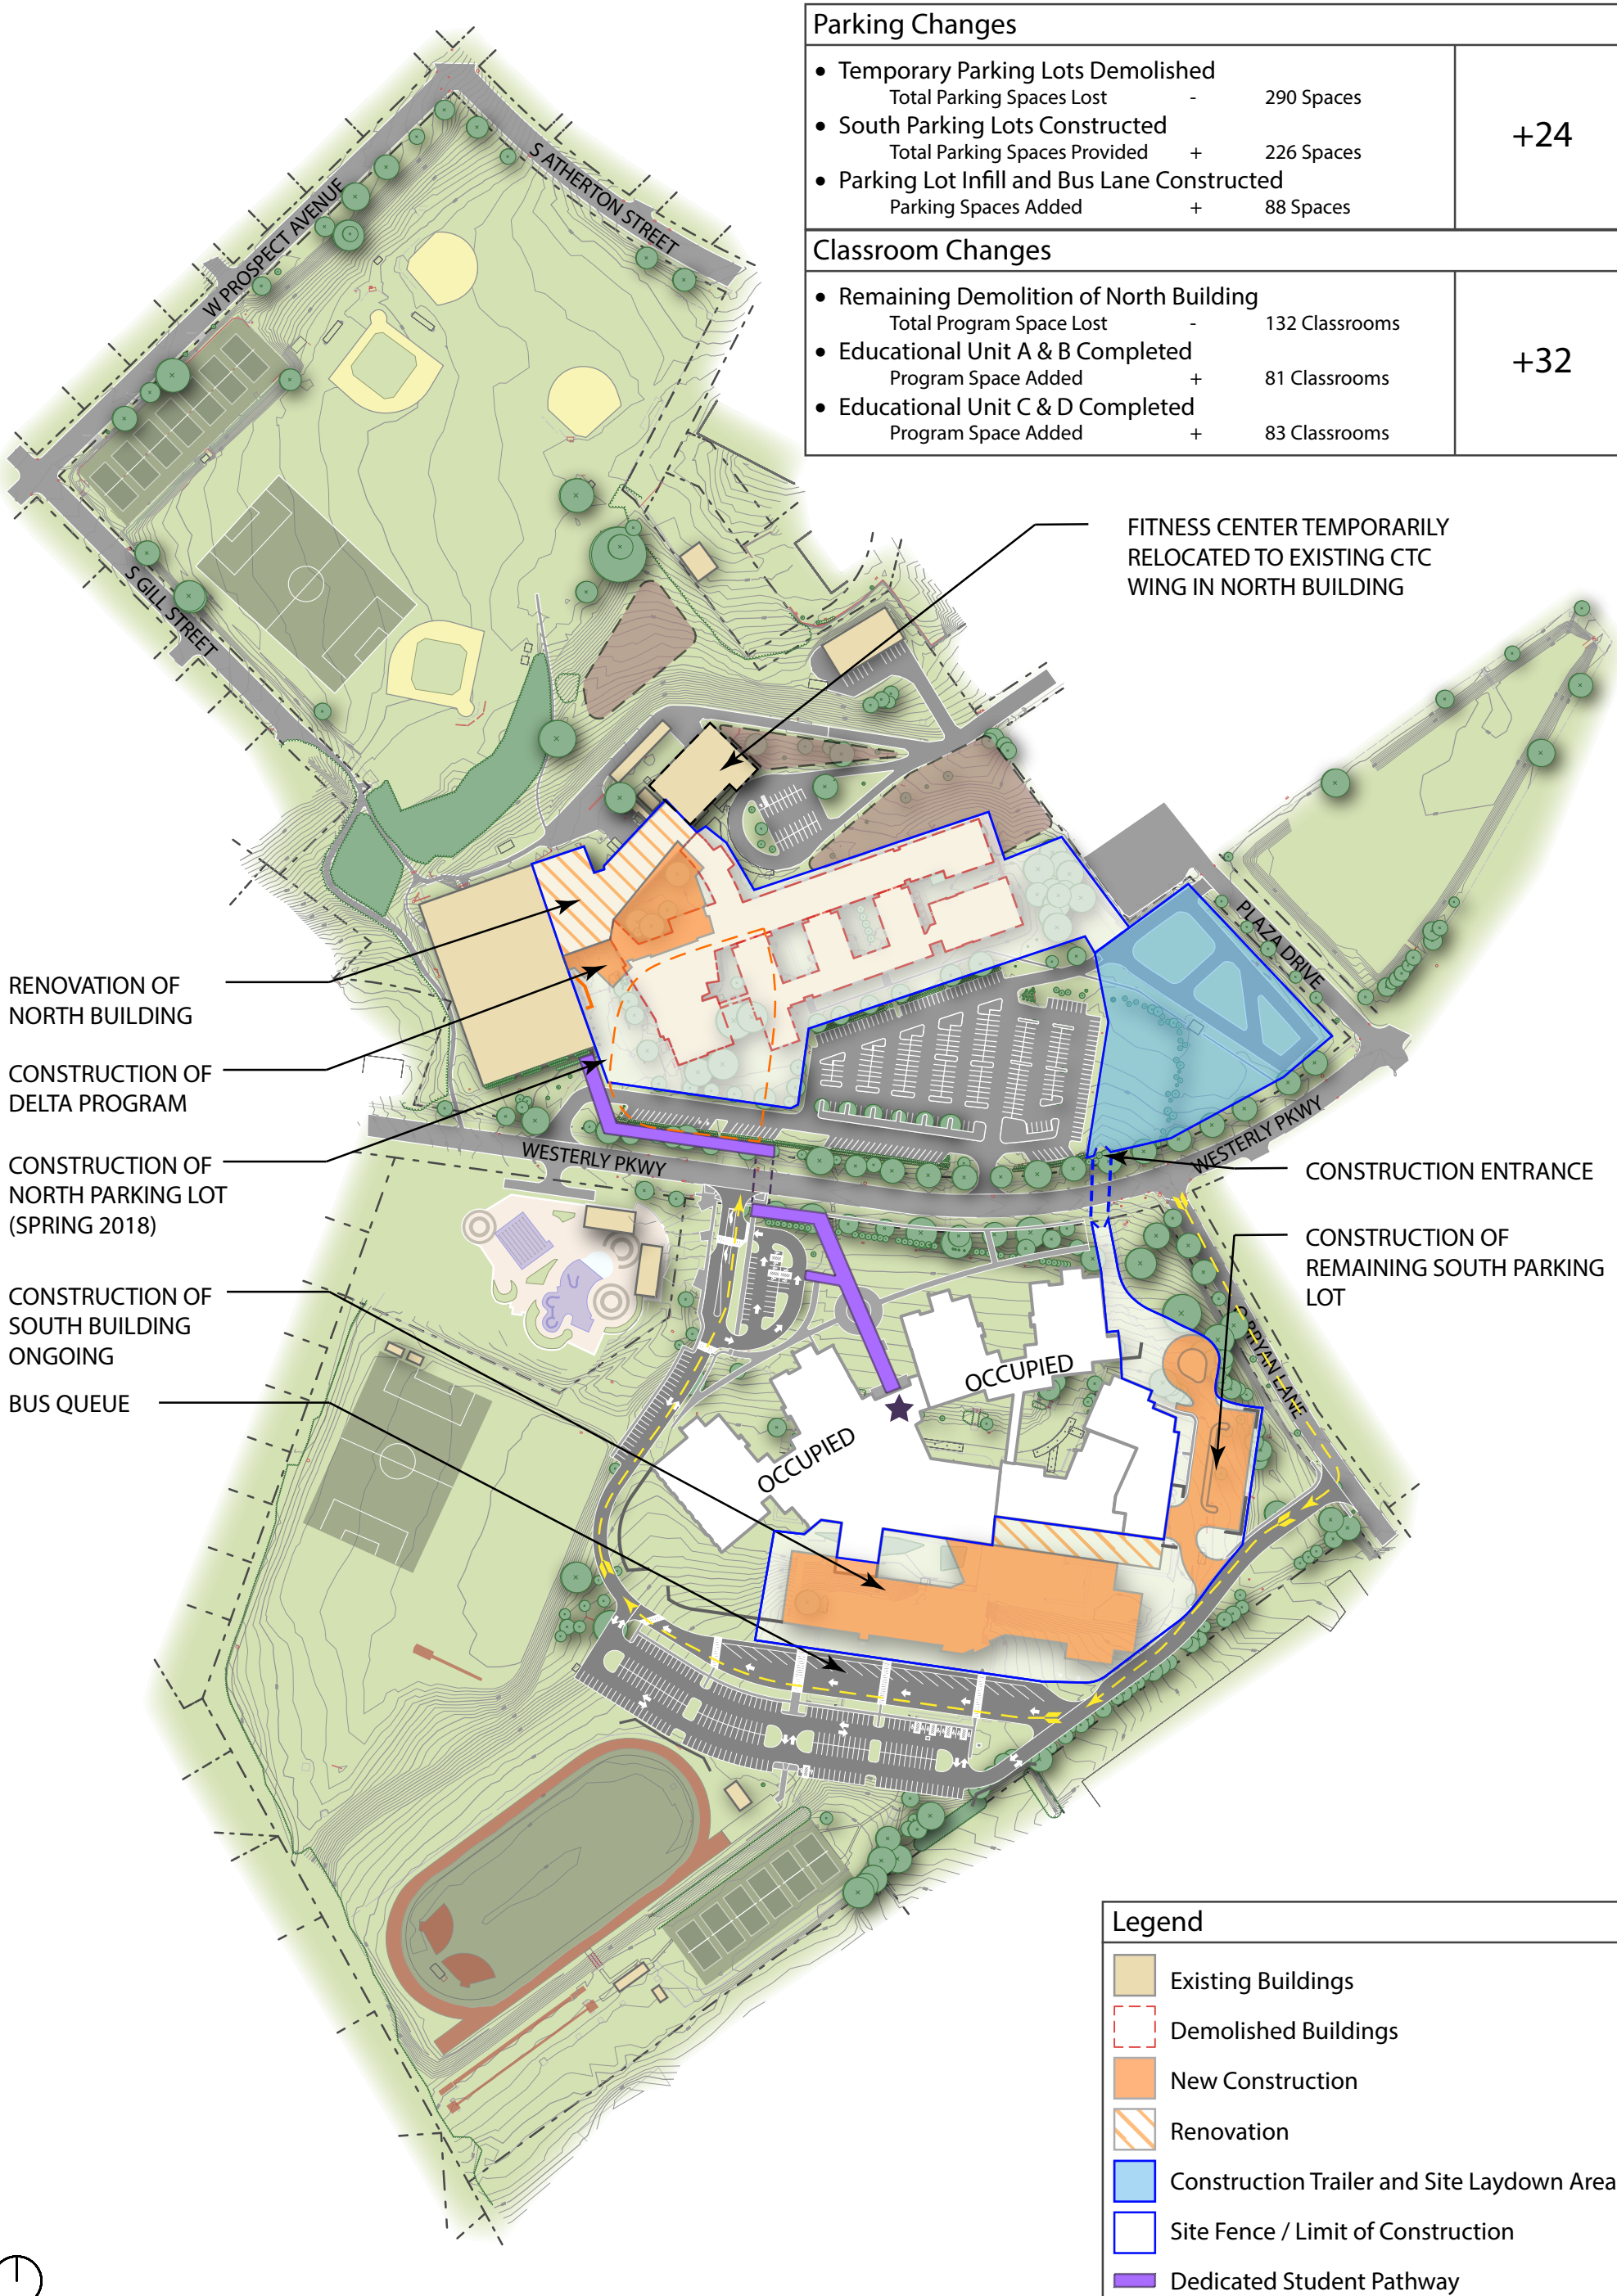

- RENOVATION OF NORTH BUILDING
- CONSTRUCTION OF DELTA PROGRAM
- CONSTRUCTION OF NORTH PARKING LOT (SPRING 2018)
- CONSTRUCTION OF SOUTH BUILDING ONGOING
- BUS QUEUE

- FITNESS CENTER TEMPORARILY RELOCATED TO EXISTING CTC WING IN NORTH BUILDING
- CONSTRUCTION ENTRANCE
- CONSTRUCTION OF REMAINING SOUTH PARKING LOT

Parking Changes			
• Temporary Parking Lots Demolished			
Total Parking Spaces Lost	-	290 Spaces	
• South Parking Lots Constructed			
Total Parking Spaces Provided	+	226 Spaces	<b>+24</b>
• Parking Lot Infill and Bus Lane Constructed			
Parking Spaces Added	+	88 Spaces	


Classroom Changes			
• Remaining Demolition of North Building			
Total Program Space Lost	-	132 Classrooms	
• Educational Unit A & B Completed			
Program Space Added	+	81 Classrooms	<b>+32</b>
• Educational Unit C & D Completed			
Program Space Added	+	83 Classrooms	

Legend	
	Existing Buildings
	Demolished Buildings
	New Construction
	Renovation
	Construction Trailer and Site Laydown Area
	Site Fence / Limit of Construction
	Dedicated Student Pathway



# Phase 3.2 - June 2018 - July 2018

## North Building Move-in, Parking and Site Work

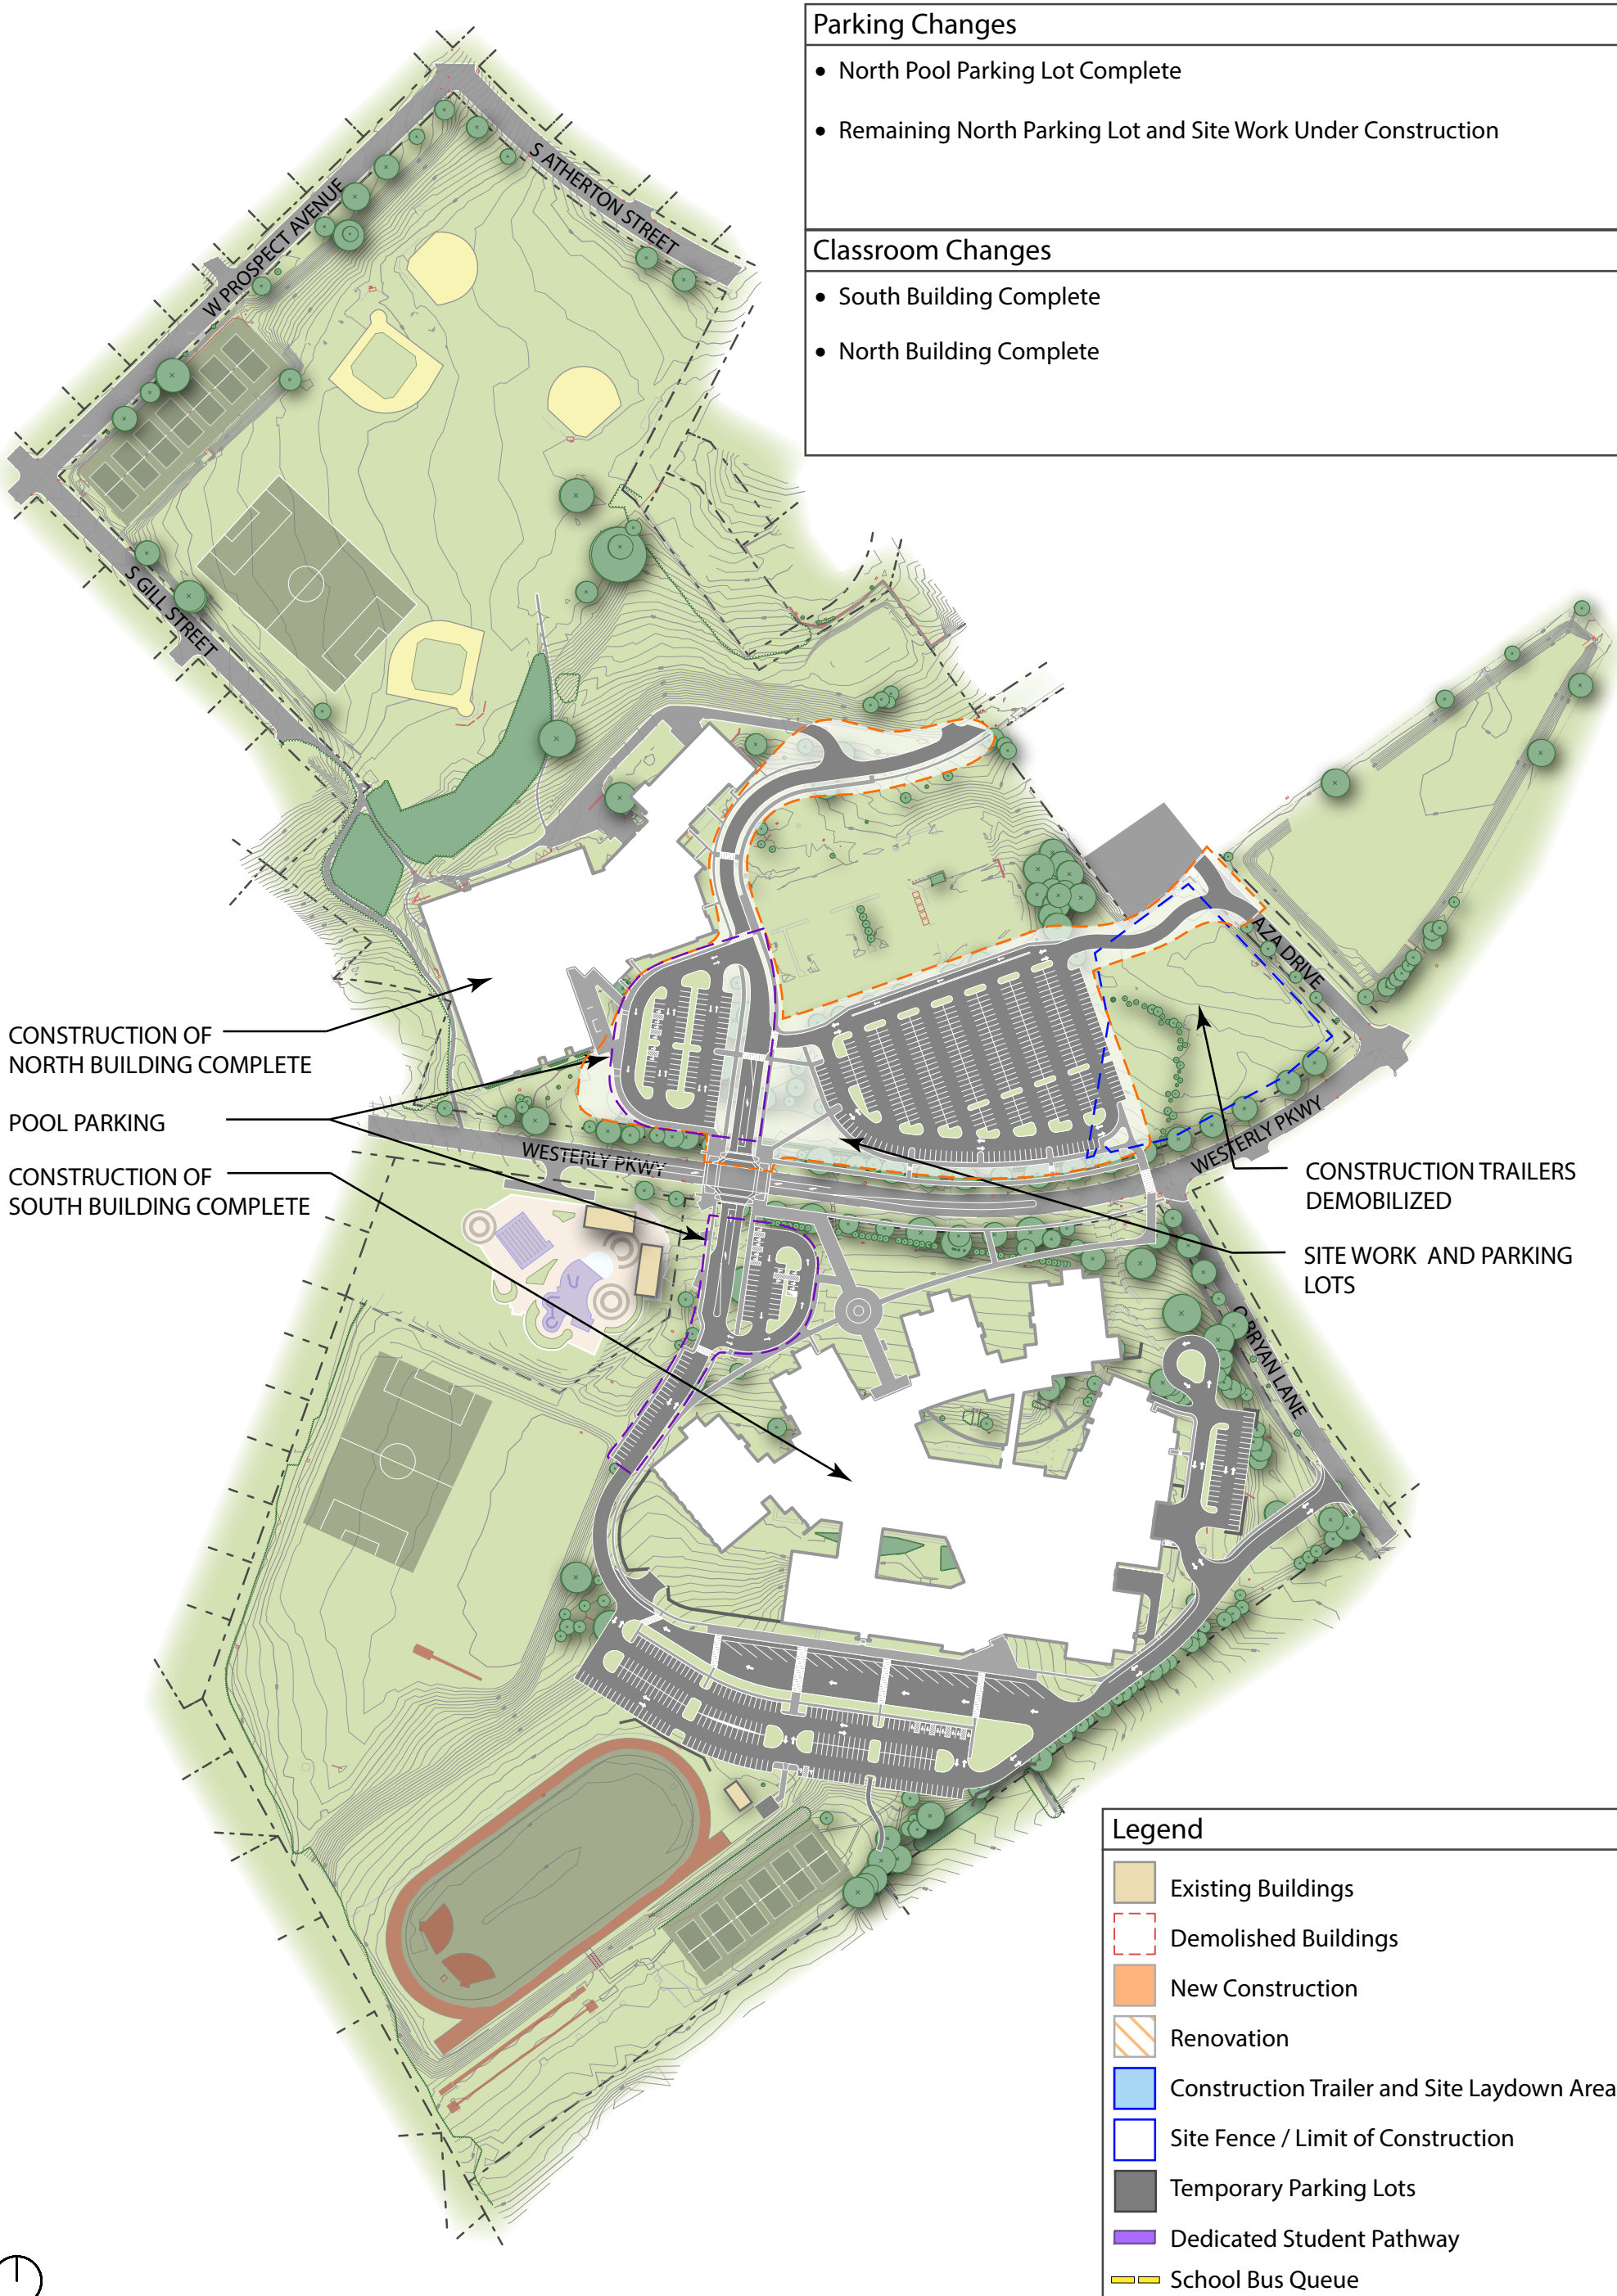

<b>Parking Changes</b>
<ul style="list-style-type: none"> <li>• North Pool Parking Lot Complete</li> <li>• Remaining North Parking Lot and Site Work Under Construction</li> </ul>
<b>Classroom Changes</b>
<ul style="list-style-type: none"> <li>• South Building Complete</li> <li>• North Building Complete</li> </ul>

CONSTRUCTION OF NORTH BUILDING COMPLETE

POOL PARKING

CONSTRUCTION OF SOUTH BUILDING COMPLETE

CONSTRUCTION TRAILERS DEMOBILIZED

SITE WORK AND PARKING LOTS

<b>Legend</b>	
	Existing Buildings
	Demolished Buildings
	New Construction
	Renovation
	Construction Trailer and Site Laydown Area
	Site Fence / Limit of Construction
	Temporary Parking Lots
	Dedicated Student Pathway
	School Bus Queue

