

BPC Presentation

Aledo Independent School District

August 4th, 2020



Aledo Elementary School No. 6



1

Since We Left Off



- Completed Design Development on 06/30/2020
- Conducted meetings with the town of Annetta monthly
- Delivered early grading package to BTC for bidding
- Received bids and GMP was approved by the AISD Bord of Trustees (BTC will begin work on the site this week)
- 90% CDS were delivered to the GC for the GMP package
- Turned drawings into Town of Annetta for plan review
- Turned drawings into 3 Party Reviewer for Storm Shelter Review
- Currently reviewing bids from Subs to determine final GMP number



2 Next Steps




- Finalize GMP
- Finalize Drawings and Specs for Construction
- Notice to proceed end of September.
- Substantial Completion August 1, 2021



3

Site Plan Updates



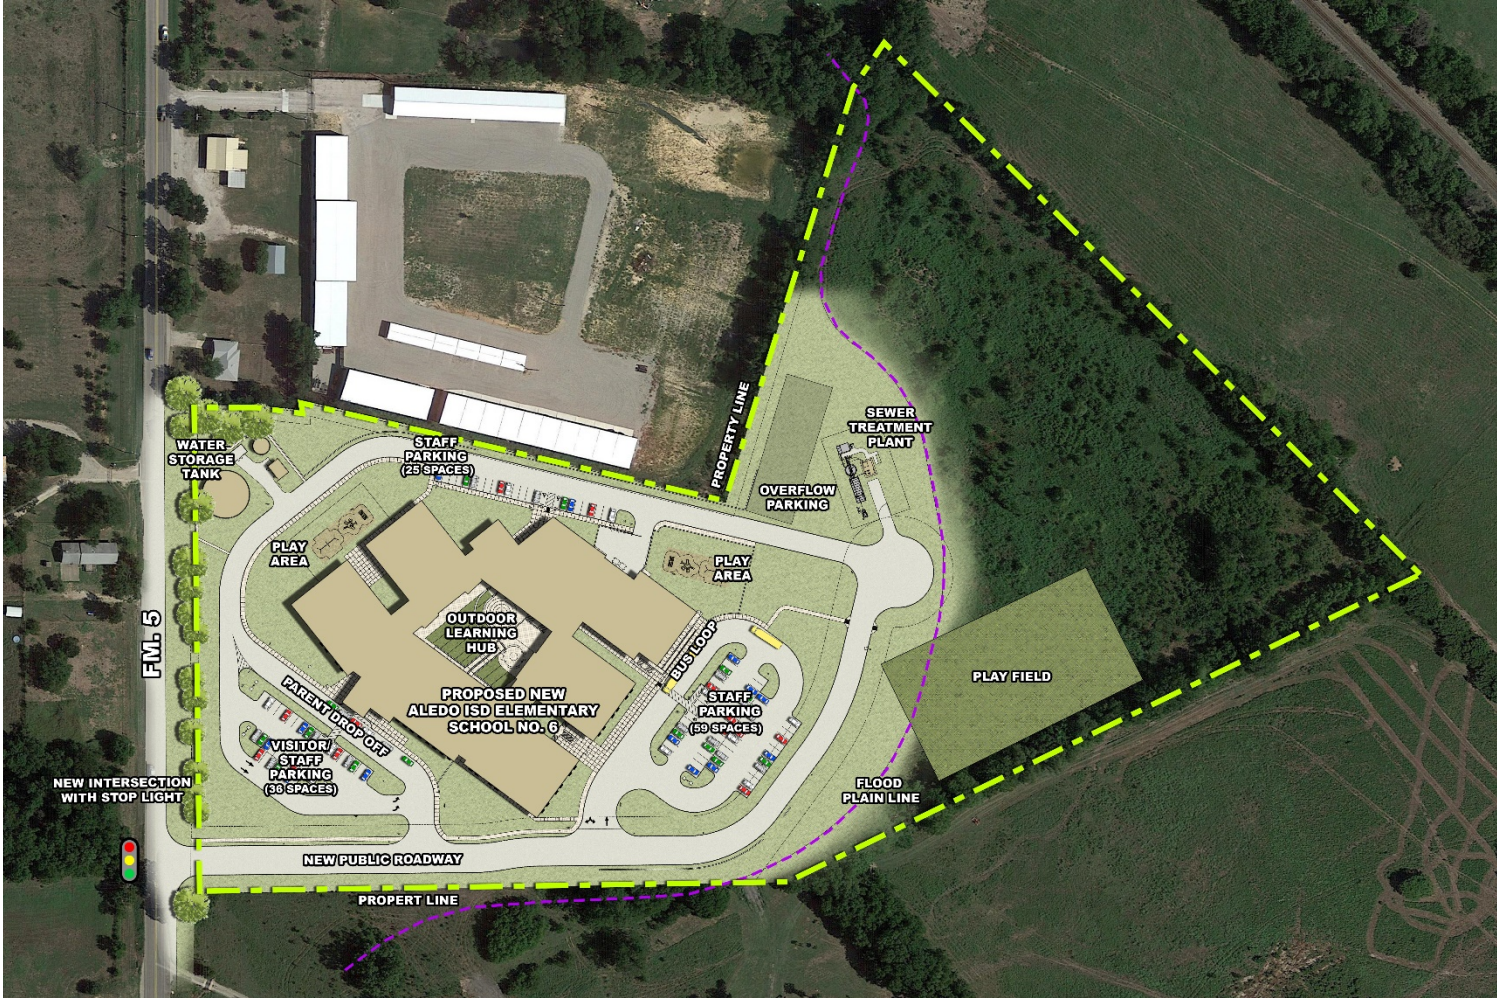

Overall Composite Site Plan




Enlarged Composite Site Plan




4

Floor Plan Updates



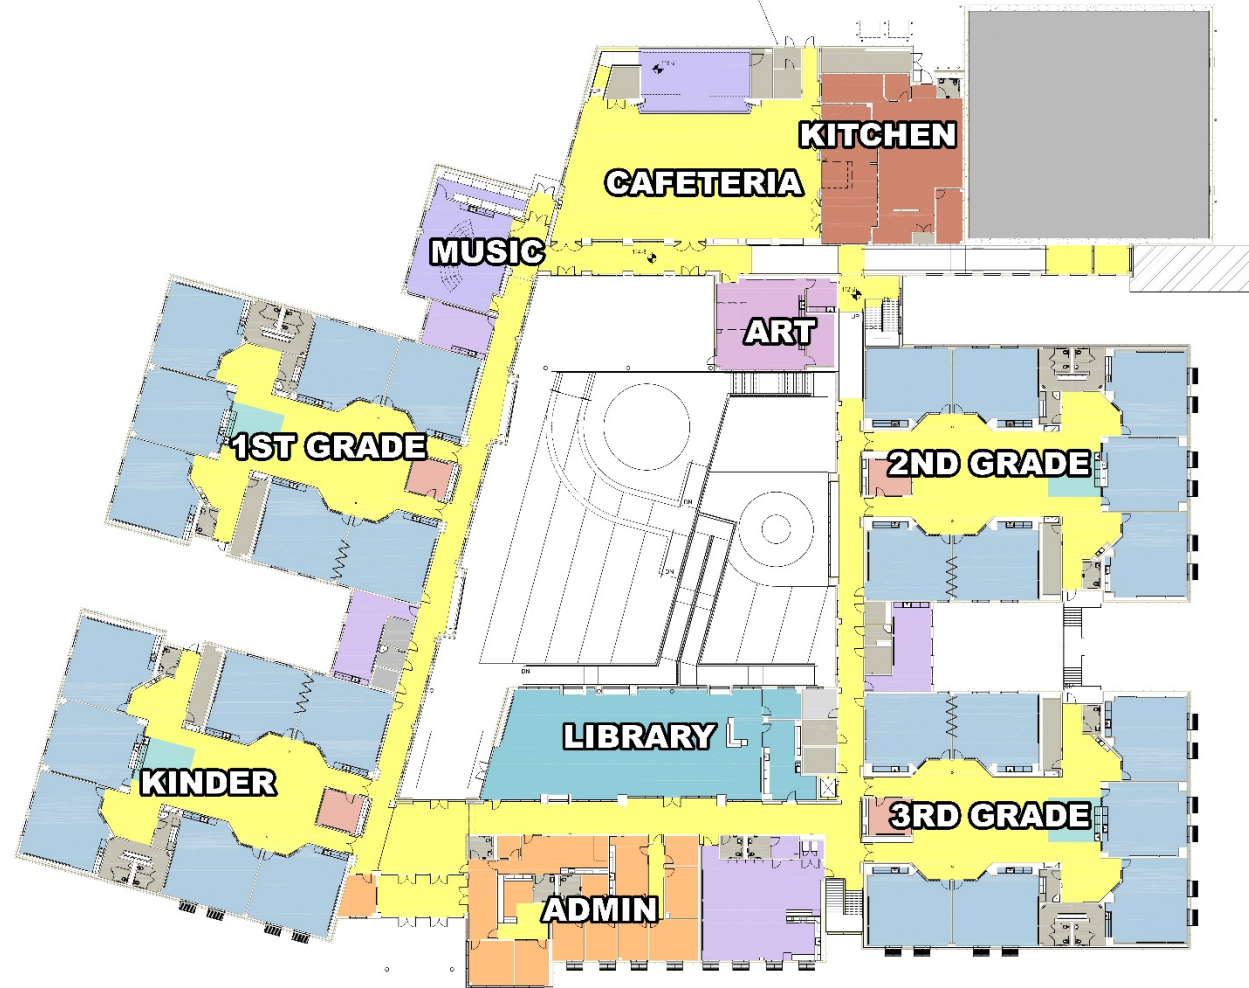

Composite First Level – Floor Plan

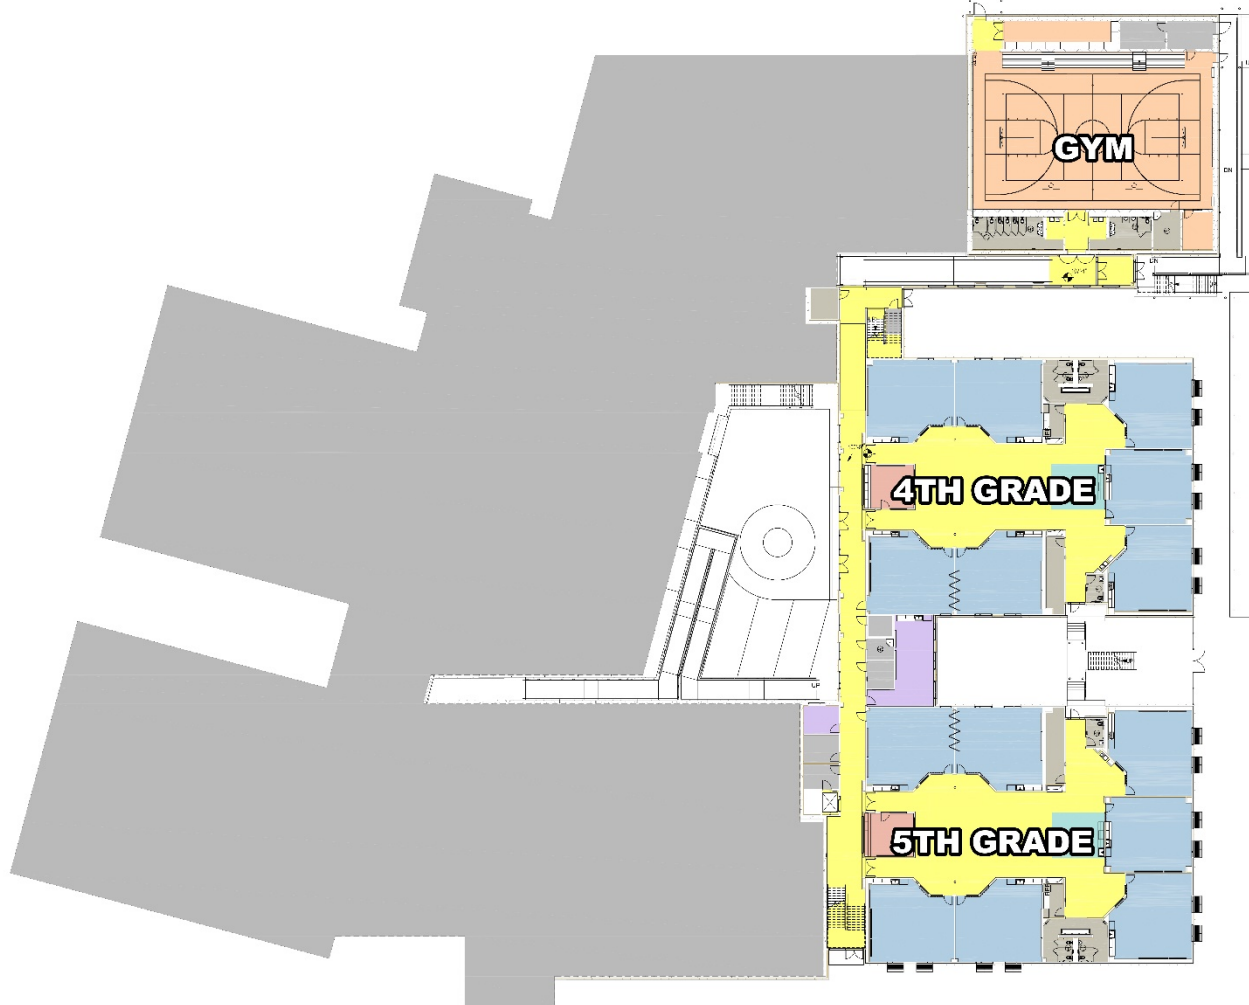

Composite Ground Level – Floor Plan

Thank you
