

HACIENDA LA PUENTE UNIFIED SCHOOL DISTRICT



School Site Improvement Projects

Regular Board Meeting
October 24, 2024

Business Services



PROJECT COMPLETE LIST

2024/2025



Site	Item Description	Funding Source	Completed Date
Fairgrove Academy	Playground & Shade Structure	Child Development	09/2024
Lassalette Elementary School	Inclusive Playground	Facilities	09/2024
Nelson Elementary School	Playground, Shade Structure, & Accessibility Path of Travel	Child Development	09/2024
Sierra Vista Middle School	HVAC Repair MPR Room	Facilities	09/2024
Dibble Adult Education	Phase II of Re-Roofing	Adult Ed	10/2024
Districtwide	Trip Hazard Repair/ Ramp Repair	Facilities	10/2024
Lassalette Elementary	Playground Restriping	Facilities	10/2024
Los Altos High School, Buildings 60s, 70s	Gym & Locker Room HVAC (65 tons of temporary HVAC units have been installed)	Facilities	10/2024
Wing Lane Elementary School	HVAC Repair	Facilities	10/2024

Projects Completed as of October 24, 2024

Fairgrove Academy – Playground & Shade Structure

NEW!



Projects Completed as of October 24, 2024



Lassalette Elementary School – Playground Restriping

NEW!

BEFORE



AFTER

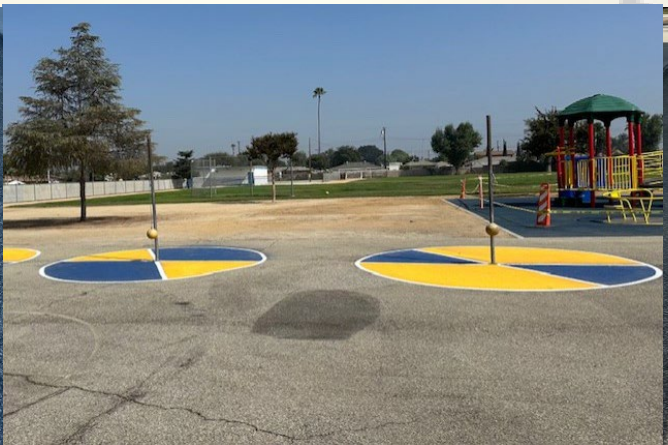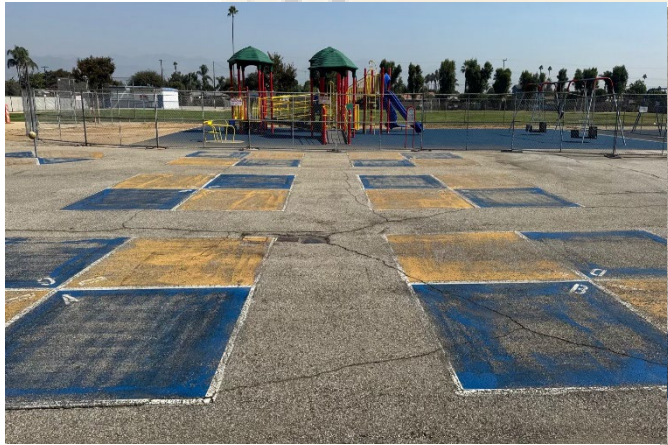

Projects Completed as of October 24, 2024

Lassalette Elementary School – Inclusive Playground

NEW!



Projects Completed as of October 24, 2024

Nelson Elementary School – Playground & Shade Structure

NEW!



NEW!

Projects Completed as of October 24, 2024

Districtwide – Trip Hazard Repair (Sierra Vista Middle School)



Projects Completed as of October 24, 2024

Districtwide – Ramp Repair

NEW!



Projects Completed as of October 24, 2024

Wing Lane Elementary School, Building 60 – HVAC Repair

NEW!



Projects In Progress

2024-2025



Projects in Progress as of October 24, 2024

Facilities

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
District Office	Data Center Move	Complete	N/A	Complete	Pending	ESSR/ General	TBD
Districtwide	HVAC System Replacement	Pending	TBD	TBD	TBD	Facilities	TBD
Grazide Elementary School	Portable 7	N/A	N/A	Pending	Pending	Facilities	TBD
Kwis Elementary School	Baseball Fields	Complete	Approved	In Progress	TBD	Grant	TBD
La Puente High School	Custom Shade Structure	Complete	Approved	Pending	Pending	Facilities	TBD
Los Altos High School	Stadium Press Box & Bleachers	Complete	Pending	Pending	Pending	Facilities	TBD
Stimson Learning Center	Phase II of re-roofing	Complete	Complete	Complete	In Progress	Facilities	12/ 2024
Wedgeworth Elementary School	K-5 Permanent School	Complete	Approved	Complete	In Progress	COPS	06/ 2025
Wilson High School	Media Center	Pending	TBD	TBD	TBD	Grant	06/ 2025
Wilson High School	Stadium Press Box & Bleachers	Complete	Pending	Pending	Pending	Facilities	TBD
Workman High School	Phase II Stadium and Baseball Field	Complete	Approved	Approved	In Progress	Facilities	TBD
Workman High School	Shade Structure, Wall, & Track Lighting	Complete	Pending	Pending	Pending	Facilities	TBD

Projects in Progress as of October 24, 2024

Child Development

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Amar Center	Entry Security Project	Complete	Approved	Pending	Pending	Child Development	TBD
Amar Center	Phase II of Re-Roofing	N/A	N/A	Pending	Pending	Child Development	TBD
Workman Elementary School Head Start	Playground & Accessibility Path of Travel	Pending	TBD	TBD	TBD	Child Development	TBD

Projects in Progress as of October 24, 2024

Adult Ed

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Center for the Performing Arts	Center for the Performing Arts	In Redesign	Complete	Pending	TBD	Adult Ed	TBD
Dibble Adult Ed	Admin Upgrade	In Progress	NA	TBD	TBD	Adult Ed	TBD
Willow Adult Ed	Marquee	Complete	NA	Pending	TBD	Adult Ed	TBD

Projects in Progress as of October 24, 2024

Nutrition Services

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Baldwin Academy	Kitchen Renovation - Three Compartment Sink Installation	Complete	NA	Pending	TBD	Food Services	TBD
District Office	Warehouse Freezer	Complete	NA	Pending	TBD	Food Services	TBD
Mesa Robles Middle School	Kitchen Renovation	Complete	Approved	Pending	TBD	Food Services	TBD
Wilson High School	Kitchen Modernization	Pending	Pending	Pending	TBD	Food Services	TBD



Next Report – December 17, 2024
