# 2018 Bond Program Executive Summary

Tammie Knauer – Bond Director September 18, 2024



## 2018 Bond Summary

<u>Strive 2025 Alignment</u> - Focus Area 4: <u>Stewardship</u> of Resources 4.3 Provide transparency in the use of district resources

#### **District Finances**

	Planned	Actual
Bond Program	\$149 mil	\$209 mil
85% in 3 years	Jan. 2022	Dec. 8, 2021

#### **District Facilities**

- > Completing what was promised & approved by our community
- > Inclusion of Community, Staff, Students with Oversight





## **Bond Timeline**







- > Work in Every Building & Charter Schools
- Finance / Materials & Procurement Coordination
- > Guidelines: Educational Specifications / Technical Guidelines / Fixtures, Furniture & Equipment






# Implementation

Schedule


THOMPSON

SCHOOL DISTRIC

- Design Process
- Site Coordination

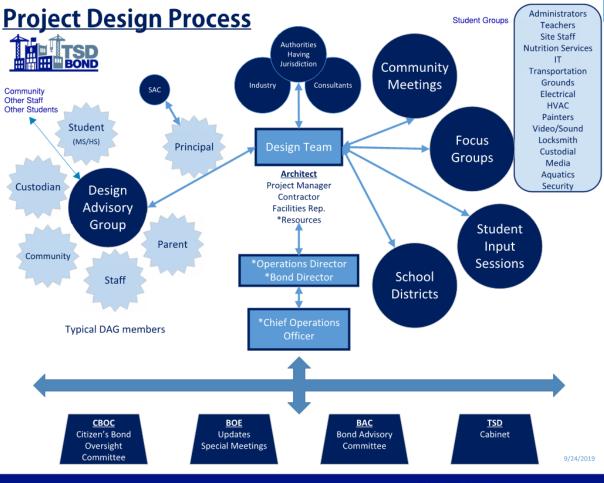

# **Budget Tracking**

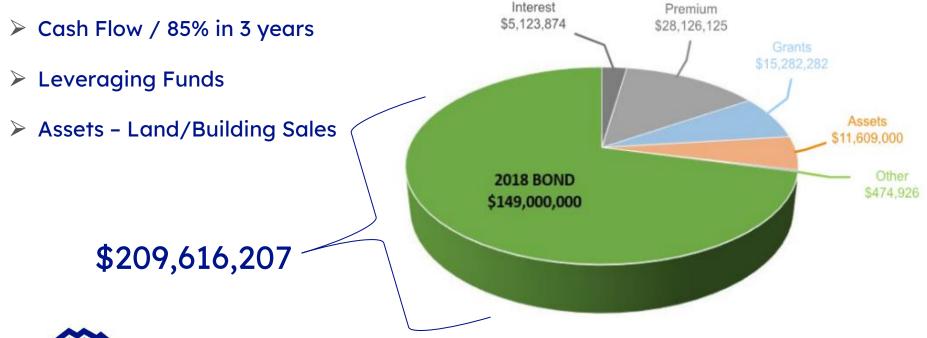







#### Most Rewarding Leveraging of Funds:

Grant/Source	Description	Funding
BEST	HVAC, Security, Inflation, Roof, Emergency	\$12,031,128
Head Start	ECE at Stansberry	\$2,389,402
The Colorado Health Foundation	Playground at PVA	\$700,000
ESSSR	Return to Learn	\$408,400
	Total:	\$15,528,930





## Contingency Projects - BOE 10/18/23

Project	Budget	Detail
High Priority Needs	\$1,800,000	BFKES, Big T., CMES, MVHS, TVHS
Safety/Security	\$620,000	3 Sites Radio. Doors/Hardware
LHS- Turf/Softball/Baseball	\$1,700,000	Also: ADA walkway to fields
Indoor Air Quality	\$2,000,000	AC: TMS, LHS, LEES, WCMS Commons
Main IT Server Room	\$375,000	Cooling, Fire Alarm System
Management	\$155,000	
	\$6,650,000	



<u>#WeAreThompson</u>

## Reporting / Transparency

- Citizen's Bond Oversight Committee
- > Bond Advisory Committee
- Board of Education
- Expense Reconciliation
- > Website

- Regular Meetings
- ✓ Diverse Members / Inclusion
- ✓ Visual Aids / Discussion and Reports
- Addressing Questions
- ✓ Updated Information







## **Reporting – Line Items**

BOND LINE ITEMS BY CATEGORY

#### 1,059 Bond Line Items

#### Tracked, Completed, Reported



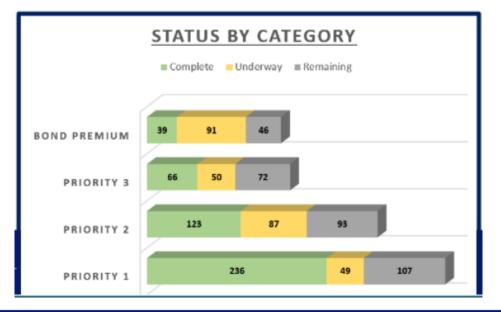



### COVID 19 - March 2020

- > 13 major projects underway @ \$90mil
- Social Distancing / Lockdowns / Daily PPE and work flow
- Spot Pricing and Inflation
- Supply Chain Issues and High Demand
  - ~ Schedule Not Compromised ~







#### Thank You Voters!

#### Every School ~ Added Scope ~ Inclusive ~ Transparent

	Planned	Actual
Bond Program	\$149 million	\$209 million
Premium	\$14.9 million	\$28.6 million
Interest	\$5.9 million	\$5.9 million
Grants	TBD	\$15.5 million
85% in 3 years	January 2022	December 8, 2021
Duration	5 years	6 years - added projects



