CLARENCE CENTRAL SCHOOL DISTRICT 2024 Capital Project Update

CI ARENCE

Kideney Architects



Together We Make Learning A Way Of Life

HIGH

SCHOOL

<u>AGENDA</u>

- Work To Date
- Building Summaries
- Budget Summary
- EPC Budget
- Upcoming Project Schedule
- Any Questions?






WORK TO DATE

- Review of Building Condition Survey
- Regular Meetings with Architects, Construction Management & District Administration
- Multiple Meetings with Board of Education Facilities Committee
- Funding Plan Prepared
- Scope of Work Determined
- Board Packet Prepared
- Public Presentations for Feedback



<u>HARRIS HILL</u>

- Playground Replacement
- Exterior Masonry & Concrete Repairs
- Replace Backflow Preventer
- Technology & PhoneUpgrades
- New Signage
- Building Budget: \$1,126,139

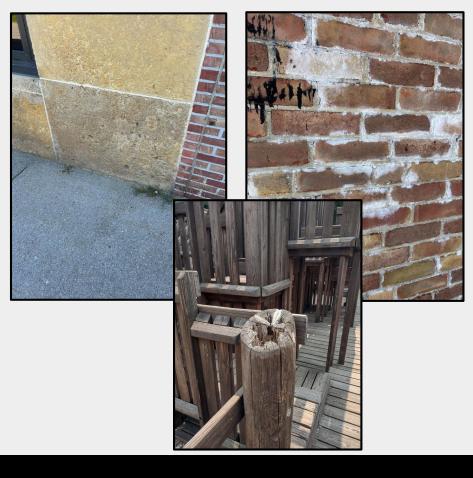



HARRIS HILL





<u>SHERIDAN HILL</u>

- East Parking Lot, Bus Drive, & Sidewalk Replacement w/ Drainage Upgrades
- Exterior Masonry & Concrete Repairs
- Septic Field Replacement
- Technology & Phone Upgrades
- New Signage
- Building Budget: \$1,035,995





CLARENCE CENTER

- Exterior Masonry Repairs
- Replace Kindergarten Exit Doors
- Window Replacement
- A/C for Technology Closet
- Replace Backflow Preventers
- Technology & Phone Upgrades
- New Signage
- Building Budget: \$539,120





LEDGEVIEW

- Exterior Masonry, Concrete & Railing Repairs
- Septic Tank Pump Replacements
- Replace Grease Trap
- Technology & Phone Upgrades
- New Signage
- Building Budget: \$640,898






MIDDLE SCHOOL

- Parking Lot Reconfiguration Including Drainage Upgrades
- Exterior Masonry Repairs
- Replace Freight Elevator
- PA System Upgrade
- Technology & Phone Upgrades
- New Signage
- Auditorium Sound System Upgrades
- Building Budget: \$3,746,371





MIDDLE SCHOOL

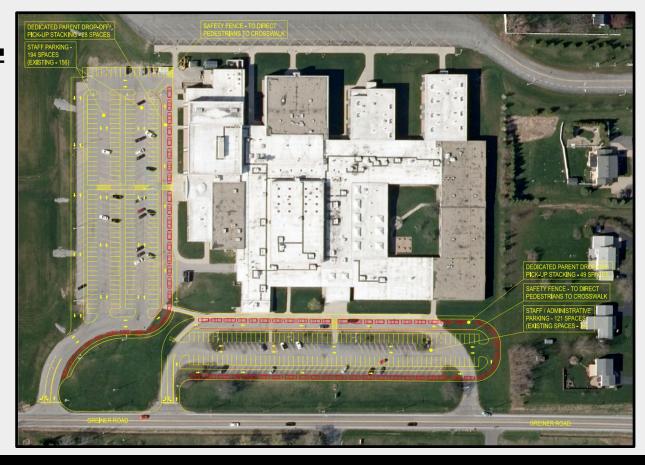



<u>HIGH SCHOOL</u>


- Front Parking Lot Reconfiguration
- Replace Site Lighting w/ New LED's
- Replace Running Track Surface
- Exterior Masonry Repairs
- Replace Sewer Line in 400 Wing Crawlspace
- Replace Select Rooftop Mechanical Units
- Select Interior Flooring ReplacementSpecial Ed office, old Weight Room
- Replace Damaged Exit Signs
- Technology & Phone Upgrades
- New Signage
- Building Budget: \$5,939,187







HIGH SCHOOL

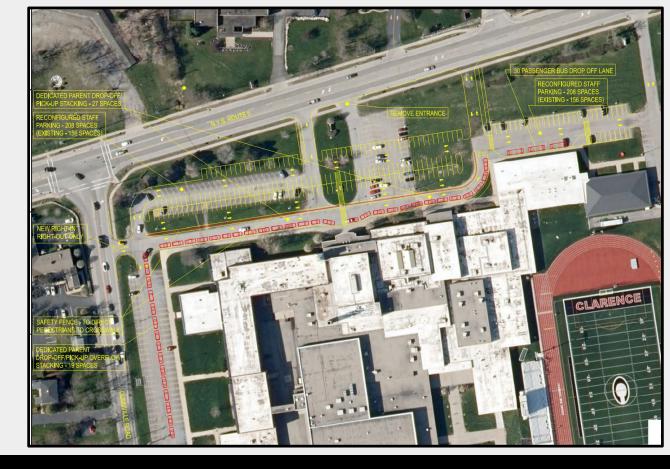



TECHNOLOGY

- Production Servers
- VDI Servers
- Wireless Access Points





DISTRICT-WIDE

- Emergency Exit Lighting Upgrades
- Signage All Buildings front signs and signs throughout campus





BUDGET SUMMARY

•	Harris Hill	\$1,126,139
•	Sheridan Hill	\$1,035,995
•	Clarence Center	\$539,120
•	Ledgeview	\$640,898
•	Middle School	\$3,746,371
•	High School	\$5,939,187
•	Subtotal	\$13,027,710
•	General Conditions, Contingencies	
	and Escalation	\$4,885,334
•	Subtotal	\$17,913,044
•	Project Incidental Costs (15%)	\$2 686 956

- Project Incidental Costs (15%) \$2,686,956
- Total Project Budget \$20,600,000



EPC (ENERGY PERFORMANCE CONTRACT)

- Upgrade to LED Lighting All School Buildings: \$5,600,000
- Replace HS Boilers:
- Project Fees:
- Project Contingencies: \$826,000
- EPC Total Budget: \$8,000,000





Together We Make Learning A Way Of Life

\$1,200,000

\$374,000

FINANCIAL CONSIDERATIONS

- Building Aid Ratio
 - **67.2%**
- Maximum Cost Allowance
- Capital Reserve Utilization
 - Anticipated \$3 Million
- Tax Neutral







UPCOMING PROJECT SCHEDULE

- October 2024- Board of Education Approval
 - SEQRA & Resolution
- November 2024- Public Hearing
- December 2024- Vote
- January to July 2025- Project Design
- August to November 2025- NYSED Review
- January 2026- Bids Received
- Spring 2026– Construction Starts





ANY QUESTIONS?



