

# Measure BB Bond

21st Century Classroom Improvements  
January 23, 2025



CUMMING  
GROUP

//////////////////// BUILDING VALUE THROUGH EXPERTISE





# HLPUSD MEASURE BB - SUMMARY

## SCHOOLS IN PROGRESS



### IN PROGRESS CONSTRUCTION

- Los Altos HS
- California ES
- Baldwin ES
- Los Molinos ES
- Graziade ES (Pending)

### READY TO BID 2-10-2025

- Kwis ES
- Fairgrove K-8
- Lassalette ES

### AT DSA FOR REVIEW

- Sierra Vista MS
- Palm ES
- Valinda ES
- Sparks ES
- Wing Lane ES
- Valley Alternative

### IN DESIGN

- Orange Grove MS

### COMPLETED

- Nelson ES
- Los Altos ES
- Workman ES
- Mesa Robles K-8
- Cedarlane K-8
- Sparks MS
- Grandview MS
- Newton MS
- Stimson EC
- Workman HS
- La Puente HS
- Wilson HS


# PHASE B PROGRESS 2024

	PROJECT STARTS	CONSTRUCTION DOCUMENTS TO DSA	DSA PLAN REVIEWS COMPLETED	PROJECTS BID	CONSTRUCTION STARTS (COMPLETED*)
La Puente HS Refresh	●	NA	NA	●	●*
Los Altos HS Refresh	●	NA	NA	●	●
Wilson HS Refresh	●	NA	NA	●	●*
Workman HS Refresh	●	NA	NA	●	●*
Stimson LC Refresh	●	NA	NA	●	●*
Baldwin ES	●	●	●	●	●
California ES	●	●	●	●	●
Grazide ES	●	●	●	●	
Los Molinos	●	●	●	●	●
Kwis ES	●	●	●		
Lassalette ES	●	●	●		
Fairgrove Academy	●	●	●		
Sierra Vista MS	●	●			
Sparks ES	●	●			
Palm ES	●	●			
Valinda ES	●	●			
Wing Lane ES	●	●			
Valley Alternative School	●	●			
Orange Grove	●				

**Estimated Completion: December 2026**

**Estimated Budget: \$148 million (Measure BB Bond Authorization)**

# HIGH SCHOOL REFRESH GROUP 2

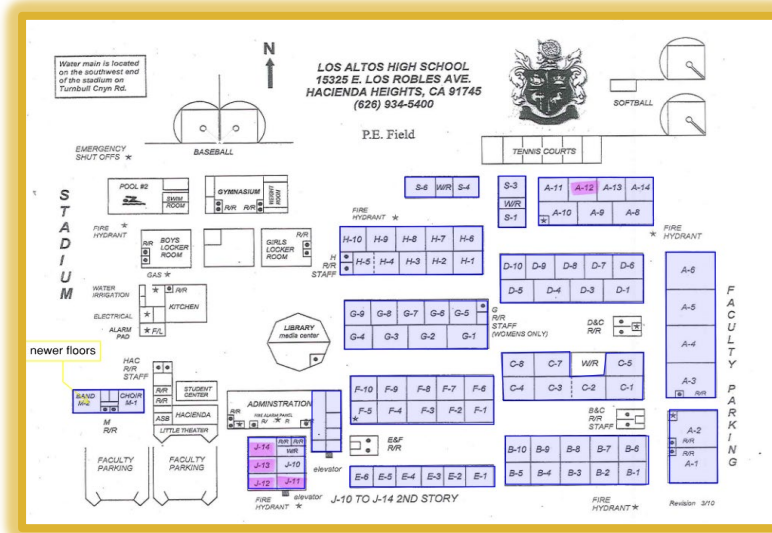

## LOS ALTOS HIGH SCHOOL 69 CLASSROOMS

SCHOOL	START DATE	ANTICIPATED COMPLETION DATE
WILSON HS	3/4/2024	Completed 48 days Ahead of Schedule
LOS ALTOS HS	3/4/2024	Phase 7: 4/18/2025 (Currently 68 Days Ahead of Schedule)




HIGH SCHOOL REFRESH  
IN PROGRESS

Los Altos High School





# Measure BB 21<sup>st</sup> Century Classroom Improvements Baldwin Academy

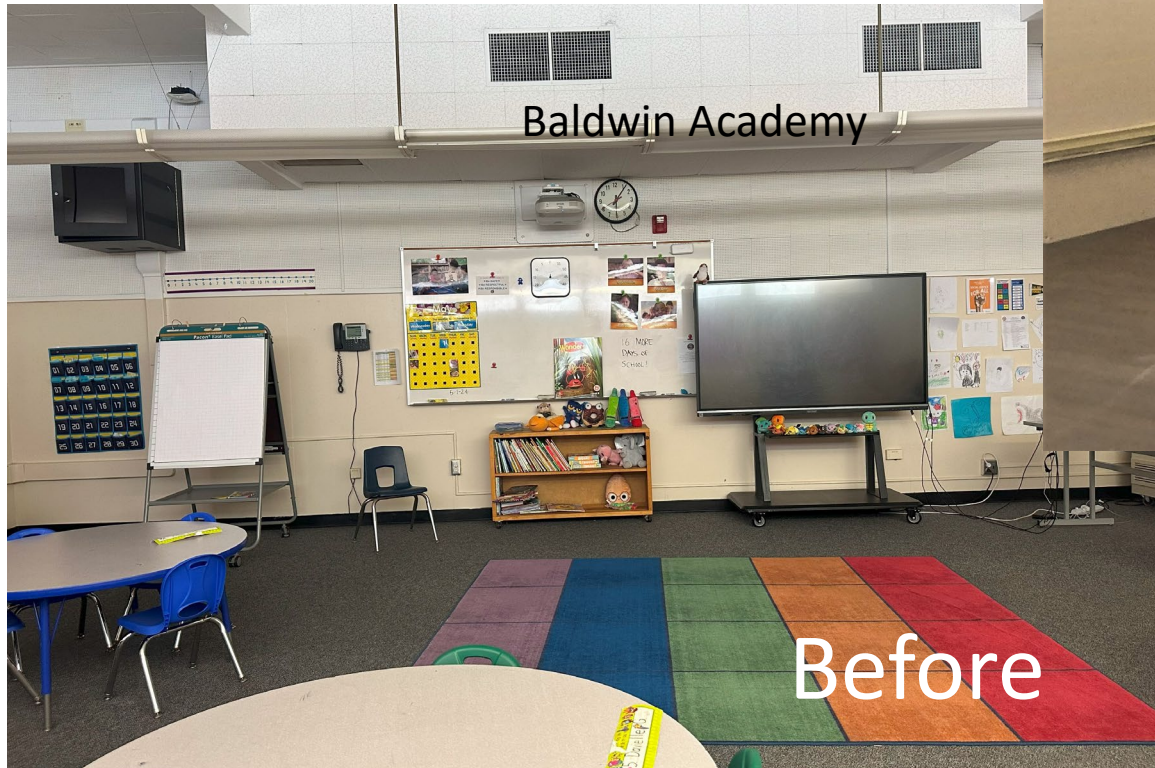

Start Date November 12, 2024  
Estimated Completion Date July 25, 2025



Measure BB 21<sup>st</sup> Century  
Classroom Improvements  
California Elementary School



IN PROGRESS



Before

Start Date November 12, 2024  
Estimated Completion Date August 25, 2025



# Measure BB 21<sup>st</sup> Century Classroom Improvements Los Molinos Elementary



Before



IN PROGRESS

Start Date November 12, 2024  
Estimated Completion Date August 25, 2025





QUESTIONS
