# HACTENIDA LA PUENTE UNITED SCHOOL DISTRICT











### School Site Improvement Projects

**Business Services** 



## PROJECT COMPLETE LIST COMPLETED 2024/2025

Site	Item Description	Funding Source	Completed Date
Cedarlane Academy	Gas Leak Repair	Facilities	1/2025
La Puente High School	Outside Lighting	Facilities	12/2024
La Puente High School	Gym Paint Refresh	Facilities	12/2024
Orange Grove Middle School	Landscape Clean-up	Facilities	12/2024
Sparks Middle School	Office Paint Refresh	Facilities	12/2024
Stimson Learning Center	Phase II of Re-roofing	Facilities	12/2024
Wilson High School	Gas Leak Repair	Facilities	12/2024
Dibble Adult Education	Trip Hazard Repair	Facilities	11/2024
District Office	Trip Hazard Repair	Facilities	11/2024
Grazide Elementary School	Portable 7 Refurbishment	Facilities	11/2024
Los Altos Elementary School	Portable Deep Clean	Facilities	11/2024
Wilson High School	Hazard Repair	Facilities	11/2024
Newton Middle School	Temporary Fencing	Facilities	10/2024

Dibble Adult School - Trip Hazard Repair













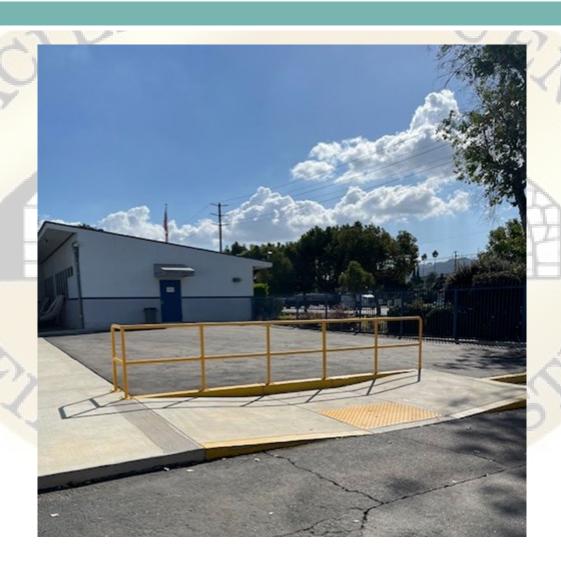




**Grazide Elementary School - Portable Refurbishment** 

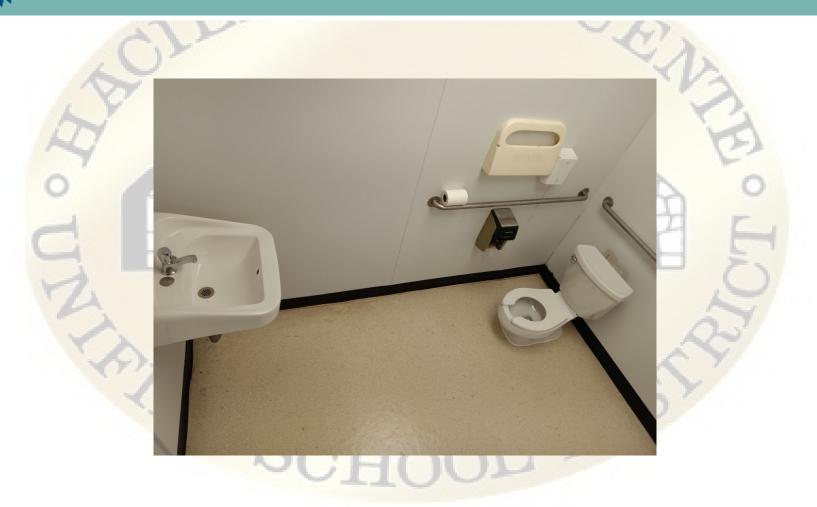


La Puente High School - Gym Paint Refresh

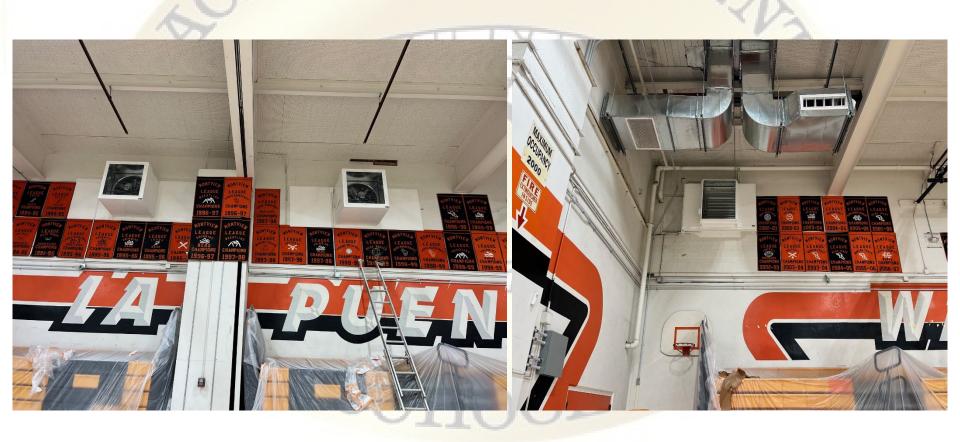

### La Puente High School – Lighting



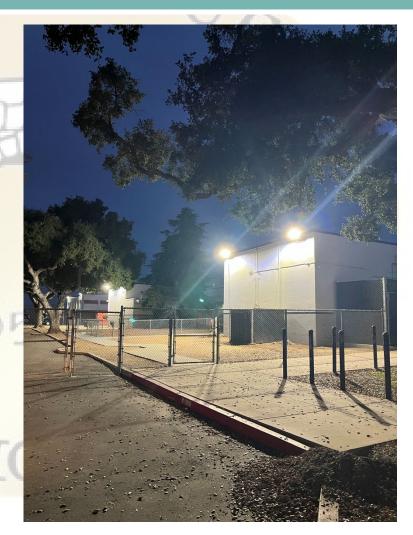














Wilson High School - Gas Leak Repair





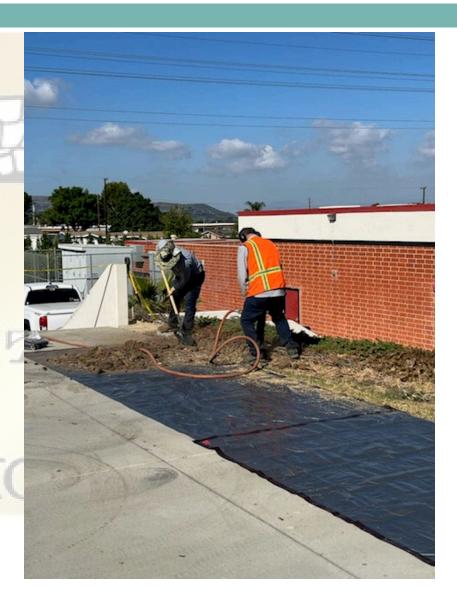

### TOALA

### Projects In Progress


2024-2025




#### **Facilities**

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
District Office	Data Center Move	Complete	N/A	Complete	In Progress	ESSR/General	04/2025
Districtwide	HVAC System Replacement	Pending	TBD	TBD	TBD	TBD	TBD
Districtwide	Network Upgrade Project	N/A	N/A	TBD	TBD	TBD	TBD
Kwis Elementary School	Baseball Fields	Complete	Approved	In Progress	TBD	Grant	TBD
La Puente High School	Custom Shade Structure	Complete	Approved	Pending	Pending	Facilities	12/2025
Los Altos High School	Stadium Press Box & Bleachers	Complete	Pending	Pending	Pending	Facilities	TBD
Newton Middle School	Fence	N/A	N/A	TBD	TBD	TBD	TBD
Wedgeworth Elementary School	K-5 Permanent School	Complete	Approved	Complete	In Progress	COPS	06/2025 (Potential Partial Soft Opening 4/2025)
Wilson High School	Classroom Sound Abatement	N/A	N/A	Pending	Pending	Facilities	TBD
Wilson High School	Media Center	Pending	TBD	TBD	TBD	Grant	06/2026
Wilson High School	Stadium Press Box & Bleachers	Complete	Pending	Pending	Pending	Facilities	TBD
Workman High School	Phase II Stadium and Baseball Field	Complete	Approved	Approved	In Progress	Facilities	12/2025
Workman High School	Shade Structure, Wall, & Track Lighting	Complete	Pending	Pending	Pending	Facilities	TBD 12

Wilson High School - Media Center Renderings

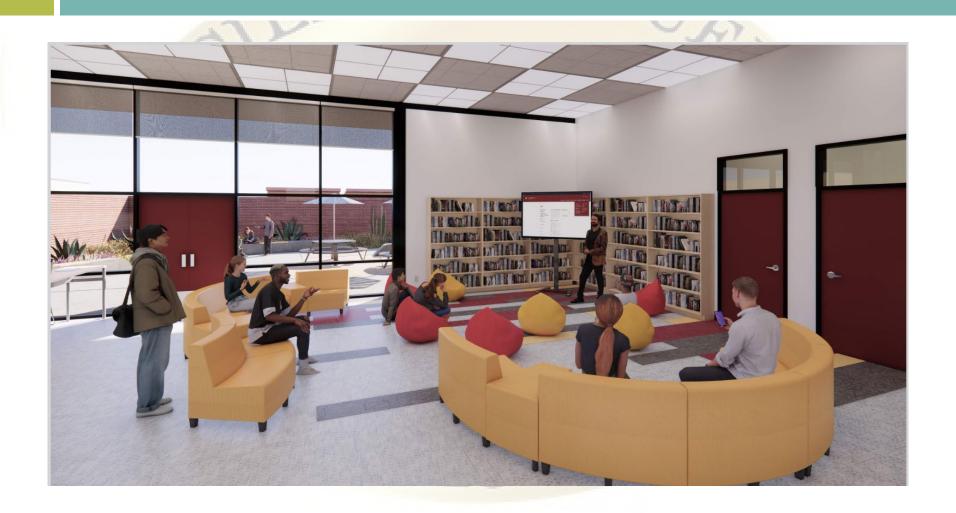

Wilson High School - Media Center Renderings

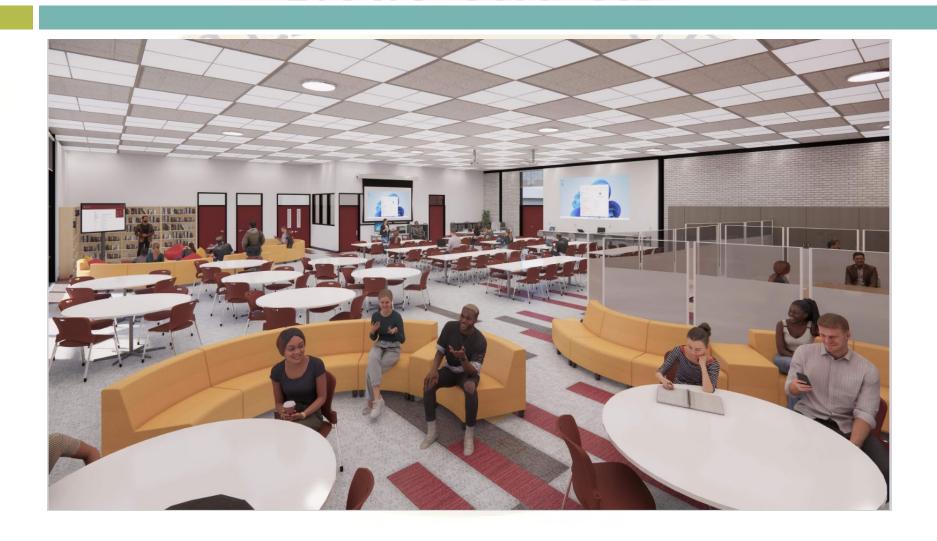

### **Child Development**

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Amar Center	Entry Security Project	Complete	Approved	Pending	Pending	Child Development	TBD
Amar Center	Phase II of Re-Roofing	N/A	N/A	Pending	Pending	Child Development	TBD
Workman Elementary School Head Start	Playground & Accessibility Path of Travel	Pending	TBD	TBD	TBD	Child Development	TBD

#### **Adult Ed**

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Center for the Performing Arts	Center for the Performing Arts	In Progress	Complete	Pending	TBD	Adult Ed	TBD
Dibble Adult Ed	Admin Upgrade	In Progress	NA	TBD	TBD	Adult Ed	TBD
Willow Adult Ed	Dental Office	NA	NA	In Progress	TBD	Adult Ed	TBD
Willow Adult Ed	Marquee	Complete	NA	In Progress	TBD	Adult Ed	TBD

#### **Nutrition Services**

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Baldwin Elementary School	Kitchen Renovation - Three Compartment Sink Installation	Complete	NA	In Progress	TBD	Food Services	TBD
District Office	Warehouse Freezer	Complete	NA	In Progress	TBD	Food Services	TBD
Mesa Robles Middle School	Kitchen Renovation	Complete	Approved	In Progress	TBD	Food Services	TBD
Wilson High School	Kitchen Modernization	Pending	Pending	In Progress	TBD	Food Services	TBD

19770

