

HACIENDA LA PUENTE UNIFIED SCHOOL DISTRICT



School Site Improvement Projects

Regular Board Meeting
February 27, 2025

Business Services



PROJECT COMPLETE LIST

2024/2025



Site	Item Description	Funding Source	Completed Date
Baldwin Academy	Restriping	Facilities	2/2024
Newton Middle School	Fence Installation	Facilities	2/2024
Los Altos High School	Paint Refresh	Facilities	2/2024
Valley High School	Paint Refresh	Facilities	2/2024
Wilson High School	Classroom Sound Abatement	Facilities	2/2024
Baldwin Academy	Trip Hazard Repair	Facilities	1/2024
Cedarlane Academy	Gas Leak Repair	Facilities	1/2024
La Puente High School	Outside Lighting	Facilities	12/2024
La Puente High School	Gym Paint Refresh	Facilities	12/2024
Orange Grove Middle School	Landscape Clean-up	Facilities	12/2024
Sparks Middle School	Office Paint Refresh	Facilities	12/2024
Stimson Learning Center	Phase II of Re-roofing	Facilities	12/2024
Wilson High School	Gas Leak Repair	Facilities	12/2024
Dibble Adult Education	Trip Hazard Repair	Facilities	11/2024
District Office	Trip Hazard Repair	Facilities	11/2024

Projects Completed as of February 27, 2025

Baldwin Academy – Trip Hazard Repair

NEW!



Projects Completed as of February 27, 2025

Baldwin Academy- Restriping

NEW!

BEFORE



AFTER



Projects Completed as of February 27, 2025

Newton Middle School – Fence Installation

NEW!



Projects Completed as of February 27, 2025

Los Altos High School – Paint Refresh

NEW!



Projects Completed as of February 27, 2025

Valley High School – Paint Refresh

NEW!



Projects In Progress

2024-2025



Projects in Progress as of February 27, 2025

Los Molinos Elementary Interim Housing Phase II



Projects in Progress as of February 27, 2025

Facilities

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
District Office	Data Center Move	Complete	N/A	Complete	In Progress	ESSR/General	04/2025
Districtwide	HVAC System Replacement	Pending	TBD	TBD	TBD	TBD	TBD
Districtwide	Network Upgrade Project	N/A	N/A	Complete	In Progress	ESSR	12/2026
La Puente High School	Custom Shade Structure	Complete	Approved	Complete	Pending	Surplus Property Sales	12/2025
Los Altos High School	Stadium Press Box & Bleachers	Complete	Pending	Pending	Pending	General Fund/ Surplus Property Sales	TBD
Sparks Middle School	Irrigation Project/ Tree Planting	N/A	N/A	Approved	In Progress	Grant	
Wedgeworth Elementary School	K-5 Permanent School	Complete	Approved	Complete	In Progress	COPS	06/2025
Wilson High School	Media Center	Pending	N/A	TBD	TBD	Grant	06/2026
Wilson High School	Stadium Press Box & Bleachers	Complete	Complete	Pending	Pending	General Fund	TBD
Workman High School	Phase II Stadium and Baseball Field	Complete	Approved	Approved	In Progress	General Fund/ Surplus Property Sales	12/2025
Workman High School	Shade Structure, Wall, & Track Lighting	Complete	Pending	Pending	Pending	General Fund/ Surplus Property Sales	TBD

Projects in Progress as of February 27, 2025

Sparks Middle School – Irrigation Project / Tree Planting



Projects in Progress as of February 27, 2025

Workman High School- ADA Ramp at Basketball Courts



Projects in Progress as of February 27, 2025

Workman High School – Football Field



Projects in Progress as of February 27, 2025

Child Development

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Amar Center	Entry Security Project	Complete	Approved	Complete	Pending	Child Development	TBD
Amar Center	Phase II of Re-Roofing	N/A	N/A	Complete	In Progress	Child Development	TBD
Workman Elementary School Head Start	Playground & Accessibility Path of Travel	Complete	Pending	TBD	TBD	Child Development	TBD


Projects in Progress as of February 27, 2025

Adult Ed

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Center for the Performing Arts	Center for the Performing Arts	In Progress	Complete	Pending	TBD	Adult Ed	TBD
Dibble Adult Ed	Front Entry Alterations & Conference Hall	Complete	NA	TBD	TBD	Adult Ed	TBD
Willow Adult Ed	Dental Office	NA	NA	Complete	In Progress	Adult Ed	TBD
Willow Adult Ed	Marquee	Complete	NA	Complete	Pending	Adult Ed	TBD

Projects in Progress as of February 27, 2025

Dibble Adult School – Front Entry Alterations Renderings

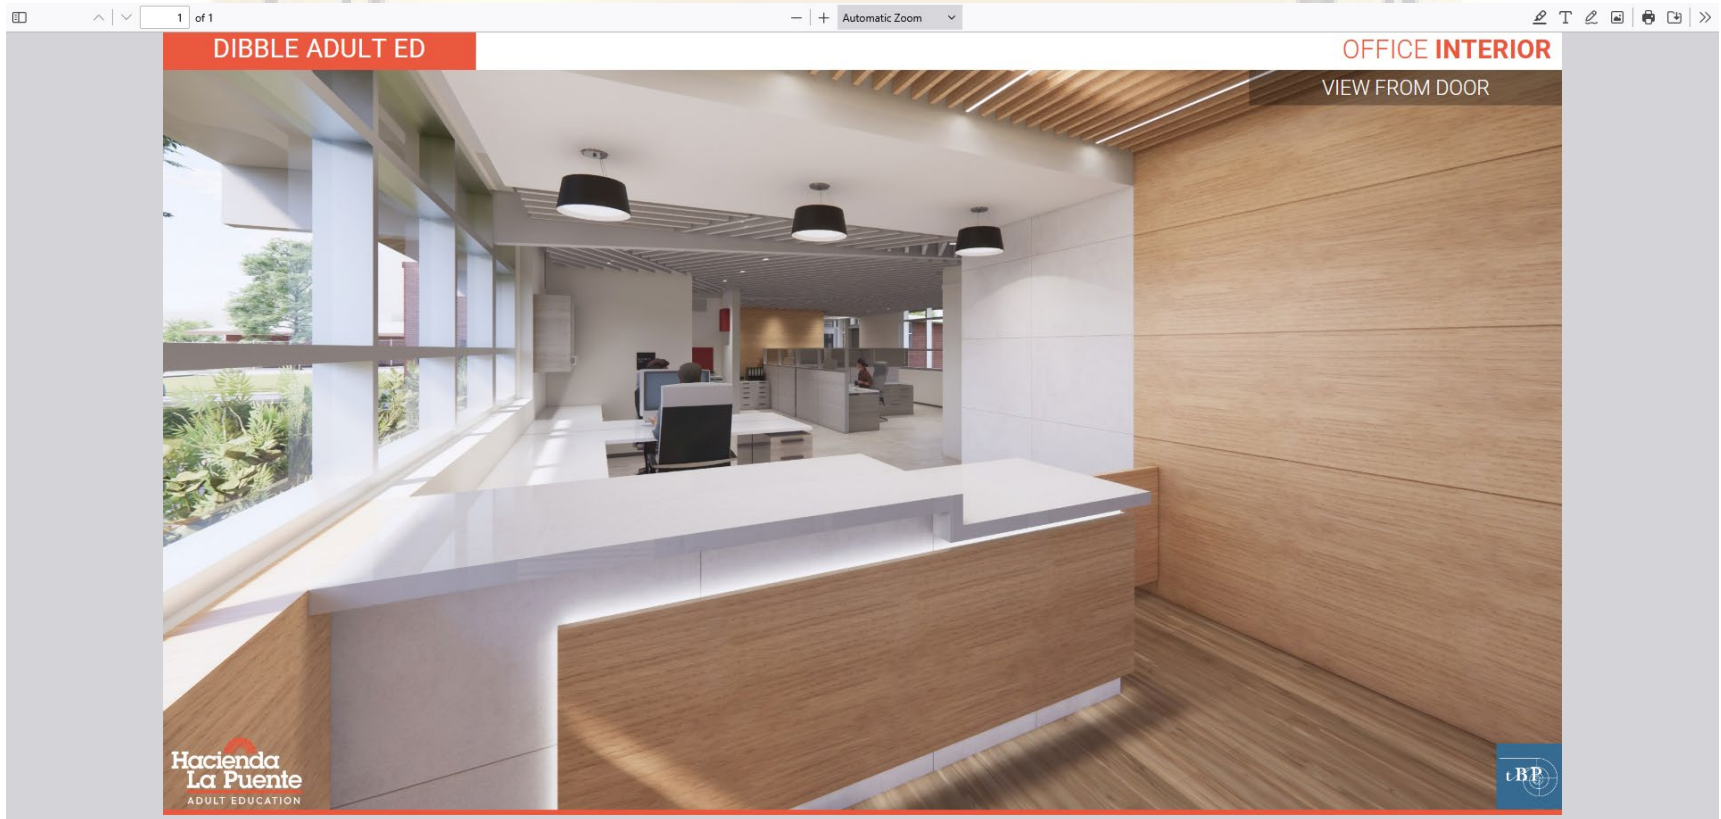

Projects in Progress as of February 27, 2025

Dibble Adult School – Conference Hall Renderings



Projects in Progress as of February 27, 2025

Nutrition Services

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Baldwin Elementary School	Kitchen Renovation - Three Compartment Sink Installation	Complete	NA	In Progress	TBD	Food Services	TBD
District Office	Warehouse Freezer	Complete	NA	Complete	Pending	Food Services	TBD
Mesa Robles Middle School	Kitchen Renovation	Complete	Approved	Complete	Pending	Food Services	TBD
Wilson High School	Kitchen Modernization	Pending	Pending	In Progress	TBD	Surplus Property Sales	TBD

Projects in Progress as of February 27, 2025

Wilson High School – Kitchen Modernization Renderings



Projects in Progress as of February 27, 2025

Wilson High School – Kitchen Modernization Renderings



Changes And Progress Since Last Report - Blue



Next Report – March 24, 2025
