




New Construction

PROGRESS UPDATE
March 2025

Fairport Harbor New Pre K-12 School



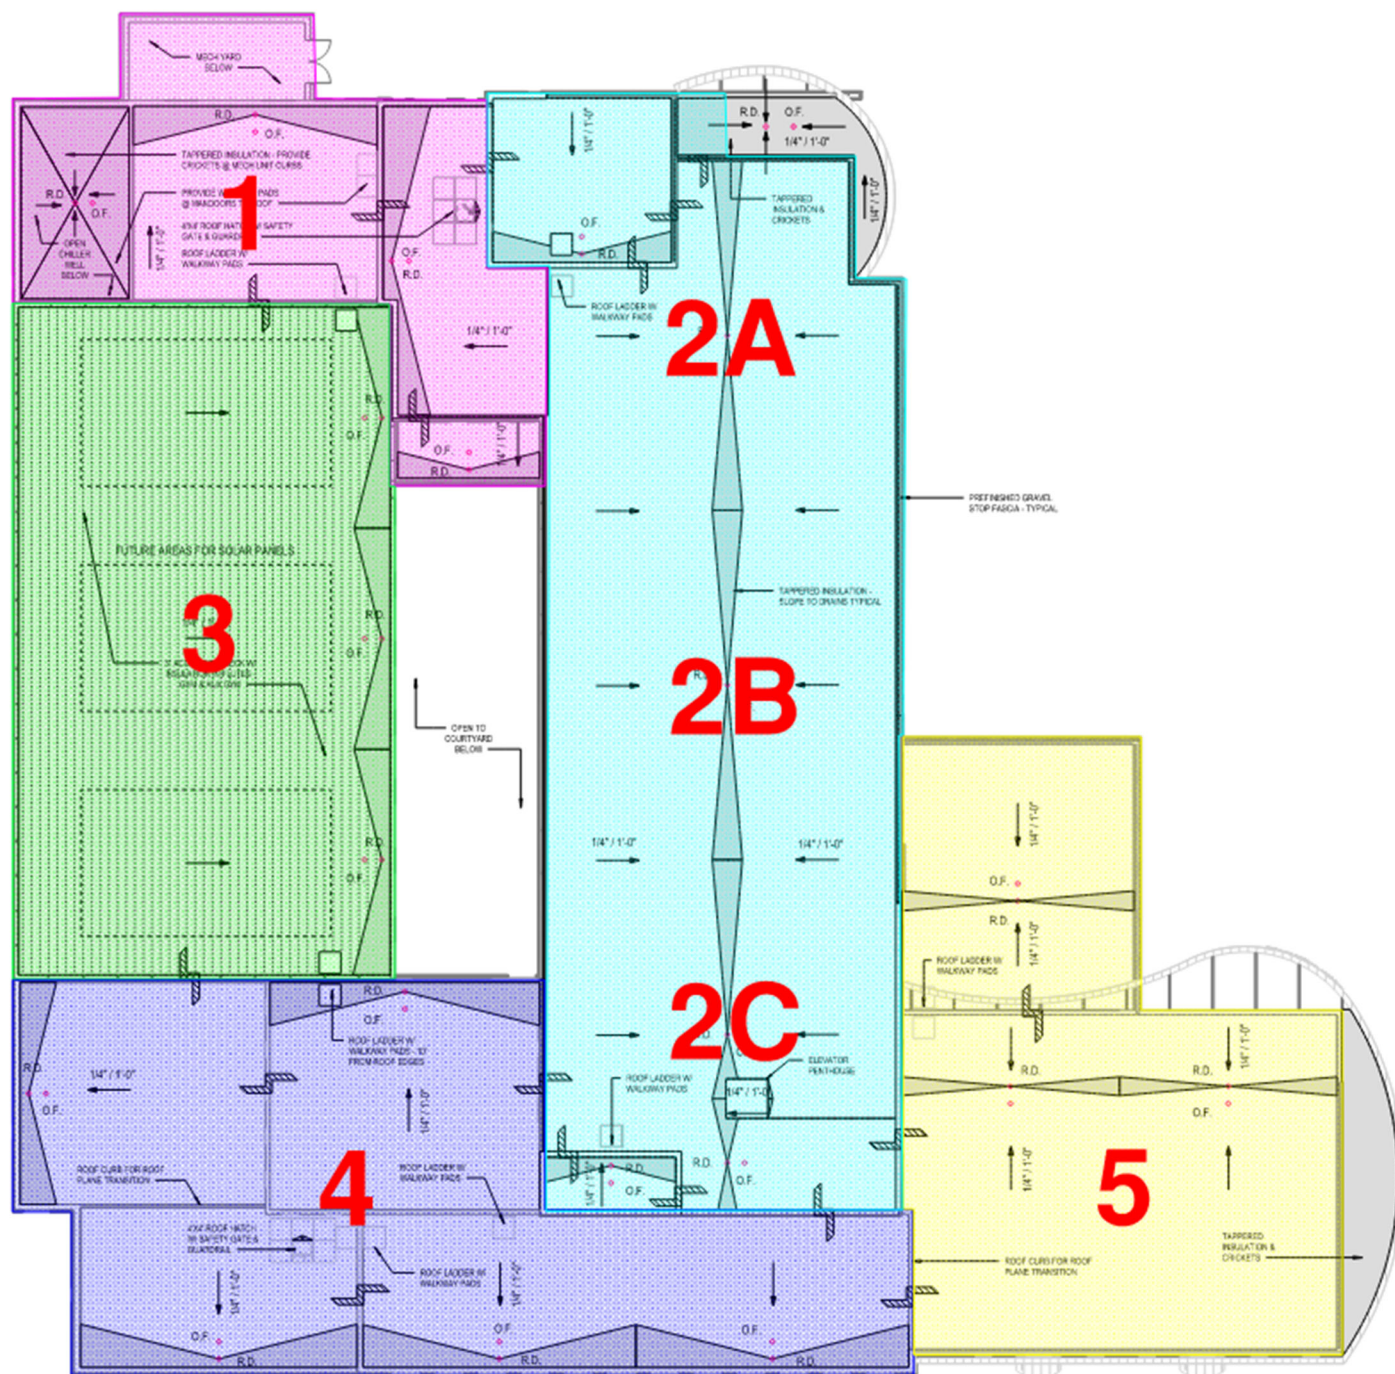

PROJECT SUMMARY

Phase 1


- Accessory Storage Areas
- Main Electrical Room
- Locker Rooms
- Exercise Rooms
- Mechanical Equipment Room

March 2025 Progress



- Building Locker Bench Bases—Complete
- Mechanical Piping Insulation—Complete
- Caulking Masonry Control Joints—Complete
- Duct Insulation—In Progress
- Drywall Taping—In Progress

Upcoming Progress

- Wall Painting

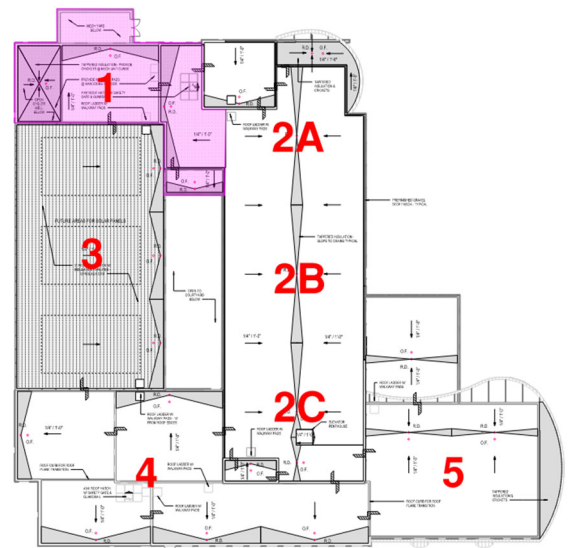

PROJECT SUMMARY

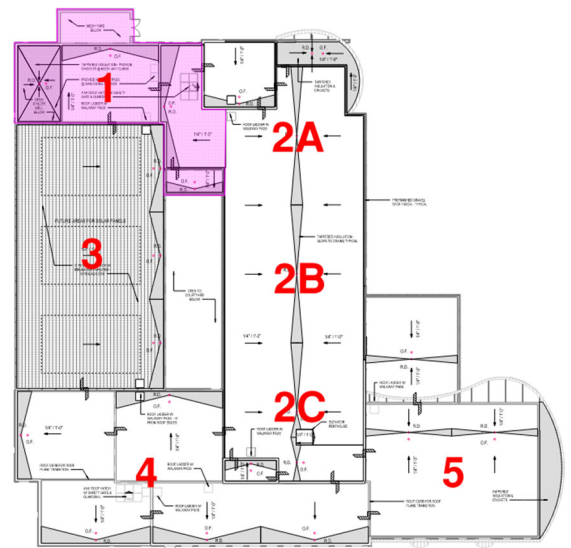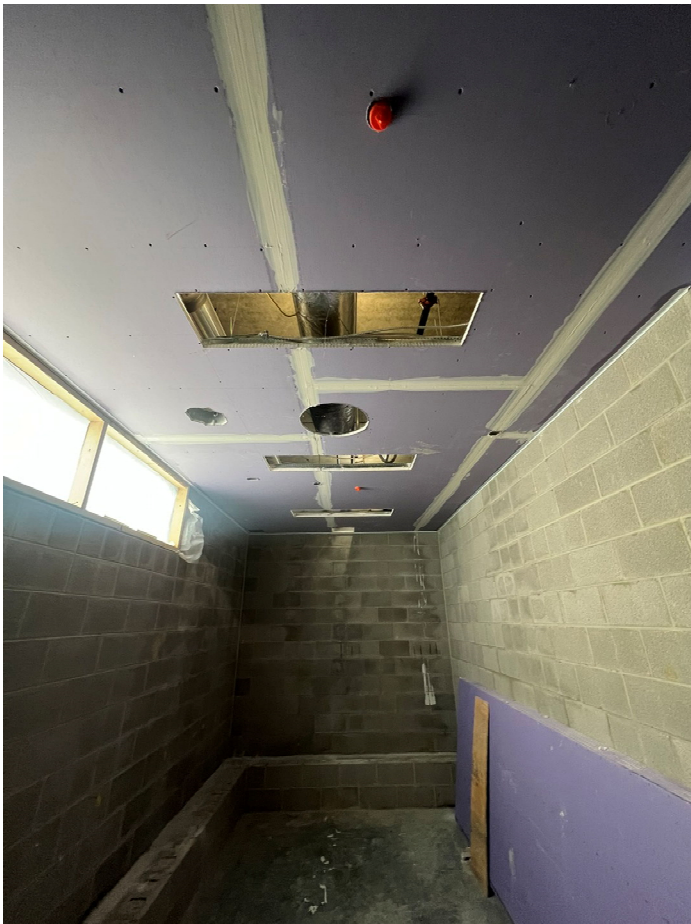

PROJECT SUMMARY

Phase 2


- Educational Classrooms

March 2025 Progress


- Overhead Plumbing Rough In on 3rd Floor—In Progress
- Overhead Electrical Rough In on 3rd Floor—Complete
- Hanging Drywall 2nd and 3rd Floor—In Progress
- Stair Tower 1 Joist and Roof Deck—In Progress
- Sprinkler Piping on 2nd Floor—In Progress
- Duct and Pipe Insulation—In Progress
- In Wall Rough In's on 3rd Floor—In Progress
- Veneer on Eastside—In Progress
- Roof Membrane—Complete

Upcoming Progress

- Wall Priming/Painting
- Windows

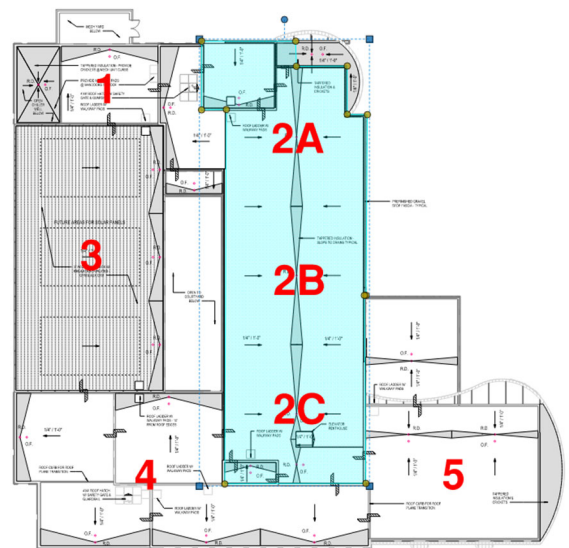

PROJECT SUMMARY

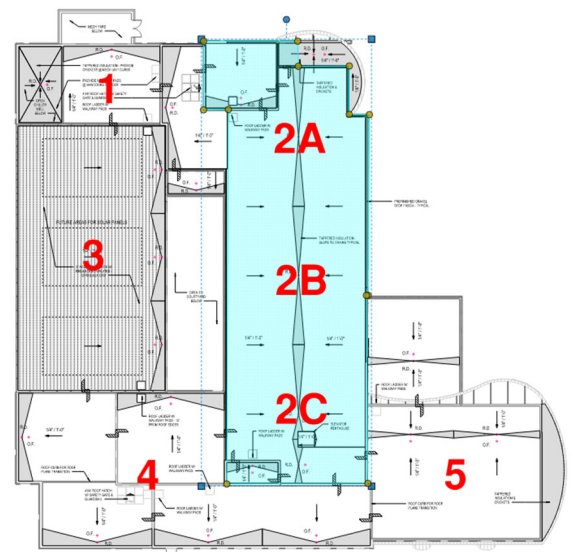

PROJECT SUMMARY

Phase 3


- **Auxiliary GYM**
- **Gymnasium**

March 2025 Progress



- **Overhead Electrical—In Progress**
- **Caulking Control Joints—Complete**
- **Drywall Finishing at Demising Wall—In Progress**
- **Prime/Paint—In Progress**
- **Overhead Technology Rough Ins—In Progress**

Upcoming Progress

- **Exterior Patch Work**

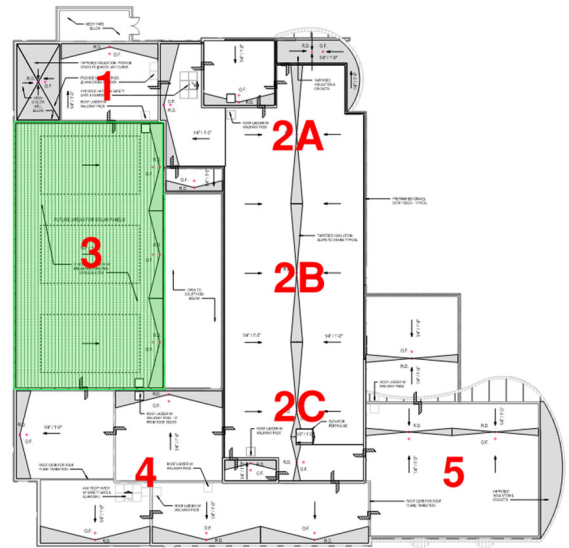

PROJECT SUMMARY

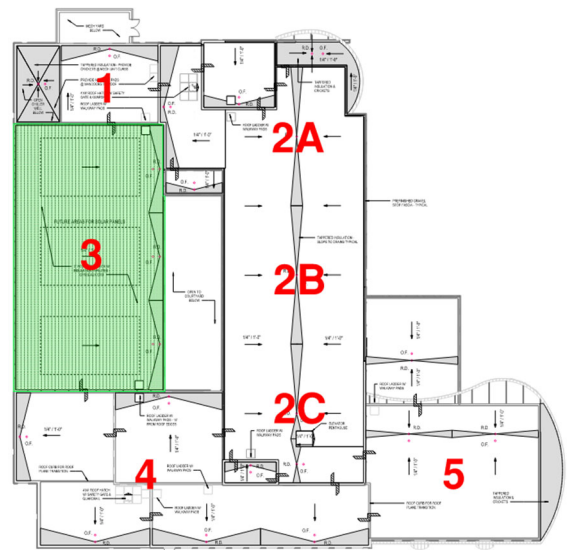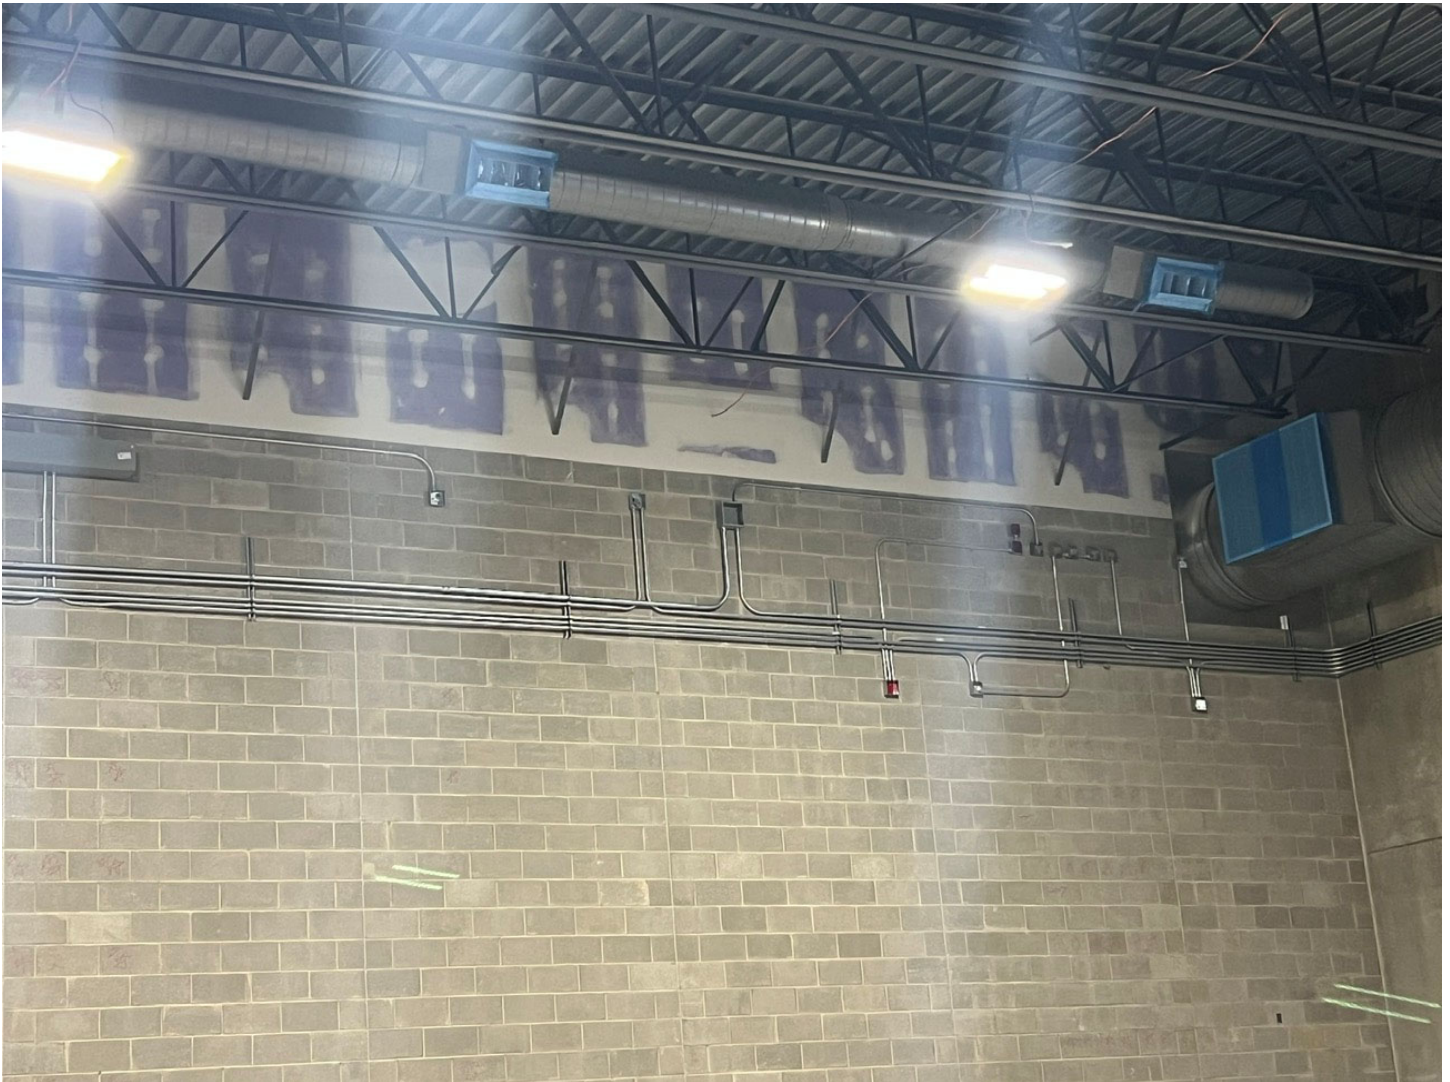

PROJECT SUMMARY

Phase 4 (West Half)


- Kitchen
- Locker Room

March 2025 Progress


- Masonry to Bearing—Complete
- Interior Nonbearing Walls—In Progress
- Joist and Deck—In Progress
- In Wall Electrical Rough In—In Progress
- In Wall Plumbing Rough In—In Progress

Upcoming Progress

- Structural Cold Form Metal Framing
- Roof Membrane

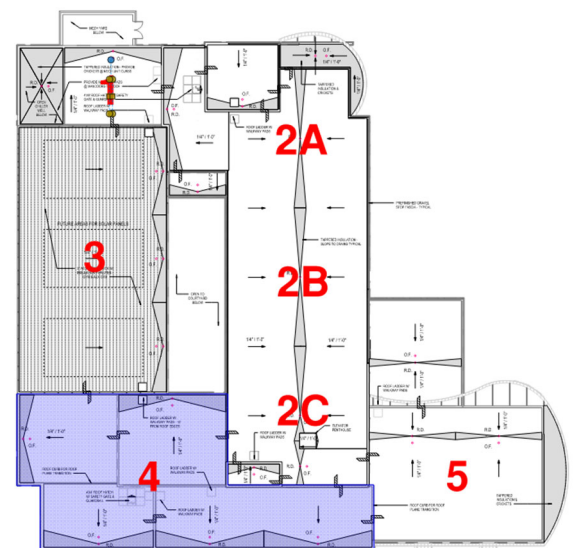

PROJECT SUMMARY

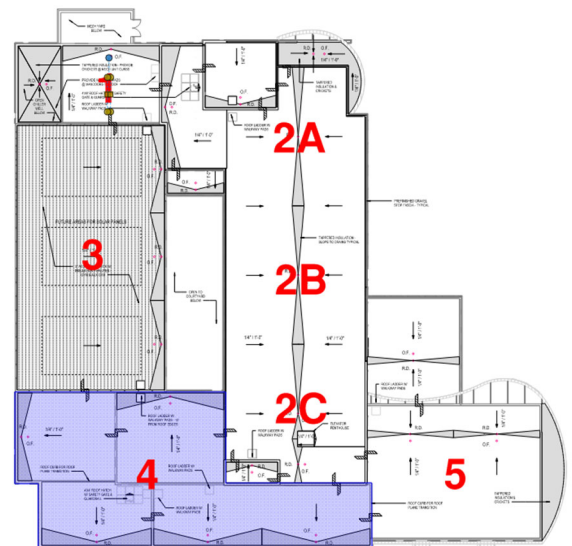

PROJECT SUMMARY

Phase 5

- Administration
- Library

March 2025 Progress

- Foundations—Complete

Upcoming Progress

- Underground Plumbing
- Underground Electrical
- Masonry to Grade
- Slab on Grade Prep

