



Monthly Progress Report

May 2025

Hempstead Union Free School District



Report prepared by Idris Mashriqi





Table of Contents

Section I – Program Summary

Section II – Work Progress May 2025

Section III – Work Projected for June 2025

Section IV – Progress Photos

Section V – Monthly Workforce Summary



Section I – Program Summary

May 2025

Project List

- **Hempstead UFSD – Phase 1 Infrastructure Upgrades @ HS – In Progress**
 - Staircase railings upgrades.
 - Classroom wall upgrades per code.
 - Install eye wash stations.
 - Install new exhaust fans.
 - Install new kitchen Ansul system valves.
- **Hempstead UFSD – Tennis Courts @ HS – In Progress**
 - Remove old asphalt tennis grounds.
 - Install new tennis courts with bleachers.
 - Install a bridge for students to access the tennis courts.



Section II - Work Progress

May 2025

Hempstead UFSD – HS Priority Infrastructure Upgrades

- Total:
 - Completed stair 20 in the pool area.
 - Received punch list from BBS.
- IMC:
 - Received punch list from BBS.
 - Started punch list items.

Hempstead UFSD – HS Tennis Courts

- United Paving
 - Installed stone roadway to courts.
 - SWPPP protection installed.
 - Completed existing asphalt removal
 - Completed retaining wall footings and walls.
 - Backfilled around retaining walls.
 - Installed storm tech drainage system.



Section III - Work Planned June 2025

Hempstead UFSD – HS Priority Infrastructure Upgrades

- Total:
 - Prepare for summer work. (C building classrooms, Handi lift, A building interior ramp)
- IMC
 - Prepare for summer work. (Complete balancing and punch list)

Hempstead UFSD – HS Tennis Courts

- United Paving
 - Install drainage piping.
 - Install mow strip concrete.
 - Start tennis court grading.



Section IV – Progress Photos



Hempstead HS – Roadway to Tennis Courts



Section IV – Progress Photos



Hempstead HS – Removal of Old Tennis Courts



Section IV – Progress Photos



Hempstead HS – SWPPP Protection



Section IV – Progress Photos



Hempstead HS – Retaining Wall Footings and Walls



Section IV – Progress Photos



Hempstead HS – Drainage Behind Retaining Walls




Section V – Workforce Summary – Company/Hours

May 2025

Manpower Chart

MANPOWER GRAPH

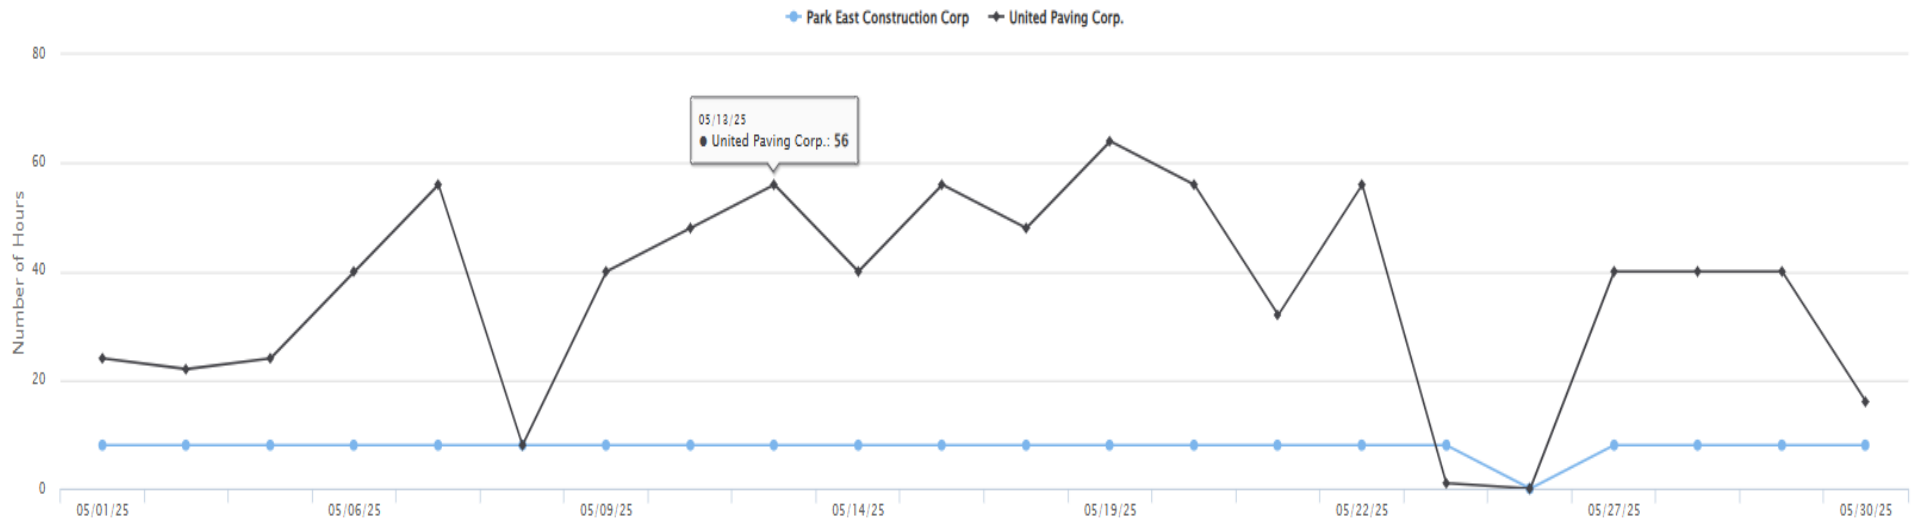

Hempstead HS – Tennis Courts



Hempstead Union Free School District

May 2025

End of Progress Report
