

HACIENDA LA PUENTE UNIFIED SCHOOL DISTRICT



School Site Improvement Projects

Regular Board Meeting
April 17, 2025

Business Services



PROJECT COMPLETE LIST


2024/2025



Site	Item Description	Funding Source	Completed Date
Los Altos High School	Countertops	Facilities	2/2025
Workman Elementary School	Student Restroom Floor	Facilities	2/2025
Baldwin Academy	Restriping	Facilities	2/2025
Newton Middle School	Fence Installation	Facilities	2/2025
Los Altos High School	Paint Refresh	Facilities	2/2025
Valley High School	Paint Refresh	Facilities	2/2025
Wilson High School	Classroom Sound Abatement	Facilities	2/2025
Baldwin Academy	Trip Hazard Repair	Facilities	1/2025
Cedarlane Academy	Gas Leak Repair	Facilities	1/2025
La Puente High School	Outside Lighting	Facilities	12/2024
La Puente High School	Gym Paint Refresh	Facilities	12/2024
Orange Grove Middle School	Landscape Clean-up	Facilities	12/2024
Sparks Middle School	Office Paint Refresh	Facilities	12/2024
Stimson Learning Center	Phase II of Re-roofing	Facilities	12/2024

Projects Completed as of April 17, 2025

Los Altos High School – Countertops

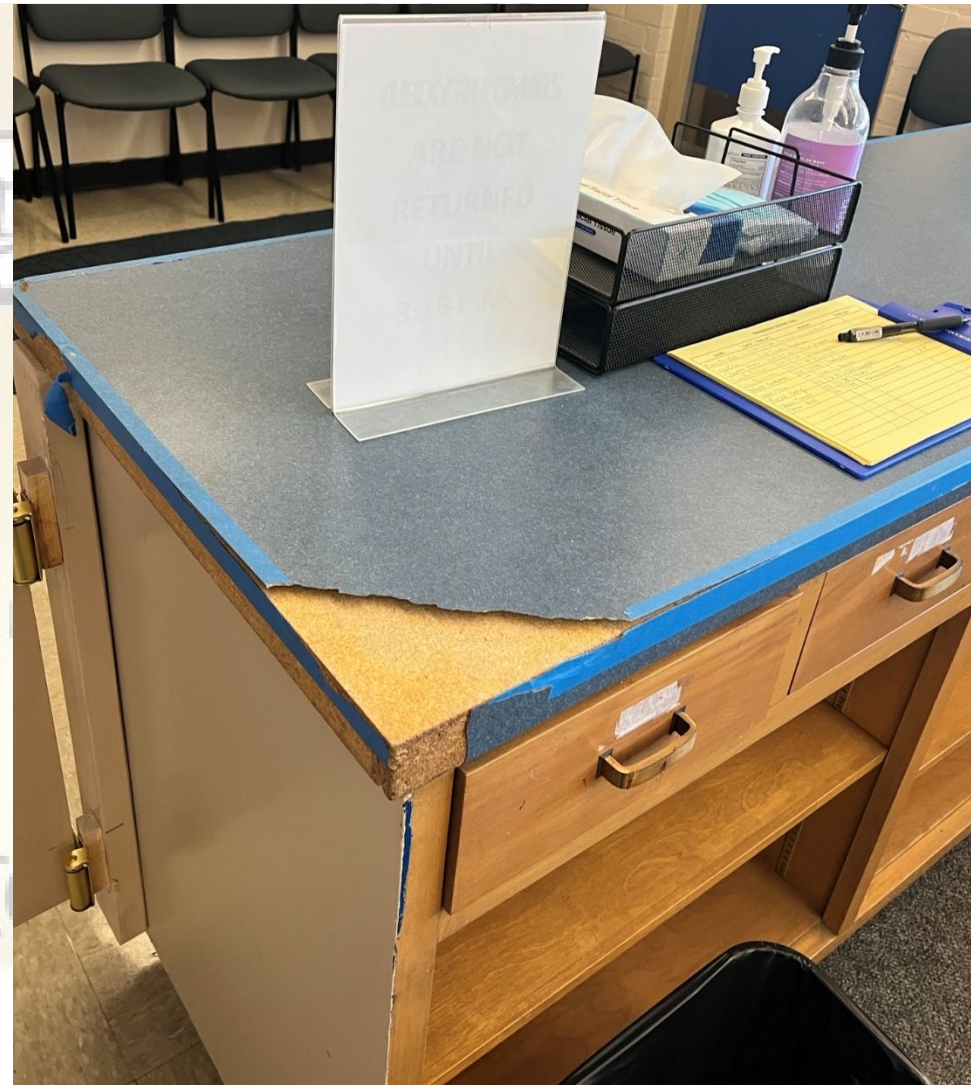

Projects Completed as of April 17, 2025

Los Altos High School – Countertops



Projects Completed as of April 17, 2025



Workman Elementary School – Bathroom Floor



Projects Completed as of April 17, 2025

Workman Elementary School – Bathroom Floor



Projects In Progress

2024-2025



Projects in Progress as of April 17, 2025

Facilities

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
District Office	Data Center Move	Complete	N/A	Complete	In Progress	ESSR/General	04/2025
Districtwide	HVAC System Replacement	Pending	TBD	TBD	TBD	TBD	TBD
Districtwide	Network Upgrade Project	N/A	N/A	Complete	In Progress	ESSR	12/2026
La Puente High School	Custom Shade Structure	Complete	Approved	Complete	In Progress	Surplus Property Sales	12/2025
Los Altos High School	Stadium Press Box & Bleachers	Complete	Pending	TBD	TBD	General Fund/ Surplus Property Sales	TBD
Sparks Middle School	Irrigation Project/ Tree Planting	N/A	N/A	Approved	In Progress	Grant	04/2025
Wedgeworth Elementary School	K-5 Permanent School	Complete	Approved	Complete	In Progress	COPS	06/2025
Wilson High School	Media Center	Pending	N/A	Complete	TBD	Grant	06/2026
Wilson High School	Stadium Press Box & Bleachers	Complete	Complete	Complete	Pending	General Fund	TBD
Workman High School	Phase II Stadium and Baseball Field	Complete	Approved	Approved	In Progress	General Fund/ Surplus Property Sales	12/2025
Workman High School	Shade Structure, Wall, & Track Lighting	Complete	Pending	TBD	TBD	General Fund/ Surplus Property Sales	TBD

Projects in Progress as of April 17, 2025

Child Development

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Amar Center	Entry Security Project	Complete	Approved	Complete	In Progress	Child Development	07/2025
Amar Center	Phase II of Re-Roofing	N/A	N/A	Complete	In Progress	Child Development	04/2025
Workman Elementary School Head Start	Playground & Accessibility Path of Travel	Complete	Pending	TBD	TBD	Child Development	TBD

Projects in Progress as of April 17, 2025

Adult Ed

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Center for the Performing Arts	Center for the Performing Arts	In Progress	Complete	Pending	TBD	Adult Ed	TBD
Dibble Adult Ed	Front Entry Alterations & Conference Hall	Complete	NA	TBD	TBD	Adult Ed	TBD
Willow Adult Ed	Dental Office	NA	NA	Complete	In Progress	Adult Ed	TBD
Willow Adult Ed	Marquee	Complete	NA	Complete	In Progress	Adult Ed	TBD

Projects in Progress as of April 17, 2025

Nutrition Services

Site	Item Description	Architect Plans	DSA Approval	Procurement	Construct	Funding Source	Target Completion Date
Baldwin Elementary School	Kitchen Renovation - Three Compartment Sink Installation	Complete	NA	In Progress	TBD	Food Services	08/2025
District Office	Warehouse Freezer	Complete	NA	Complete	Pending	Food Services	10/2025
Mesa Robles Middle School	Kitchen Renovation	Complete	Approved	Complete	Pending	Food Services	09/2025
Wilson High School	Kitchen Modernization	Pending	Pending	In Progress	TBD	Surplus Property Sales	TBD



Next Report – May 8, 2025
