




Quarterly Executive Summary  
Phase V – Tennis Court Projects  
Q2 2025

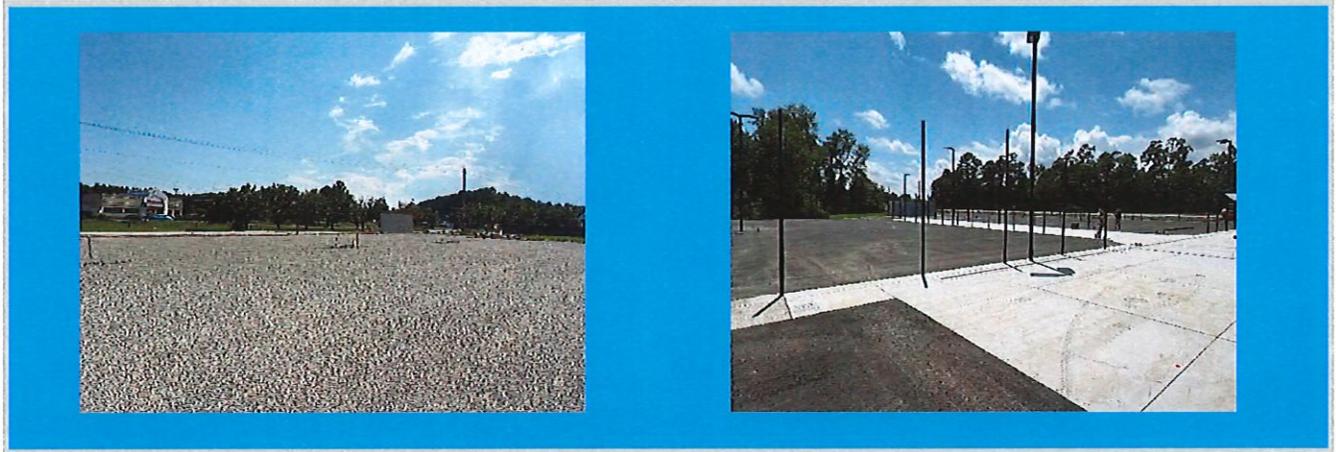

**HCS Project Manager:** Trevor Turner

**Schools:** Aynor High School, North Myrtle Beach High School, St. James High School, and Socastee High School

**Architect/Engineer:** CHA Consulting

**Contractor:** Contract Construction

**Project Scope:** To upgrade athletics at all nine high schools, with a focus on tennis courts, running tracks, and stadium playing surfaces. Current phase addresses tennis courts at four facilities. Additional school parking improvements were added to the scope and budget at North Myrtle Beach High School and St. James High School.

**Current Status:** Under Construction.

**Budget:** \$5,000,000 Board Approved Date: May 1, 2023  
\$ 500,000 Board Approved Additional Funding Date: May 13, 2024  
\$5,500,000

**Budget Issues:** None.

**Schedule:** **North Myrtle Beach High:** Completed  
**St. James High:** Tennis Complete. Awaiting permits from coastal agencies for parking lot at St. James High School.  
**Aynor High:** Working through some pavement and patch issues with design team and contractor, completion delayed until Fall  
**Socastee High:** Tennis In-Progress; expected completion 9/1/25

**Schedule Issues:** None.

**Achievements:** NMBH & SJHS tennis completed.
