




Quarterly Executive Summary Black Water Middle Outside Air Unit Replacement Q2 2025

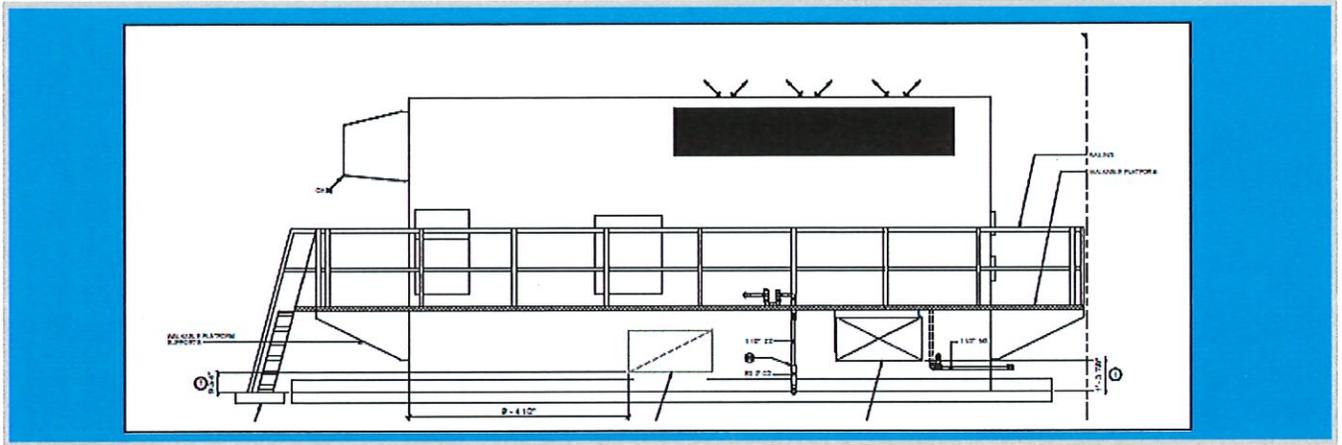

Project Manager: Amber Barnhill

Principal: Brandice Gore

Design: RMF Engineering, Inc.

Contractor: Piedmont Service Group, LLC

Project Scope: Replacement of Outside Air Units

Current Status: The project was awarded to Piedmont Service Group, LLC. The three MAU's have been ordered. There is long lead time on these units. They're expected to arrive in October. Piedmont has completed their part inside of the building that can be done for now. Minor fire alarm work to finish inside.

Budget: Original Budget: \$1,500,000.00 Board Approved Date: May 13, 2024

Budget Issues: None

Schedule: Project to be completed during Fall of 2025. Schedule is dependent on mechanical equipment lead times.

Schedule Issues: None

Achievements: The project has been awarded.
