




**Quarterly Executive Summary
Burgess Elementary Outdoor Air Unit Replacement
Q2 2025**

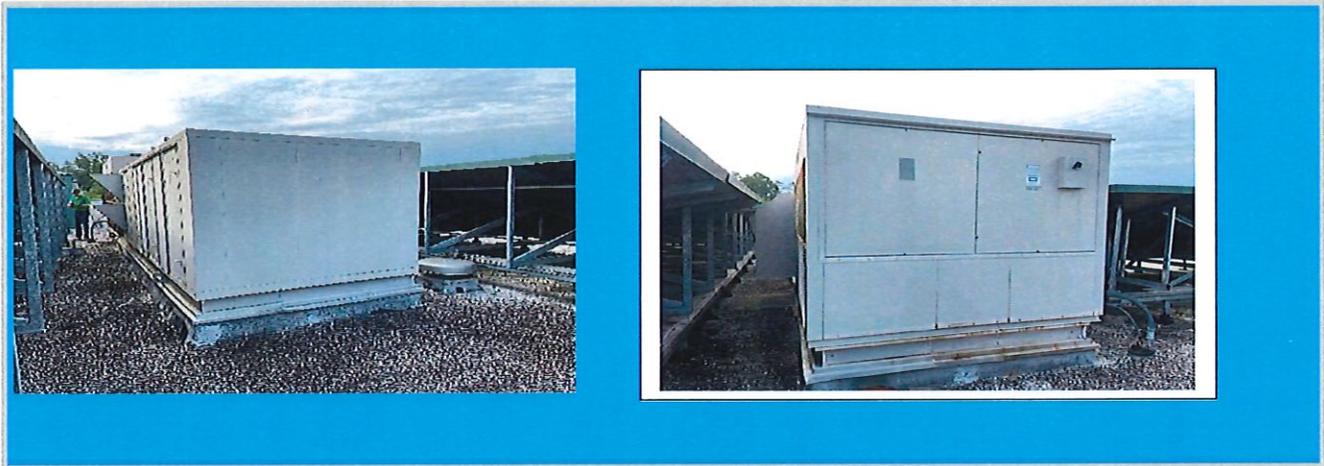

HCS Project Managers: Tricia Lemeur

Principal: Catherine Hampton

Design: Owens & Associates

Contractor: RC Jacobs Plumbing,
Heating and AC, Inc

Project Scope: Replacement of Outside Air Units.

Current Status: Curbs and units have been set. Contractor to complete tie in of gas piping.

Budget: Original Budget: **\$1,300,000.00** Board Approved Date: May 13, 2024

Budget Issues: None currently.

Schedule: Project to be completed in Summer 2025.

Schedule Issues: None currently.

Achievements: New curbs and units are set.
