




Monthly Progress Report

September 2025

Hempstead Union Free School District



Report prepared by Idris Mashriqi





Table of Contents

Section I – Program Summary

Section II – Work Progress **September 2025**

Section III – Work Projected for **October 2025**

Section IV – Progress Photos

Section V – Monthly Workforce Summary



Section I – Program Summary September 2025

Project List

- **Hempstead UFSD – Phase 1 Infrastructure Upgrades @ HS – In Progress**
 - Staircase railings upgrades.
 - Classroom wall upgrades per code.
 - Install eye wash stations.
 - Install new exhaust fans.
 - Install new kitchen Ansul system valves.
- **Hempstead UFSD – Tennis Courts @ HS – In Progress**
 - Remove old asphalt tennis grounds.
 - Install new tennis courts with bleachers.
 - Install a bridge for students to access the tennis courts.
- **Hempstead UFSD – Window replacement at McNeil and Paterson elementary school – In Progress**
 - Removal of caulking under abatement.
 - Removal of existing windows.
 - Installation of new windows and new caulking.
- **Hempstead UFSD – Boiler replacement at McNeil elementary school – In Progress**

Boiler and piping replacement.



Section II - Work Progress September 2025

Hempstead UFSD – HS Priority Infrastructure Upgrades

- Total:
 - Waiting for October to complete Handi-lift

Hempstead UFSD – HS Tennis Courts

- United Paving:
 - Punch list items completed.
 - Waiting bridge delivery.

Hempstead UFSD – Window replacement

- Arrow Steel Windows:
 - Waiting for window delivery.

Hempstead UFSD – Boiler replacement

- Thermotech:
 - Drained down and isolated boiler from overall system.
 - Disconnected all electrical connections.



Section III - Work Planned October 2025

Hempstead UFSD – HS Priority Infrastructure Upgrades

- Total:
 - Complete Handi-lift work.

Hempstead UFSD – HS Tennis Courts

- United Paving
 - Complete remaining punch list items.
 - Complete bridge footings.

Hempstead UFSD – Window replacement

- Arrow steel windows
 - Wait on window delivery. Expected mid-October.

Hempstead UFSD – Boiler replacement

- Thermotech:
 - Complete boiler demo.
 - Complete prefabrication of piping.
 - Turn back on existing boiler.



Section IV – Progress Photos




Hempstead McNeil– Boiler Replacement



Section V – Workforce Summary – Company/Hours

September 2025

MANPOWER GRAPH

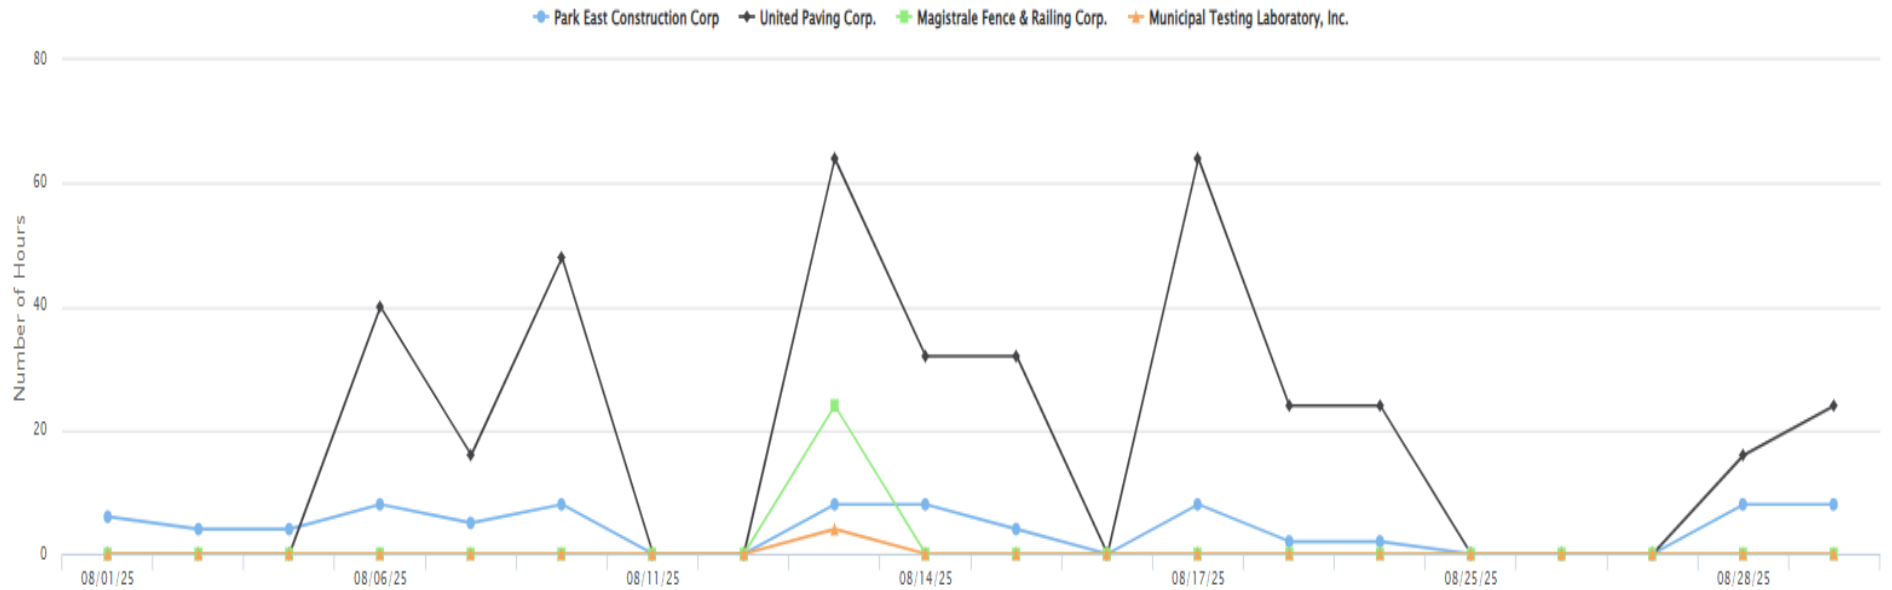


Hempstead HS – Tennis Courts



Section V – Workforce Summary – Company/Hours

September 2025

▼ MANPOWER GRAPH

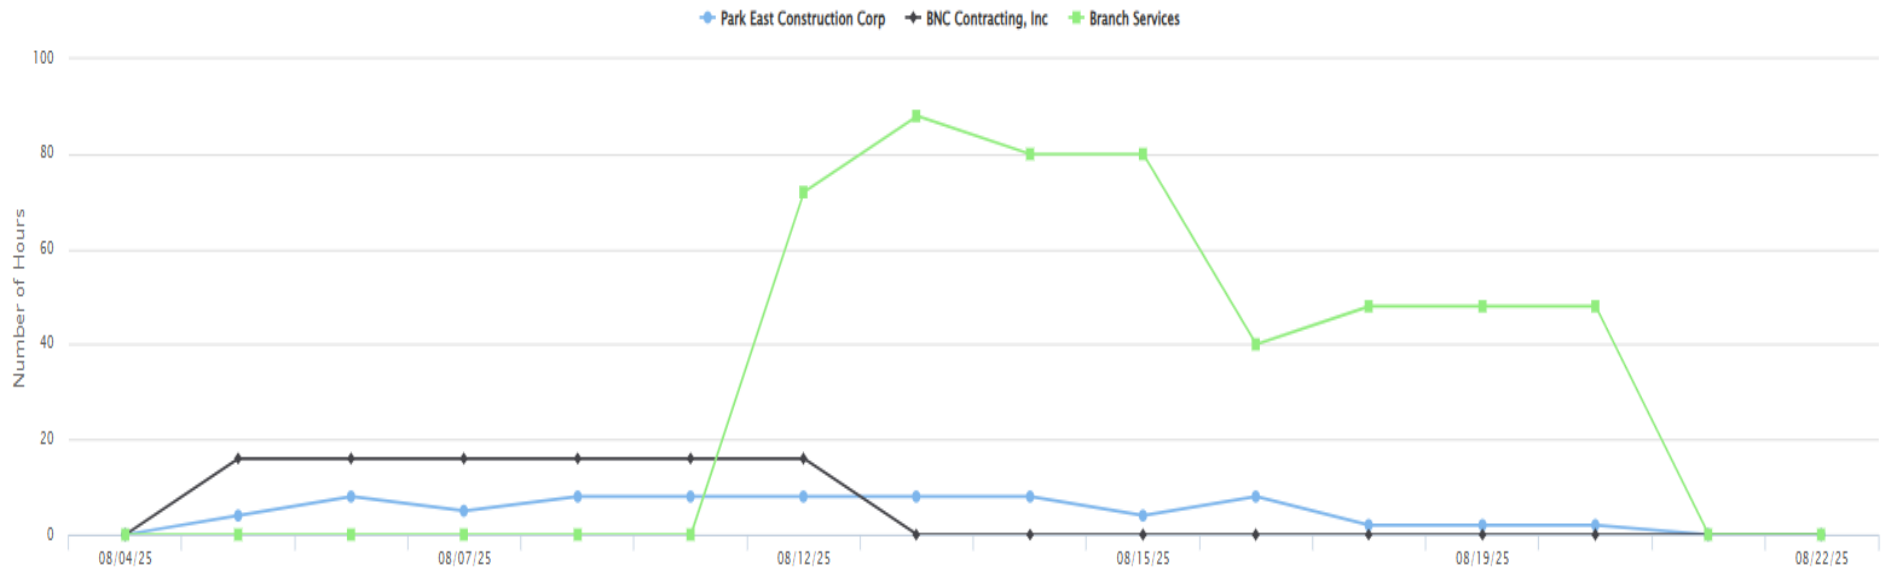

Hempstead McNeil – Boiler replacement



Hempstead Union Free School District
September 2025

End of Progress Report
