




Monthly Progress Report

January 2026

Hempstead Union Free School District



Report prepared by Idris Mashriqi





Table of Contents

Section I – Program Summary

Section II – Work Progress **January 2026**

Section III – Work Projected for **February 2026**

Section IV – Progress Photos

Section V – Monthly Workforce Summary



Section I – Program Summary

January 2026

Project List

- **Hempstead UFSD – Phase 1 Infrastructure Upgrades @ HS – In Progress**
 - Staircase railings upgrades.
 - Classroom wall upgrades per code.
 - Install eye wash stations.
 - Install new exhaust fans.
 - Install new kitchen Ansul system valves.
- **Hempstead UFSD – Tennis Courts @ HS – In Progress**
 - Remove old asphalt tennis grounds.
 - Install new tennis courts with bleachers.
 - Install a bridge for students to access the tennis courts.
- **Hempstead UFSD – Window replacement at McNeil and Paterson elementary school – In Progress**
 - Removal of caulking under abatement.
 - Removal of existing windows.
 - Installation of new windows and new caulking.
- **Hempstead UFSD – Boiler replacement at McNeil elementary school – In Progress**
 - Boiler and piping replacement.
- **Hempstead UFSD – IAQ at Various School – In Progress**
 - Indoor air quality and mechanical upgrades.
 - Electrical upgrades.
- **Hempstead UFSD – 2022 Bond Phase 3 – In Progress**

Infrastructure upgrades throughout all schools.



Section II - Work Progress January 2026

Hempstead UFSD – HS Priority Infrastructure Upgrades

- **Total:**
 - Completed 75% of the installation and ran into fabrication issue. Work is currently on hold.

Hempstead UFSD – HS Tennis Courts

- **United Paving:**
 - Waiting on bridge delivery, currently projected to be delivered first week of Feb.

Hempstead UFSD – Window replacement

- **Arrow Steel Windows:**
 - Delivered trailers to Paterson ES.
 - Received window delivery.
 - Started replacing windows.

Hempstead UFSD – Boiler replacement

- **Thermotech:**
 - Received punch list from BBS.

Hempstead UFSD – IAQ at Various Schools

- **Reliance:**
 - Continuing of low voltage wiring at McNeil and Paterson.
 - Working on BMS for McNeil and Paterson.
 - Installed chilled water piping at Prospect ES.
 - Poured pad for chilled water pumps. Installed pumps on pads.
- **Eldor:**
 - Continued roughing in ceilings and on walls at Paterson ES and McNeil ES.



Hempstead UFSD – 2022 Bond Phase 3

- **J Cole:**
 - Delivered garbage dumpster to Jackson Main ES.
 - Started making openings at Jackson Main ES.
- **IPS:**
 - Surveyed all schools and planned to start work during February winter break.



Section III - Work Planned February 2026

Hempstead UFSD – HS Priority Infrastructure Upgrades

- **Total:**
 - Complete Handi-lift work.

Hempstead UFSD – HS Tennis Courts

- **United Paving**
 - Complete bridge Installation and remaining asphalt walkways.

Hempstead UFSD – Window replacement

- **Arrow steel windows**
 - Continue replacing windows at Paterson ES.

Hempstead UFSD – Boiler replacement

- **Thermotech:**
 - Closeout process.

Hempstead UFSD – IAQ at Various Schools


- **Reliance:**
 - Install chiller pad and bollards at Prospect ES.
 - Continue chilled water piping.
 - Continue low voltage roughing.
- **Eldor:**
 - Continue to rough in ceilings at Paterson ES, McNeil ES, and Prospect ES.

Hempstead UFSD – 2022 Bond Phase 3

- **J Cole:**
 - Continue making openings at Jackson Main ES for mechanical work access.
 - Start making openings at Obama ES.
- **IPS:**
 - Replace sinks and water fountains during winter break.



Section IV – Progress Photos

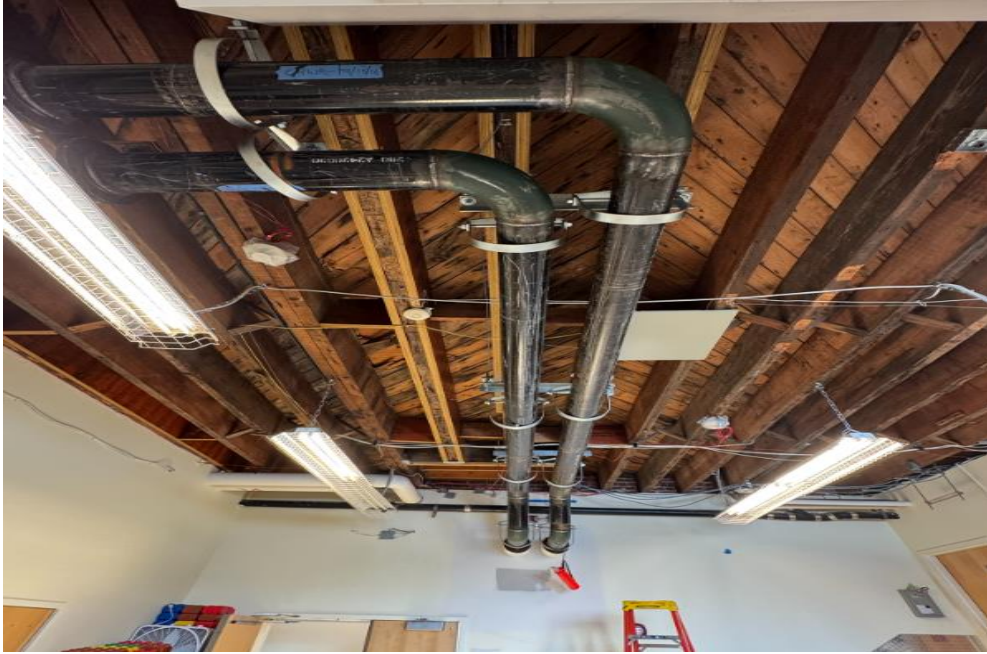

Hempstead IAQ – Prospect ES Chilled Water Piping



Section IV – Progress Photos



Hempstead IAQ – Chilled water system




Section IV – Progress Photos



Hempstead UFSD – 2022 Bond Ph. 3



Section IV – Progress Photos

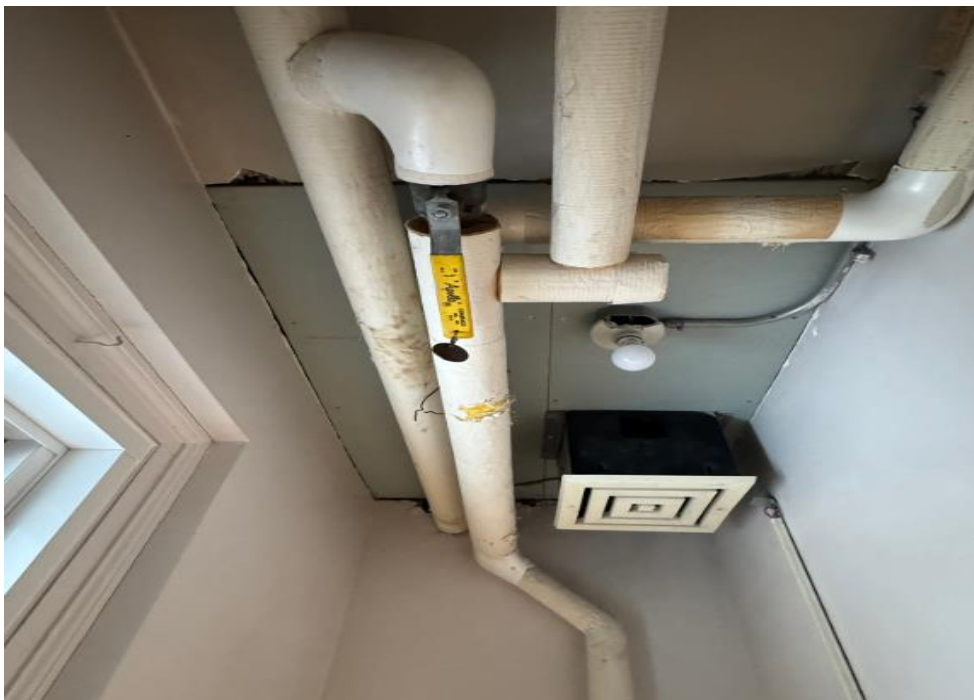


Hempstead UFSD – 2022 Bond Ph. 3



Section V – Workforce Summary – Company/Hours

January 2026

▼ MANPOWER GRAPH

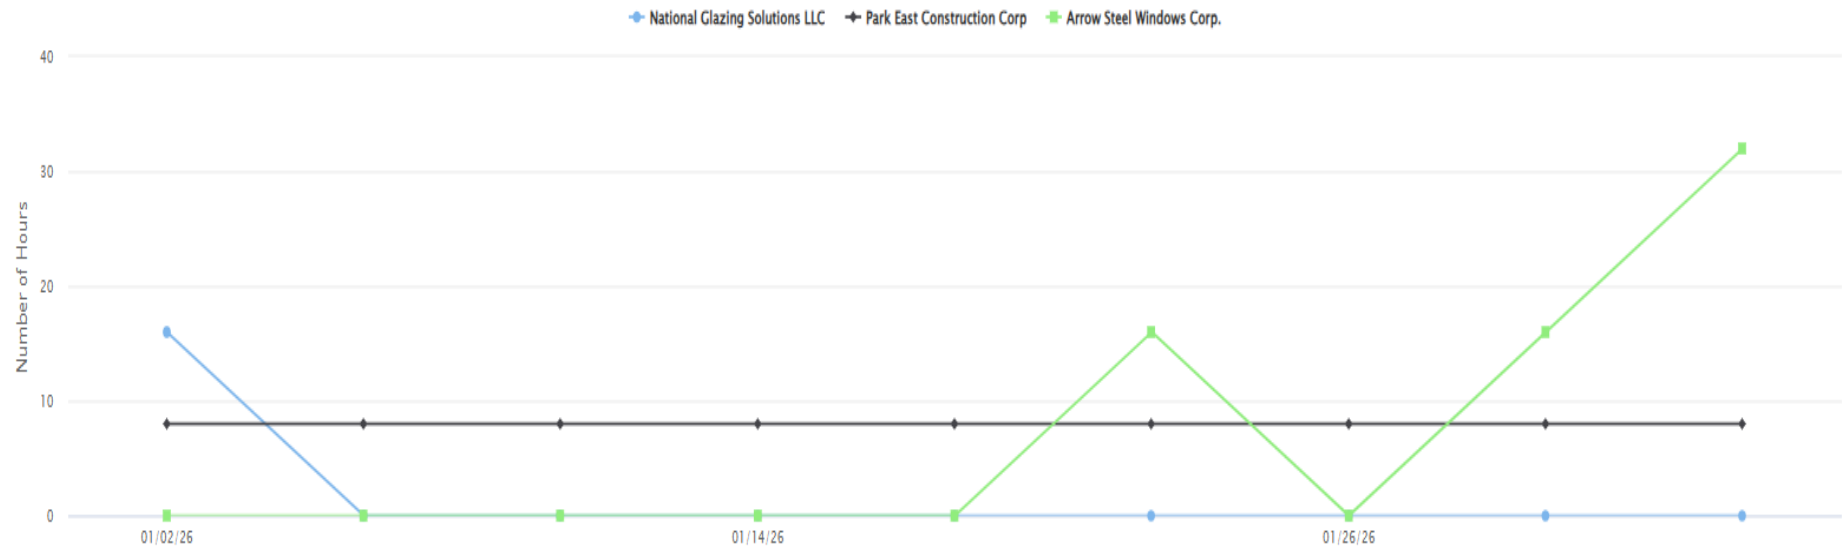


Hempstead UFSD – Window Replacement



Section V – Workforce Summary – Company/Hours

January 2026

MANPOWER GRAPH

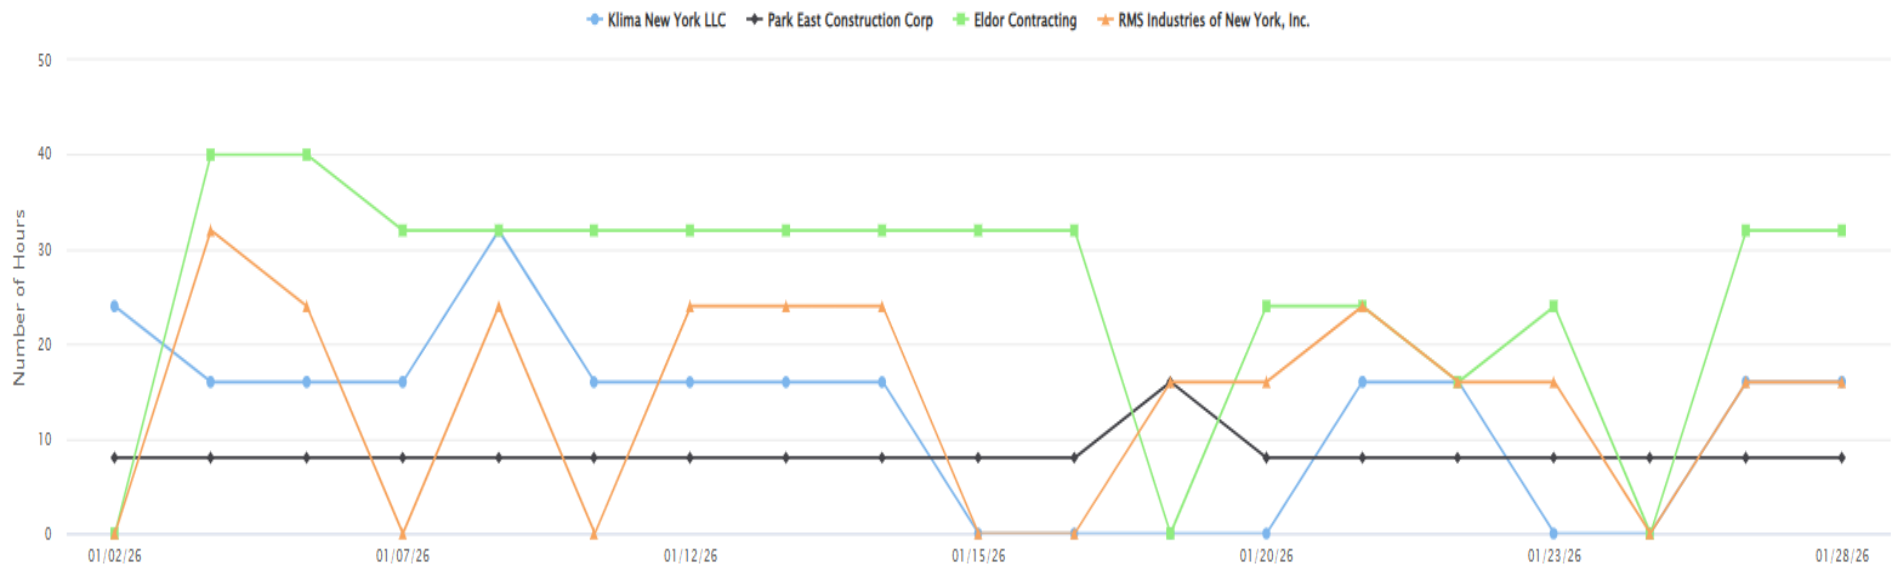


Hempstead UFSD – IAQ at Various Schools



Section V – Workforce Summary – Company/Hours

January 2026

▼ MANPOWER GRAPH

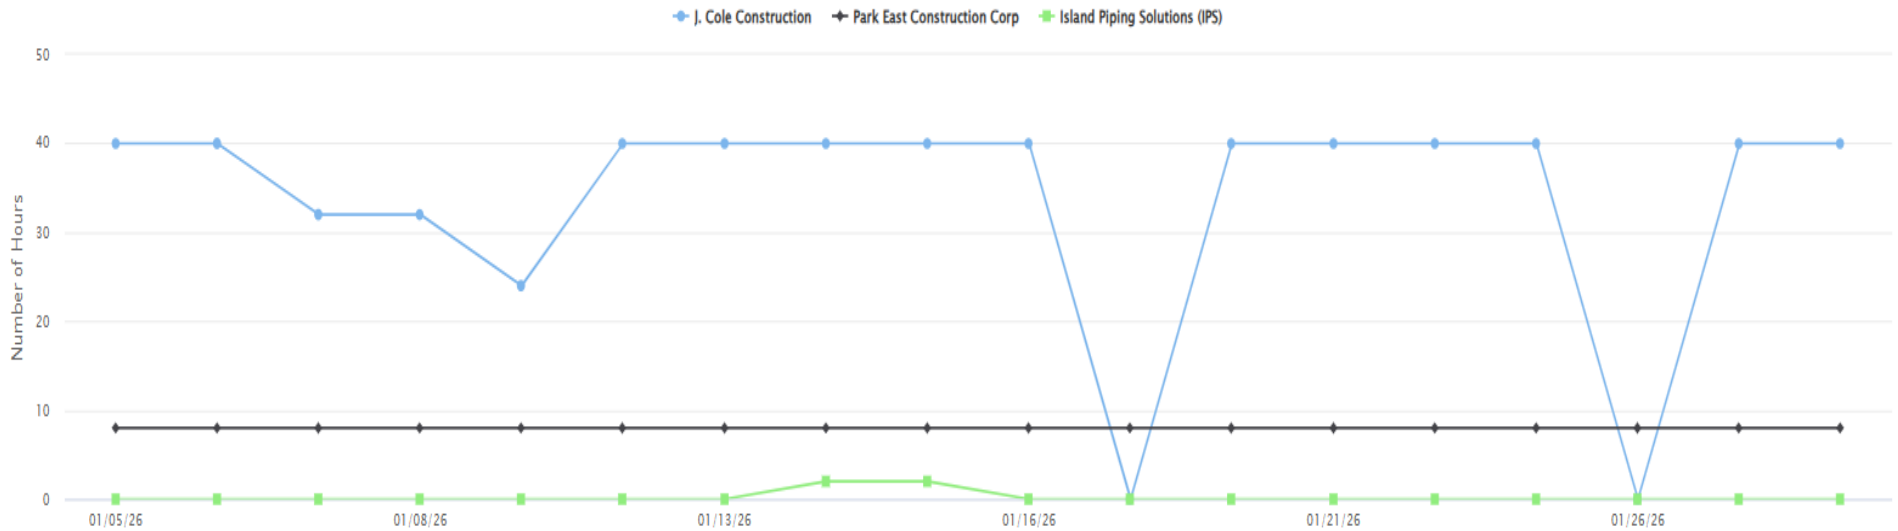

Hempstead UFSD – 2022 Bond Phase 3



Hempstead Union Free School District
January 2026

End of Progress Report
