




2023 BOND

# MAJOR PROJECTS UPDATE

MARCH 2024



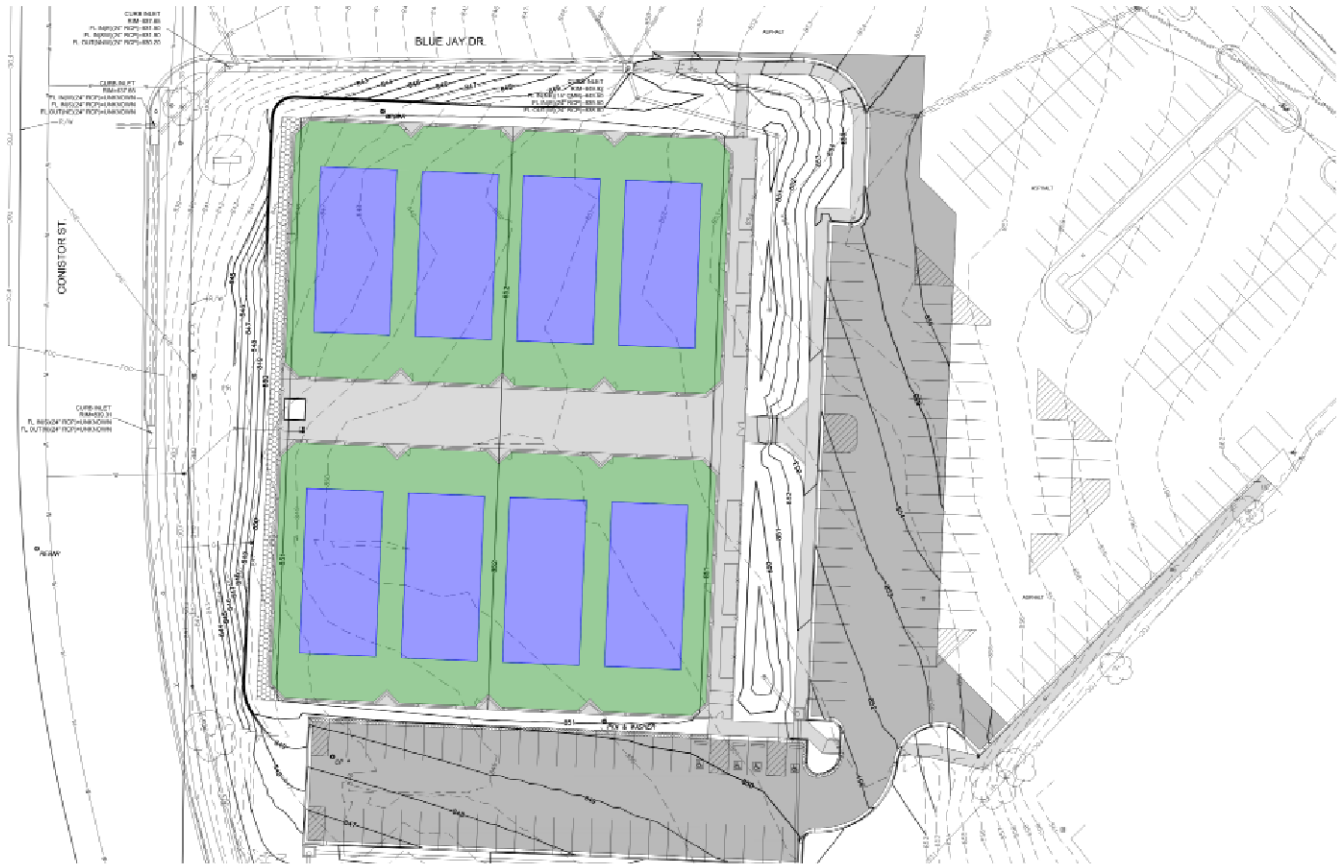

## Liberty High School Tennis

- (8) Competition Tennis Courts
- Post-Tensioned Concrete slab with DecoTurf brand acrylic surfacing
- 10'-0" tall perimeter fence with windscreen
- Retaining wall and asphalt parking lot improvements

**Construction Start:** Spring 2023

**Construction Complete:** Fall 2023

**WEEKLY  
PROGRESS  
REPORT**

# Tennis Courts 11/13/2023

Liberty Public Schools



## PROJECT STATUS

- Courts Substantially Complete
- Turned Over 10/31
- Final Punch List Items Being Completed

## UPCOMING

Project Completion October 2023



North Courts Looking West



North Courts Looking Southwest



East Concourse Looking South



East Concourse Looking North


# WEEKLY PROGRESS REPORT



South Courts Looking West



Center Spectator Concourse Looking West

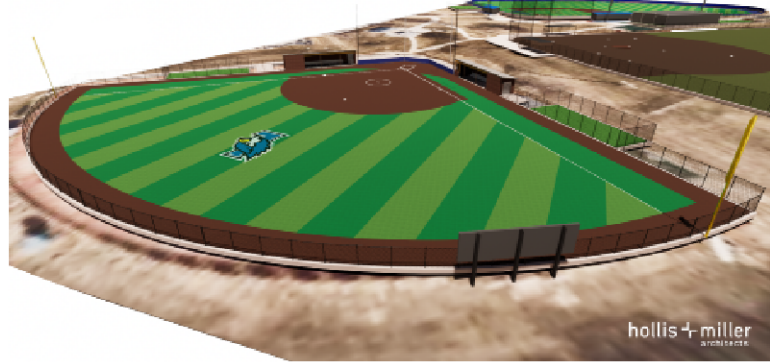

## Liberty High School Baseball/Softball Complex

### Baseball Field

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Pitching and Batting Practice areas

### Softball Field

- New Dugouts
- Reduced Field Dimensions to 210' outfield, 25' Foul Territory, Softball
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

### Multi-purpose Field

- Revised grading, perimeter fencing and infield improvements

**Construction Start:** Fall 2023

**Construction Complete:** Summer 2024

WEEKLY  
PROGRESS  
REPORT

# Baseball Softball 03/11/2024

## Liberty Public Schools



### PROJECT STATUS

- LHS
- Punch List Ongoing
- TCO received 3/4/24
  
- Aux Field Grading Ongoing
- Aux MEP Underground Ongoing
  
- Softball Turf Subgrade Ongoing
- Softball MEP Underground Complete
- Softball Curbs & Fencing Ongoing

### UPCOMING

- LHS -
- Baseball Batting Tunnel
  
- Aux Field Backstop Posts and Concrete
- Aux Field Irrigation
  
- Softball Backstop Posts and Concrete

Project Completion  
Baseball March 2024/Softball May 2024



LHS - Baseball



LHS - Baseball



LHS - Multi-Purpose



LHS - Softball


# WEEKLY PROGRESS REPORT



LHS - Baseball




LHS - Overall Site

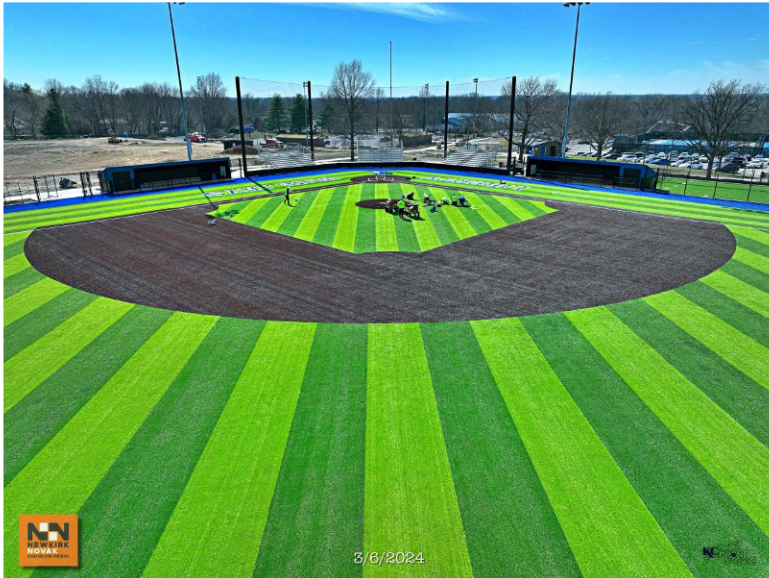

LHS - Baseball



LHS - Softball

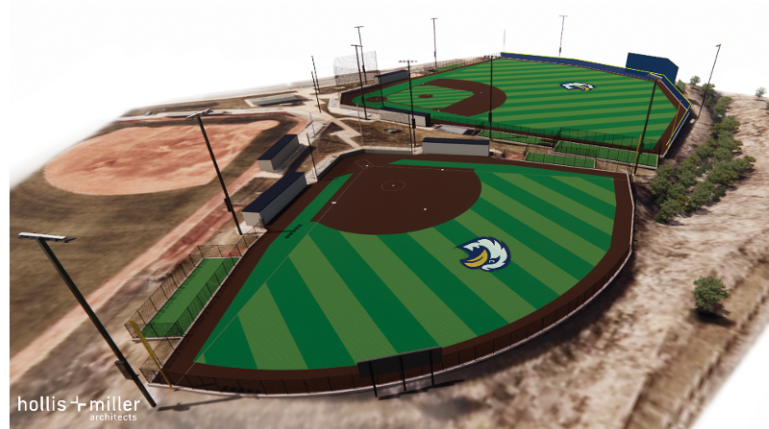

## Liberty North High School Baseball/Softball Complex

### Baseball Field

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Center field Batter's Eye
- Additional Bullpen Space
- ChampionWall PVC Athletic Fence System at Outfield

### Softball Field

- Increased Field Dimensions - 194'(L) - 200'(C) - 195'(R)
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

**Construction Start:** Fall 2023

**Construction Complete:** Summer 2024

## PROJECT STATUS

### LNHS

#### Baseball

- Baseball Punch List Ongoing
- Baseball TCO Received 2/27/24

#### Softball

- Turf Subgrade Ongoing
- Fence Post & Perimeter Curb Ongoing

## UPCOMING

### LNHS-

#### Baseball

- Logo behind Home plate

#### Concourse

- Landscaping

#### Softball

- Turf Installation
- Backstop Posts & Concrete

#### Project Completion

Baseball March 2024/Softball May 2024



LNHS - Baseball



LNHS - Baseball



LNHS - Full Site



LNHS - Softball

# WEEKLY PROGRESS REPORT



LNHS - Baseball



LNHS - Softball



LNHS - Baseball



LNHS - Overall Site



LED Lighting upgrades are planned throughout the District and will be sequenced with other projects as possible between the fall of 2023 through fall of 2026.

## PROJECT STATUS

- South Valley MS - Upgrades Complete
- Discovery MS - Upgrades Complete
- EPiC Elementary - Upgrades Complete
- Liberty North High School - Upgrades Ongoing

## UPCOMING

- Energy Inspections - All Four Schools
- Emergency LED Fixtures

Project Completion  
December 2023




Liberty North HS



Liberty North HS



Liberty North HS

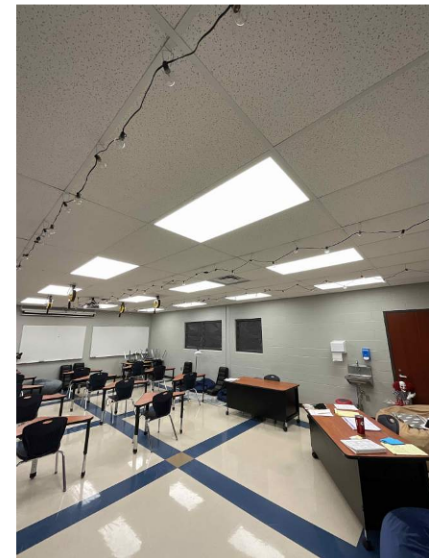

Liberty North HS

## PROJECT STATUS

South Valley MS- Upgrades Complete

Discovery MS - Upgrades Complete


EPiC Elementary - Upgrades Complete

LNHS - Upgrades Ongoing


## UPCOMING

Energy Inspections All Four Schools  
Emergency LED Fixtures

Project Completion  
December 2023

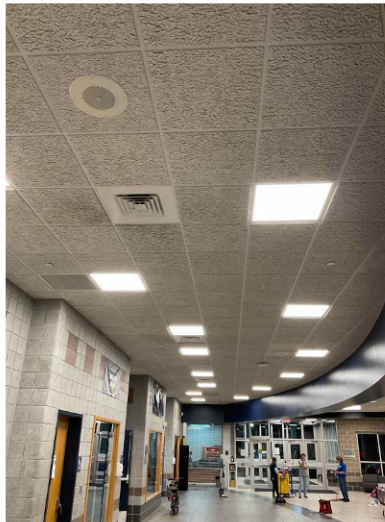


South Valley Middle School

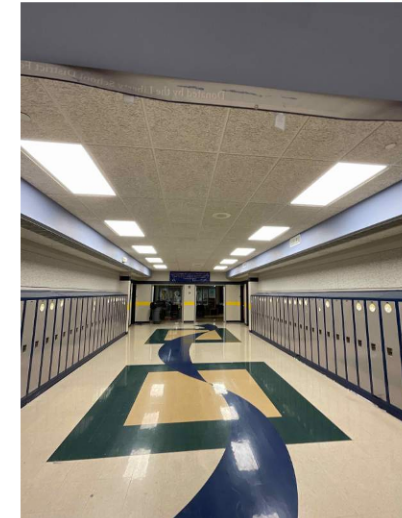

South Valley Middle School



Discovery Middle School

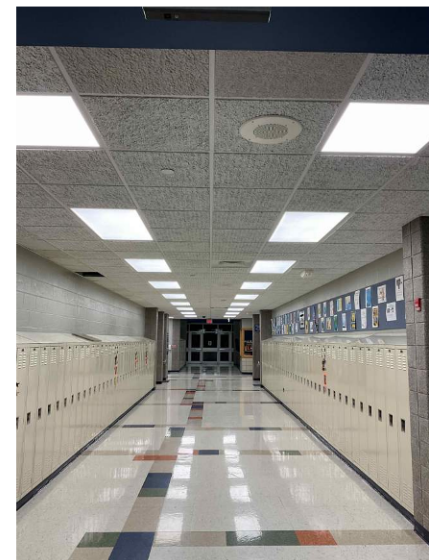

Discovery Middle School

# WEEKLY PROGRESS REPORT



Epic Elementary




Epic Elementary



Liberty North High School




Liberty North High School

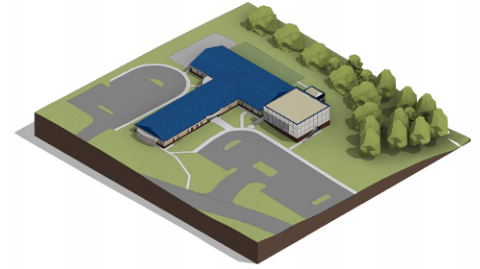


### EPiC Elementary Addition

- 8000 Square Foot Building Addition & Renovation
- New Gym & Performance Space
- New Art Classroom
- Renovated Restrooms, Mother's Room and New Walk-in Cooler / Freezer
- Construction Start: Spring 2024
- Construction Complete: Summer 2025

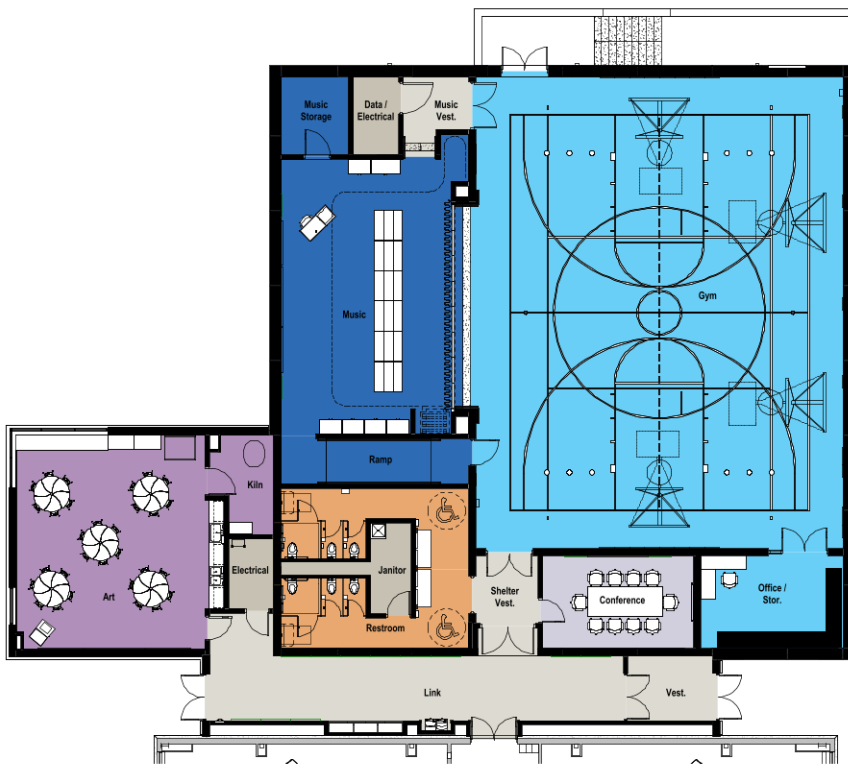

▲ Addition

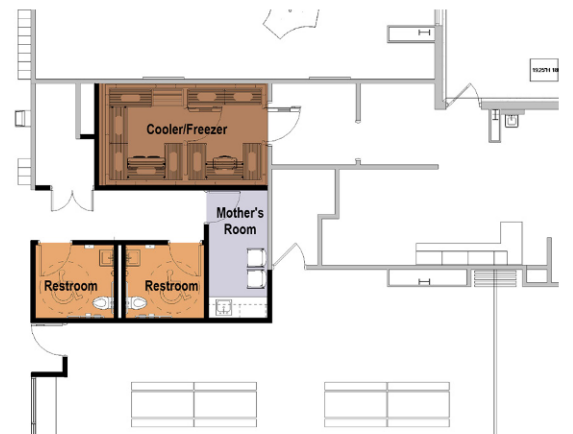

▲ Renovation Area

## PROJECT STATUS

- EPiC Elementary
- Site Utilities Completed
  - Underground Plumbing Completed
  - Building Pad Completed
  - Building Footings Ongoing

## UPCOMING

- EPiC Elementary
- Structural Steel
  - Existing Building Interior Renovation

Project Completion  
EPiC Feb 2025/DMS&SVMS June 2025



EPiC Elementary - Building Pad



EPiC Elementary



EPiC Elementary - Building Pad





EPiC Elementary



### Discovery Middle School

- 11,000 square foot addition
  - ICC 500 rated shelter
  - Additional PE space
- Raised performance stage
- Theatrical AV and lighting
- Increased audience capacity
  - Additional storage
- Projected Construction Schedule:  
Spring 2024–Summer 2025

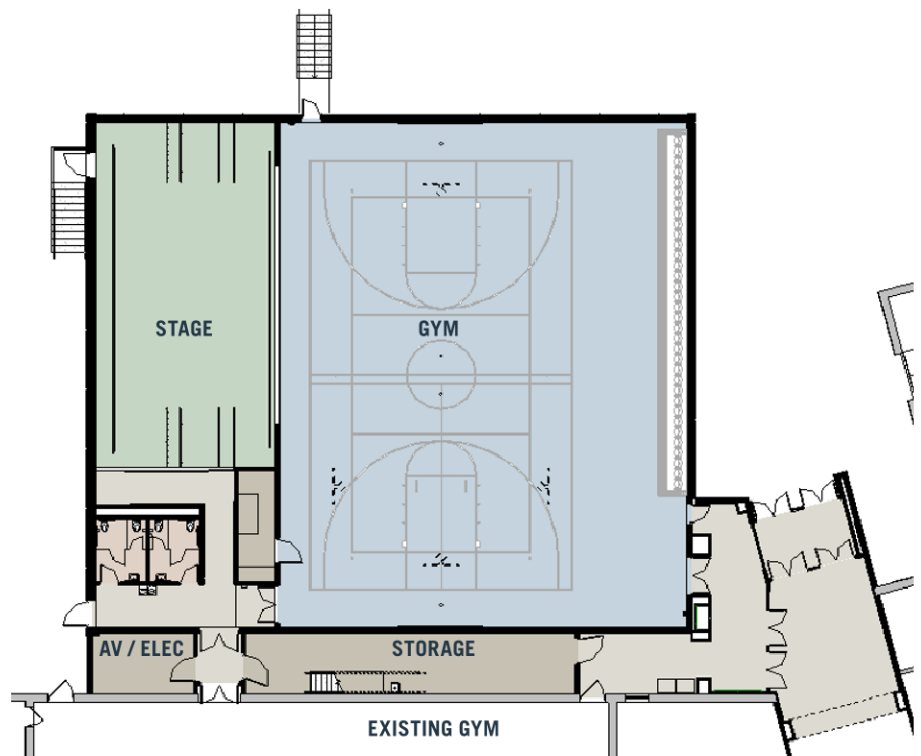

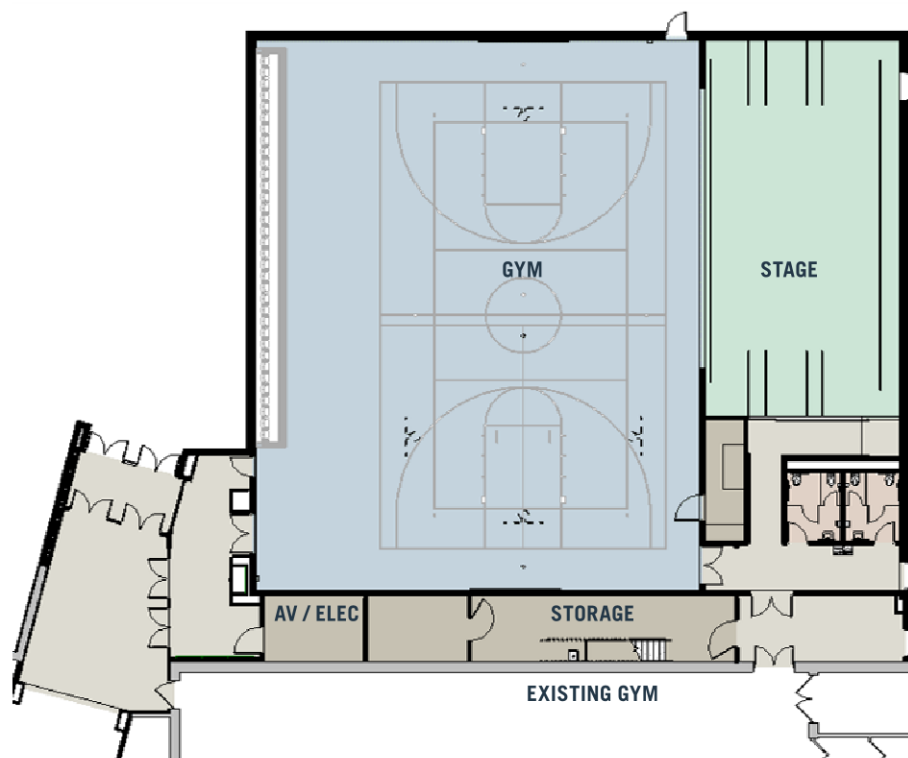

### South Valley Middle School

- 11,000 square foot addition
- ICC 500 rated shelter
- Additional PE space
- Raised performance stage
- Theatrical AV and lighting
- Increased audience capacity
- Additional storage
- Projected Construction Schedule: Spring 2024–Summer 2025



hollis + miller



hollis + miller



hollis + miller



hollis + miller

## Distribution Center

- 29,000 Square Foot New Building
- Storage Warehouse
- Dry Food Warehouse
- Large Storage Freezer
- New Office Space
- New Copy Center
- Additional Parking
- Projected Construction Schedule: Fall 2023–Spring 2025



3/8/24

## PROJECT STATUS

- Deep fills complete
- Building pad complete
- Storm line 1 complete
- Storm 4 & 5 complete

## UPCOMING

- Site Utilities ongoing
- Flow fill existing storm line 1
- Replacing water line
- Test Replacement Water Line
- Install new domestic line
- Install new fire line
- Settlement delay ongoing
- Mock-up ongoing

Project Completion  
June 2025



Overall Site/Building Pad



Overall Site/Building Pad



Overall Site/Building Pad



Storm Structure 1-3 & 4-2



Cooler Pad



Storm Structure 1-3



Storm Structure 4-3

Fine Arts  
 Kid's Zone  
 Technology  
 Shared Amenities  
 Building Systems  
 Future Phase



### District Technology Center

- Renovated workspace for District's Technology, Fine Arts, and Kid's Zone departments
- Shell space for future growth
- Minor exterior patch + repair improvements
- Projected Construction Schedule: Fall 2023 - Summer 2024

3/8/24

## PROJECT STATUS

- District Technology Center:
- Completed Wall Framing
  - Glazing Installation at New Openings
  - MEP Wall Rough In Underway
  - MEP Overhead Rough In Underway
  - Communications Install Began
  - Concrete Sitework Continues
  - Fence Installation Began
  - Drywall Installation Began
  - Drywall Finishing Began
  - Begin Paint

## UPCOMING

- District Technology Center:
- Complete MEP In Wall Rough In
  - Complete MEP Overhead Rough-IN
  - Complete Generator/XFMR Pad Install
  - Complete Door Frame Install
  - Begin Fire Alarm Install
  - Begin Tile Installation
  - Continue Drywall Installation
  - Continue Drywall Finishing
  - Continue Paint




District Technology Center



District Technology Center



District Technology Center

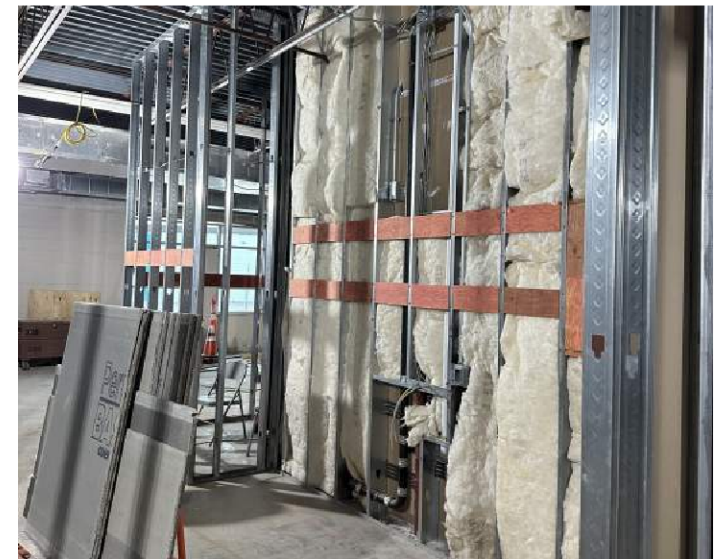

District Technology Center



District Technology Center



District Technology Center



District Technology Center




District Technology Center



### Heritage Middle School

- 39,000 square feet academic renovation
- Grade level neighborhoods with flex collaboration spaces
  - Integrated SPED resources
  - Renovated cafeteria & scramble
    - Restroom renovations
- Exterior masonry repair & window replacement
  - Elevator replacement
- Projected Construction Schedule: Spring 2024–Fall 2025

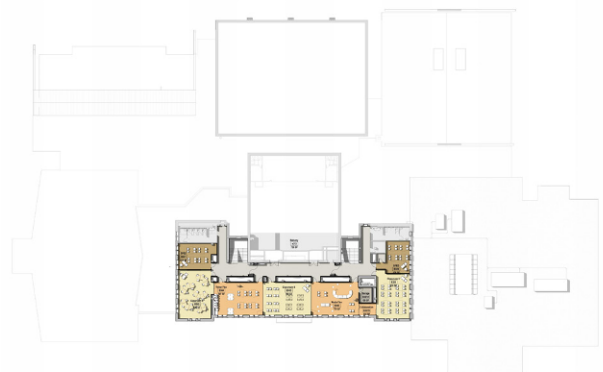

LEVEL 3




LEVEL 2



LEVEL 1



LEVEL 0

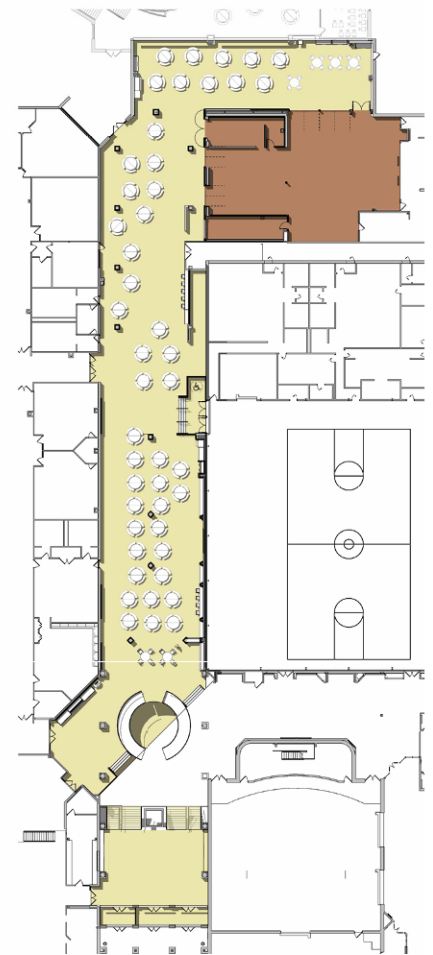

PHASE 2

### Liberty High School

- Square footage: 40,800 SF
- Renovation to FACS, SPED and Art classrooms
- Renovated scramble & dining area
- LED lighting replacement
- Project Construction Schedule: Summer – Fall 2024 & 2025




PHASE 1



## Shop Building



- 1,800 Square Foot New Building
- Flexible Open Plan
- Patio & Secure Breezway
- Woodworking Area
- Metalworking Area
- Flex-space for Lectures or Large Projects
- Projected Construction Schedule: Spring 2024–Spring 2025

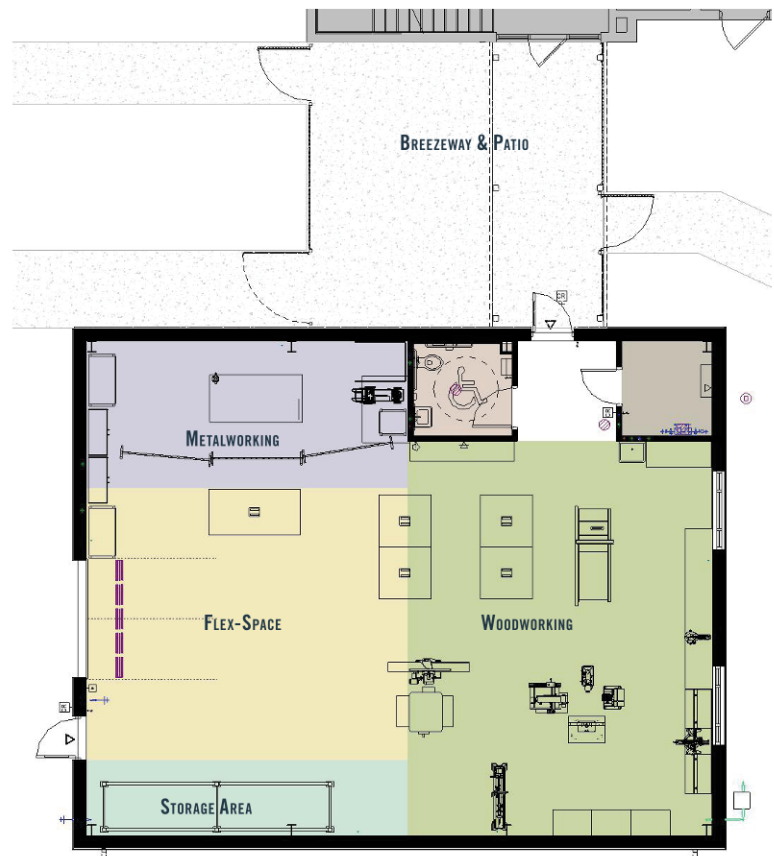

▲ Floor Plan


## Recreation Court

- 3,531 Square Foot New Court
- Court Lines for Basketball & Pickleball
- Additional Area for Temporary Bleachers
- Projected Construction Schedule:  
Spring 2024–Spring 2025

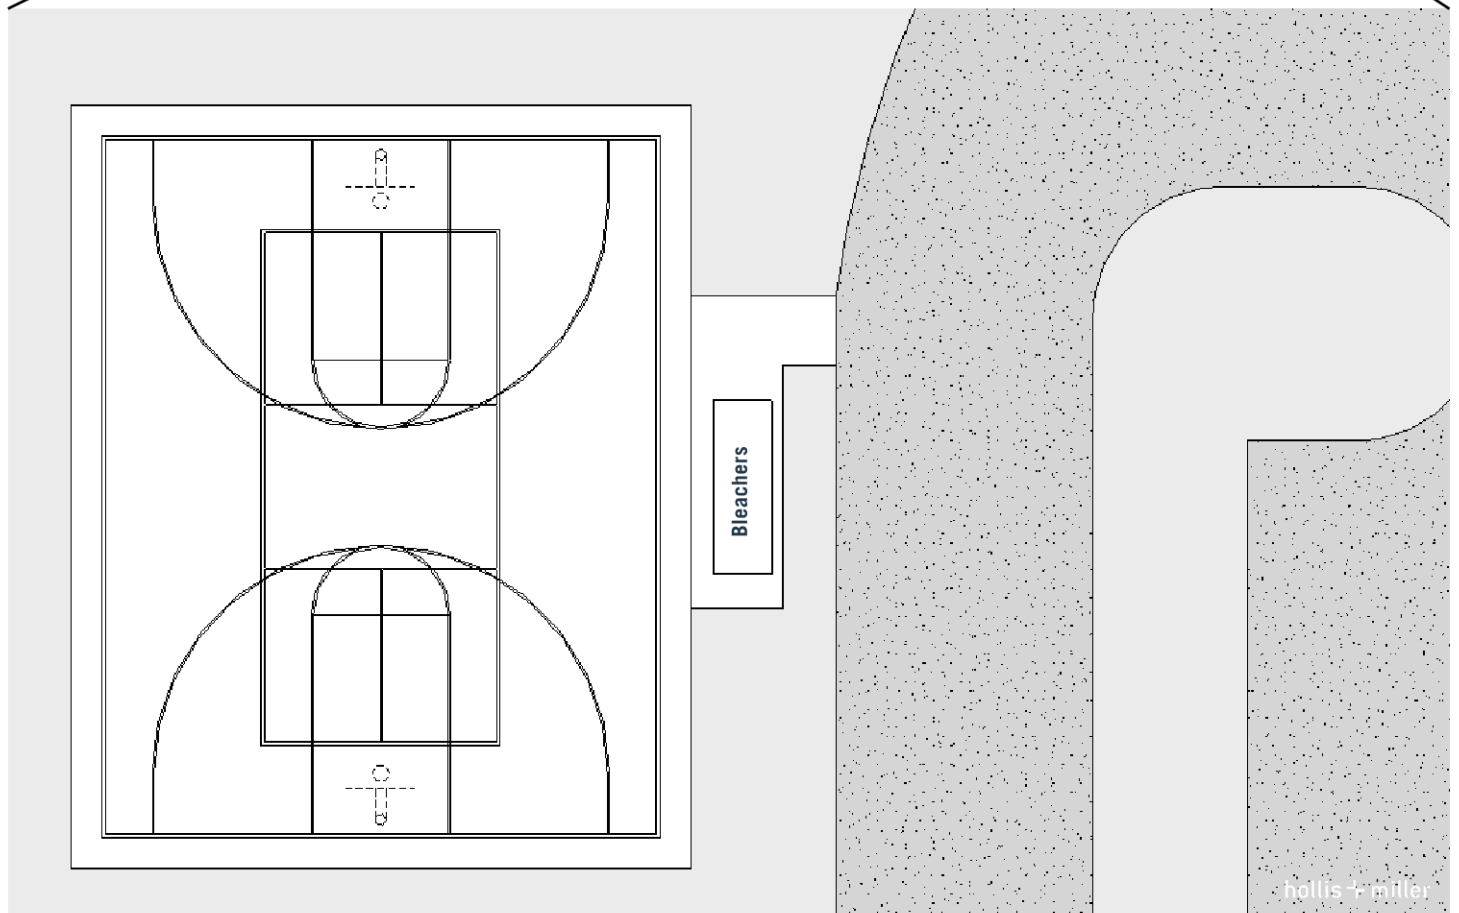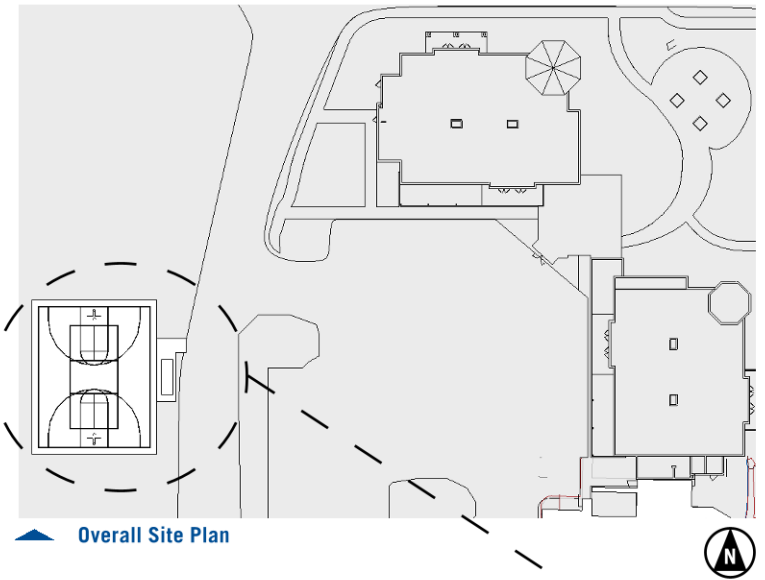


## Interior Renovation

- Nurse Room Relocation
- Renovated Teacher Workroom
- SPED Classroom Toilet Renovation
- New Admin Reception Entry Door & Counter
- Staff Restroom Renovation
- Lactation Room
- Projected Construction Schedule:  
May 2024 - August 2025

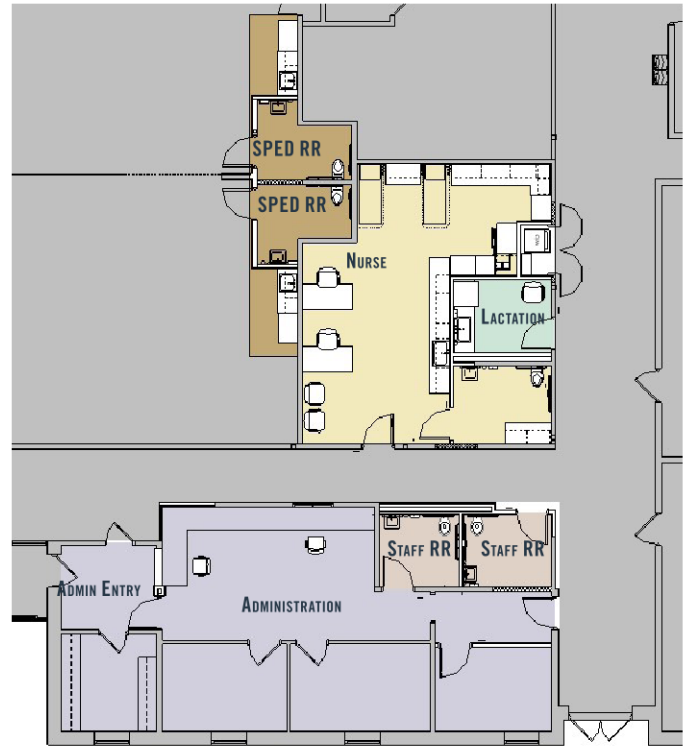

▲ Enlarged Floor Plan

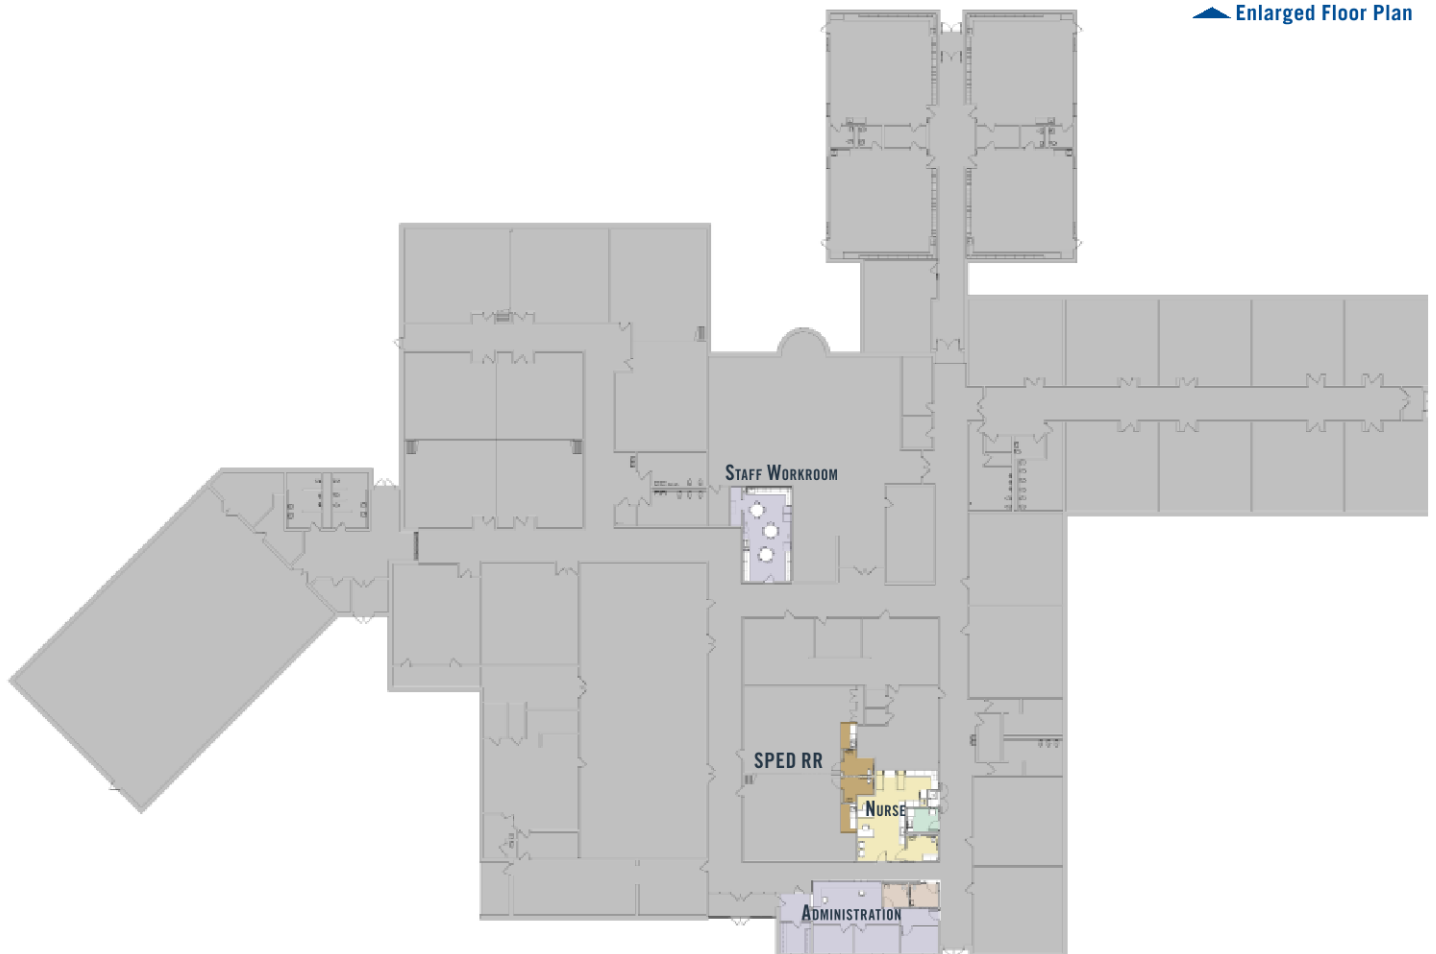


▲ Overall Floor Plan

## Interior Renovation


- Nurse Room Renovation
- Administration Office Renovation
- New Admin Reception Desk & Entry Door
- Lactation Room
- Group & Staff Restroom Renovation
- LED Lighting Replacement
- HVAC Replacement
- Projected Construction Schedule:  
May 2024 - August 2025



Administration

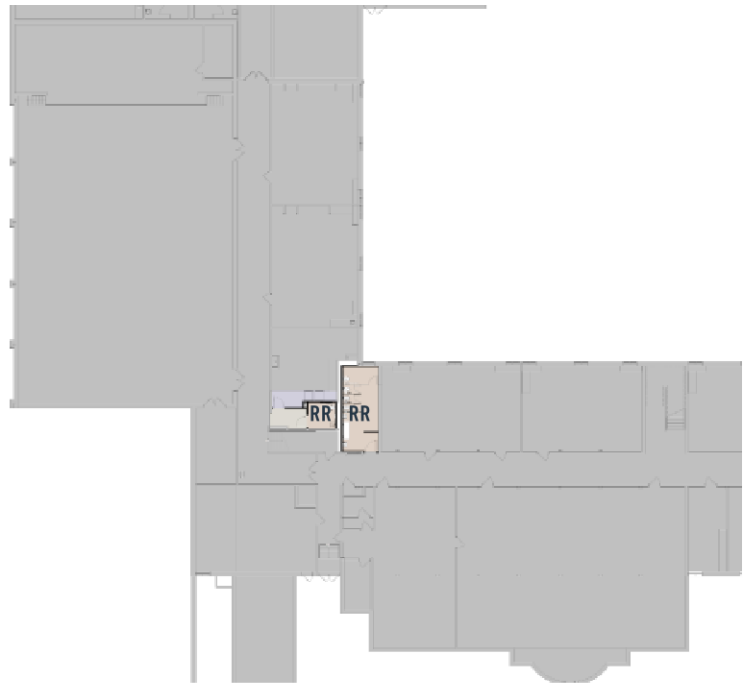

Partial First Level Floor Plan

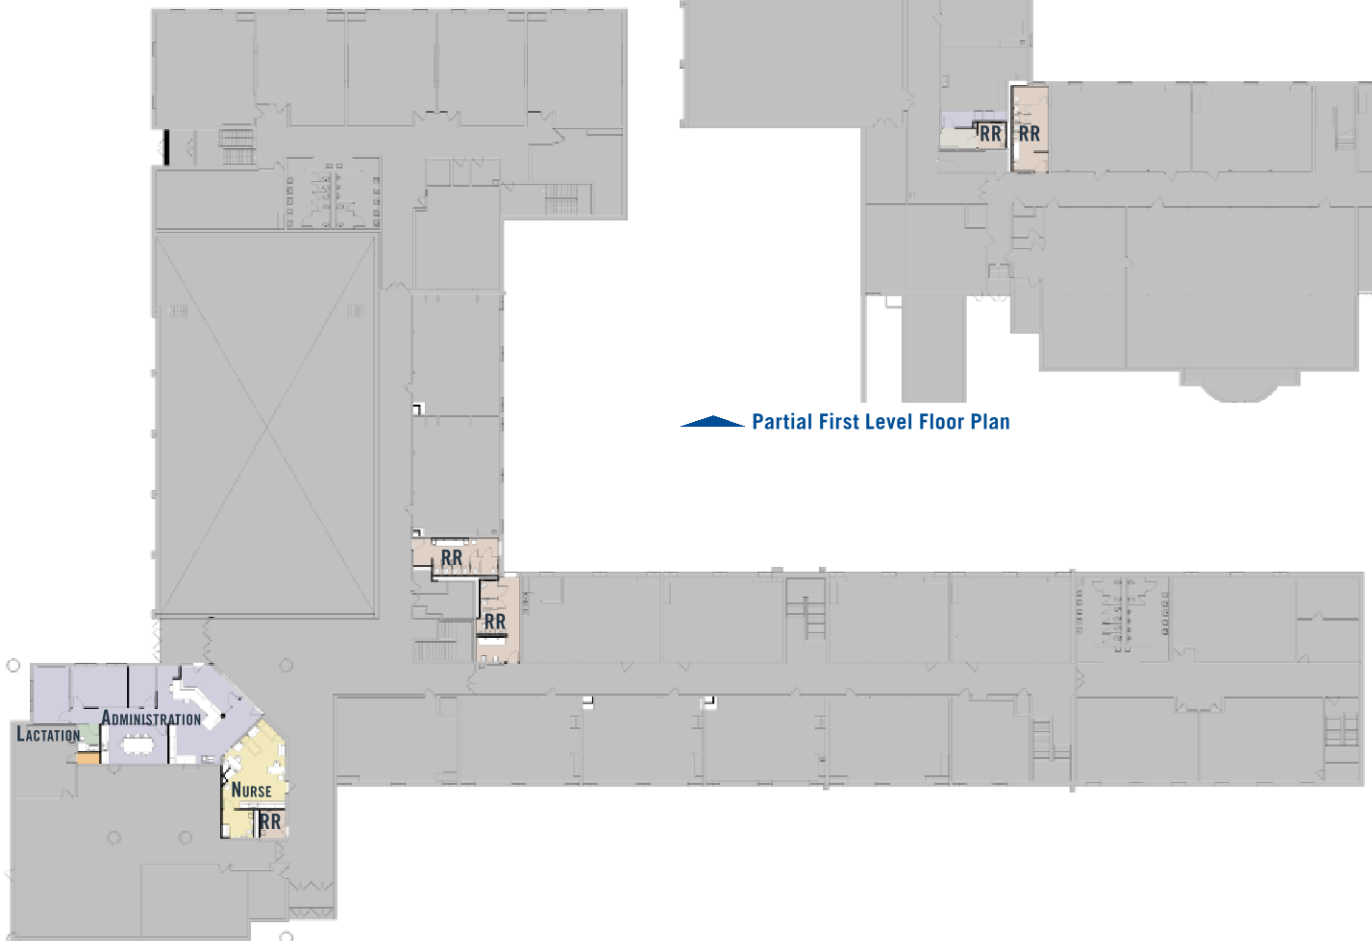


Overall Second Level Floor Plan

## Interior Renovation

- Nurse Room Relocation
- Group & Staff Restroom Renovation
- New Admin Reception Desk & Entry Door
- Gym Stage Renovation into Staff Offices & PE Storage
- Lactation Room
- Media Center Wing LED Lighting
- Projected Construction Schedule:  
May 2024 - August 2025



Administration

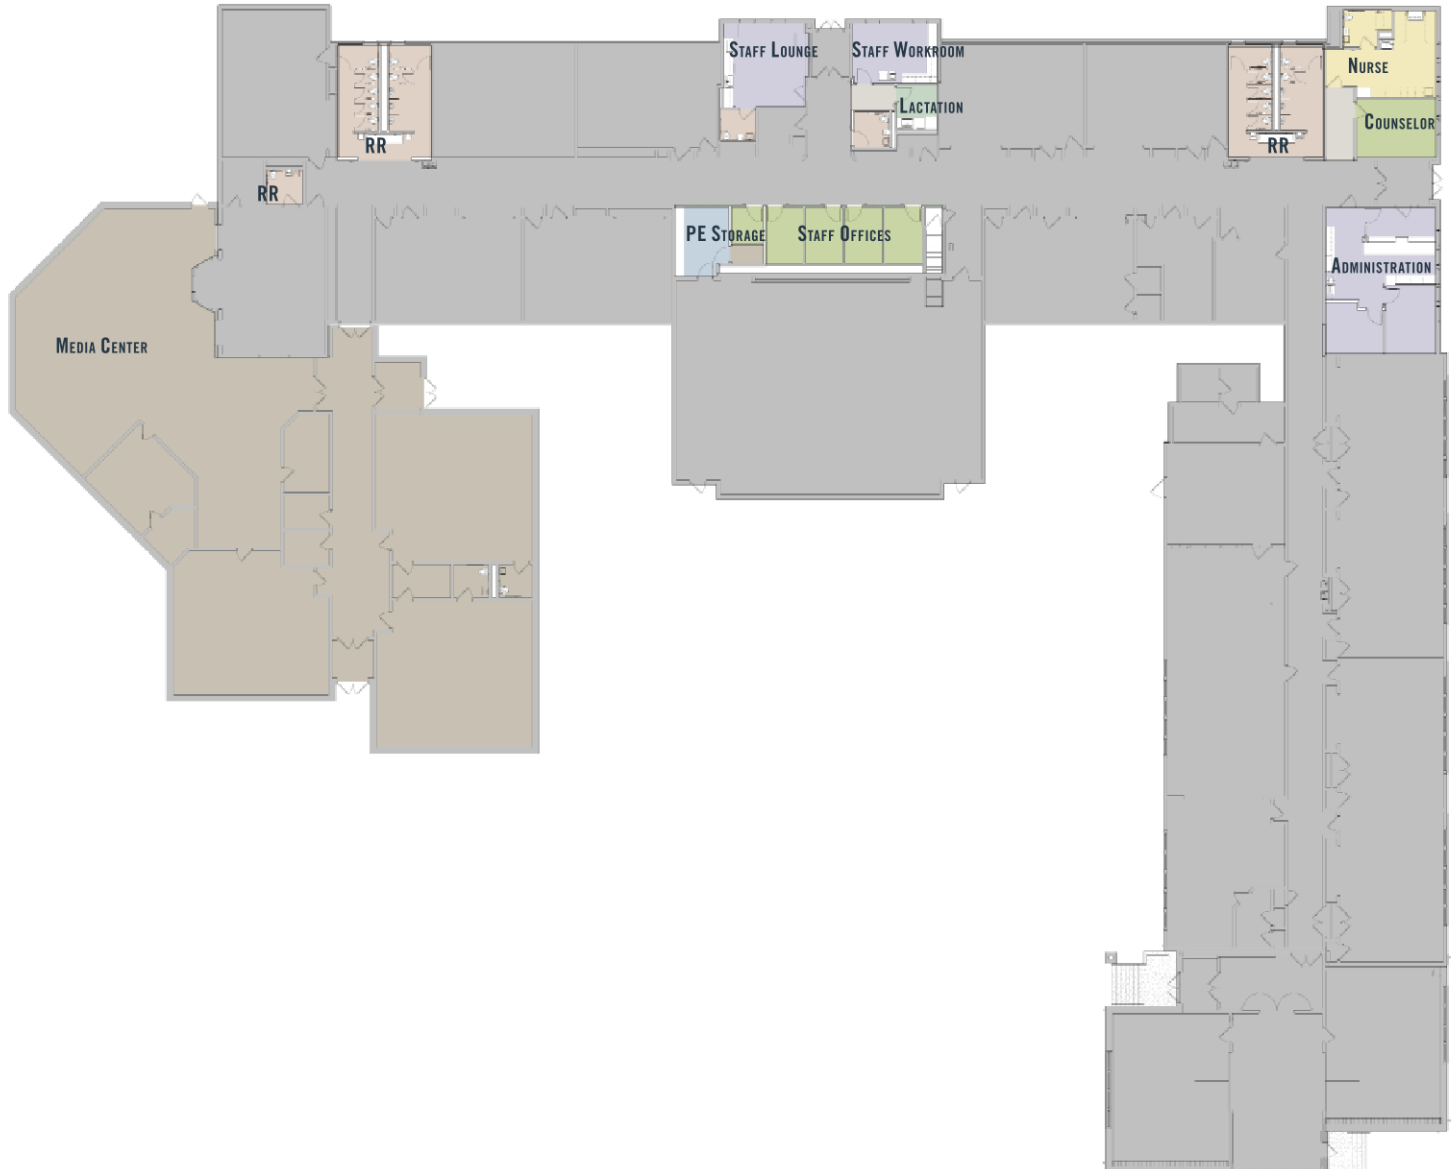

Overall Floor Plan
