




2023 BOND

# MAJOR PROJECTS UPDATE

MAY 2024



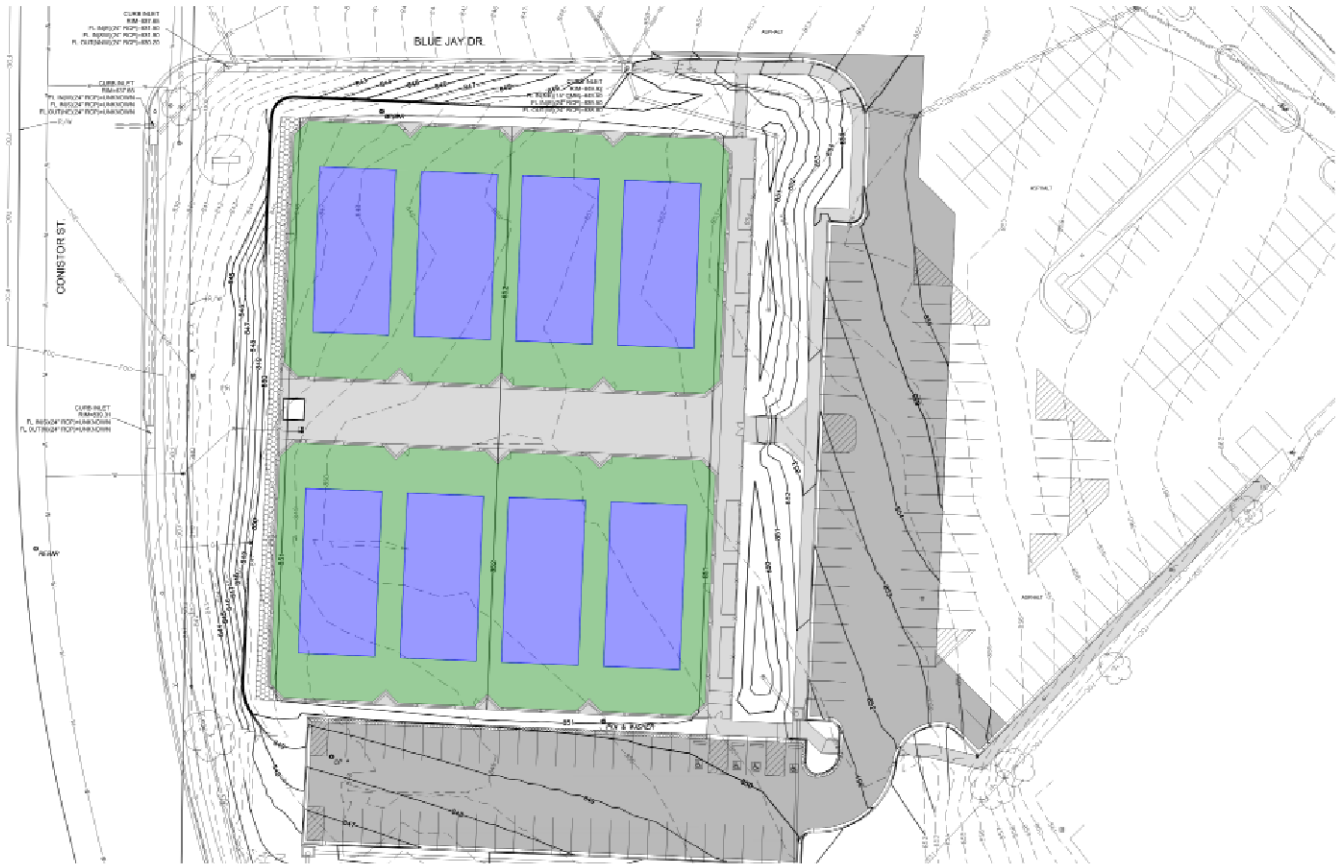

## Liberty High School Tennis

- (8) Competition Tennis Courts
- Post-Tensioned Concrete slab with DecoTurf brand acrylic surfacing
- 10'-0" tall perimeter fence with windscreen
- Retaining wall and asphalt parking lot improvements

**Construction Start:** Spring 2023

**Construction Complete:** Fall 2023

**WEEKLY  
PROGRESS  
REPORT**

# Tennis Courts 11/13/2023

Liberty Public Schools



## PROJECT STATUS

- Courts Substantially Complete
- Turned Over 10/31
- Final Punch List Items Being Completed

## UPCOMING

Project Completion October 2023



North Courts Looking West



North Courts Looking Southwest



East Concourse Looking South



East Concourse Looking North


# WEEKLY PROGRESS REPORT



South Courts Looking West



Center Spectator Concourse Looking West

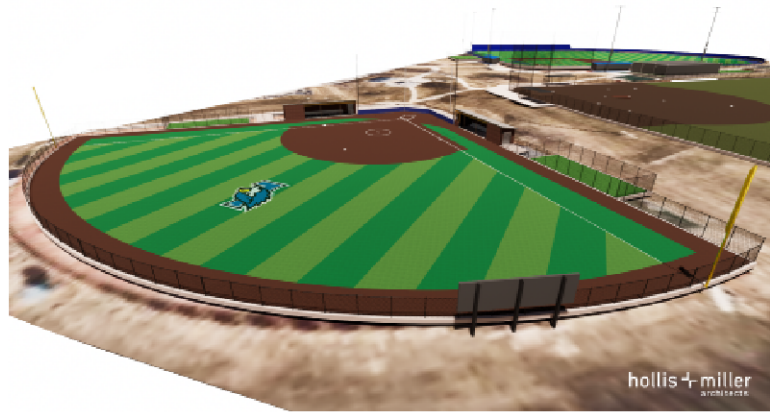

## Liberty High School Baseball/Softball Complex

### Baseball Field

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Pitching and Batting Practice areas

### Softball Field

- New Dugouts
- Reduced Field Dimensions to 210' outfield, 25' Foul Territory, Softball
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

### Multi-purpose Field

- Revised grading, perimeter fencing and infield improvements

**Construction Start:** Fall 2023

**Construction Complete:** Summer 2024

**WEEKLY  
PROGRESS  
REPORT**

# LHS Ball Fields 5/09/2024

Liberty Public Schools



## PROJECT STATUS

### Baseball

- Punch List Ongoing

### Aux Field

- Fencing Ongoing
- Backstop Paving Ongoing
- Irrigation Complete

### Softball

- Turf Complete
- Punch List Ongoing
- Backstop Netting Complete

## UPCOMING

### Concourse

- Batting Tunnel
- Sod
- Added Concrete Sidewalks

### Softball

- Dugout Scorer's Booth

### Aux Field

- Outfield Sod
- Infield Mix



Aux Field



Baseball Field




Overall Site



Softball Field



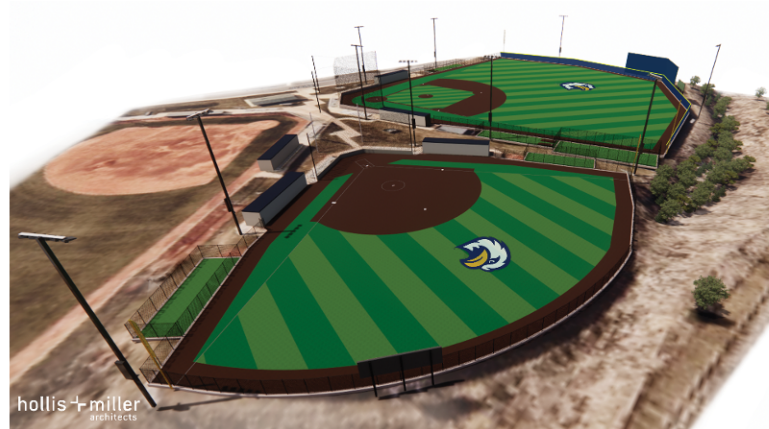

## Liberty North High School Baseball/Softball Complex

### Baseball Field

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Center field Batter's Eye
- Additional Bullpen Space
- ChampionWall PVC Athletic Fence System at Outfield

### Softball Field

- Increased Field Dimensions - 194'(L) - 200'(C) - 195'(R)
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

**Construction Start:** Fall 2023

**Construction Complete:** Summer 2024

**WEEKLY  
PROGRESS  
REPORT**

# LNHS Ball Fields 5/09/2024

Liberty Public Schools



## PROJECT STATUS

- Baseball
  - Punch List Ongoing
- Softball
  - Turf Complete
  - Punch List Ongoing

## UPCOMING

- Concourse
  - Sod
  - Added Concrete Sidewalks
  - Access Road Addition

Project Completion  
Baseball March 2024/Softball May 2024



Overall Site



Overall Site



Softball



Baseball



LED Lighting upgrades are planned throughout the District and will be sequenced with other projects as possible between the fall of 2023 through fall of 2026.

## PROJECT STATUS

- South Valley MS - Upgrades Complete
- Discovery MS - Upgrades Complete
- EPiC Elementary - Upgrades Complete
- Liberty North High School - Upgrades Ongoing

## UPCOMING

- Energy Inspections - All Four Schools
- Emergency LED Fixtures

Project Completion  
December 2023




Liberty North HS



Liberty North HS



Liberty North HS

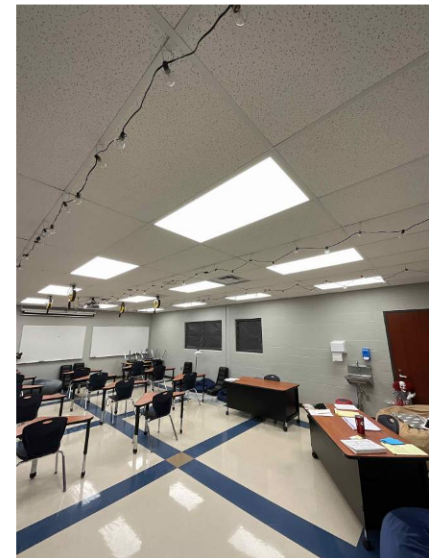

Liberty North HS

## PROJECT STATUS

South Valley MS- Upgrades Complete

Discovery MS - Upgrades Complete


EPiC Elementary - Upgrades Complete

LNHS - Upgrades Ongoing


## UPCOMING

Energy Inspections All Four Schools  
Emergency LED Fixtures

Project Completion  
December 2023

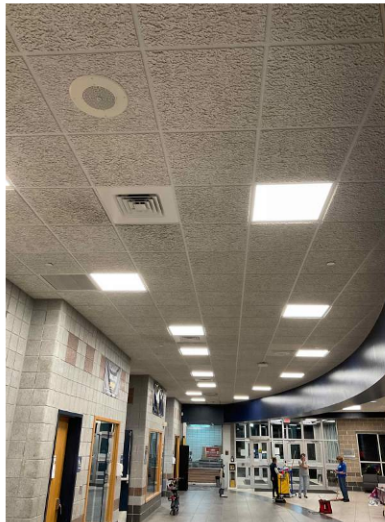


South Valley Middle School

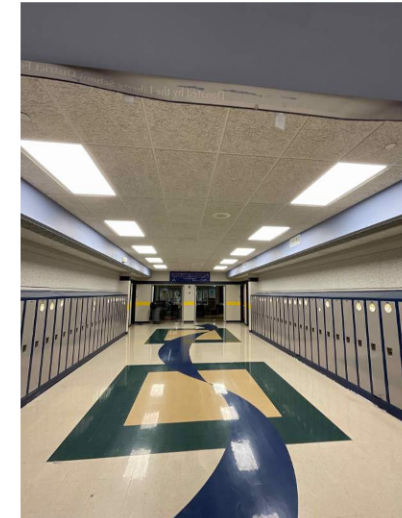

South Valley Middle School



Discovery Middle School

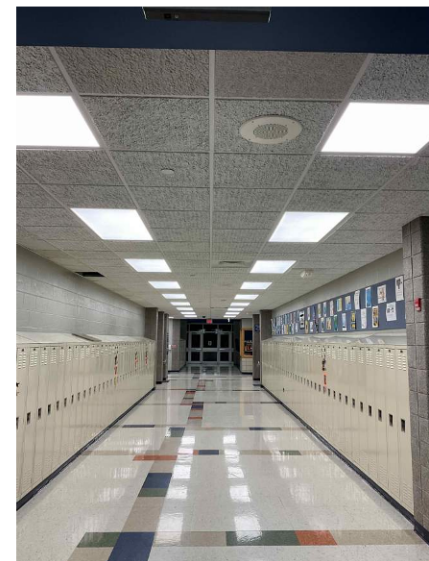

Discovery Middle School

# WEEKLY PROGRESS REPORT



Epic Elementary



Epic Elementary



Liberty North High School




Liberty North High School




### EPiC Elementary Addition

- 8000 Square Foot Building Addition & Renovation
- New Gym & Performance Space
- New Art Classroom
- Renovated Restrooms, Mother's Room and New Walk-in Cooler / Freezer
- Construction Start: Spring 2024
- Construction Complete: Summer 2025

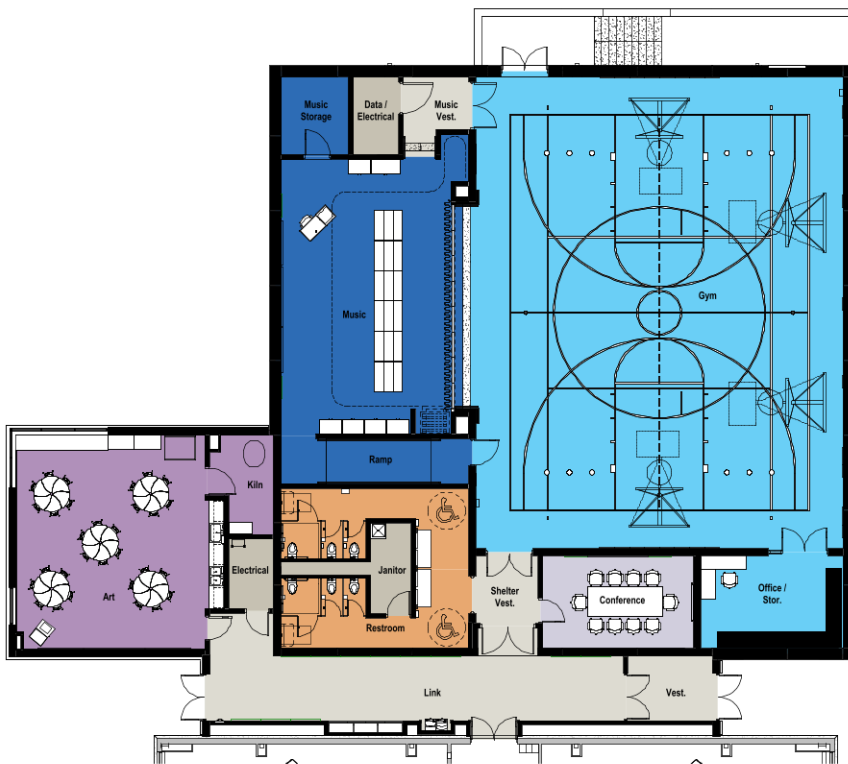

▲ Addition

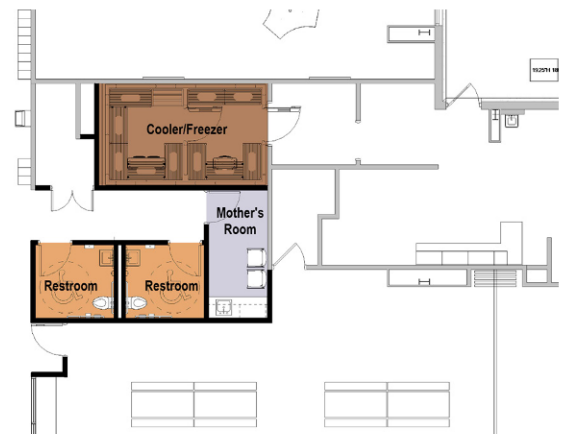

▲ Renovation Area

## PROJECT STATUS

- EPiC Elementary
- Building Footings Ongoing
- Underground Electrical Rough In

## UPCOMING

- EPiC Elementary
- Structural Steel
- Existing Building Interior Renovation

Project Completion  
EPiC Feb 2025/DMS&SVMS June 2025



EPiC Elementary - Footing Prep



EPiC Elementary - Digging Footings



EPiC Elementary - Footing Pour





EPiC Elementary - Digging Footings



### Discovery Middle School

- 11,000 square foot addition
  - ICC 500 rated shelter
  - Additional PE space
- Raised performance stage
- Theatrical AV and lighting
- Increased audience capacity
  - Additional storage
- Projected Construction Schedule:  
Spring 2024–Summer 2025

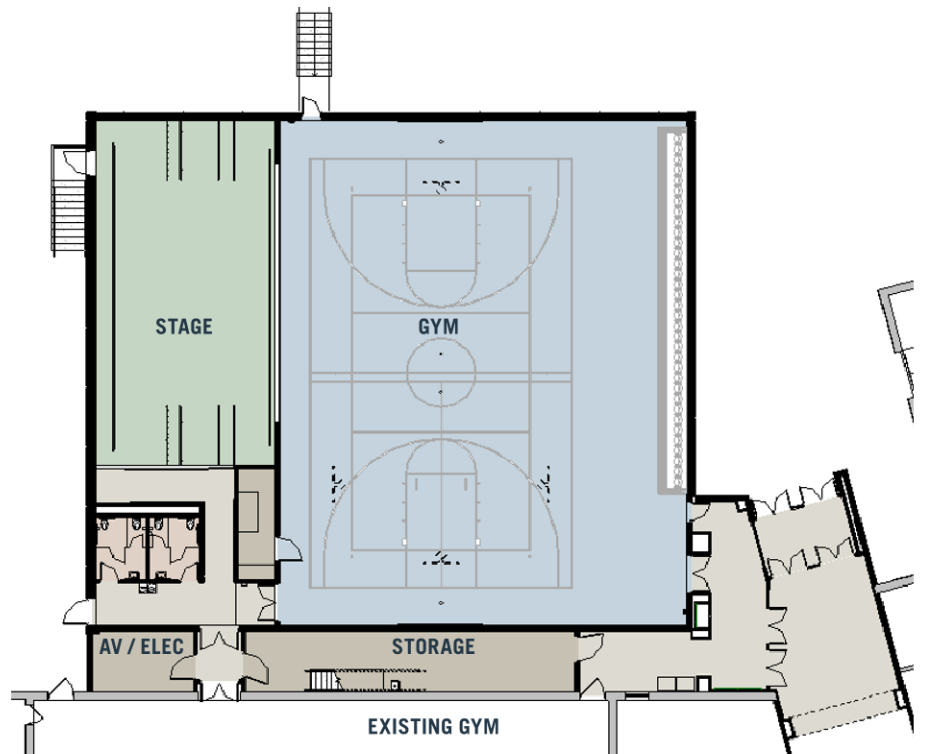

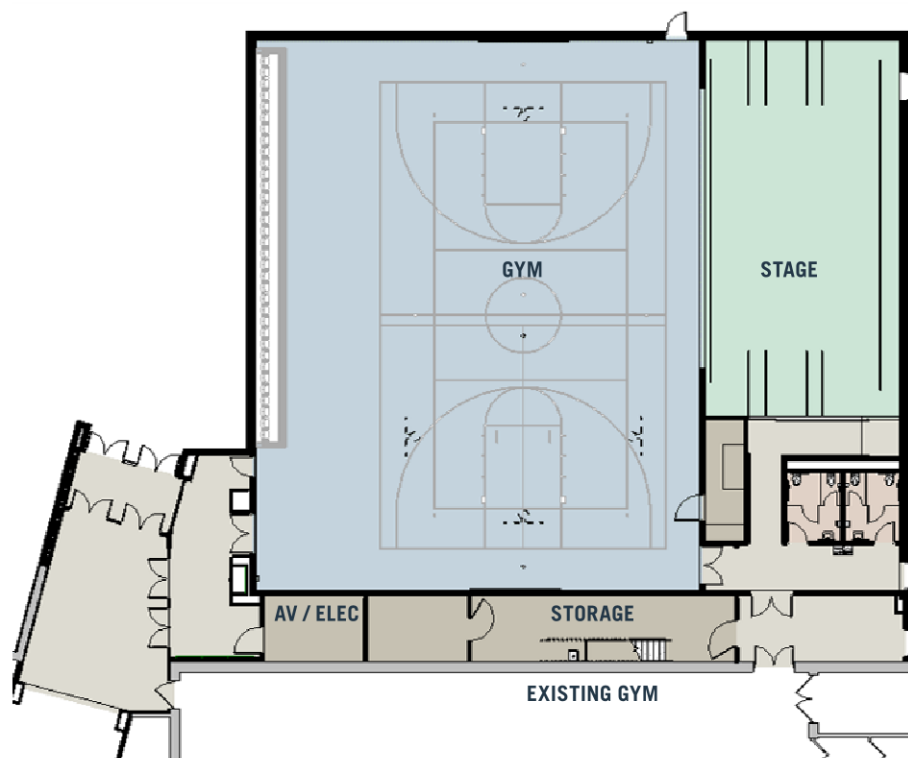

### South Valley Middle School

- 11,000 square foot addition
- ICC 500 rated shelter
- Additional PE space
- Raised performance stage
- Theatrical AV and lighting
- Increased audience capacity
- Additional storage
- Projected Construction Schedule: Spring 2024–Summer 2025



hollis + miller



hollis + miller



hollis + miller



hollis + miller

## Distribution Center

- 29,000 Square Foot New Building
- Storage Warehouse
- Dry Food Warehouse
- Large Storage Freezer
- New Office Space
- New Copy Center
- Additional Parking
- Projected Construction Schedule: Fall 2023–Spring 2025



**WEEKLY  
PROGRESS  
REPORT**

# Distribution Center 5/8/24

## Liberty Public Schools



5/7/24

### PROJECT STATUS

- Footing complete this week
- Concrete curb and paving complete
- Striping complete
- Power transfer complete

### UPCOMING

- Slab on grade prep
- Pour lab on grade sequence 1
- Pour slab on grade sequence 2
- Remaining deep fills
- Detention Basin
- Storm line 2 & 6

Project Completion  
June 2025



New Drive at North Entrance



Pouring New Drive at North Entrance



Footing at Southeast Corner of Building



Footing at Southeast Corner of Building



Overall Site



Overall Site



Overall Site



Overall Site

Fine Arts  
 Kid's Zone  
 Technology  
 Shared Amenities  
 Building Systems  
 Future Phase



### District Technology Center

- Renovated workspace for District’s Technology, Fine Arts, and Kid’s Zone departments
- Shell space for future growth
- Minor exterior patch + repair improvements
- Projected Construction Schedule:  
 Fall 2023 - Summer 2024

5/3/24

## PROJECT STATUS

District Technology Center:

- Completed Wall Framing
- Completed Drywall Installation
- Completed Drywall Finishing
- Completed MEP Overhead Rough
- Communications Install Continued
- Continued Paint
- Began Flooring Install
- Completed Break room Tile Install
- Completed Exterior Door Install
- Continued EIFS Finishing

## UPCOMING

District Technology Center:

- Begin MEP Trimout
- Begin Setting Data Equipment
- Set Generator
- Complete Interior Door Install
- Complete Paint
- Continue Flooring Install
- Complete Asphalt Patch Back
- Complete EIFS Patching
- Begin Landscaping/Fence Install

Project Completion June 2024



Restroom Finishes



EIFS Installation



Sliding Glass Wall in Fine Arts Open Office



Fine Arts Workshop



Tech Support Reception Area




Data Room



Break Room Casework and Tile



Main Corridor

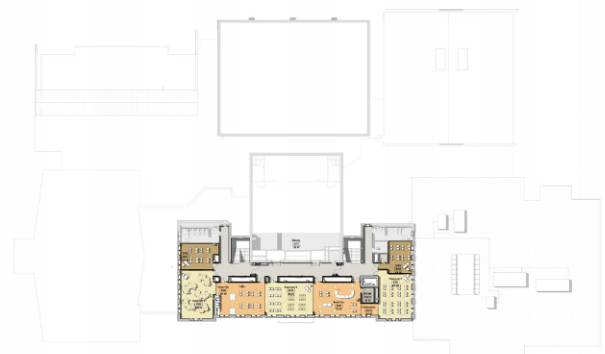

LEVEL 3



LEVEL 2




LEVEL 1



LEVEL 0

## Heritage Middle School

- 39,000 square feet academic renovation
- Grade level neighborhoods with flex collaboration spaces
  - Integrated SPED resources
  - Renovated cafeteria & scramble
    - Restroom renovations
- Exterior masonry repair & window replacement
  - Elevator replacement
- Projected Construction Schedule: Spring 2024–Fall 2025

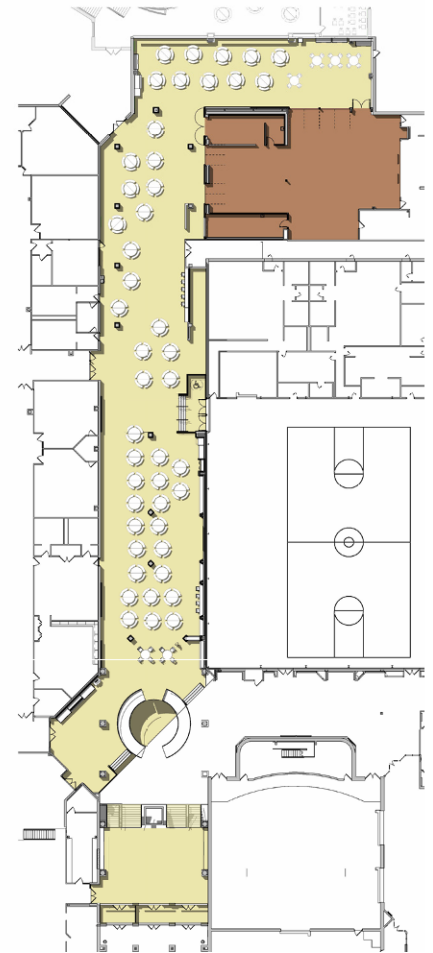

PHASE 2

### Liberty High School

- Square footage: 40,800 SF
- Renovation to FACS, SPED and Art classrooms
- Renovated scramble & dining area
- LED lighting replacement
- Project Construction Schedule: Summer – Fall 2024 & 2025




PHASE 1



## Shop Building



- 1,800 Square Foot New Building
- Flexible Open Plan
- Patio & Secure Breezway
- Woodworking Area
- Metalworking Area
- Flex-space for Lectures or Large Projects
- Projected Construction Schedule: Spring 2024–Spring 2025

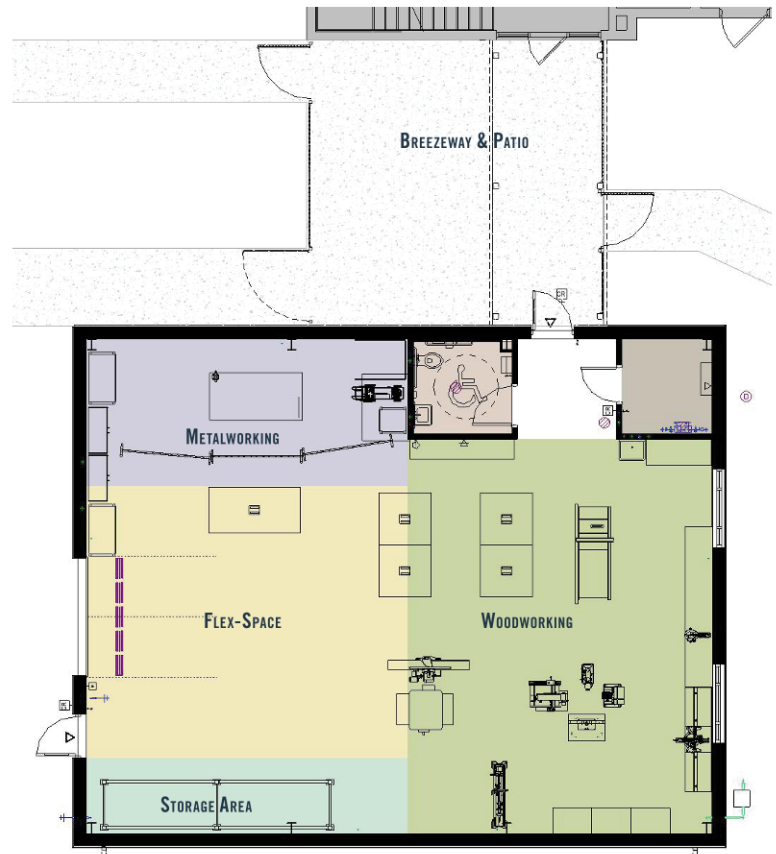

▲ Floor Plan


## Recreation Court

- 3,531 Square Foot New Court
- Court Lines for Basketball & Pickleball
- Additional Area for Temporary Bleachers
- Projected Construction Schedule:  
Spring 2024–Spring 2025

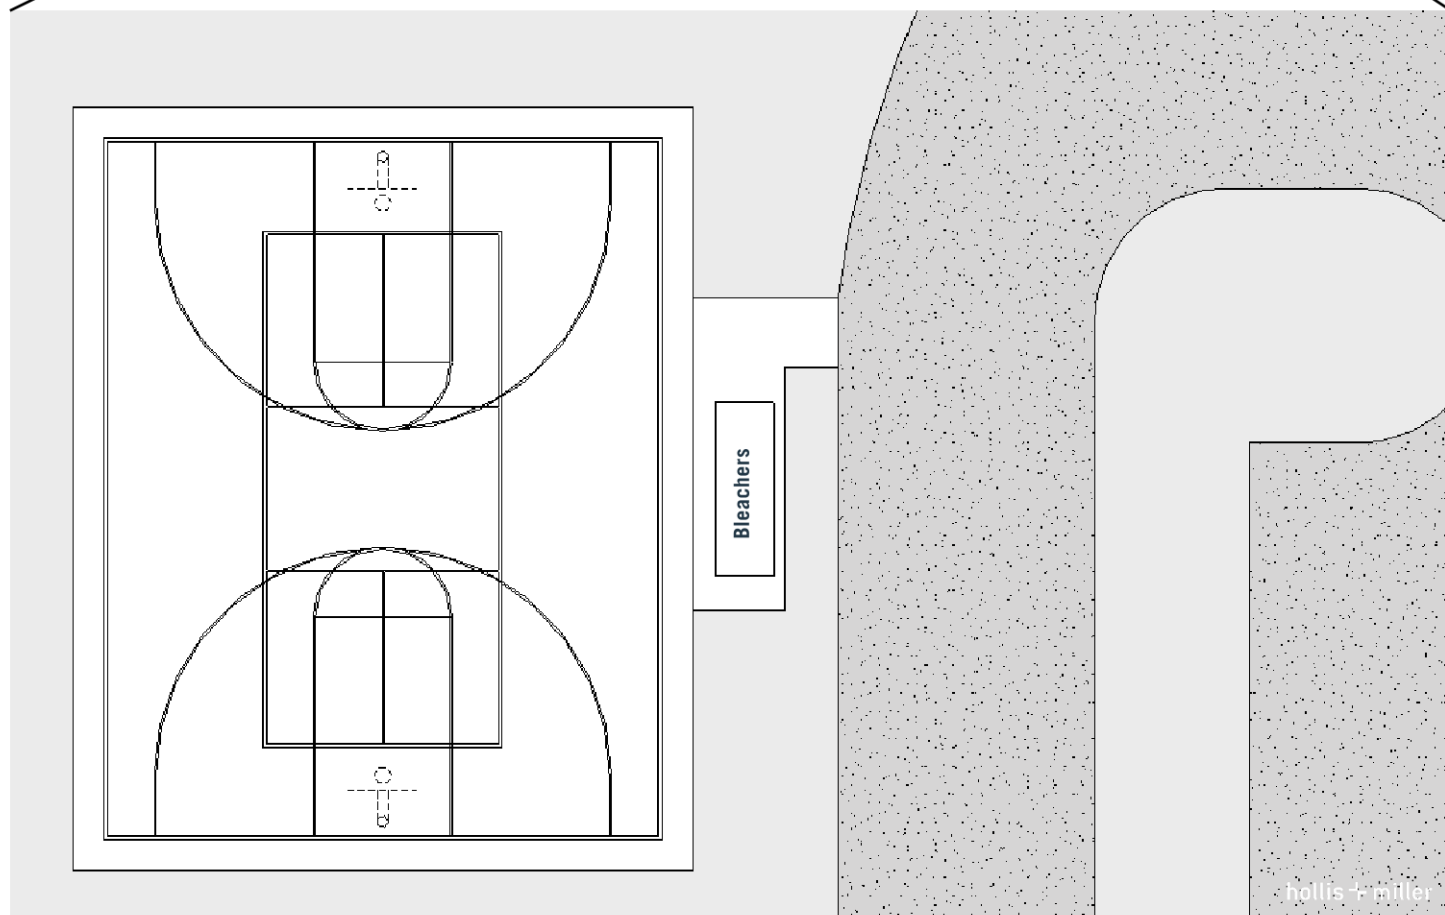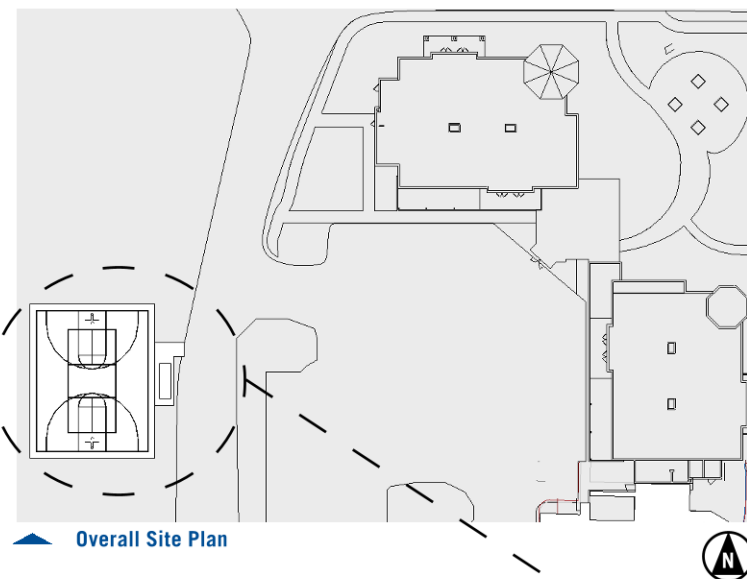


## Interior Renovation

- Nurse Room Relocation
- Renovated Teacher Workroom
- SPED Classroom Toilet Renovation
- New Admin Reception Entry Door & Counter
- Staff Restroom Renovation
- Lactation Room
- Projected Construction Schedule:  
May 2024 - August 2025

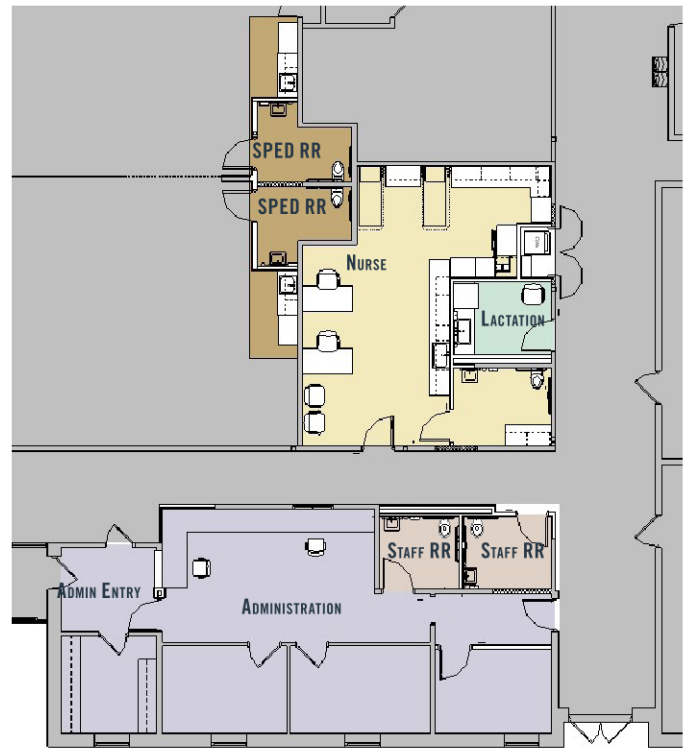

▲ Enlarged Floor Plan

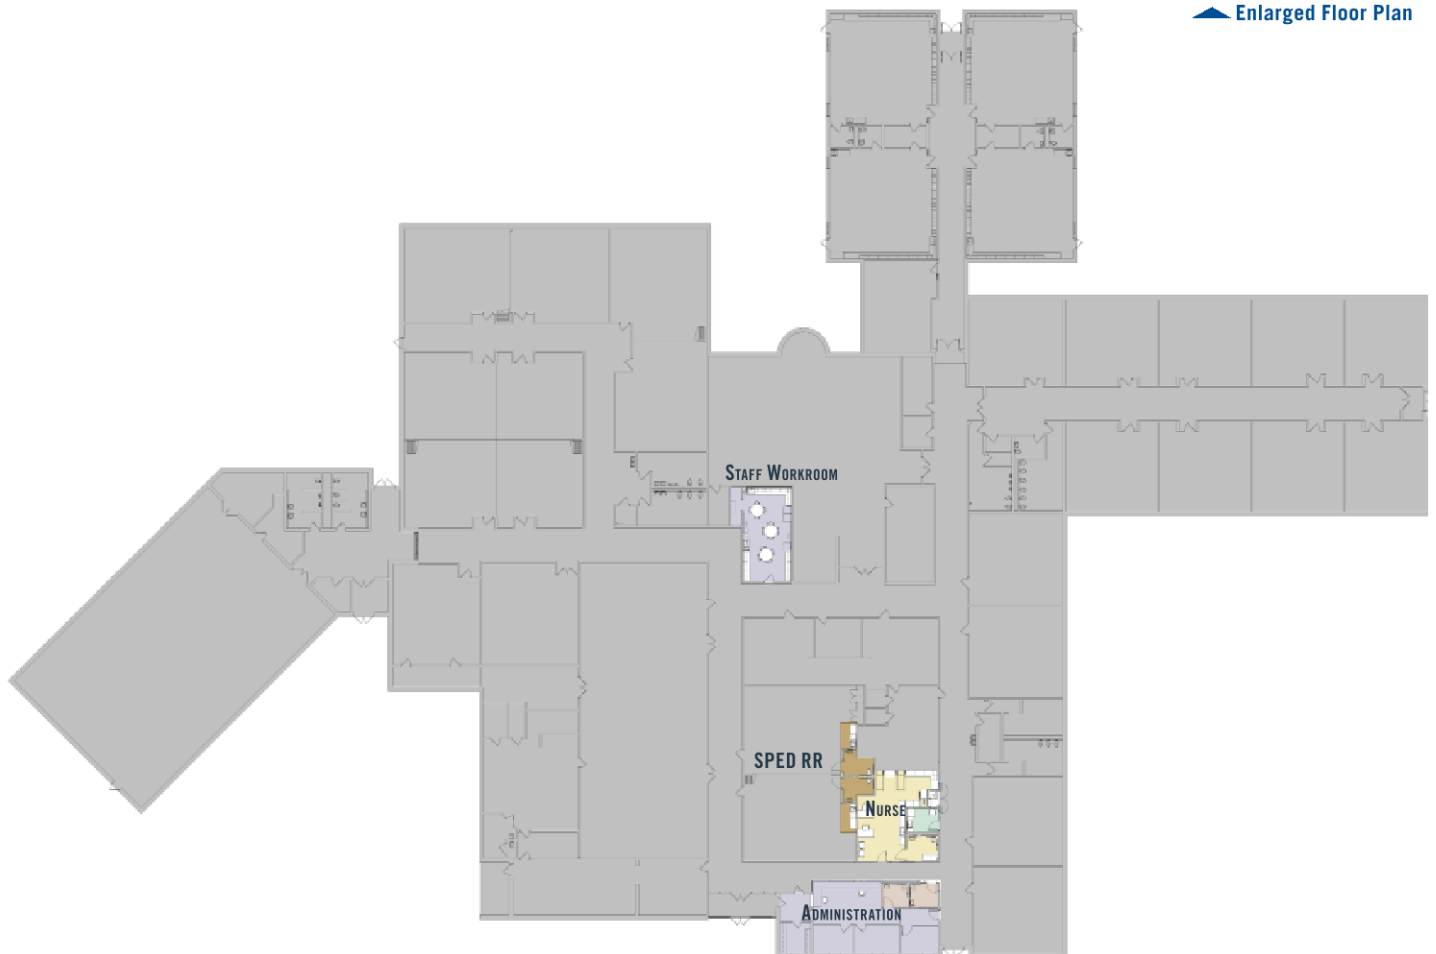


▲ Overall Floor Plan

## Interior Renovation

- Nurse Room Renovation
- Administration Office Renovation
- New Admin Reception Desk & Entry Door
- Lactation Room
- Group & Staff Restroom Renovation
- LED Lighting Replacement
- HVAC Replacement
- Projected Construction Schedule:  
May 2024 - August 2025



Administration

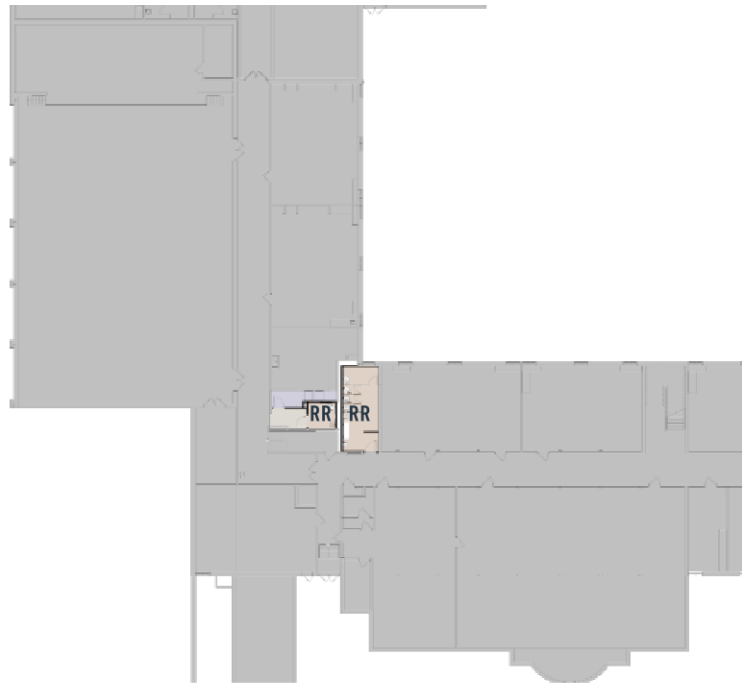

Partial First Level Floor Plan




Overall Second Level Floor Plan

## Interior Renovation

- Nurse Room Relocation
- Group & Staff Restroom Renovation
- New Admin Reception Desk & Entry Door
- Gym Stage Renovation into Staff Offices & PE Storage
- Lactation Room
- Media Center Wing LED Lighting
- Projected Construction Schedule:  
May 2024 - August 2025



Administration

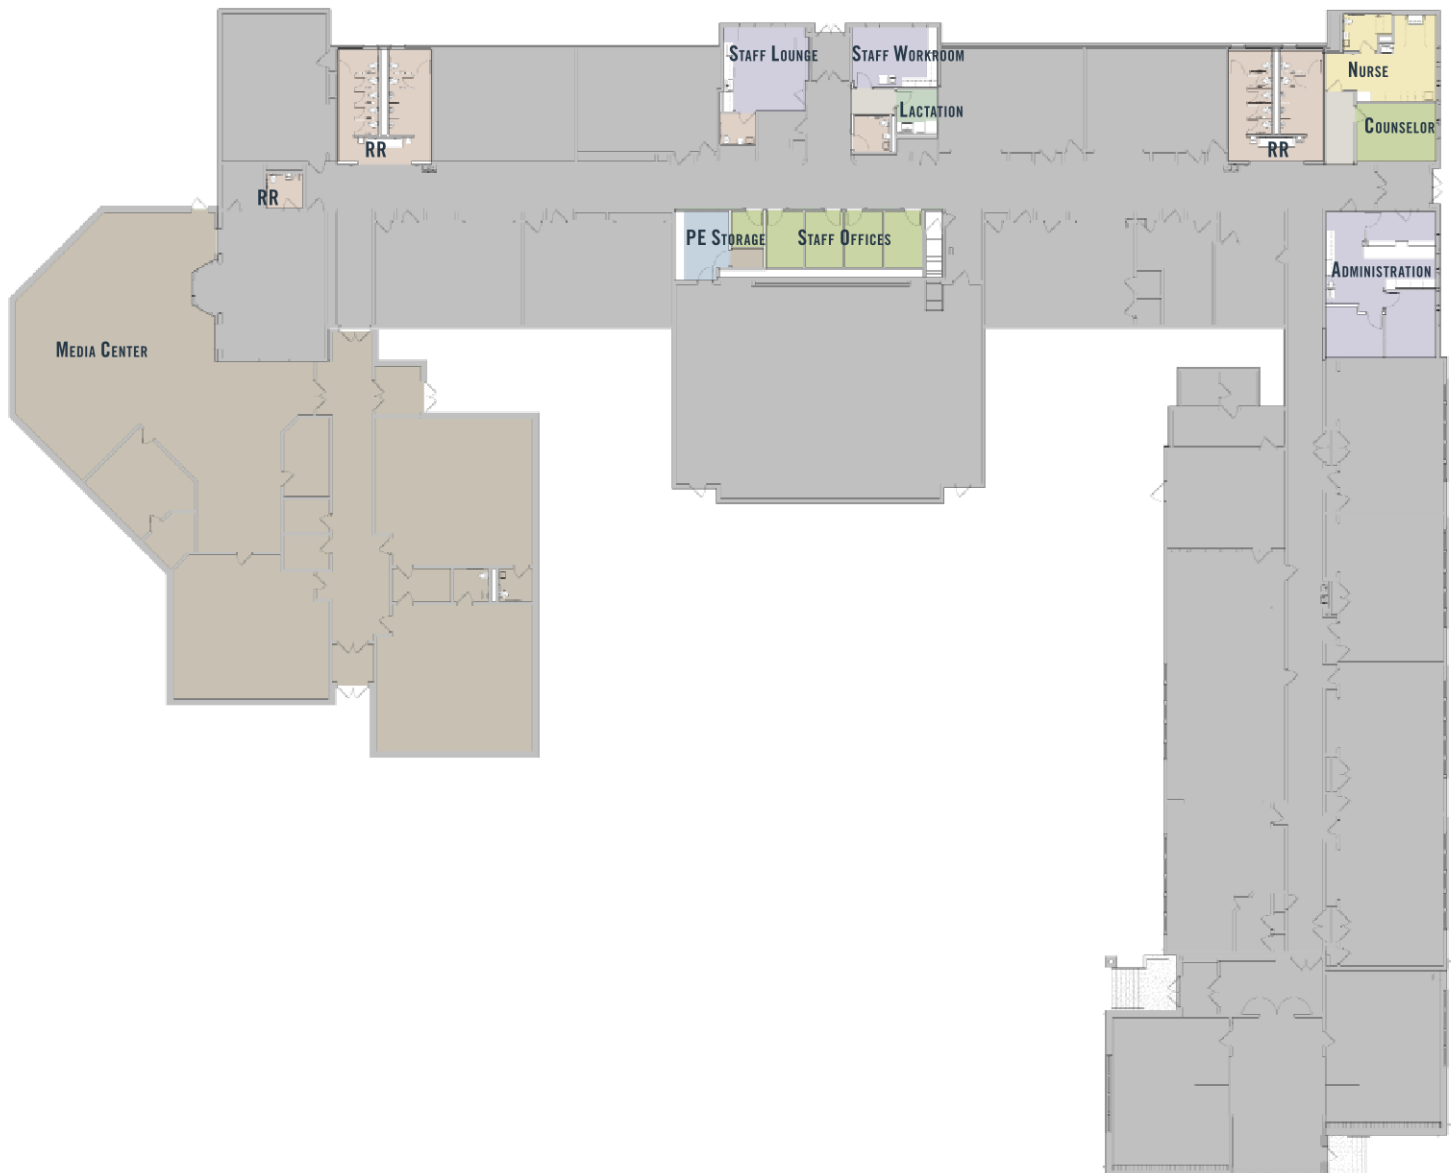

Overall Floor Plan
