

Measure BB Bond

21st Century Classroom Improvements
April 2026




CUMMING
GROUP

//////////////////// BUILDING VALUE THROUGH EXPERTISE



HLPUSD MEASURE BB - SUMMARY

SCHOOLS IN PROGRESS

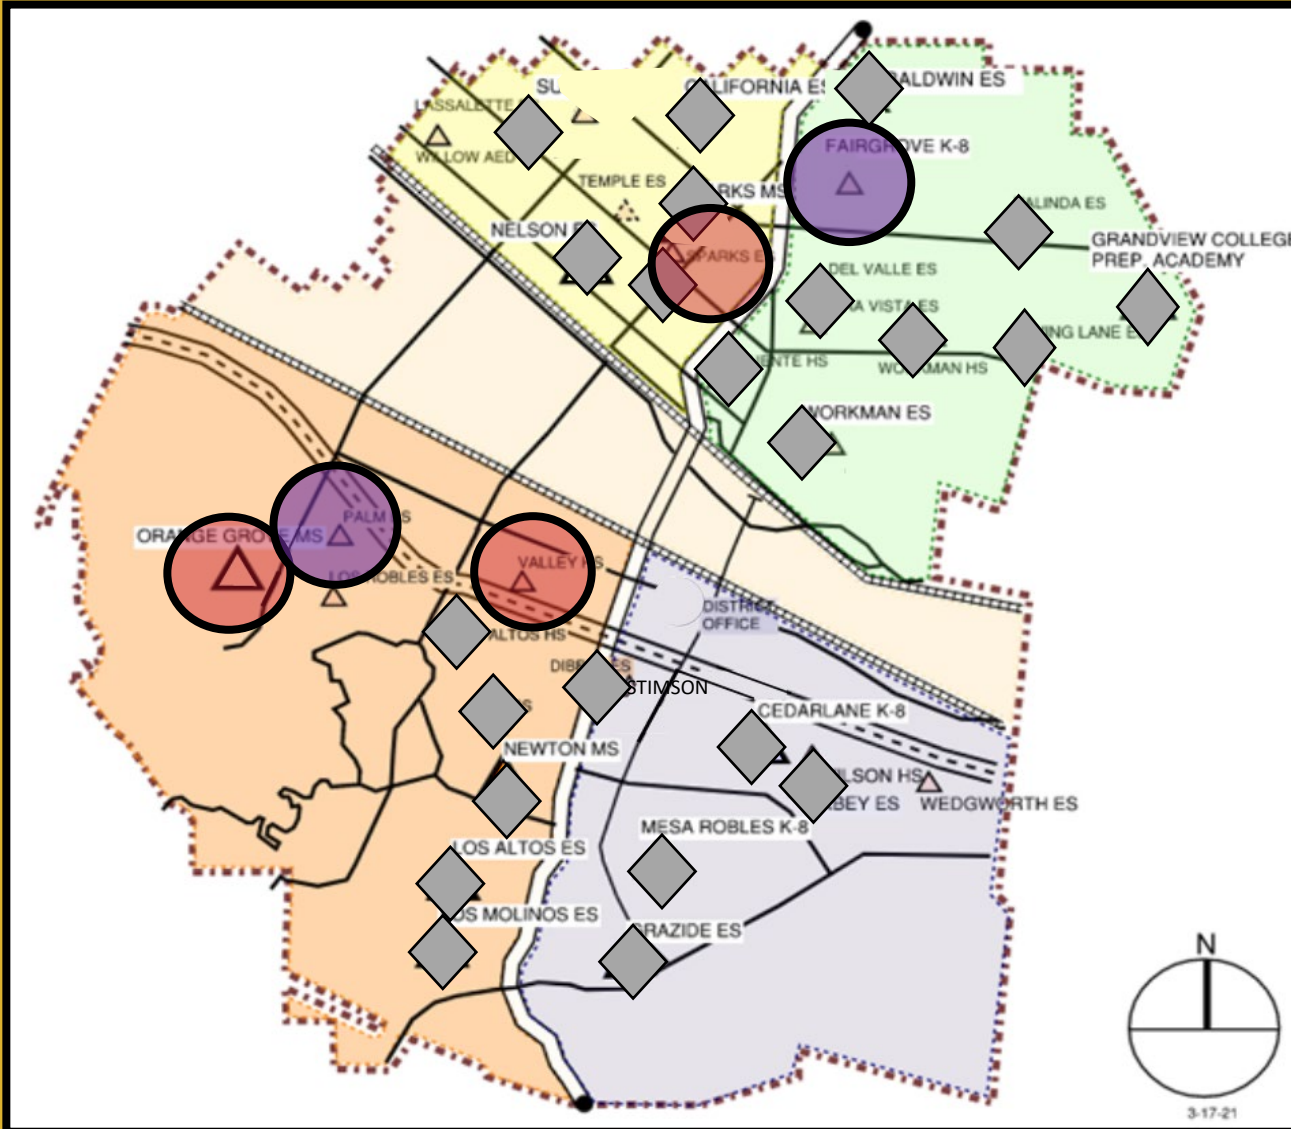

- IN PROGRESS CONSTRUCTION**
 - Fairgrove K-8
 - Palm ES
- PENDING BID**
 - Valley Alternative School
 - Orange Grove MS
- IN DESIGN**
 - Sparks MS II

- COMPLETED**
 - Baldwin ES
 - California ES
 - Lassalette ES
 - Nelson ES
 - Sparks ES
 - Sparks MS
 - Cedarlane K-8
 - Mesa Robles K-8
 - Grandview MS
 - La Puente HS
 - Los Altos ES
 - Los Altos HS
 - Los Molinos ES
 - Newton MS
 - Sierra Vista MS
 - Stimson EC
 - Wilson HS
 - Workman ES
 - Workman HS
 - Grazide ES
 - Kwis ES
 - Valinda ES
 - Wing Lane ES

PROJECT STATUS

2025-2026		In DSA	DSA Approved	Bid Date	Start Date	Complete	Certification
21st century Classroom Implements							
Bid 6	Baldwin Academy		30-Jan-24	24-Oct-24	12-Nov-24	31-Jul-25	Pending
	California Elementary School		27-Jun-24	24-Oct-24	12-Nov-24	31-Jul-25	Pending
	Los Molinos Elementary School		29-Aug-24	24-Oct-24	12-Nov-24	31-Jan-25	Pending
	Grazide Elementary School		9-Aug-24	24-Oct-24	27-May-25	2-Feb-26	Pending
Bid 7	Kwis Elementary		11-Dec-24	27-Feb-25	25-Mar-25	3-Nov-25	Pending
	Lassalette Elementary		7-Feb-25	27-Feb-25	25-May-25	9-Mar-26	Pending
	Sierra Vista Middle School		22-Jan-25	27-Feb-25	12-May-25	3-Nov-25	Pending
Bid 7B	Fairgrove		18-Nov-24	27-Feb-25	25-May-25	30-Apr-26	Pending
Bid 8	Palm Elementary School		6-Feb-25	20-May-25	30-Mar-26	20-Jul-26	Pending
	Sparks Elementary School		18-Mar-25	21-May-25	7-Jul-25	19-Jan-26	Pending
	Valinda Elementary School		7-Feb-25	22-May-25	8-Jul-25	9-Mar-26	Pending
	Wing Lane Elementary School		18-Mar-25	23-May-25	9-Jul-25	9-Mar-26	Pending

Fairgrove K-8

Phase 1 Completed

Phase 2 Under Construction



Kwis Elementary

Complete




KINDERGARTEN



CLASSROOM

Lassalette Elementary

Complete

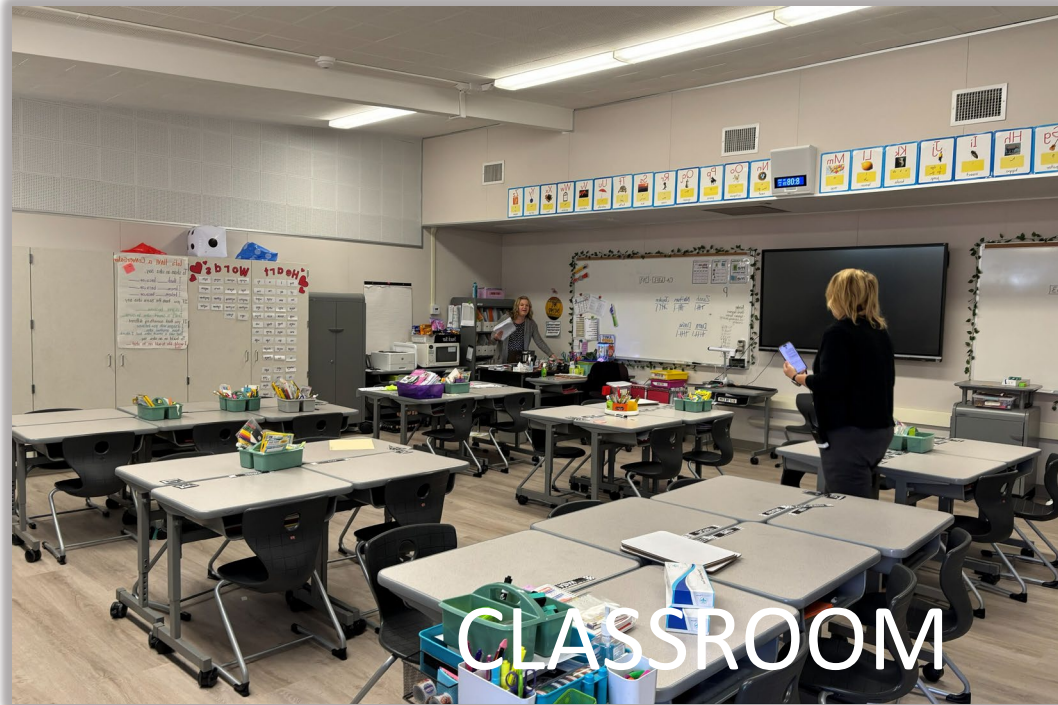


Sparks Elementary

Complete



Valinda Elementary

Complete

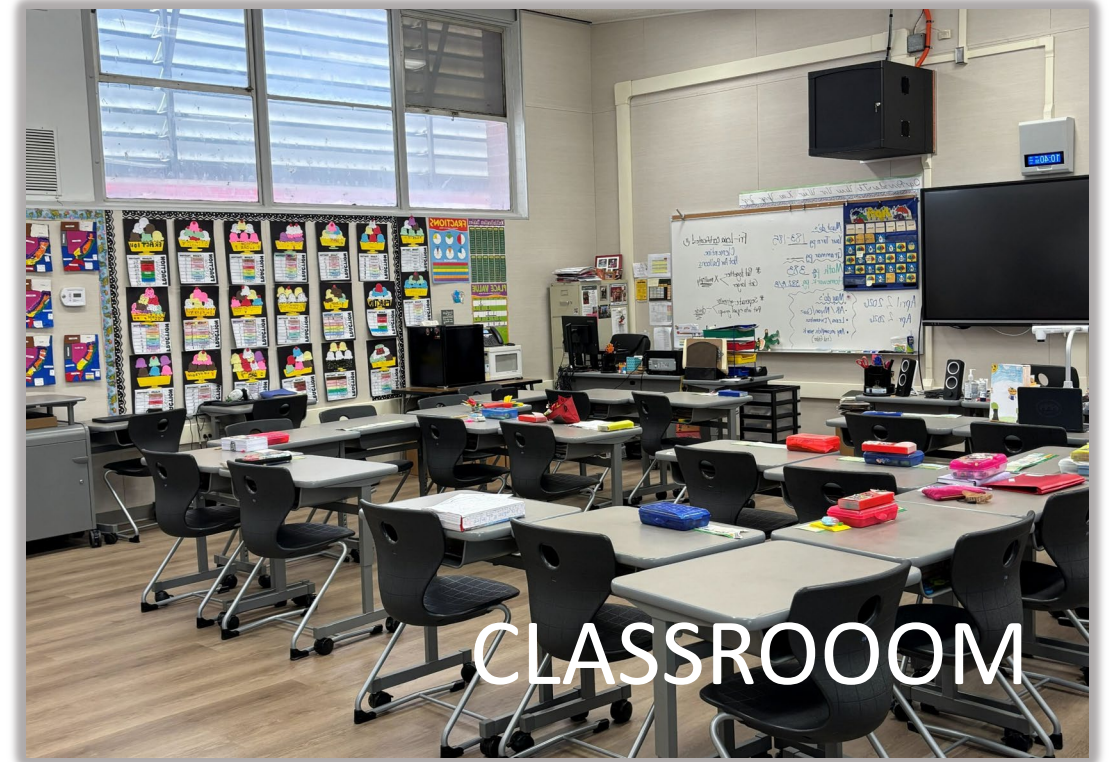

Wing Lane Elementary

Complete





QUESTIONS & ANSWERS
