




Monthly Progress Report

April 2026

Hempstead Union Free School District



Report prepared by Idris Mashriqi





Table of Contents

Section I – Program Summary

Section II – Work Progress **April 2026**

Section III – Work Projected for **May 2026**

Section IV – Progress Photos

Section V – Monthly Workforce Summary



Section I – Program Summary

April 2026

Project List

- **Hempstead UFSD – IAQ at Various School – In Progress**
 - Indoor air quality and mechanical upgrades.
 - Electrical upgrades.
- **Hempstead UFSD – 2022 Bond Phase 3 – In Progress**
 - Infrastructure upgrades throughout all schools.
- **Hempstead UFSD – Boiler replacement at Prospect Elementary School – In Progress**
 - Boiler and piping replacement.
- **Hempstead UFSD – 2022 Bond Phase 4 – In Progress**
 - Infrastructure upgrades throughout all schools.
- **Hempstead UFSD – 2024 Bond Phase 2 – Bidding Process**
 - Infrastructure upgrades throughout all schools.



Section II - Work Progress April 2026

Hempstead UFSD – IAQ at Various Schools

- **Reliance:**
 - Excavated for new chiller piping.
 - Installed new pad and bollards for Chiller.
 - Rigged chiller on pad.
 - Working on BMS for all schools.
- **Eldor:**
 - Continued roughing in ceilings and on walls at Paterson ES and McNeil ES.
 - Started swapping out old panels for new panels.
 - Continued roughing in Prospect ES.

Hempstead UFSD – 2022 Bond Phase 3

- **J Cole:**
 - Demo and install new staircases at Prospect ES and McNeil ES.
 - Demo and install new sidewalks at McNeil ES.
- **IPS:**
 - Remove existing sump pump and install new pump with lift gate for access.
- **Eldor:**
 - Continued to rough at McNeil ES and Prospect ES.



Section III - Work Planned May 2026

Hempstead UFSD – IAQ at Various Schools

- **Reliance:**
 - Start up chiller and associated equipment.
 - Start up VRF systems.
 - Complete BMS systems for all schools.
- **Eldor:**
 - Complete all power runs to all equipment.
 - Complete site work.

Hempstead UFSD – 2022 Bond Phase 3

- **J Cole:**
 - Prep for summer work
- **IPS:**
 - Prep for summer work.
- **RMS:**
 - Prep for summer work.
- **Eldor:**
 - Start HS parking lot light pole replacements.
- **Hempstead UFSD – Boiler replacement at Prospect Elementary School – In Progress**
 - Start demo of boilers and associated piping.



Section IV – Progress Photos



Hempstead IAQ – Paterson Transformer Pad



Section IV – Progress Photos



Hempstead IAQ – Prospect ES CHW Piping



Section IV – Progress Photos



Hempstead IAQ – Prospect ES Conduit Runs



Section IV – Progress Photos



Hempstead 2022 Bond Ph. 3 – Sump Pump



Section IV – Progress Photos



Hempstead 2022 Bond Ph. 3 – Concrete Work



Section IV – Progress Photos



Hempstead 2022 Bond Ph. 3 – Concrete Work



Section IV – Progress Photos




Hempstead 2022 Bond Ph. 3 – Concrete Work



Section V – Workforce Summary – Company/Hours

April 2026

MANPOWER GRAPH

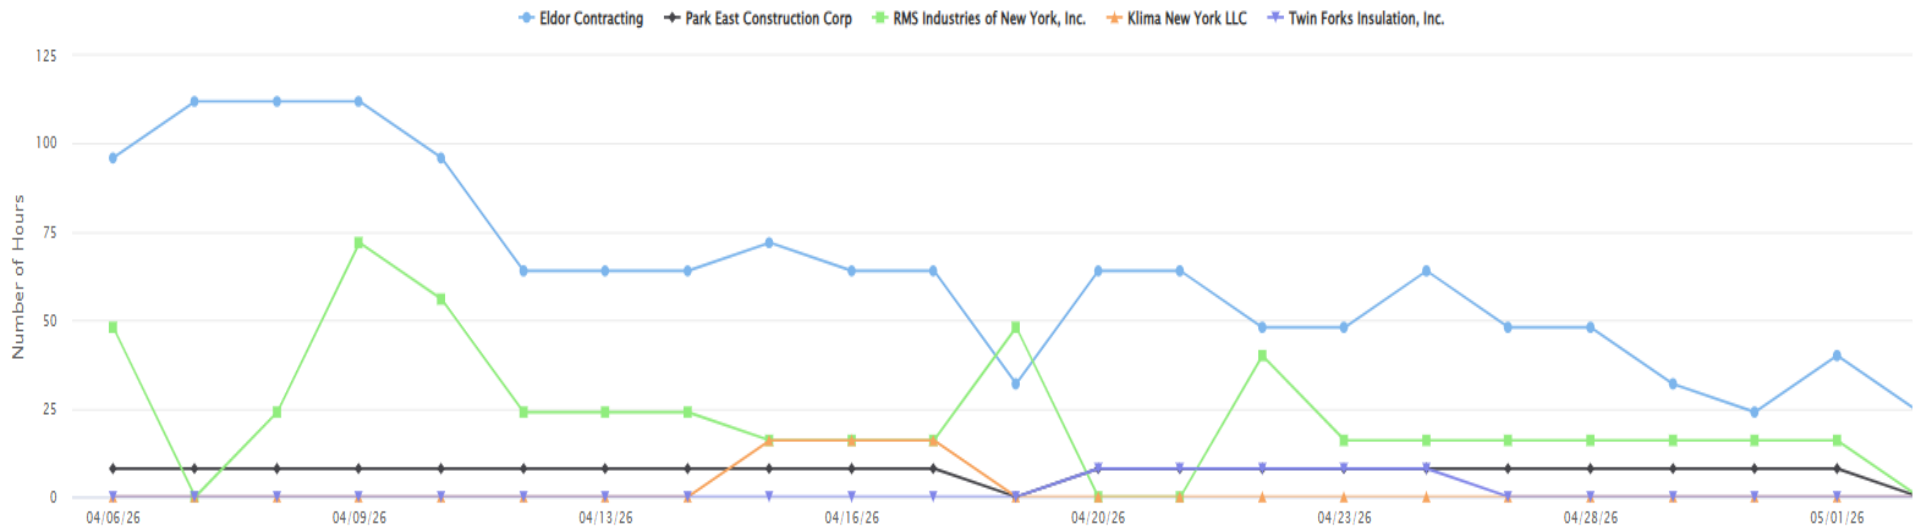


Hempstead UFSD – IAQ at Various Schools



Section V – Workforce Summary – Company/Hours

April 2026

MANPOWER GRAPH

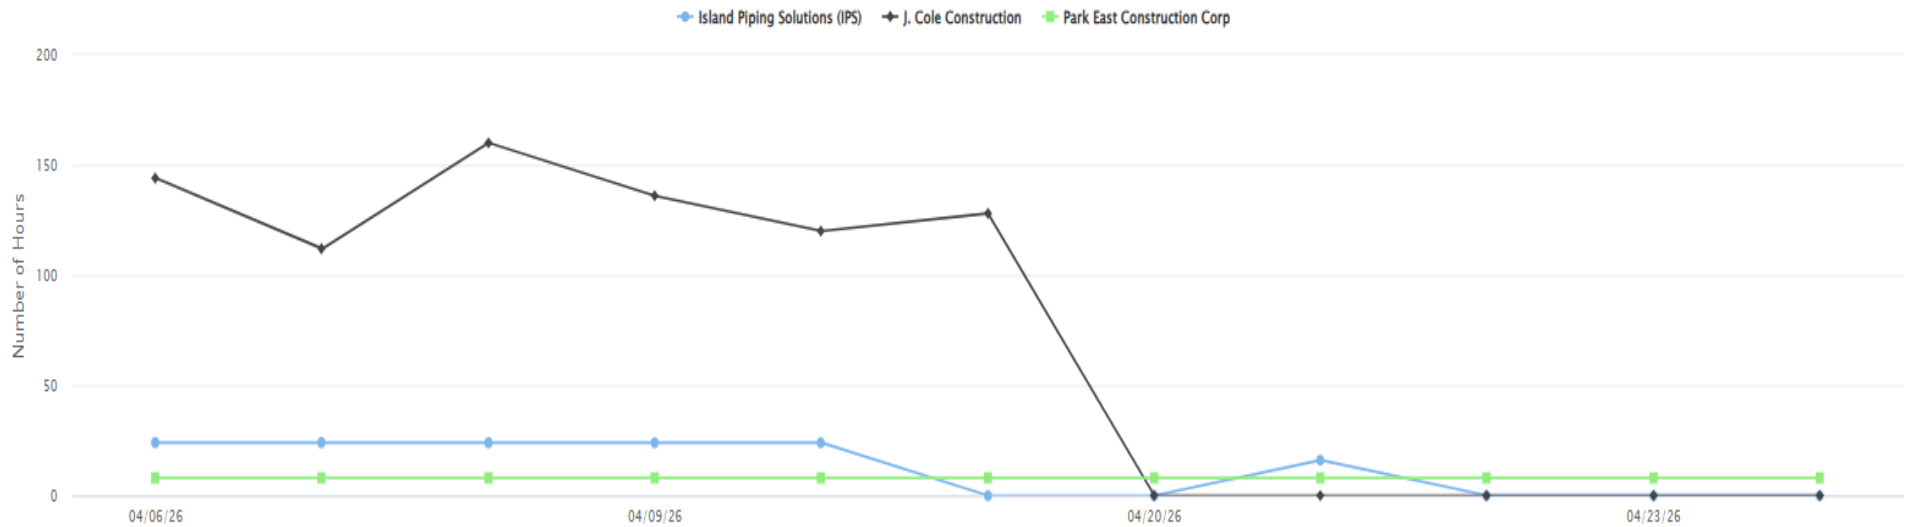

Hempstead UFSD – 2022 Bond Phase 3



Hempstead Union Free School District

April 2026

End of Progress Report
