




Quarterly Executive Summary Baseball & Softball Renovations – Phase 1 Q1 2026

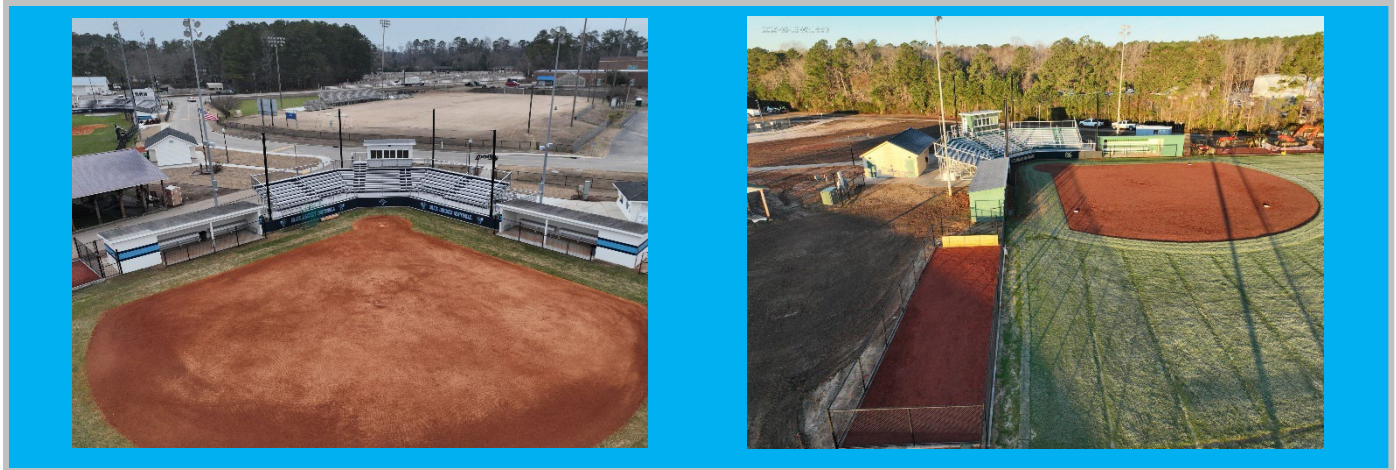

HCS Project Manager: Trevor Turner

Schools: Aynor High School & Conway High School

Architect/Engineer: CHA Consulting

Contractor: Thompson Turner

Project Scope: To upgrade the baseball and softball complexes at each high school. Project scope includes, press boxes, restrooms and concessions (where applicable), new bleacher seating field irrigation and drainage, fencing, batting cages & bullpens, backstop walls & netting, new field accessories (foul poles, mounds, bases, etc., and general site improvements.

Current Status: Under Construction. Currently pricing Group 2 (CFHS and GSFHS) to begin work summer of 2026.

Budget: **\$5,000,000 annually.** Board Approved Date: May 1, 2023 .
\$8,600,000 added to overall funding for all phases. Board Approved Date: November 17, 2025.

Budget Issues: Phase 1 came in over original budget. Board approved additional overall funding of \$8,600,000 for all phases.

Schedule:
AHS Softball – Completed
CHS Baseball – Completed
CHS Softball – Completed
AHS Baseball (minus field work) – Completed
AHS Baseball Field Work – To begin late May 2026

Schedule Issues: None.
