




Quarterly Executive Summary
Phase V – Tennis Court Projects
Q1 2026

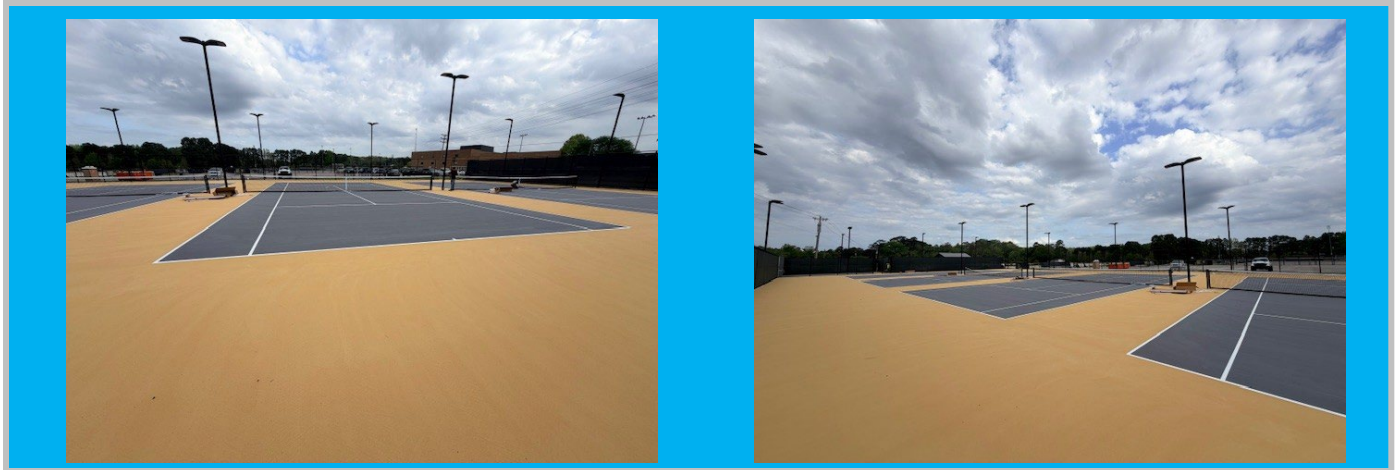

HCS Project Manager: Trevor Turner

Schools: Aynor High School, North Myrtle Beach High School, St. James High School, and Socastee High School

Architect/Engineer: CHA Consulting

Contractor: Contract Construction

Project Scope: To upgrade athletics at all nine high schools, with a focus on tennis courts, running tracks, and stadium playing surfaces. Current phase addresses tennis courts at four facilities. Additional school parking improvements were added to the scope and budget at North Myrtle Beach High School and St. James High School.

Current Status: Under Construction.

Budget (Tennis): \$5,000,000 Board Approved Date: May 1, 2023
\$ 500,000 Board Approved Additional Funding Date: May 13, 2024
\$5,500,000

Budget Issues: None.

Schedule:
North Myrtle Beach High: Completed
St. James High: Tennis Complete. Parking lot paving to begin in May.
Aynor High: Remediation work and final surfacing to begin in April.
Socastee High: Completed

Schedule Issues: None.

Achievements: NMBH, SJHS and SHS tennis completed.
