




# Monthly Progress Report

May 2026

Hempstead Union Free School District



Report prepared by Idris Mashriqi





# Table of Contents

**Section I** – Program Summary

**Section II** – Work Progress **May 2026**

**Section III** – Work Projected for **June 2026**

**Section IV** – Progress Photos

**Section V** – Monthly Workforce Summary



## Section I – Program Summary May 2026

### Project List

- **Hempstead UFSD – IAQ at Various School – In Progress**
  - Indoor air quality and mechanical upgrades.
  - Electrical upgrades.
- **Hempstead UFSD – 2022 Bond Phase 3 – In Progress**
  - Infrastructure upgrades throughout all schools.
- **Hempstead UFSD – Boiler replacement at Prospect Elementary School – In Progress**
  - Boiler and piping replacement.
- **Hempstead UFSD – 2022 Bond Phase 4 – In Progress**
  - Infrastructure upgrades throughout all schools.
- **Hempstead UFSD – 2024 Bond Phase 2 – Bidding Process**
  - Infrastructure upgrades throughout all schools.



## Section II - Work Progress May 2026

### **Hempstead UFSD – IAQ at Various Schools**

- **Reliance:**
  - Started up chiller at Prospect ES.
  - Started up split units at McNeil ES.
  - Insulated chilled water piping.
- **Eldor:**
  - Completed Prospect ES, and McNeil electrical upgrades.
  - Paterson ES waiting on switchgear arrival.

### **Hempstead UFSD – 2022 Bond Phase 3**

- **J Cole:**
  - Installed new doors at McNeil ES.
- **Eldor:**
  - Continued to rough at McNeil ES.

### **Hempstead UFSD – Boiler replacement at Prospect Elementary School**

- **KG Mechanical**
  - Submitted insurances and bonds.
  - Submitted major equipment submittals.
  - Start date will be June 1<sup>st</sup> for demo.

### **Hempstead UFSD – 2022 Bond Phase 4**

- Prime contractors submitted SOV's for approval.
- Prime contractors started submitting insurances and bonds.

### **Hempstead UFSD – 2024 Bond Phase 2**

- Prime contractors submitted SOV's for approval.
- Prime contractors started submitting insurances and bonds.



## Section III - Work Planned June 2026

### **Hempstead UFSD – IAQ at Various Schools**

- **Eldor:**
  - Receive Paterson ES switchgear.
  - Work on switching over from exiting switchgear to new.

### **Hempstead UFSD – 2022 Bond Phase 3**

- **J Cole:**
  - Prep for summer work
- **IPS:**
  - Prep for summer work.
- **RMS:**
  - Prep for summer work.
- **Eldor:**
  - Start HS parking lot light pole replacements.
  - Continue roughing in all schools.

### **Hempstead UFSD – Boiler replacement at Prospect Elementary School**

- **KG Mechanical**
  - Start demo of boilers.
  - Start new pad work.

### **Hempstead UFSD – 2022 Bond Phase 4**

- Continue submitting insurances and bonds.
- Start submitting necessary submittals.
- Prep for start of work.

### **Hempstead UFSD – 2024 Bond Phase 2**

- Continue submitting insurances and bonds.
- Start submitting necessary submittals.
- Prep for start of work.




## Section IV – Progress Photos



Hempstead IAQ – Chilled water piping



## Section IV – Progress Photos

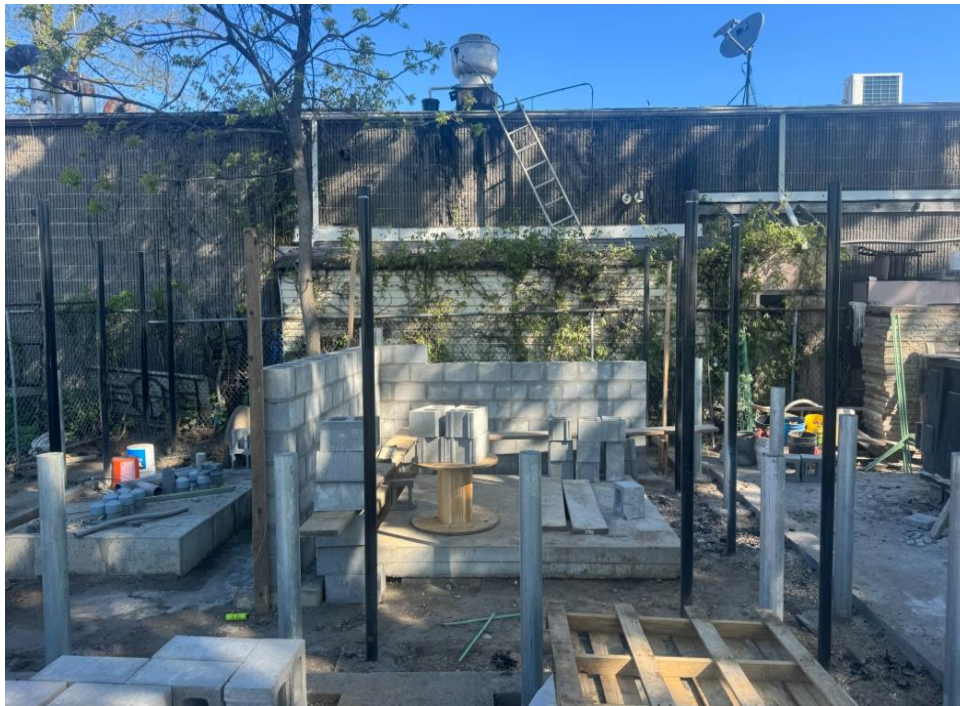


Hempstead IAQ – Switchgear pad/area



## Section V – Workforce Summary – Company/Hours

### May 2026

#### MANPOWER GRAPH

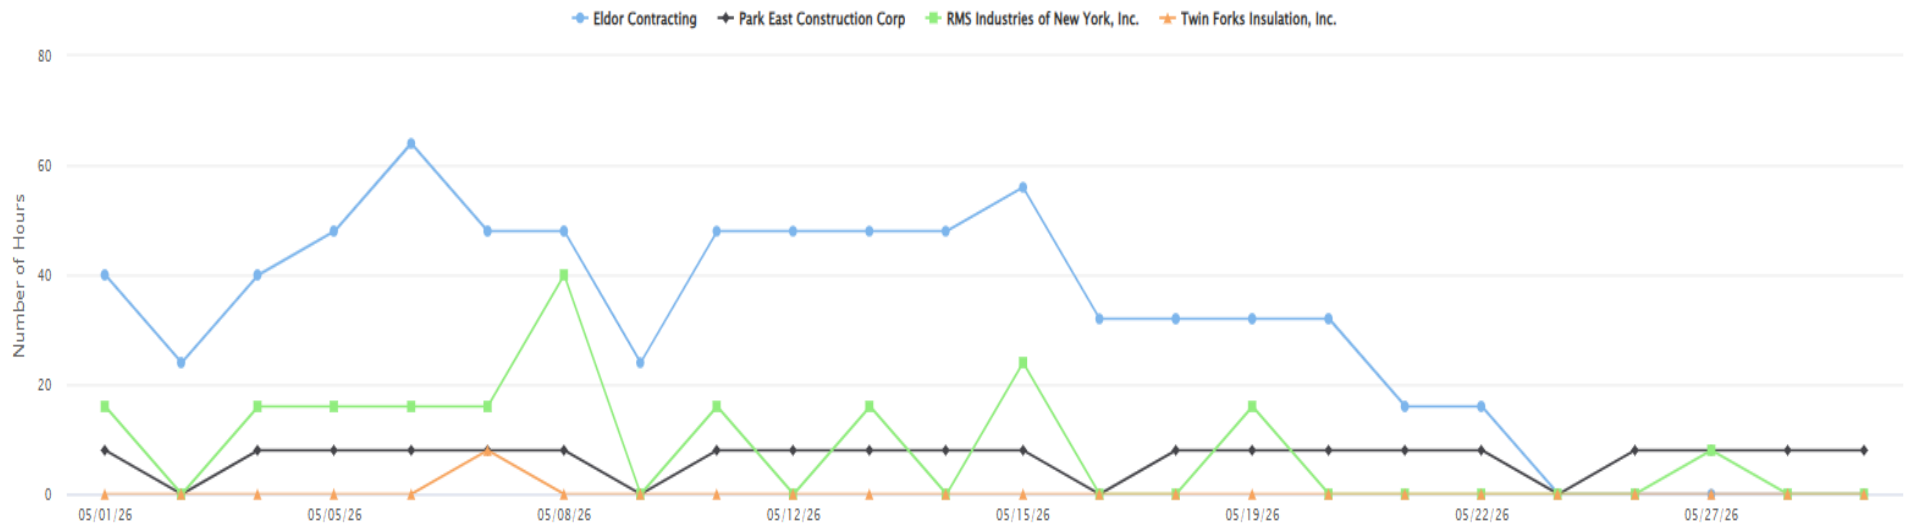


### Hempstead UFSD – IAQ at Various Schools



## Section V – Workforce Summary – Company/Hours

### May 2026

MANPOWER GRAPH

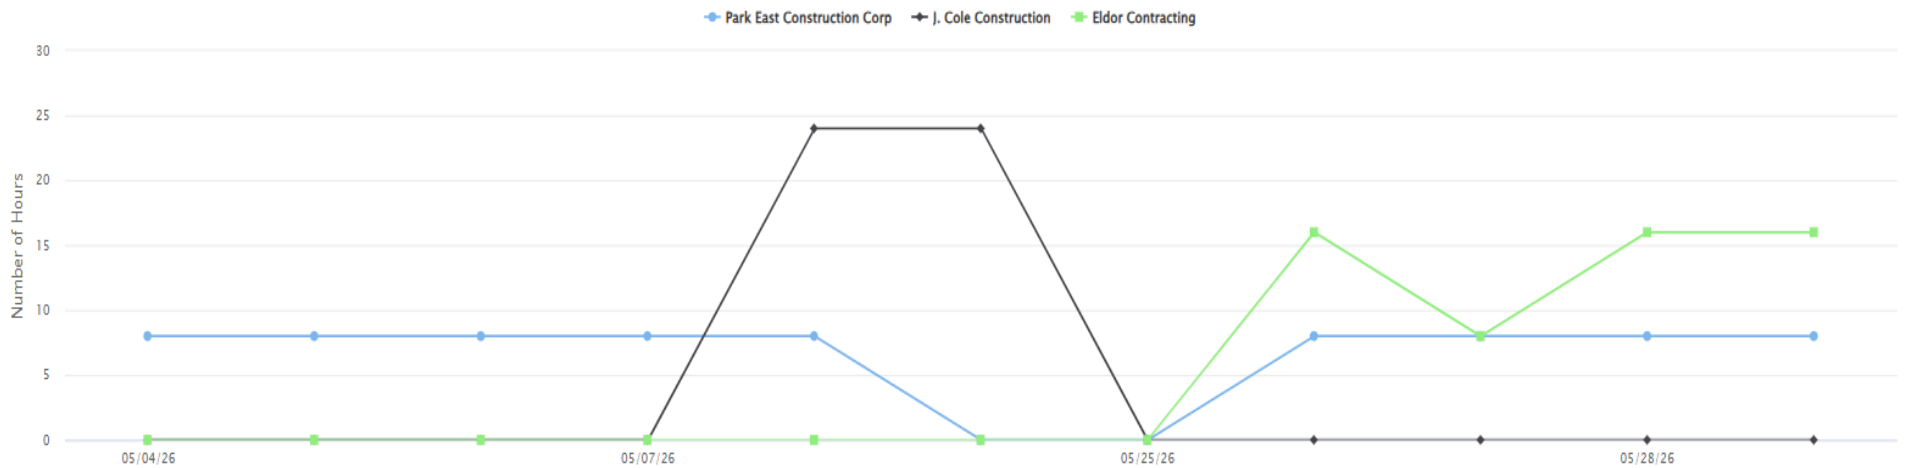

Hempstead UFSD – 2022 Bond Phase 3



Hempstead Union Free School District

May 2026

## End of Progress Report
