



Project Update Report

Report Date	September 24, 2026
Project Name/Number	Wynbrooke ES – Security Vestibule & HVAC System 37535
Facility Name	Wynbrooke ES
Area Superintendent	Dr. Michelle Jones
Principal	Mrs. Devetra Ushery
School Contact	Mrs. Devetra Ushery
Project Manager	Shina Devon
Architect	CDH
Contractor	Centennial Contractors Enterprises, Inc.

Scope of Work

The scope of this project is the addition of a new Security Vestibule and new Gymnasium HVAC System at Wynbrooke Elementary School - 440 Wicksbury Way, Stone Mountain, Georgia 30087.

Scope will consist of the following, but not limited to:

- Installation of HVAC system servicing the gymnasium;
- MEP upgrades;
- Security Vestibule and Administration Relocation/Renovation;
- Minor interior improvements;
- Replacement of ceiling tiles.

Project Construction Budget: \$687,605.00

Project Schedule Milestones

- Construction Substantial Completion – 07.24.26
- Punch List Completed – 08.07.26

Current Project Status:

- Closeout document submission ongoing.
- Additional flooring work at Security Vestibule planned for Fall Break 2026.

4-Week Look Ahead


- Completion of closeout documentation.
- Additional flooring work at Security Vestibule planned for October during Fall Break.

End of Project Update Report

Photographs




Spiral Duct Painted and HVAC System Start-up Complete

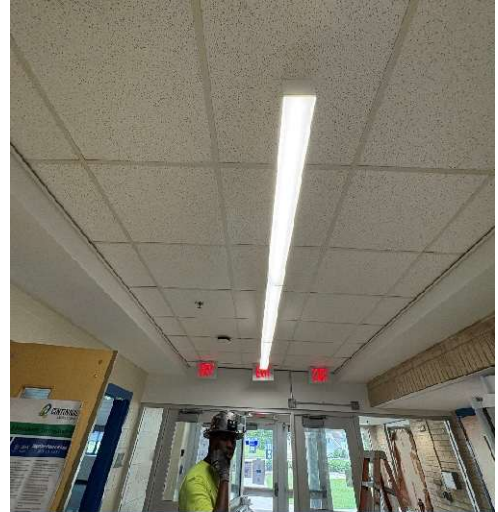

New Light in Security Vestibule Installed



New Storefront for Security Vestibule Installed

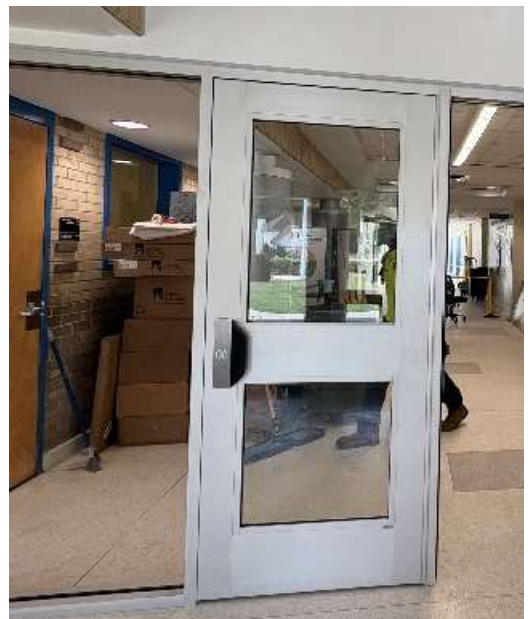

New Storefront for Security Vestibule Installed

