

# MONTHLY REFFERENDUM REPORT DETAILED - as of July 31, 2021




**Battery Creek High School**  
**1 Blue Dolphin Dr, Beaufort 29906**  
 Cluster: Battery Creek      Principal: Chad Cox

|                          |              |                      |              |
|--------------------------|--------------|----------------------|--------------|
| Original Appropriations: | \$56,075,773 | Encumbered and Paid: | \$52,727,597 |
| Transfers/Adjustments:   | \$0          | Paid to Date:        | \$1,540,326  |
| Revised Budget:          | \$56,075,773 | Available Budget:    | \$3,348,176  |

## 2019 Bond Referendum Renovation

Project ID: 51925392-1

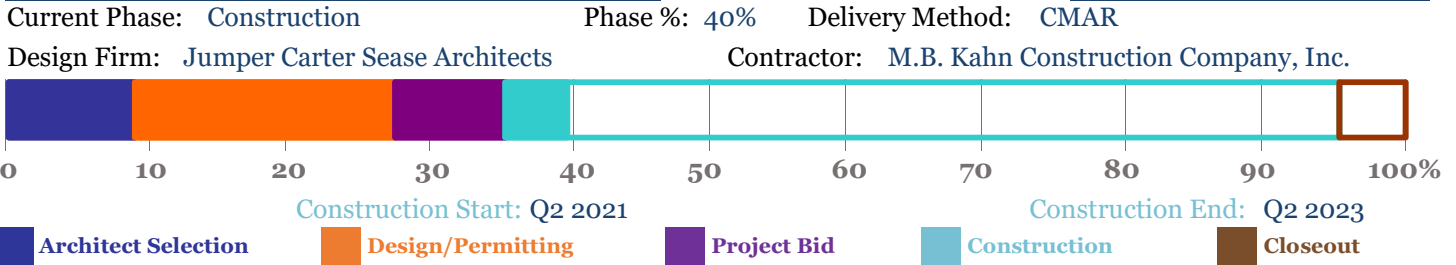

- Scope: 2019 Bond Referendum**
- Athletics
  - CATE expansion
  - Renovations
  - Safety/Security
  - Technology /Infrastructure

**Project Details:** Scope to include renovation work of the classroom areas, athletic improvements to the track/turf field and concession, safety/security upgrades of bullet resistant glass and security system, and renovations of existing spaces for CATE program expansion.

**Monthly Progress:** Construction in progress. Demolition is complete in various areas. HVAC installation is in progress in D Hall. Electrical work has commenced in D and H Halls and locker rooms. Restroom plumbing is in progress.
