




2023 BOND

# MAJOR PROJECTS UPDATE

NOVEMBER 2023



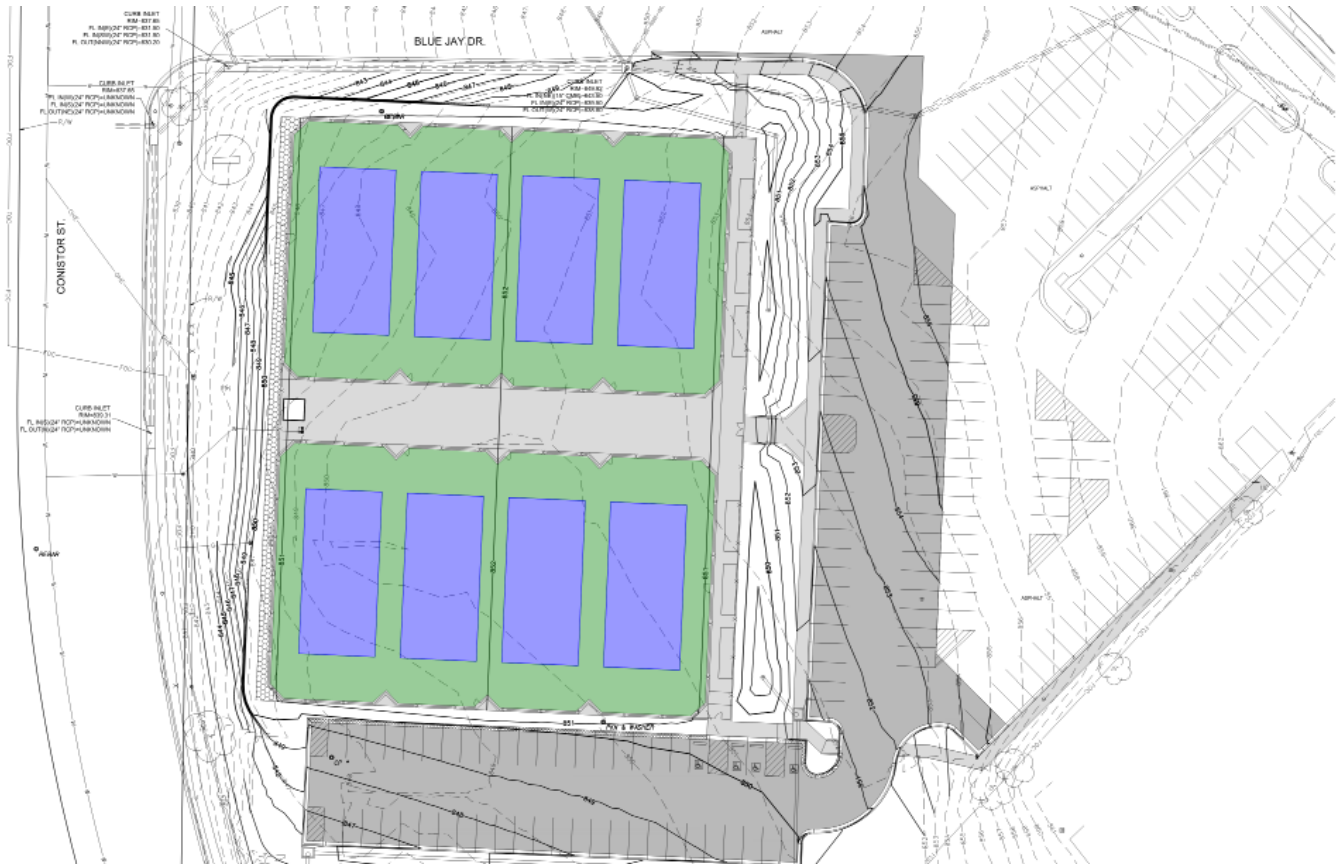

## Liberty High School Tennis

- (8) Competition Tennis Courts
- Post-Tensioned Concrete slab with DecoTurf brand acrylic surfacing
- 10'-0" tall perimeter fence with windscreen
- Retaining wall and asphalt parking lot improvements

**Construction Start:** Spring 2023

**Construction Complete:** Fall 2023

## PROJECT STATUS

- Courts Substantially Complete
- Turned Over 10/31
- Final Punch List Items Being Completed

## UPCOMING

Project Completion October 2023




North Courts Looking West



North Courts Looking Southwest



East Concourse Looking South

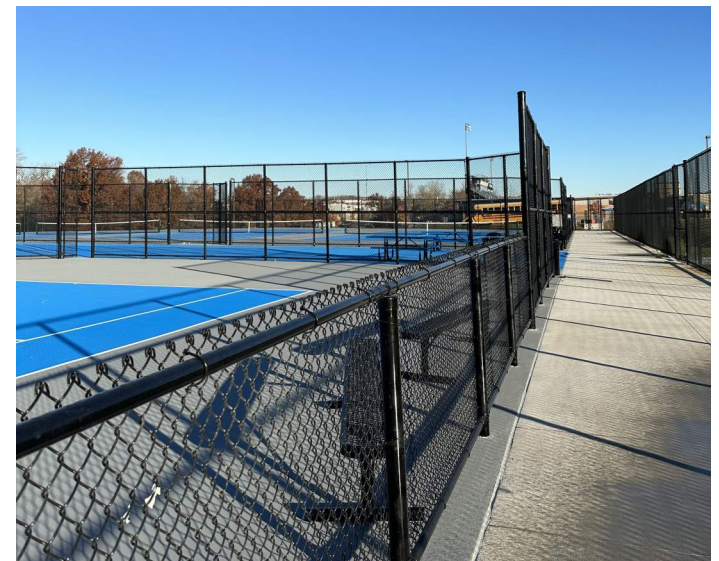

East Concourse Looking North


# WEEKLY PROGRESS REPORT



South Courts Looking West



Center Spectator Concourse Looking West

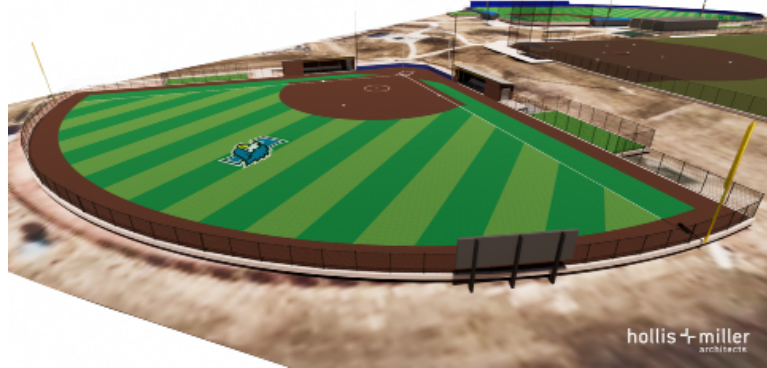

## Liberty High School Baseball/Softball Complex

### Baseball Field

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Pitching and Batting Practice areas

### Softball Field

- New Dugouts
- Reduced Field Dimensions to 210' outfield, 25' Foul Territory, Softball
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

### Multi-purpose Field

- Revised grading, perimeter fencing and infield improvements

**Construction Start:** Fall 2023

**Construction Complete:** Summer 2024

## PROJECT STATUS

- LHS
- Baseball Backstop Footings Complete
  - Baseball Champion Wall Footings Complete
  - Baseball Fence Post & Perimeter Curb Complete
  - Aux Field Grading Ongoing
  - Aux MEP Underground Ongoing
  - Softball Field Demo & Grading Ongoing

## UPCOMING

- LHS -
- Baseball Field Drainage / Rock
  - Baseball Turf Subgrade
  - Baseball Backstop Paving
  - Aux Finish Grading
  - Aux Fence Post & Perimeter Curb
  - Aux Irrigation Install
  - Softball Finish Grading
  - Softball MEP Underground
  - Softball Dugout Footings

Project Completion:  
Baseball March 2024/Softball May 2024



LHS - Baseball



LHS - Baseball



LHS - Baseball



LHS - Baseball

# WEEKLY PROGRESS REPORT



LHS - Multi-Purpose




LHS - Multi-Purpose



LHS - Multi-Purpose



LHS - Softball

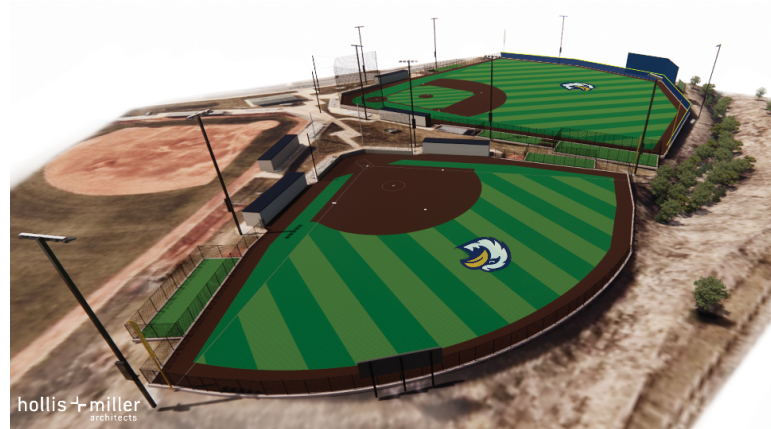

## Liberty North High School Baseball/Softball Complex

### Baseball Field

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Center field Batter's Eye
- Additional Bullpen Space
- ChampionWall PVC Athletic Fence System at Outfield

### Softball Field

- Increased Field Dimensions - 194'(L) - 200'(C) - 195'(R)
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

**Construction Start:** Fall 2023

**Construction Complete:** Summer 2024



**WEEKLY  
PROGRESS  
REPORT**

# Baseball Softball 11/13/2023

Liberty Public Schools



## PROJECT STATUS

- LNHS
- Baseball Backstop Footings Complete
  - Baseball Field Curb/ Fencing Complete
  - Baseball Turf Subgrade Ongoing
  - Baseball Champion Wall Footings Ongoing
- Softball Field Demo & Grading Complete

## UPCOMING

- LNHS-
- Baseball MEP Underground
  - Baseball Backstop Paving
  - Baseball Fence Fabric
- Softball Finish Grading
- Softball Field Drainage
- Softball Fence Post & Perimeter Curb


Project Completion  
Baseball March 2024/Softball May 2024



LNHS - Baseball



LNHS - Baseball

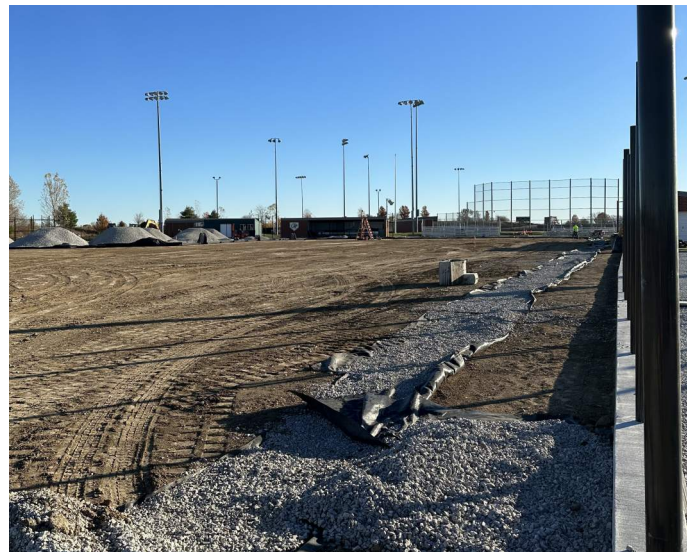

LNHS - Baseball



LNHS - Softball

# WEEKLY PROGRESS REPORT



LNHS - Softball



LNHS - Softball



LED Lighting upgrades are planned throughout the District and will be sequenced with other projects as possible between the fall of 2023 through fall of 2026.

## PROJECT STATUS

South Valley MS- Upgrades Complete

Discovery MS - Upgrades Complete


EPiC Elementary - Upgrades Complete

LNHS - Upgrades Ongoing


## UPCOMING

Energy Inspections All Four Schools  
Emergency LED Fixtures

Project Completion  
December 2023

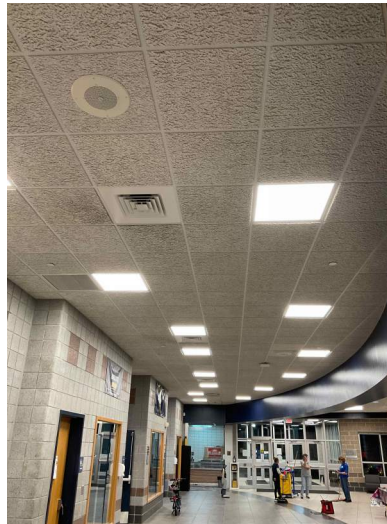


South Valley Middle School

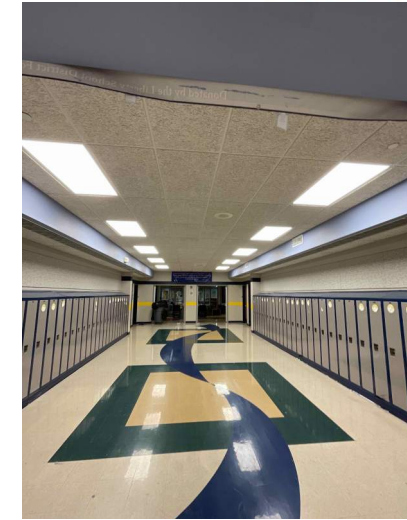

South Valley Middle School



Discovery Middle School

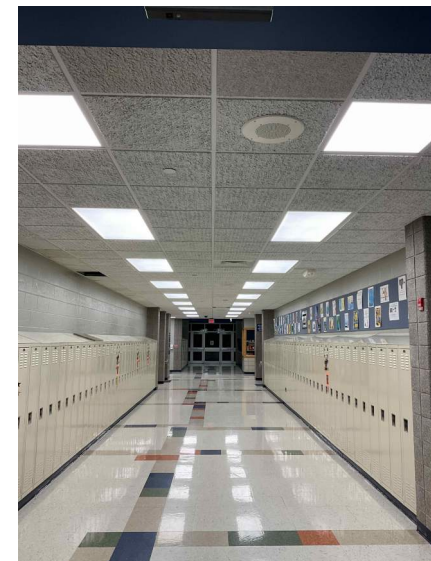

Discovery Middle School

# WEEKLY PROGRESS REPORT



Epic Elementary




Epic Elementary



Liberty North High School




Liberty North High School

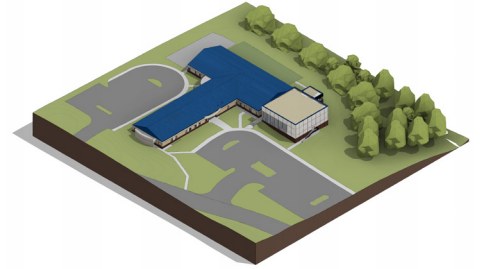


### EPiC Elementary Addition

- 8000 Square Foot Building Addition & Renovation
- New Gym & Performance Space
- New Art Classroom
- Renovated Restrooms, Mother’s Room and New Walk-in Cooler / Freezer
- Construction Start: Spring 2024
- Construction Complete: Summer 2025

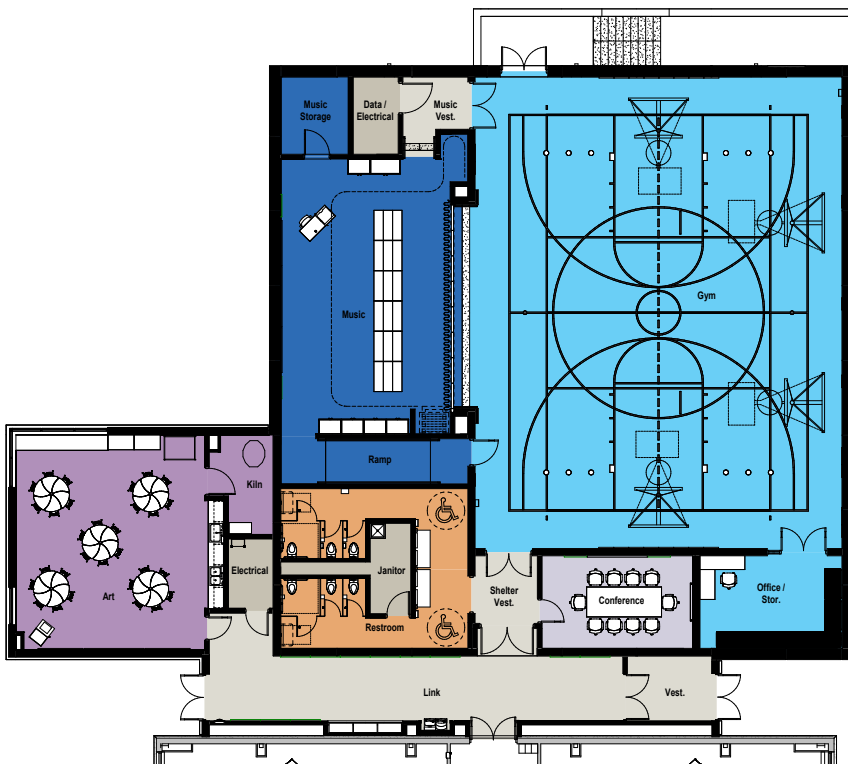

▲ Addition

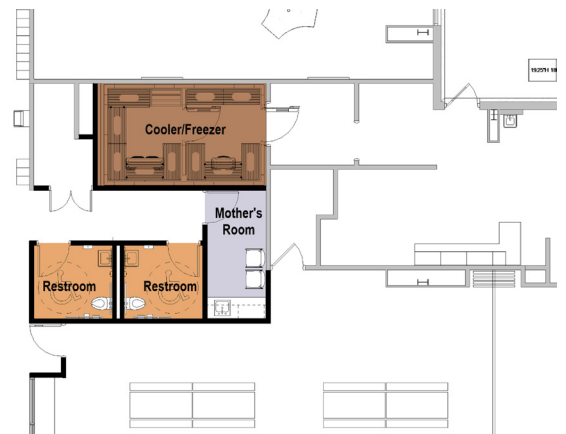



▲ Renovation Area



### Discovery Middle School

- 11,000 square foot addition
  - ICC 500 rated shelter
  - Additional PE space
- Raised performance stage
- Theatrical AV and lighting
- Increased audience capacity
  - Additional storage
- Projected Construction Schedule:  
Spring 2024–Summer 2025

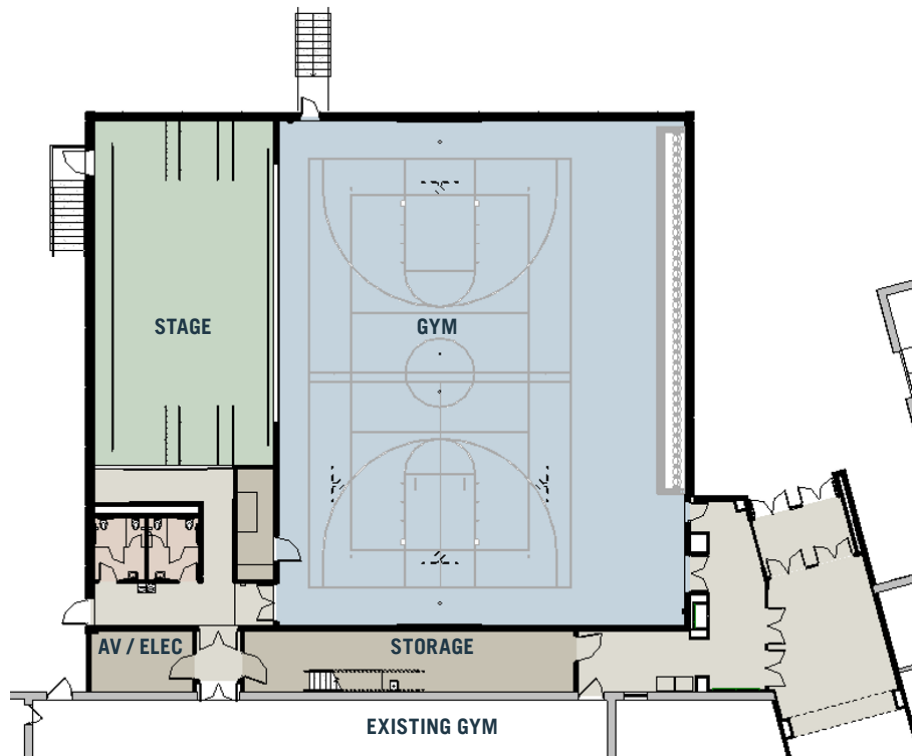

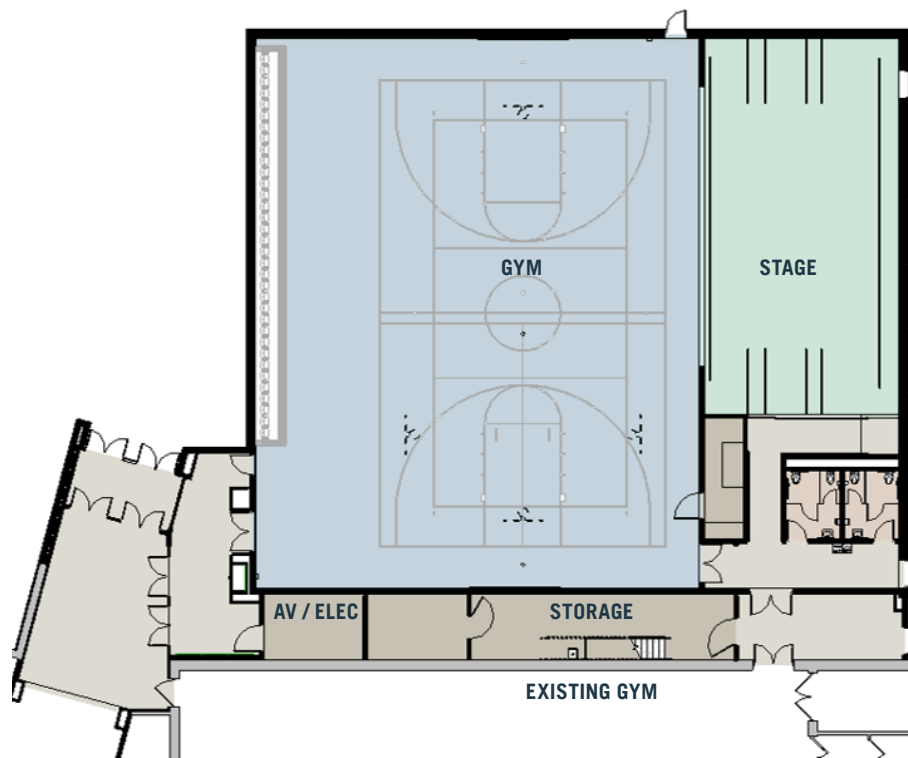

### South Valley Middle School

- 11,000 square foot addition
- ICC 500 rated shelter
- Additional PE space
- Raised performance stage
- Theatrical AV and lighting
- Increased audience capacity
- Additional storage
- Projected Construction Schedule: Spring 2024–Summer 2025





hollis + miller



hollis + miller



hollis + miller



hollis + miller

## Distribution Center

- 29,000 Square Foot New Building
- Storage Warehouse
- Dry Food Warehouse
- Large Storage Freezer
- New Office Space
- New Copy Center
- Additional Parking
- Projected Construction Schedule: Fall 2023–Spring 2025




Fine Arts  
 Kid's Zone  
 Technology  
 Shared Amenities  
 Building Systems  
 Future Phase



### District Technology Center

- Renovated workspace for District’s Technology, Fine Arts, and Kid’s Zone departments
- Shell space for future growth
- Minor exterior patch + repair improvements
- Projected Construction Schedule: Fall 2023 - Summer 2024

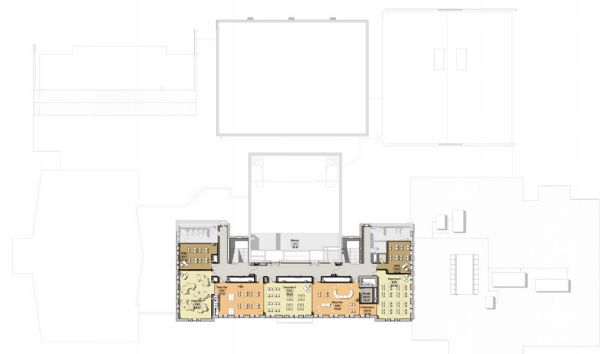

LEVEL 3



LEVEL 2



LEVEL 1



LEVEL 0

### Heritage Middle School

- 39,000 square feet academic renovation
- Grade level neighborhoods with flex collaboration spaces
  - Integrated SPED resources
  - Renovated cafeteria & scramble
    - Restroom renovations
- Exterior masonry repair & window replacement
  - Elevator replacement
- Projected Construction Schedule: Spring 2024–Fall 2025
