




2023 BOND

MAJOR PROJECTS UPDATE

OCTOBER 2023



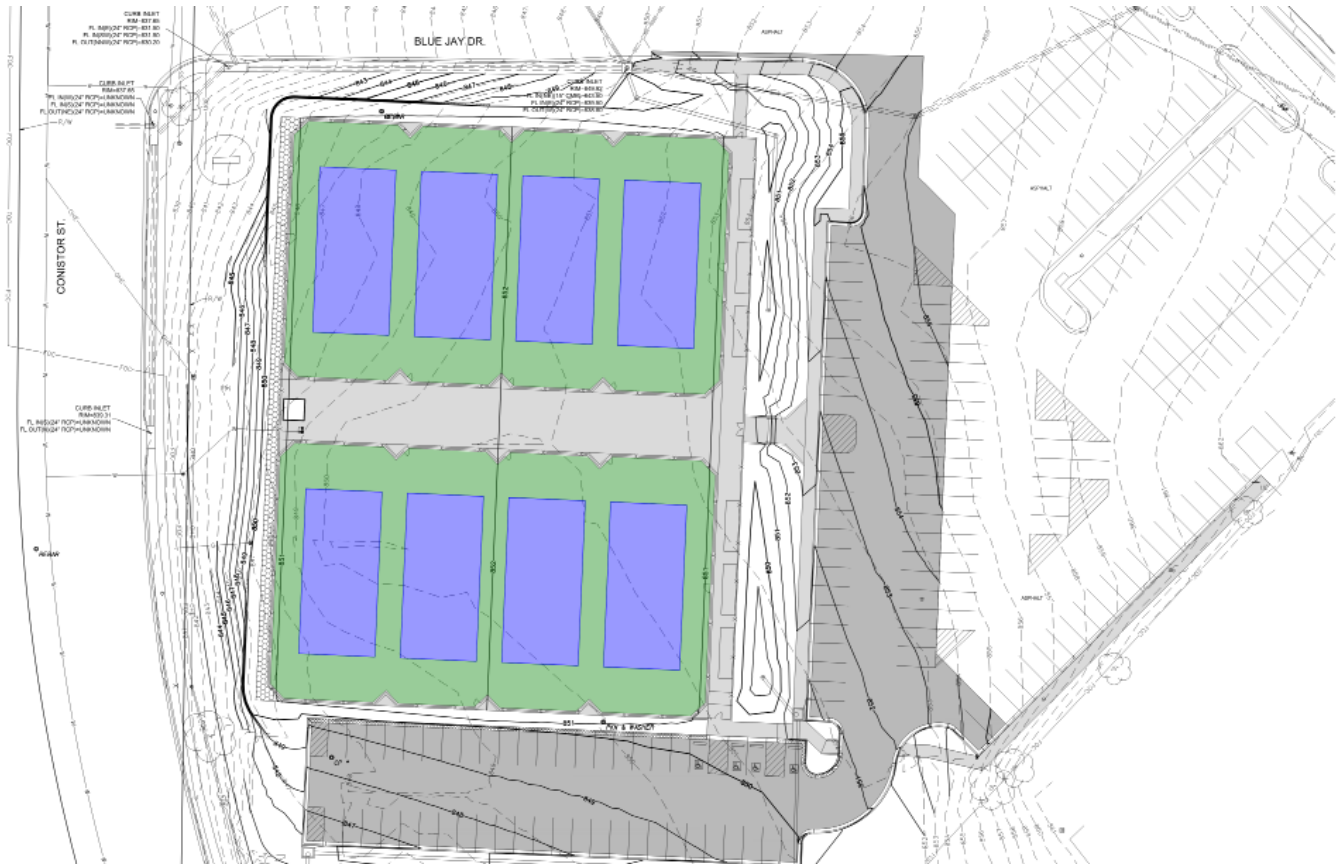

Liberty High School Tennis

- (8) Competition Tennis Courts
- Post-Tensioned Concrete slab with DecoTurf brand acrylic surfacing
- 10'-0" tall perimeter fence with windscreen
- Retaining wall and asphalt parking lot improvements

Construction Start: Spring 2023

Construction Complete: Fall 2023


PROJECT STATUS

- Courts Prepped for Surfacing
- Court Fencing Completed
- Flatwork & Paving
- Black Dirt Completed

UPCOMING

- Sod
- Court and Center Concourse Surfacing
- Asphalt
- Windscreen & Sports Equipment

Project Completion October 2023

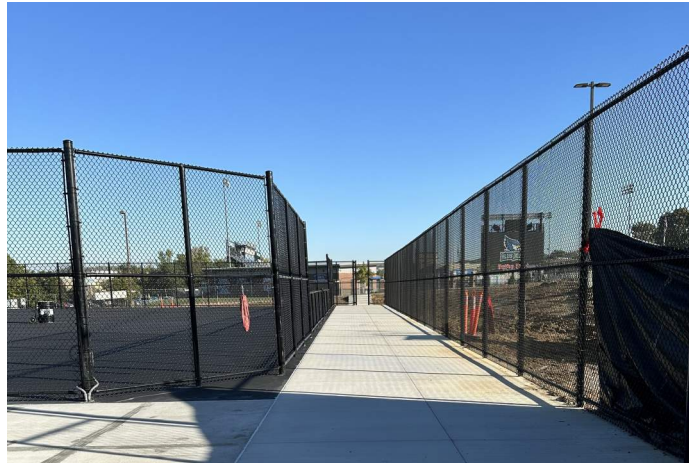

East Concourse Looking North



East Concourse Looking South




South Courts Looking West



North Courts Looking Northwest


WEEKLY PROGRESS REPORT

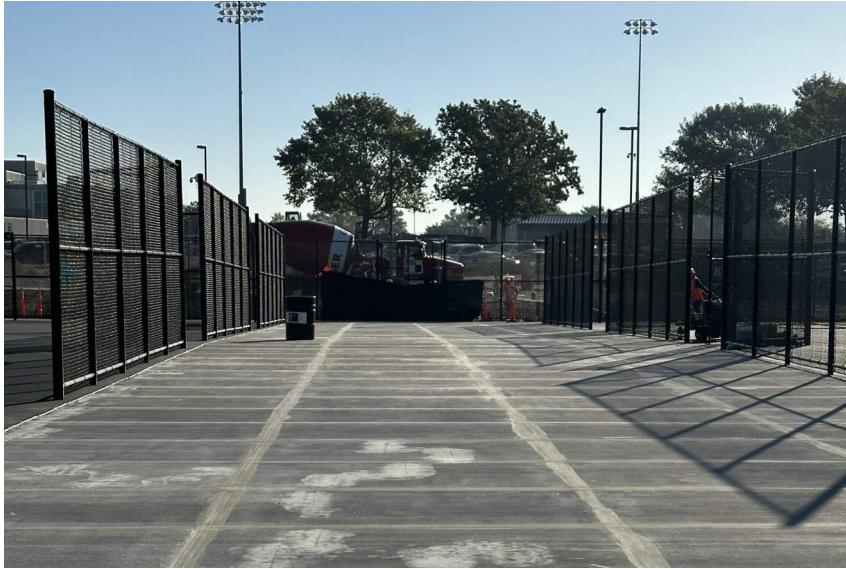

Center Concourse Looking East



Center Spectator Area Surfacing Prep - Looking West

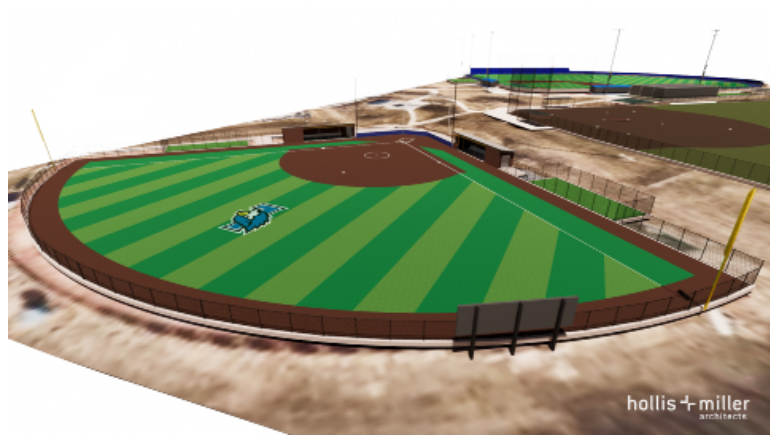

Liberty High School Baseball/Softball Complex

Baseball Field

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Pitching and Batting Practice areas

Softball Field


- New Dugouts
- Reduced Field Dimensions to 210' outfield, 25' Foul Territory, Softball
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

Multi-purpose Field

- Revised grading, perimeter fencing and infield improvements

Construction Start: Fall 2023

Construction Complete: Summer 2024

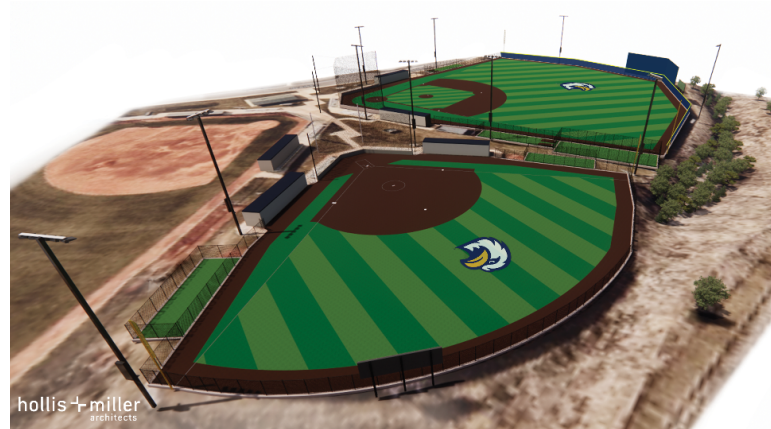

Liberty North High School Baseball/Softball Complex

Baseball Field

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Center field Batter's Eye
- Additional Bullpen Space
- ChampionWall PVC Athletic Fence System at Outfield

Softball Field

- Increased Field Dimensions - 194'(L) - 200'(C) - 195'(R)
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

Construction Start: Fall 2023

Construction Complete: Summer 2024

PROJECT STATUS

LHS Baseball -
- Site Demo Completed
- Site Grading Completed

LNHS Baseball -
- Site Grading Completed
- Forming Perimeter Curbs - 1st & 3rd
Baselines
- Field Drainage

UPCOMING

LHS Baseball -
- Backstop Footings and Sleeves
- Champion Wall Footings
- Field Curb / Fencing
- Field Drainage / Rock
LNHS Baseball -
- Field Drainage
- Perimeter Curbs
- Bullpen Curb

Project Completion
Baseball March 2024
Softball May 2024



LHS - Baseball



LHS - Baseball



LHS - Baseball



LNHS - Baseball

WEEKLY PROGRESS REPORT



LNHS - Baseball




LNHS - Baseball




EPiC Elementary Addition

- 8000 Square Foot Building Addition & Renovation
- New Gym & Performance Space
- New Art Classroom
- Renovated Restrooms, Mother’s Room and New Walk-in Cooler / Freezer
- Construction Start: Spring 2024
- Construction Complete: Summer 2025

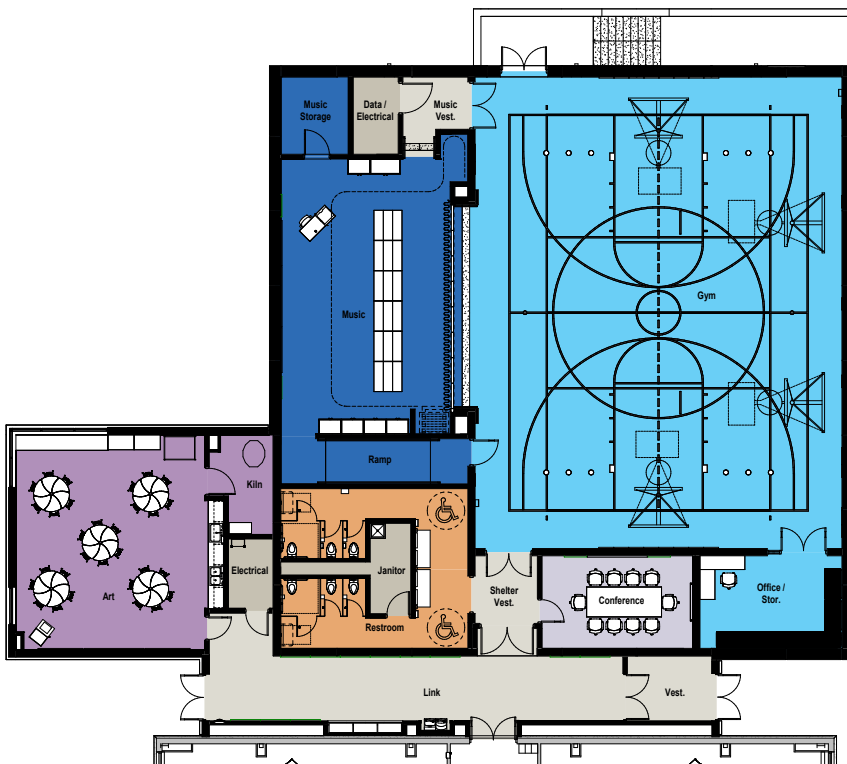

▲ Addition

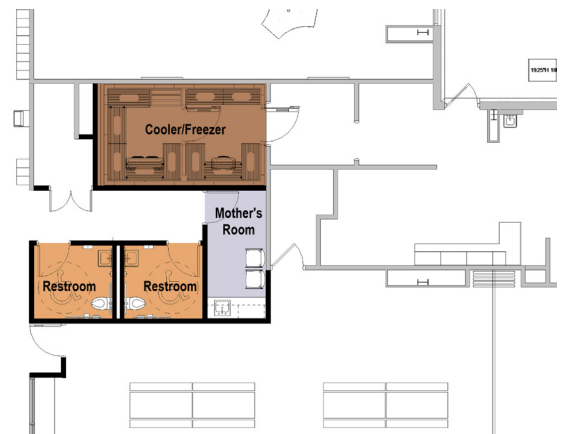



▲ Renovation Area



Discovery Middle School

- 11,000 square foot addition
 - ICC 500 rated shelter
 - Additional PE space
- Raised performance stage
- Theatrical AV and lighting
- Increased audience capacity
 - Additional storage
- Projected Construction Schedule:
Spring 2024–Summer 2025

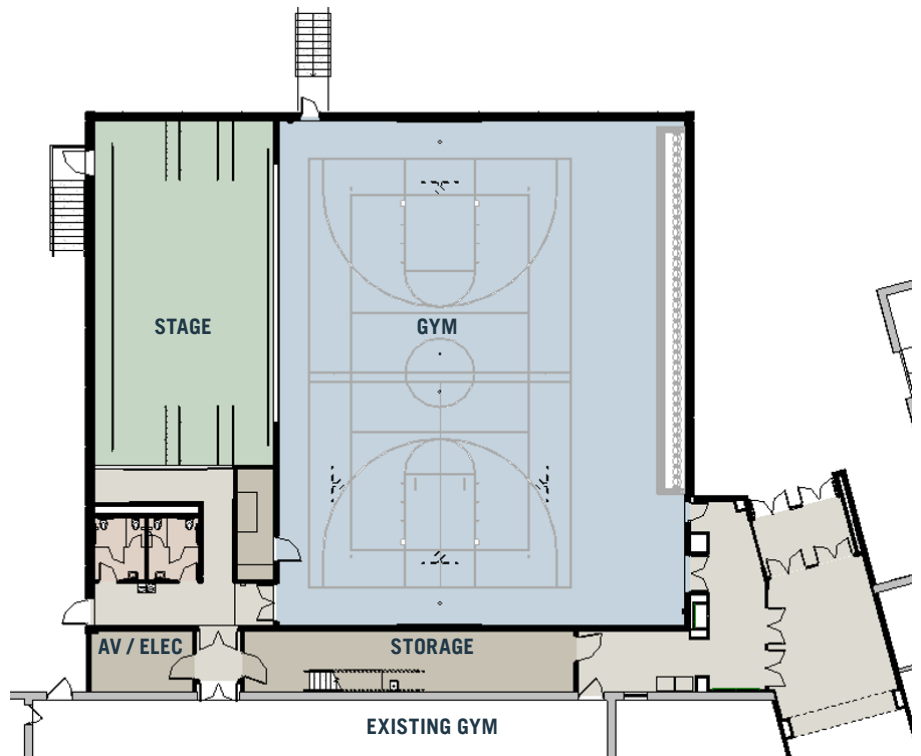

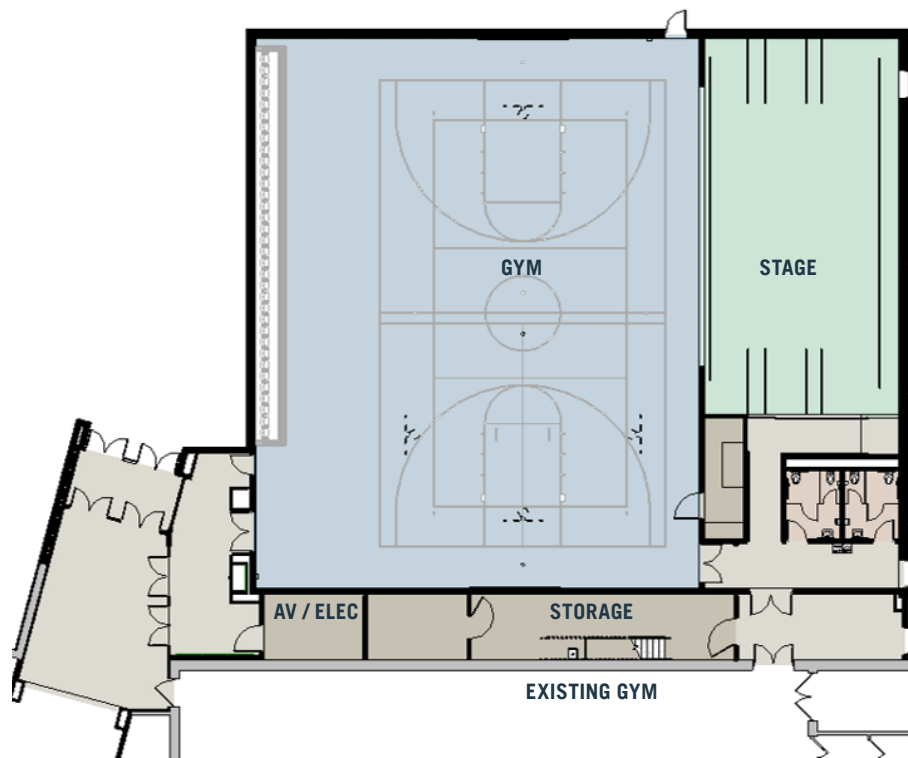

South Valley Middle School

- 11,000 square foot addition
- ICC 500 rated shelter
- Additional PE space
- Raised performance stage
- Theatrical AV and lighting
- Increased audience capacity
- Additional storage
- Projected Construction Schedule: Spring 2024–Summer 2025



hollis + miller



hollis + miller



hollis + miller




hollis + miller

Distribution Center

- 29,000 Square Foot New Building
- Storage Warehouse
- Dry Food Warehouse
- Large Storage Freezer
- New Office Space
- New Copy Center
- Additional Parking
- Projected Construction Schedule:
Fall 2023–Spring 2025



Fine Arts
 Kid's Zone
 Technology
 Shared Amenities
 Building Systems
 Future Phase

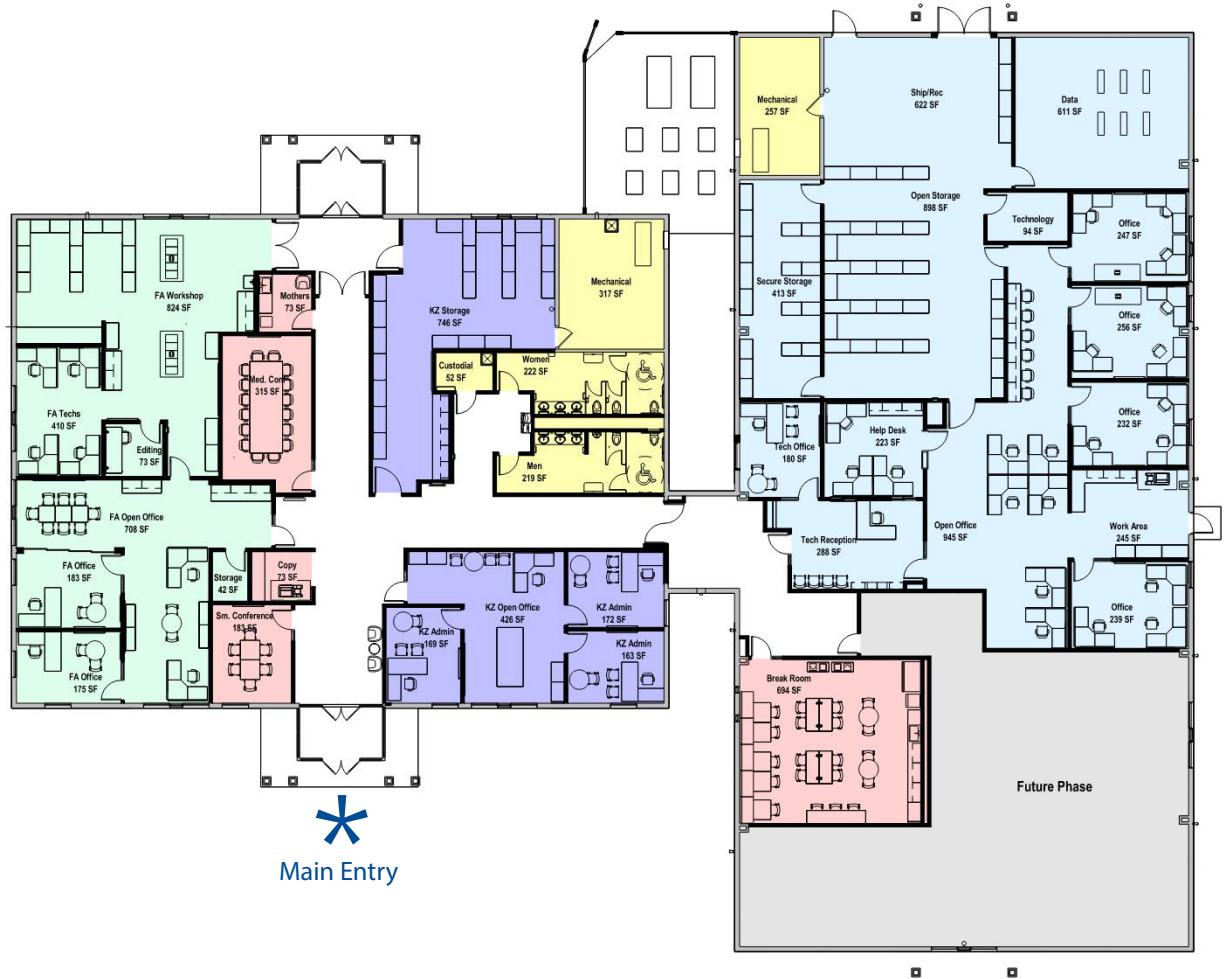

District Technology Center

- Renovated workspace for District’s Technology, Fine Arts, and Kid’s Zone departments
- Shell space for future growth
- Minor exterior patch + repair improvements
- Projected Construction Schedule: Fall 2023 - Summer 2024
