

AUGUST 14, 2024



# UPDATE

## NORTH SPRINGS HIGH SCHOOL


**NOEL MALOOF**  
CHIEF OPERATIONS OFFICER  
CAPITAL PROGRAMS TEAM

*Fulton*  
County Schools  
Where Students Come First

# North Springs High School Replacement

## Current Status

- Update
- Design Status
- Site Work Logistics  
Summer 2024
- Next Milestone

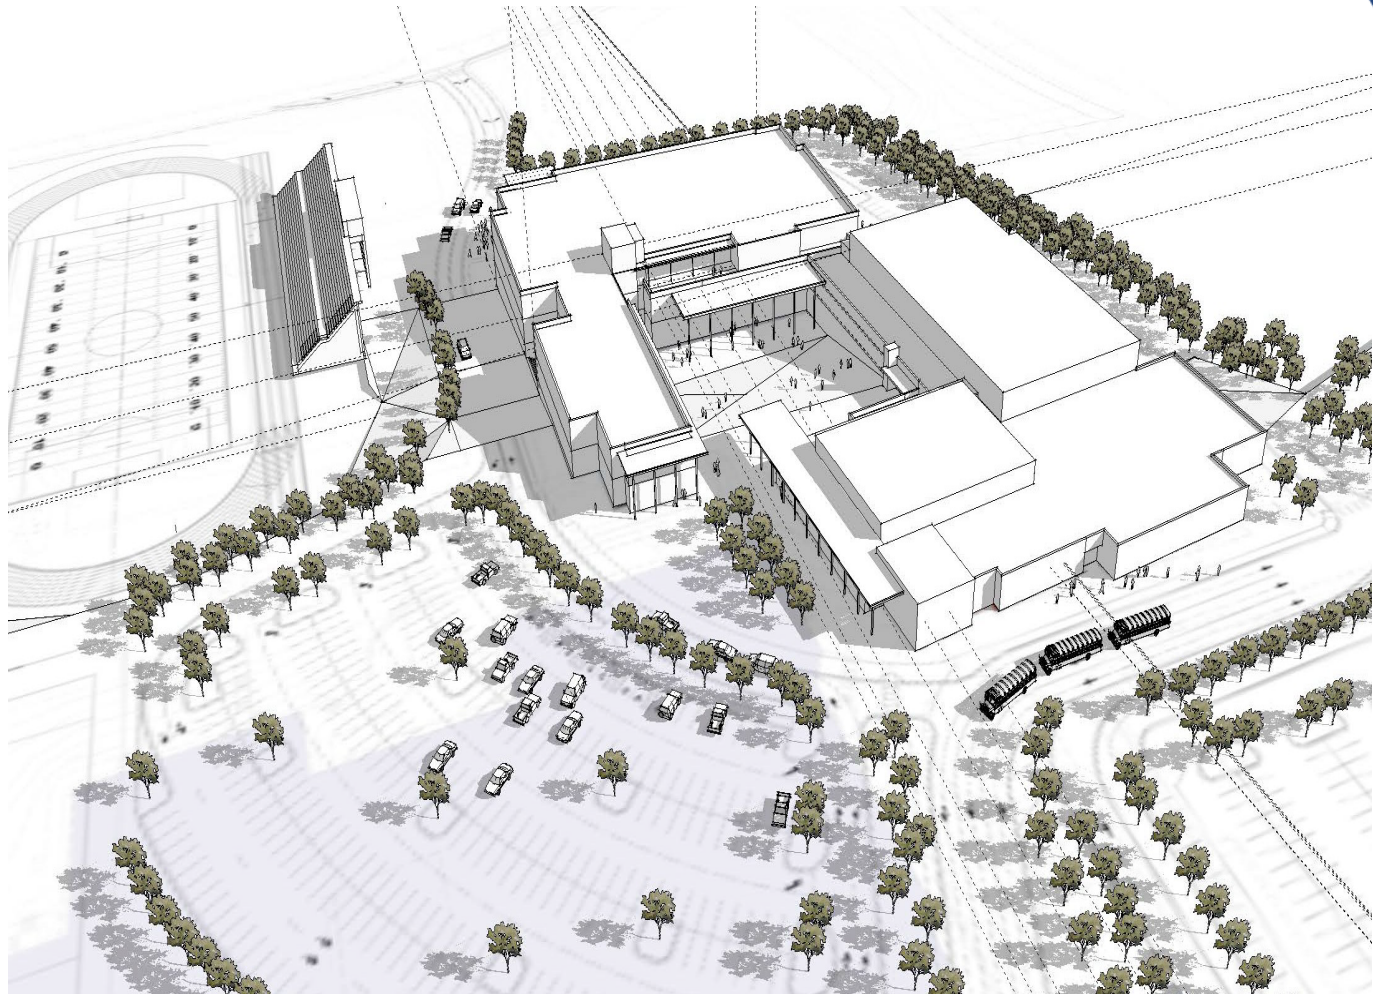



# North Springs High School Replacement

## Summer 2024

- Stadium and other site buildings were demolished
- New bus loop completed
- Electrical and gas supply to existing building re-routed
- Trowbridge construction entrance in place
- Contractor is on schedule
- Groundbreaking scheduled for August 27<sup>th</sup> @ 10am







# North Springs High School Replacement

## Progress

*Fulton*  
County Schools  
Where Students Come First

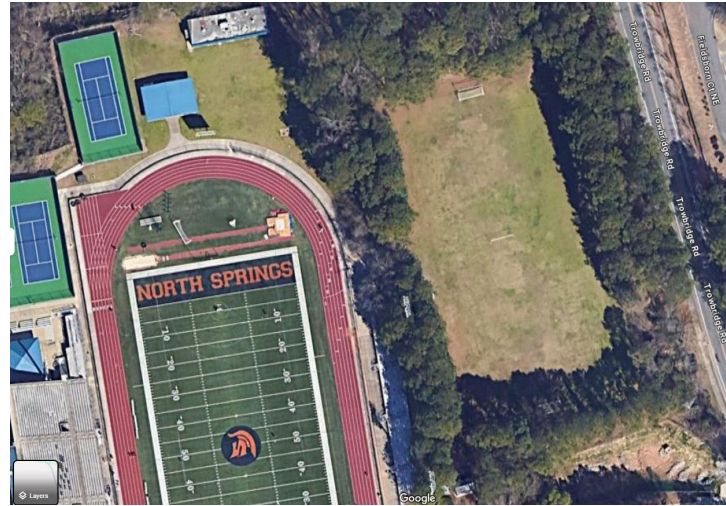




# North Springs High School Replacement



Rendering:  
Northwest  
aerial view



# North Springs High School Replacement

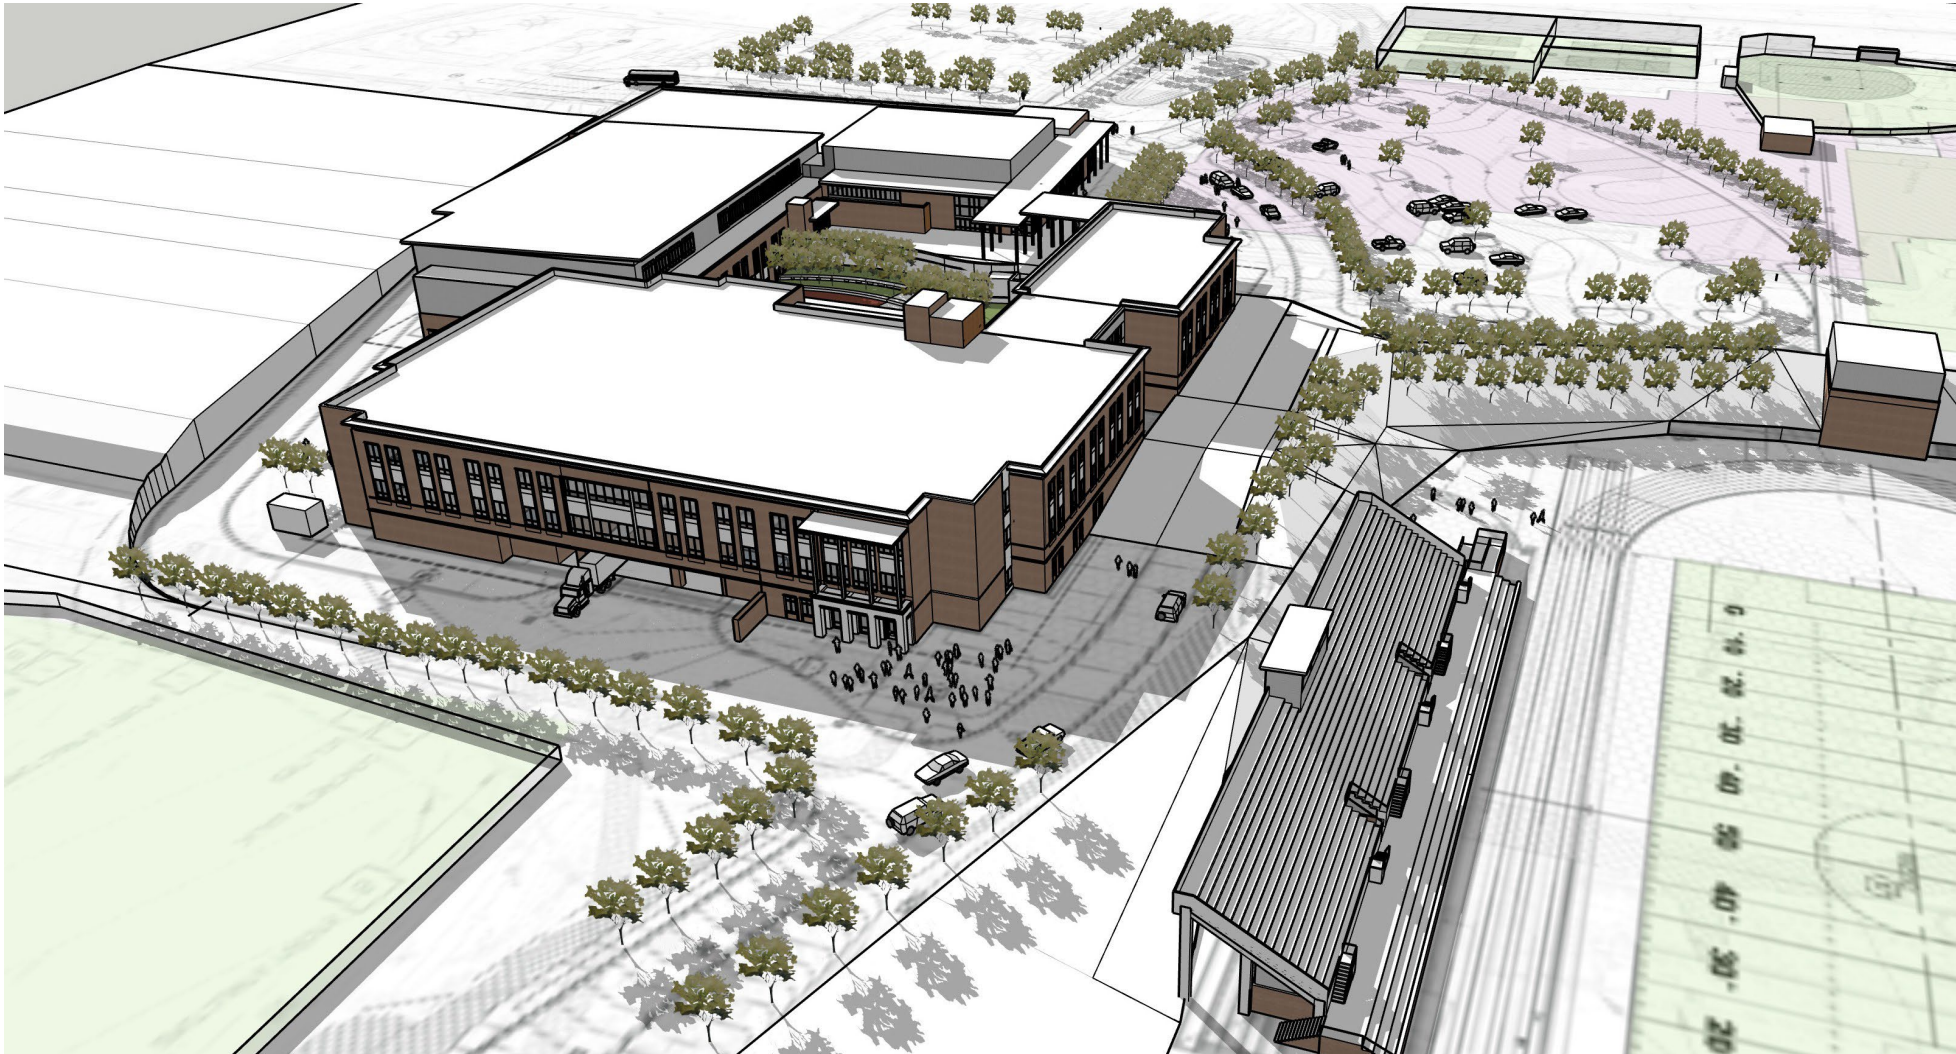

Rendering:  
Northeast  
aerial view

# North Springs High School Replacement



## Additional Scope Discussion

- Athletic Facilities enhanced by boosters



# North Springs High School Replacement



## Milestones

- New North Springs High School-1500 FTE
- Construction documents are underway and will be reviewed by BOE later this month
- **Site Package began construction June 1st. and is on schedule.**
- Building package will be complete before the end of the year
