

NOVEMBER 06, 2024



UPDATE

NORTH SPRINGS HIGH SCHOOL


NOEL MALOOF
CHIEF OPERATIONS OFFICER
CAPITAL PROGRAMS TEAM

Fulton
County Schools
Where Students Come First

North Springs High School Replacement

Current Status

- Update
- Design Status
- Site Work Status
- Next Milestone

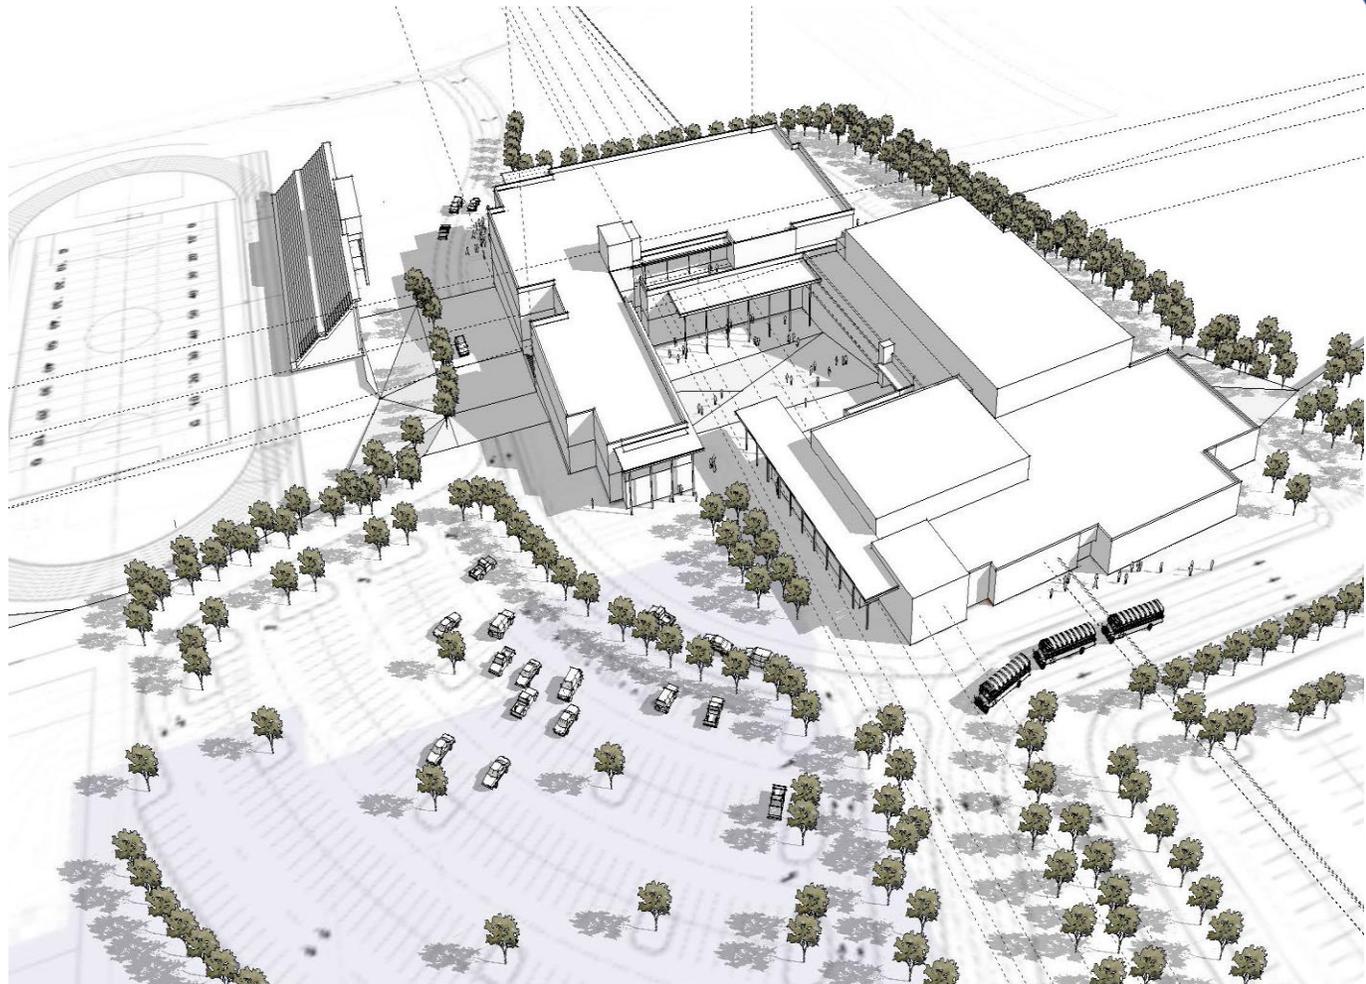

North Springs High School Replacement




Rendering:
Northwest
aerial view

North Springs High School Replacement




Rendering:
Northeast
aerial view

North Springs High School Replacement

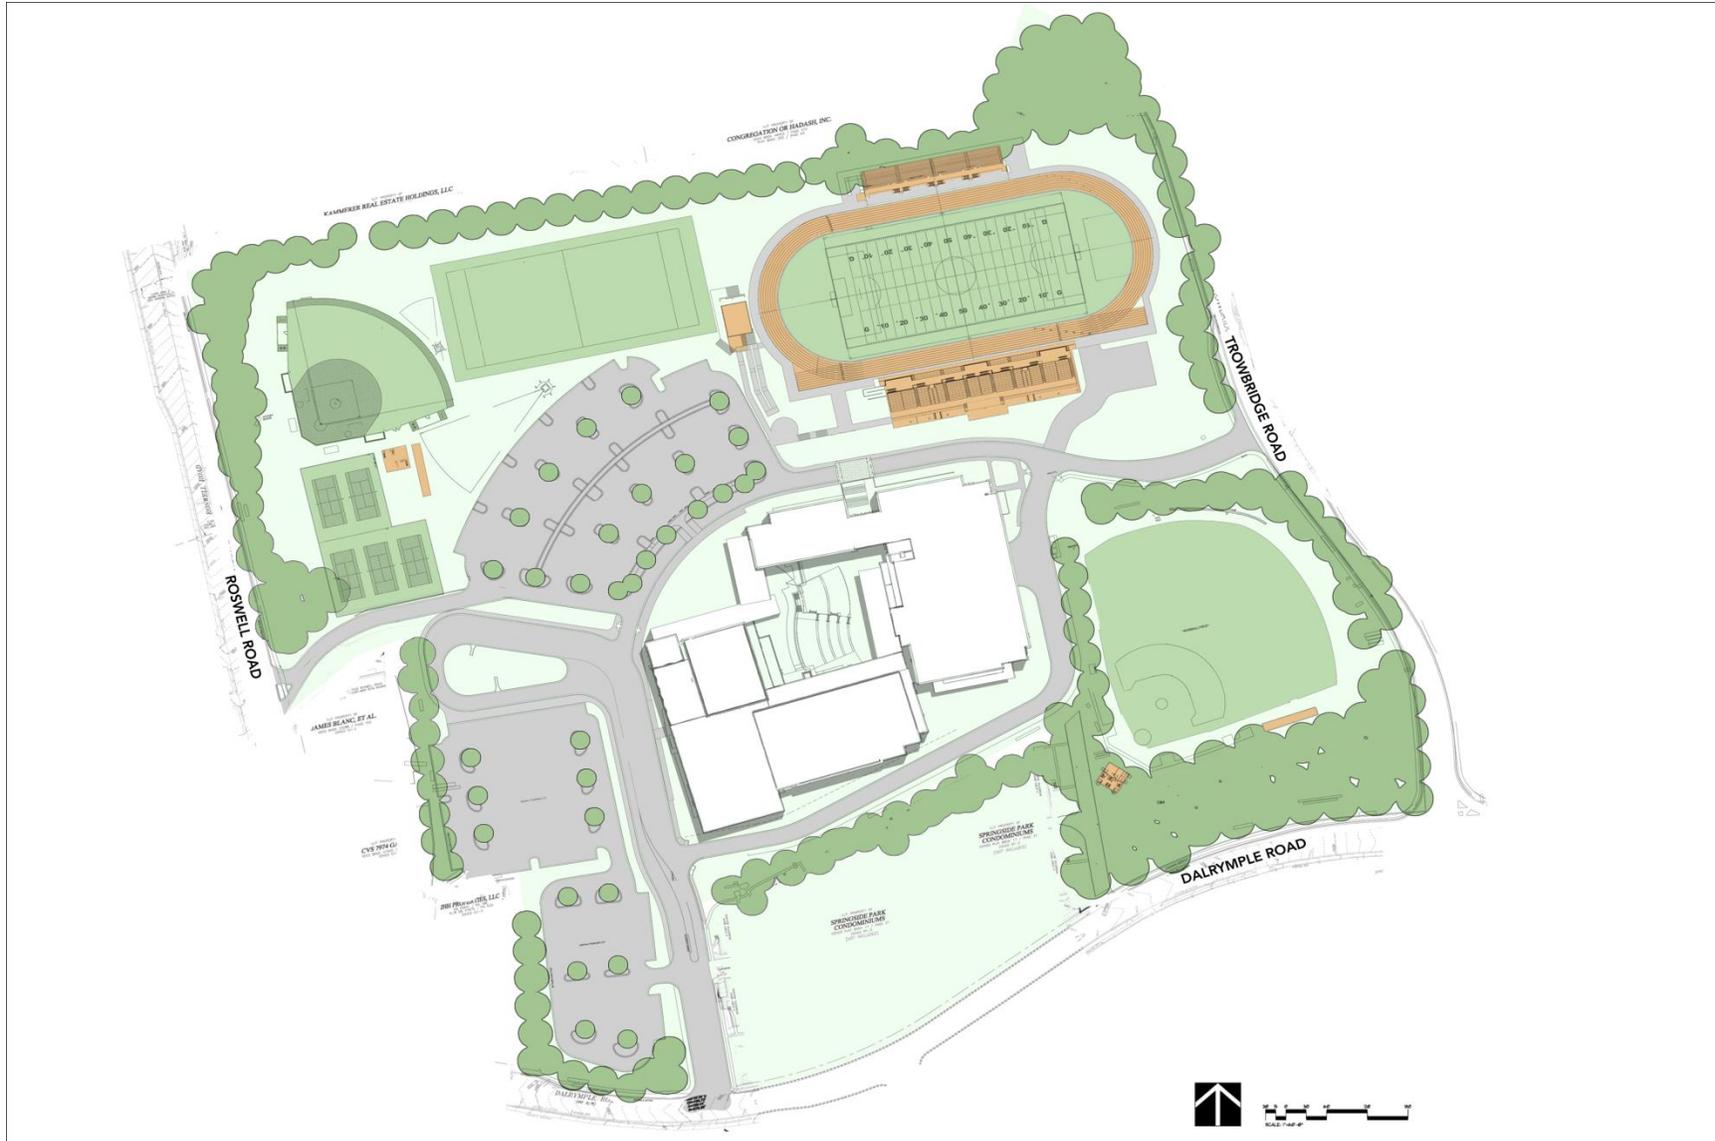

Future Site Plan

North Springs High School Replacement

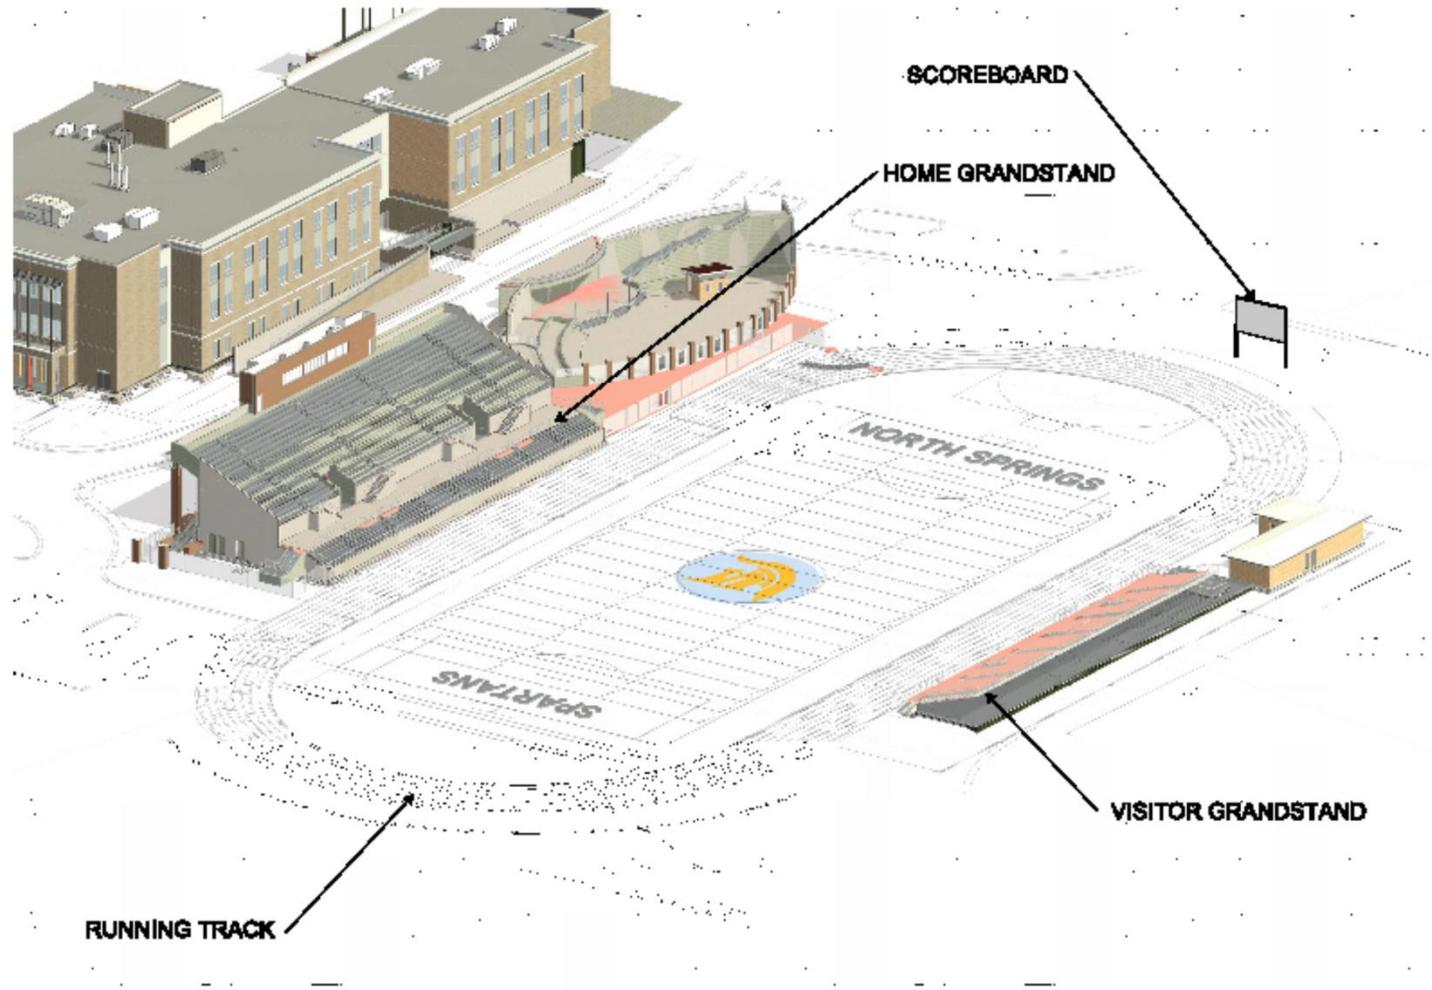

North Springs High School Replacement




Auditorium



Auditorium Lobby

North Springs High School Replacement

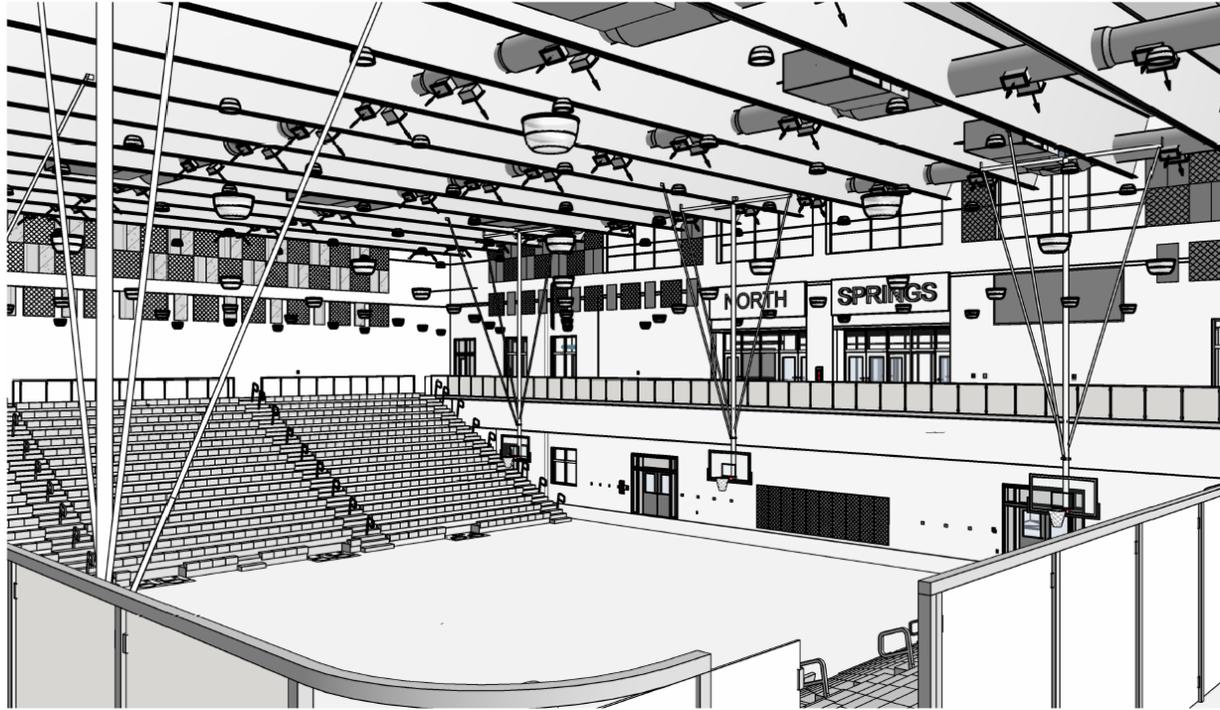

Gymnasium



Gym Lobby

North Springs High School Replacement



Site Work (Phase 1 Status)


- Underground Detention Storage Installed
- Retaining walls being installed
- Site grading ongoing
- Underground utilities (storm/Sanitary/Water) ongoing
- Work is progressing well

North Springs High School Replacement

Site Work in Progress




North Springs High School Replacement

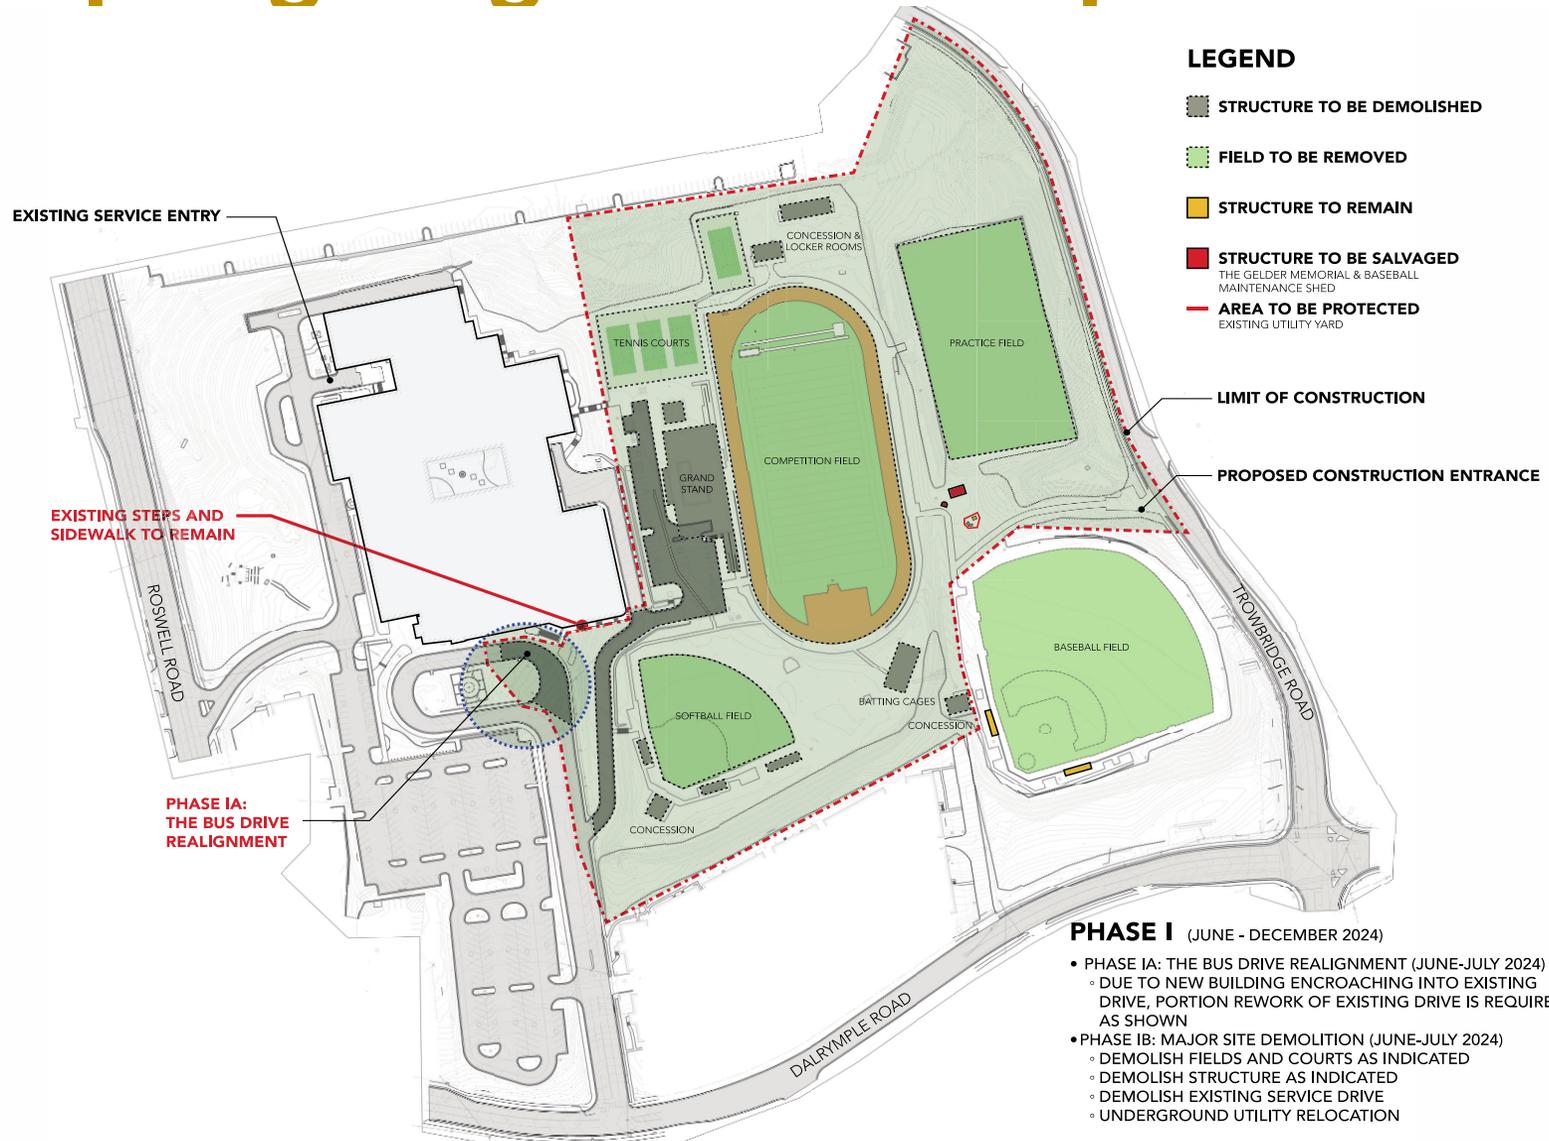


Demolition Phase 1 Plan

North Springs High School Replacement

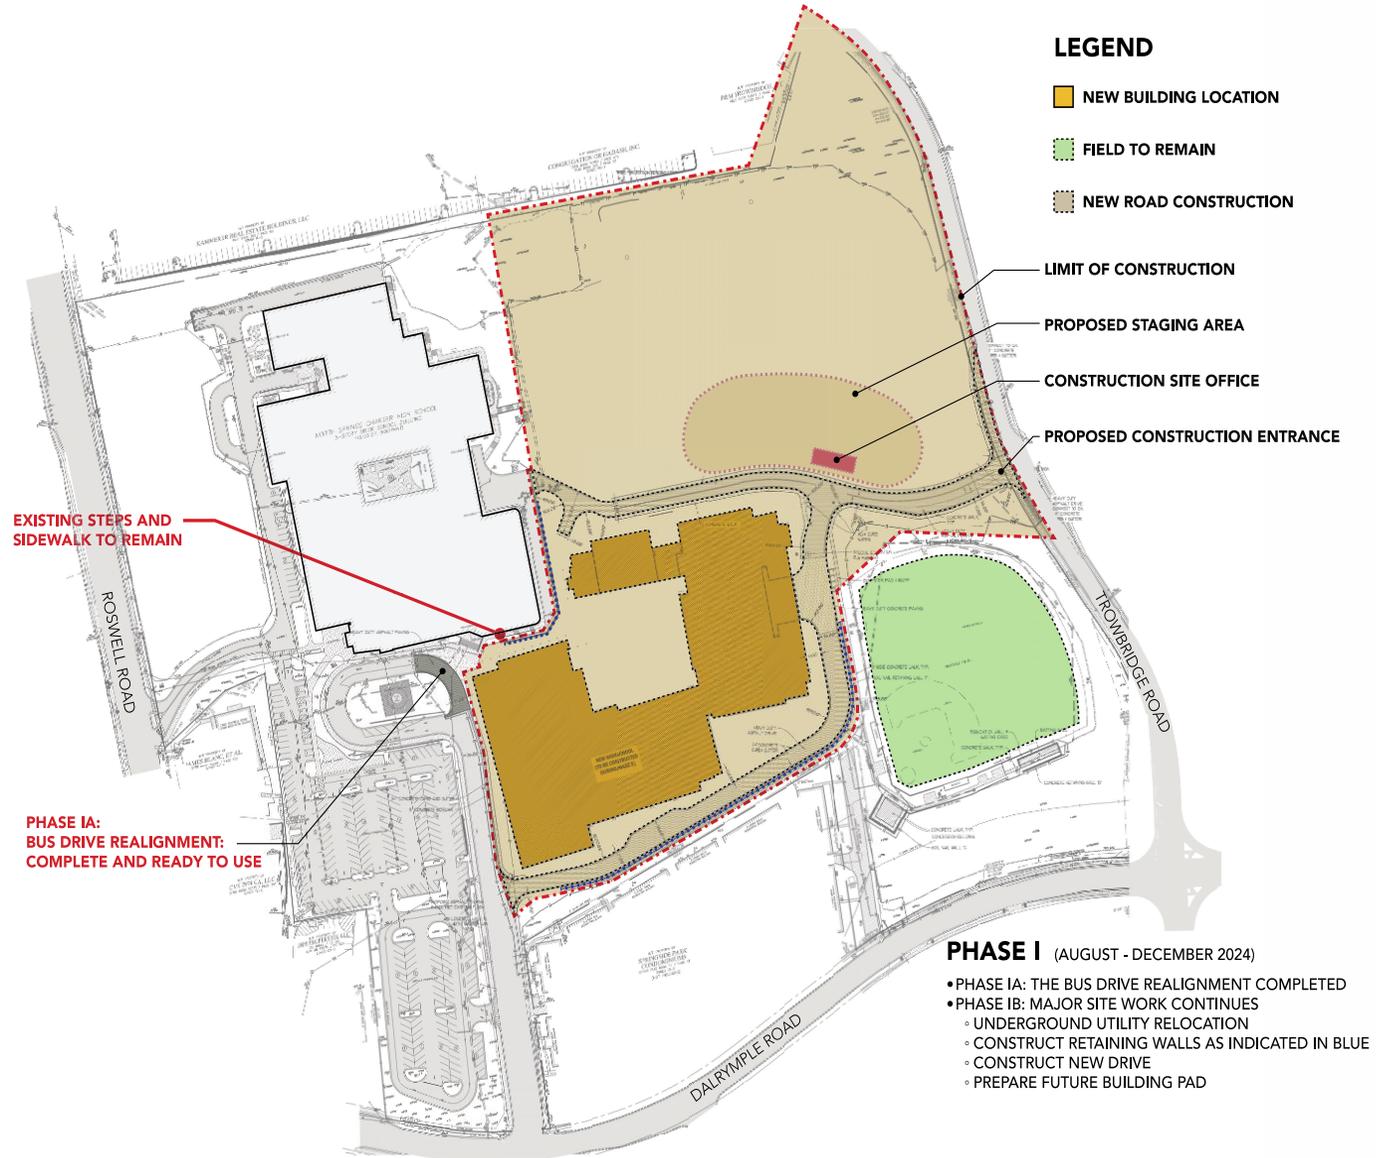


Demolition Phase 1 Plan

North Springs High School Replacement

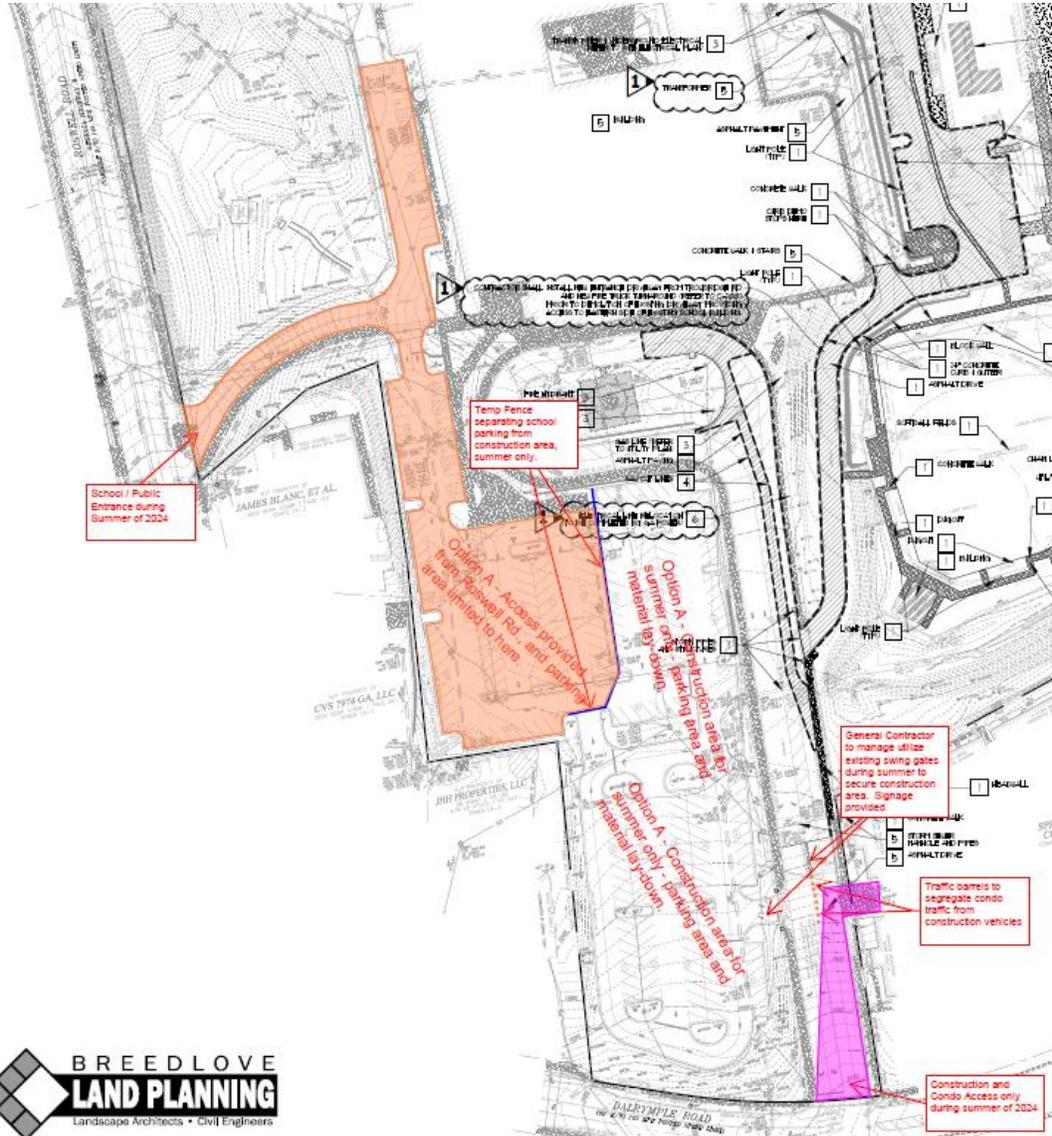

Summer Parking and Vehicle Logistics Plan

North Springs High School Replacement

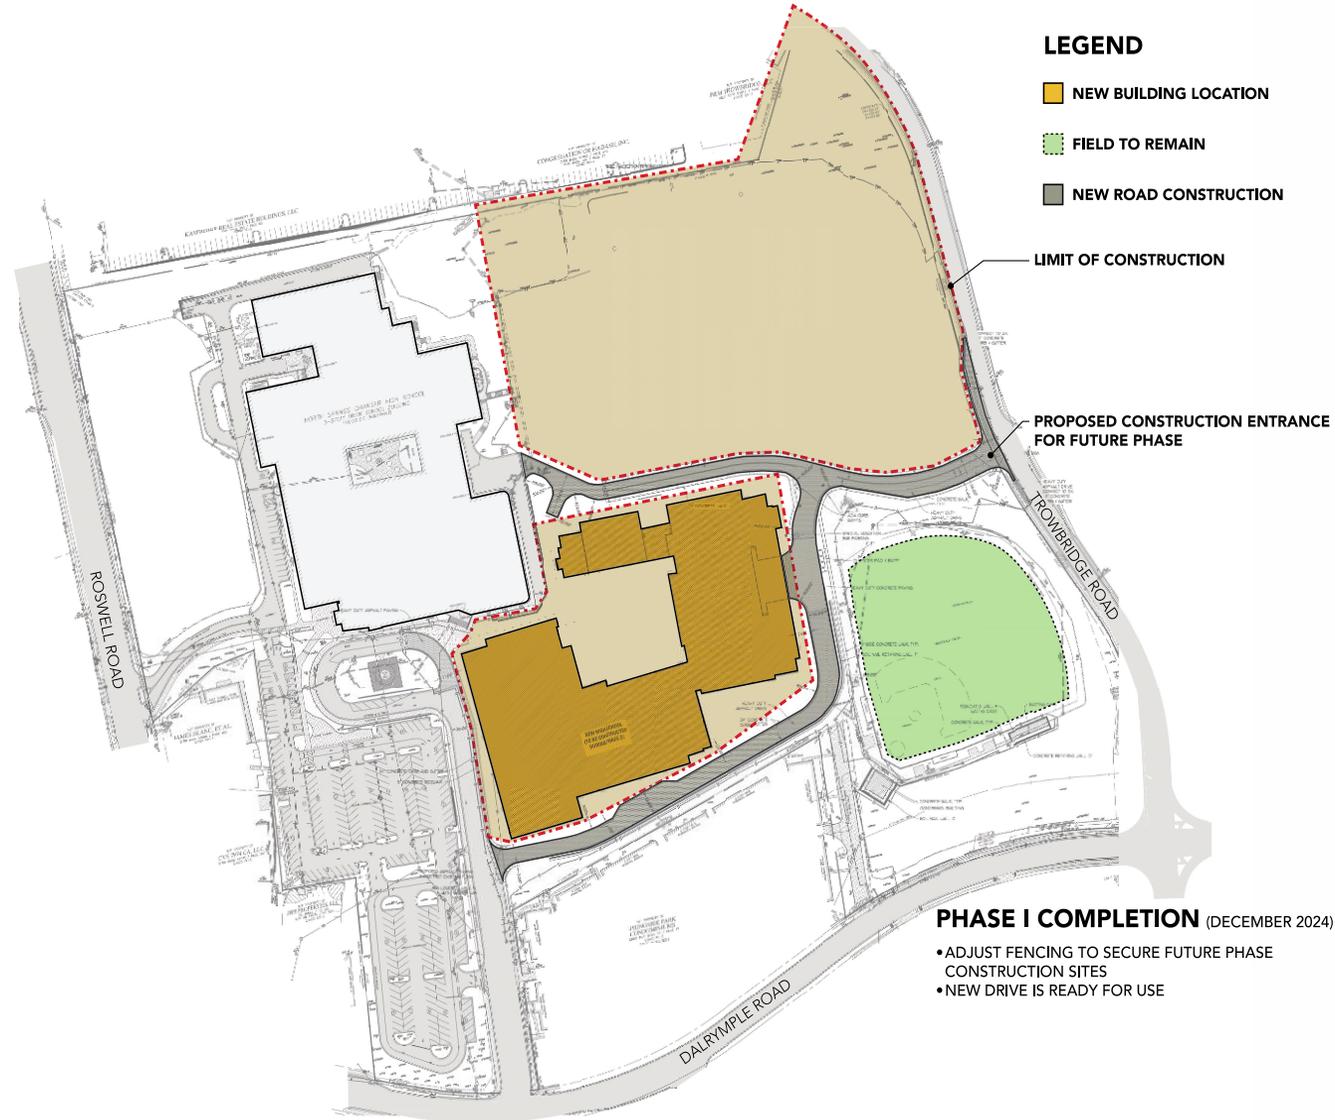

Phase I Completion

North Springs High School Replacement



Additional Scope Discussion

- Athletic Facilities enhanced by boosters
 - Covering the baseball batting cages
 - Larger stadium scoreboard
 - Improve sponsor board
 - Locker/changing room for girls close to softball field

North Springs High School Replacement



Milestones

- **Site Package began construction June 1st. and is on schedule.**
- Building package will be complete before the end of the year
- Solicitation for building construction will go out in January 2025
