



LONG BEACH
UNIFIED • SCHOOL • DISTRICT



Artist Renderings, Subject to Change.

Long Beach Unified School District
CITIZENS' OVERSIGHT COMMITTEE
Bond Measure K, Measure E and Measure Q
2023-2024 Annual Community Report



**BUILDING ON
SUCCESS**
LBUSD CAMPUS IMPROVEMENTS

Table of Contents

	Letter From The Chair1
	Measure K, E & Q Bond Overview2
1.0	COC Overview3
2.0	Purpose3
3.0	Membership3
4.0	Committee Activities4
5.0	District Support5
6.0	Meeting Dates5
7.0	Project Updates5
	Total of Expenditures through June 30, 2024	
	Current & Future Expenditures through June 30, 2024	
	Completed, In Progress & Planned Projects as of June 30, 2024	
8.0	Audit Findings14
9.0	Conclusion14
10.0	Additional Information	

All anticipated completion dates subject to change based on project development and unforeseen circumstances

LETTER FROM THE CHAIR

The Citizens' Oversight Committee (COC) is proud to present this Annual Report, highlighting the achievements of the Long Beach Unified School District's bond program during the fiscal year spanning July 1, 2023, to June 30, 2024.

This past year marked a pivotal moment in the District's bond program, with significant progress in upgrading and enhancing school facilities. Among the most notable advancements, LBUSD successfully completed the installation of high-efficiency heating, ventilation, and air conditioning (HVAC) systems at schools across the District. As of June 30, 2024, 84% of Long Beach Unified Schools are equipped with air conditioning systems. These improvements have created a more comfortable and productive learning environment, providing better climate control and air quality while also supporting energy efficiency.

In addition, we made substantial strides in the development of Measure K-funded aquatic centers at several of the District's comprehensive high schools. These state-of-the-art facilities will offer year-round opportunities for competitive swimming, water polo and recreational use, benefiting both student-athletes and the broader community.

The COC also reviewed expenditures, financial statements, and staff reports on capital projects funded by the District's bond measures. After thorough evaluation, an independent audit firm awarded the District its highest financial accountability and performance rating. This marks the program's twelfth consecutive year receiving this prestigious recognition.

We're pleased to affirm the auditor's findings, and we're honored to oversee a program that provides students with the learning spaces they need to succeed.

As we reflect on the progress made in the 2023-24 fiscal year, we are excited about the future. In the next school year, we look forward to the beginning of transformation at Washington Middle School and Polytechnic High School, two projects that will provide lasting pride and benefits for students, staff and the community.

Michael Bishop

Chairperson

LBUSD Citizens' Oversight Committee

MEASURE K, E AND Q BOND OVERVIEW

Measure K is a ballot initiative, approved by 71 percent of voters in November 2008, which makes available \$1.2 billion from property taxes to build, renovate and improve schools in the Long Beach Unified School District. The funds come from issuance of a series of bonds to occur four to six times in about ten years.

Since the measure was approved, steady progress has been made to reconfigure and restore Long Beach Unified School District's aging schools. The funds have paid for three new small high schools (McBride, Sato and Browning) and construction of a new swimming pool at Cabrillo High, renovation of the auditoriums at Poly and Wilson high schools and the rebuilding of Jordan High School.

Dozens of Measure K projects, identified as the most critical, have already been completed. These include district-wide wireless data communication, seismic retrofitting, accessibility upgrades, telecommunications systems upgrades, fire alarm/ intercom/clock replacements, boiler replacement and outdated portable removal.

In addition, these funds paid for building Nelson Academy and the complete rebuilding of Newcomb Academy and Roosevelt Elementary.

In response to strong public support for repairing aging schools, the Long Beach Unified School District Board of Education approved the placement of **Measure E**, a \$1.5 billion school repair and safety bond initiative on the November 2016 ballot. Approved by 75 percent of voters, Measure E funds:

REPAIRS: Many campuses were built 60 to 70 years ago and needed important health and safety repairs. Also, buildings must meet handicap accessibility and earthquake standards, old restrooms and leaky roofs must be replaced, and further upgrades made to fire alarms and security systems, plumbing, electrical and other infrastructure.

TECHNOLOGY: To enable students' future success, modern science and computer labs, libraries, and classroom technology will be funded.

AIR CONDITIONING: When temperatures rise, schools with inadequate or no air conditioning are forced to send students home due to overheated classrooms. By installing modern energy efficient air conditioning systems, LBUSD will help improve learning by making sure classrooms are always comfortable and ventilated.

SAFETY: Improving indoor and outdoor recreational areas, including fields, gyms and swimming pools, will allow afterschool programs to be expanded and provide supervised activities designed to reduce gang involvement and increase graduation rates.

Measure Q, the Long Beach Unified School District's health, safety and student achievement bond measure, was approved by local voters by a yes vote of 60.72% in November 2022. This bond measure provides the District \$1.7 billion for school renovations and the possibility of state matching funds totaling millions of dollars over the life of the bond, funding fund health and safety improvements at all District schools and select projects in the [Facility Master Plan](#) priority categories, including expansion of pre-kindergarten/transitional kindergarten programs, wellness and green spaces, career and technical education classrooms, and high-tech media centers, among other enhancements.

1.0 COC Overview

The Long Beach Unified School District (the "District") successfully obtained voter approval in the November 4, 2008 election (the "2008 Bond Election") to issue up to \$1,200,000,000 in general obligation bonds, known as "Measure K." An Independent Citizens' Bond Oversight Committee was established for Measure K on February 3, 2009. In addition, the District gained approval in the November 8, 2016 election to issue up to \$1,500,000,000 in general obligation bonds. Most recently, the District was successful in the November 8, 2022 election (the "2022 Bond Election"), in which voters approved the issuance of up to \$1,700,000,000 in general obligation bonds, referred to as "Measure Q." Together, the 2008, 2016, and 2022 elections are collectively known as the "Elections," and Measure K, Measure E, and Measure Q are referred to as the "Measures."

These Elections were conducted under Proposition 39, known as the Strict Accountability in Local School Construction Bonds Act of 2000 (Chapter 15264 et seq. of the Education Code, "Prop 39"). In accordance with Section 15278 of the Education Code, the District is required to establish an Independent Citizens' Bond Oversight Committee for Measure Q to ensure compliance with Prop 39's accountability standards.

The Board of Education of the Long Beach Unified School District (the "Board") formally establishes and assigns the duties and responsibilities of the Independent Citizens' Bond Oversight Committee (the "Committee") as outlined in the [Bylaws](#). It is important to note that the Committee does not have independent legal authority outside of the District.

2.0 Purpose

The purposes of the Committee are set forth in Prop 39 and the Bylaws are specifically made subject to the applicable provisions of Prop 39 as to the duties and rights of the Committee. The Committee shall be deemed to be subject to the Ralph M. Brown Public Meetings Act of the State of California (the "Ralph M. Brown Act") and shall conduct its meetings in accordance with the provisions thereof. The District shall provide necessary administrative support to the Committee as shall be consistent with the Committee's purposes, as set forth in Prop 39. The Committee shall serve as the statutory Oversight Committee for each of the Measures.

3.0 Membership

The Committee shall consist of at least seven (7) members appointed by the Board of Education from a list of candidates submitting written applications, and based on criteria established by Prop 39, to wit:

- (a)** One (1) member shall be the parent or guardian of a child enrolled in the District.
- (b)** One (1) member shall be both a parent or guardian of a child enrolled in the District and active in a parent-teacher organization, such as the Parent Teacher Association or a school site council.
- (c)** One (1) member active in a business organization representing the business community located in the District.
- (d)** One (1) member active in a senior citizens' organization.
- (e)** One (1) member active in a bona-fide taxpayers association.
- (f)** Two (2) members of the community at-large.

In accordance with applicable law, committee members will be appointed to serve a term of two (2) years and no member may serve more than three (3) consecutive terms. The Citizens' Bond Oversight Committee shall meet at least once a year but no more frequently than up to six (6) times a year.

The following table lists the 2023-2024 members, represented group, and current terms.

Member	Representation Group	Current Term
Michael Bishop	Chairperson, Senior Citizens' Organization	3rd term expires 9/2025
Pamela Williams	Vice Chairperson, Parent/PTO	2nd term expires 10/2024
Osvaldo Avila	Member, Community-At-Large	1st term expires 11/2025
Steve Davis	Member, Business Representative	1st term expires 10/2025
Raul Nario	Member, Parent/PTO	2nd term expires 6/2025
Rebecca Turrentine	Member, Community-At-Large	3rd term expires 09/2024
Vacant	Member, Taxpayers' Association	Accepting Applications

**** Citizens' Oversight Committee Member Recruitment ****

As part of our continued commitment to growth and excellence, we have made significant efforts this year to attract and recruit new members. Filling key vacancies across all levels of the organization remains a top priority, ensuring we have the talent and diversity needed to drive our mission forward.

4.0 Committee Activities

In order to perform the duties as set forth within the Bylaws, the Committee engaged in the following authorized activities (where applicable):

1. District staff presented financial reports, various processes and approaches, communications, and regular updates on current projects. Handouts were distributed at the meetings and subsequently posted to the District's Bond website;
2. Receive and review copies of the District's annual independent performance audit and annual independent financial audit as required by Article XIILA of the California Constitution;
3. Inspected District facilities and grounds for which bond proceeds have been or will be expended;
4. Reviewed efforts by the District to maximize bond proceeds by implementing various cost-saving measures;
5. Received from the Board, within three months of the District receiving the Audits, responses to any and all findings, recommendations, and concerns addressed in the Audits, and review said responses.

5.0 District Support

The District provided the Committee with technical and administrative assistance as follows:

- 1) Prepared and posted public notices, as required by the Ralph M. Brown Act. Ensured that all notices to the public were provided in the same manner as notices regarding meetings of the District Board;
- 2) Provided meeting rooms with audio/visual equipment;
- 3) Prepared and distributed copies of meeting materials, such as agendas and reports;
- 4) Retained all Committee records and provided public access on the District website; and
- 5) Attended Committee proceedings and reported on the status of projects and expenditures of Measure E, K and Q bond proceeds. The following District staff provided administrative support:
 - Alan Reising Assistant Superintendent, Business Services;
 - David Miranda, Executive Director, Facilities Development and Planning;
 - Sara Slater, Facilities Project Accountant; and
 - Maria Ruiz, Administrative Secretary.

6.0 Meeting Dates

During the 2023-2024 school year, the Committee met four times. In addition to conducting the meetings at sites, District staff conducted tours as part of the meetings.

July 2023 through June 2024 Meetings

- September 26, 2023 (Location: Jordan High School);
- December 14, 2023 (Location: Video Conference – via Zoom);
- February 6, 2024 (Location: Washington Middle School); and
- May 23, 2024 (Location: Video Conference – via Zoom).

7.0 Project Updates

The following projects were completed since the last annual report, covering July 1, 2023 to June 30, 2024:

- Bancroft Middle School: Heating, Ventilation & Air Conditioning;
- Avalon K-12: Heating, Ventilation & Air Conditioning;
- Holmes Middle School: Heating, Ventilation & Air Conditioning;
- Birney Elementary School: Heating, Ventilation & Air Conditioning;
- Emerson Elementary School: Heating, Ventilation & Air Conditioning; and
- Jordan High School: Ph 3, Buildings 200, 300 & 1000.

Construction started or continued on the following projects, July 1, 2023 through June 30, 2024:

- Hamilton Middle School: Gymnasium;
- Jordan High School: Phase 5A: Stadium Modernization (Bleacher & Athletic Fields);
- Jordan High School: Phase 6: Gymnasium and Pool;
- Millikan High School: Electrical Upgrades
- Lakewood High School: Aquatic Center;
- Wilson High School: Aquatic Center;
- Gant Elementary School: Heating, Ventilation and Air Conditioning (HVAC) Plus;
- Gompers Elementary School: Heating, Ventilation and Air Conditioning (HVAC);
- Emerson Elementary School: Heating, Ventilation and Air Conditioning (HVAC);
- Stanford Middle School: Heating, Ventilation and Air Conditioning (HVAC);
- Tincer Preparatory School: Heating, Ventilation and Air Conditioning (HVAC) Plus;
- Tincer Preparatory School: All-Weather Field; and
- Avalon K-12 School: Site Improvements: Baseball Field.

BOND PROJECT UPDATES

Heating, Ventilation & Air Conditioning (HVAC) District Wide

LBUSD has made significant strides toward creating a safer, more comfortable learning environment by fast-tracking the installation of HVAC systems across its schools. Originally planned for a longer rollout, this project was accelerated in response to record-breaking heatwaves and increasing concerns over extreme temperatures and poor air quality. This proactive approach ensures students and staff are protected from the impacts of extreme weather sooner than anticipated.

Completed by June 30, 2024: Birney Elementary School, Emerson Elementary School and Gompers Elementary School.

Beginning Fall 2024: Gant Elementary School and Tincher Preparatory School will begin HVAC projects.

Following Year: Six additional LBUSD campuses will start HVAC installations: Millikan High School, Henry Elementary School, Hoover Middle School, Carver Elementary School, Marshall Academy of the Arts and Los Cerritos Elementary School.

Next Three Years: After wrapping up with Sato, Tucker and Washington Middle School, all district schools will have new air conditioning systems, with the exception of Polytechnic High School.

2028: Polytechnic High School will begin its Poly HVAC installation soon; however, completion is scheduled for 2028, aligning with the broader campus transformation necessitating building teardown and rebuild.

Thanks to the support of Measure E bonds approved by voters, this ambitious project has become a reality. With HVAC systems now installed at 71 out of 84 Long Beach Unified schools, LBUSD is committed to creating a healthier, more sustainable learning environment for students. For campuses still in the planning or installation phases, heat mitigation measures are already in place to ensure students and staff remain comfortable while the upgrades are completed.



Stanford Middle School



Gompers Elementary School



Gant Elementary School

HVAC Projects Started: 2017

Anticipated Project Completion: 2028, concluding with Polytechnic High School

As of June 30, 2024:

- **Funding Sources:**
 - \$ Measure E Bond Fund

Total Project Expenditures: \$710,188,183

AVALON

HVAC + Modernization

This project consisted of:

- HVAC Modernization of all buildings including classrooms, kitchen, mpr and offices.
- Comprehensive upgrades to support systems, including utilities, safety and security features and technology networks.
- Accessibility improvements and exterior painting of all buildings
- New interior wall layout in the administration building

Completed Work as of June 30, 2024:

- Fire Alarm installation and programing of devices
- Installation of signage at the portables

Currently Working On:

- Painting of perimeter fencing

Upcoming Work:

- None. The project is set to be closed out.



Construction Started:
Completed:

January 2022
November 2024

As of June 30, 2024:

Total Budget: \$49,269,540

• Funding Sources:

- \$38,828,080 Measure E Bond Fund
- \$5,441,460 State SFP Funds
- \$5,000,000 Developer Fees

Total Commitment (Encumbrances): \$46,556,127

Total Project Expenditures: \$42,526,482

Artist Renderings, Subject to Change.

Ball Field

This project consists of:

- Redesigning the baseball field to include enlarged synthetic turf play field with the use of retaining walls
- Accessibility improvements to include accessible parking spaces, and path of travel to the field area

Completed Work as of June 30, 2024:

- For the north side construction, soldier pipe installation
- Excavation and compaction for shotcrete wall
- Shotcrete tieback wall installation

Currently Working On:

- Sanding and installing pipes for underground supply and waste plumbing on the east side construction
- Installing electrical ground boxes

Upcoming Work:

- Install underground electrical conduits for the east side construction
- RFP retaining walls at ramps



Construction Started:
Anticipated Completion:

September 2023
August 2025

As of June 30, 2024:

Total Budget: \$33,875,481

• Funding Sources:

- \$33,875,481 Measure E Bond Fund

Total Commitment (Encumbrances): \$32,498,891

Total Project Expenditures: \$10,166,265



Construction Started: May 2024
Anticipated Completion: September 2025

As of June 30, 2024:

Total Budget: \$35,532,785

- **Funding Sources:**

- \$35,532,785 Measure K Bond Fund

Total Commitment (Encumbrances): \$33,902,410

Total Project Expenditures: \$13,482,583

Hamilton Middle School – Gymnasium

This project consists of:

- Construction of a new gymnasium and locker room building, along with associated site work.
- Demolition of the existing gymnasium and locker room building.
- Modernization of two SDC classrooms in the existing Building 500.

Completed Work as of June 30, 2024:

- CMU wall lifts for gym and locker areas
- Slab-on-grade concrete pours

Currently Working On:

- Installation of gymnasium trusses.
- Installation and welding of high roof beams.

Upcoming Work:

- Installation of steel decking for both high and low roofs.
- Exterior metal stud framing.

Jordan High School - Gymnasium + Pool

This project consists of:

- A new aquatic center and one-story gymnasium building.
- The gymnasium, covering 65,000 square feet, will include competition and practice gymnasiums, weight room, wrestling room, dance room, fitness room, trainer room, offices, team rooms, locker rooms, and storage spaces.
- The aquatic center, located west of the gym, will feature a competition swimming pool, restrooms, team room, pool equipment building, ticket/storage building, and sports lighting.
- New aluminum bleachers will be installed in the western section of the aquatic center.
- Additional features include a concrete pool deck, scoreboard, stadium lights, hardscaped areas, low site walls, and new utility lines.
- The aquatic center will have CMU perimeter walls.

Completed Work as of June 30, 2024:

- To date, no work has been completed.

Currently Working On:

- Abatement and demolition

Upcoming Work:

- Site and Utility Improvement



Construction Started: August 2024
Anticipated Completion: August 2027

As of June 30, 2024:

Total Budget: \$84,330,001

- **Funding Sources:**

- \$84,330,001 Measure K Bond Fund

Total Commitment (Encumbrances): \$67,480,520

Total Project Expenditures: \$3,088,0800

Wilson Aquatic Center



Construction Started: March 2023
Anticipated Completion: April 2025

As of June 30, 2024:

Total Budget: \$42,879,494

- **Funding Sources:**

- \$42,879,494 Measure K Bond Fund

Total Commitment (Encumbrances): \$40,258,157

Total Project Expenditures: \$14,943,235

The project consists of:

- A pool with bleachers, shade structure, Musco poles, and scoreboard.
- A mechanical building with public restrooms, storage rooms, and a pool attendant's office.
- A locker room building featuring a multipurpose room, ticket booth, concessions, and coach's offices.

Completed Work as of June 30, 2024:

- Site underground mechanical, plumbing and electrical.
- Swimming pool over-excavation.
- Over-excavation for the 15000, 16000, and 17000 Buildings.

Currently Working On:

- Site: Underground electrical throughout the site.
- 15000 Building: Form slab on grade at Building 15000. Installing vapor barrier at 15000.
- 16000 Building: Excavate for building foundations. Form, Reinforce, Pour Building Foundations. Install Underground plumbing and electrical.
- Swimming Pool: Installation of Plumbing trenches and under slab drainage piping.

Upcoming Work:

- 15000 Building: Install CMU. Pour Slab on Grade.
- 16000 Building: Waterproofing at concrete stem walls. Pour slab on grade.
- Swimming pool: Backfill and fine grade. Reinforcement for pool slab on grade. Pour pool slab on grade.

Lakewood Aquatic Center

This project consists of:

- A pool with bleachers, shade structure, Musco poles, and scoreboard.
- A mechanical building with public restrooms, storage rooms, and a pool attendant's office.
- A locker room building featuring a multipurpose room, ticket booth, concessions, and coach's offices.
- New softball field and resurface tennis courts.

Completed Work as of June 30, 2024:

Currently Working On:

- Finishes in the Mechanical Building
- Rough-in work at the Locker Room Building
- CMU walls and exterior finishes on site

Upcoming Work:

- Permanent power installation
- Site concrete work
- Finishes in the Locker Room Building
- Startup and commissioning



Construction Started: June 2023
Anticipated Completion: June 2025

As of June 30, 2024:

Total Budget: \$48,825,726

- **Funding Sources:**

- \$48,825,726 Measure K Bond Fund

Total Commitment (Encumbrances): \$46,700,677

Total Project Expenditures: \$21,992,304

HOME OF SCHOLARS AND CHAMPIONS

Polytechnic High School, a Long Beach icon, is set for a transformation that will blend its rich history with future-forward spaces for learning and growth. Starting in the 2024-25 school year, interim housing will be in place as the school begins its renovations. The construction of a three-story classroom building will kick off in 2025, featuring a simulation lab for the medical pathway and essential upgrades like air conditioning, technology, and seismic improvements.

Looking to the future, the master plan includes new facilities for the arts, with dedicated spaces for drama and music programs, along with outdoor learning areas. An aquatic center, slated for 2028, will complement a new two-story gym set to open in 2029. A new softball diamond, tennis courts with rooftop seating, and a plaza to honor Poly's CIF and state titles will enhance the campus further.

Poly's last major renovation in 2017 revitalized the 87-year-old auditorium, preserving its historic charm while adding modern features. This next phase includes a new food services facility, a student drop-off area, and a wellness garden.

By the 2031-32 school year, Polytechnic High will be a dynamic, modern campus that honors its legacy while providing an inspiring environment for future generations.



Artist Renderings, Subject to Change.

Polytechnic High School – Campus Transformation

Construction Start: Summer 2025

Anticipated Completion: Fall 2030 *subject to change based on project development and unforeseen circumstances*

As of June 30, 2024:

Total Budget: \$301,932,578

- **Funding Sources:**

- \$301,932,578 Measure Q Bond Fund

Total Commitment (Encumbrances): \$11,447,808

Total Project Expenditures: \$1,250,128



This project consists of:

- Demolition of buildings 150, 550, 700, 800, 850, and gym buildings 1000, 1100, and 1200.
- Construction of five new buildings:
 - Building 150: A one-story performing arts building housing flexible drama and band classrooms.
 - Building 700: A two-story student services building featuring a new lobby entrance, a college and career center, a wellness center, and school administrators' offices.
 - Building 800: A two-story gymnasium building with a large and small gym on the second floor, and a first floor housing wrestling and weight rooms, along with team rooms and locker rooms serving the new pool.
 - Building 850: A single-story pool equipment building associated with the new pool, deck, and spectator bleachers.
 - Building 1000: A two-story classroom building.
- Site reconstruction, including:
 - Redesign of Jackrabbit Lane with an improved parking layout and new designated drop-off and pick-up lanes.
 - Upgraded baseball field with sports lighting.
 - New exterior basketball courts and resurfacing of existing tennis courts.
 - Enhanced exterior landscape courtyards and gardens with fixed seating.

IT'S A GREAT DAY TO BE A WASHINGTON WOLF!

Exciting changes are underway at Washington Middle School, one of the oldest and most densely populated campuses in the Long Beach Unified School District. With over 900 students on just 5.1 acres, the school is undergoing a complete teardown and rebuild, thanks to the support of LBUSD's Measure Q bond.

What began as an HVAC upgrade quickly evolved into a \$176 million transformation of the entire campus. This project will create a modern, state-of-the-art space designed to meet the needs of the entire community. The new layout includes a vibrant courtyard, advanced classrooms, a new gymnasium, and a combined cafeteria and auditorium. A new administration building, with expanded classrooms, will also replace the outdated structure, while preserving elements of the school's historic roots.

Additionally, the campus will feature a rooftop all-weather field and an underground parking garage to support the growing needs of the students and staff. These changes are not just about new buildings; they're about creating a better future for Washington's students—providing them with the tools and spaces they need to thrive.

This revitalization is part of a broader transformation in the Washington neighborhood, representing progress and pride for the community. As the project moves forward, the school will stand as a beacon of hope and opportunity for generations to come.



EXTERIOR DESIGN DEVELOPMENT

WASHINGTON MIDDLE SCHOOL // LONG BEACH UNIFIED SCHOOL DISTRICT // 07.22.2024



EXTERIOR DESIGN - VIEW FROM SPORTS FIELD

WASHINGTON MIDDLE SCHOOL // LONG BEACH UNIFIED SCHOOL DISTRICT // 07.22.2024



Washington Middle School – Campus Transformation

Construction Start: November 2024

Anticipated Completion: 2028 *subject to change based on project development and unforeseen circumstances*

As of June 30, 2024:

Total Budget: \$176,030,397

Funding Sources:

- \$435,792 Measure E Bond Fund
- \$175,594,605 Measure Q Bond Fund

Total Commitment (Encumbrances): \$144,238,457

Total Project Expenditures: \$4,957,846

This project consists of:

- Complete demolition of all existing (5) permanent buildings, (1) portable and staff parking lot.
- Construction of (4) New Buildings which includes a two-three story Admin/Classroom/Kitchen & Dining Building, Auditorium, Gym/Locker and Classroom Building, and a Synthetic Soccer turf field with subterranean parking structure
- New Courtyard with outdoor learning structures, hardscape and landscaping
- New HVAC, Electrical, Plumbing and Fire Protection Systems
- New A/V projector and screens in all classrooms
- New Photovoltaic Systems on roofs of each new Building
- All Electric Campus
- New student drop/off located off Cedar Avenue

"Washington's campuswide renovations have been thoughtfully planned to enhance student learning and create an inviting campus community," said David Miranda, LBUSD's executive director of Facilities Development and Planning. "We look forward to starting the project."

BOND PROJECTS BY THE NUMBERS



1.927B+

Expended on the improvement of our schools



63K+

Students benefiting from at least one bond-funded project



35


Schools with new heating, ventilation and air conditioning




All 84

Schools have campus wide Wi-Fi


TOTAL PROJECT EXPENDITURES THROUGH JUNE 30, 2024

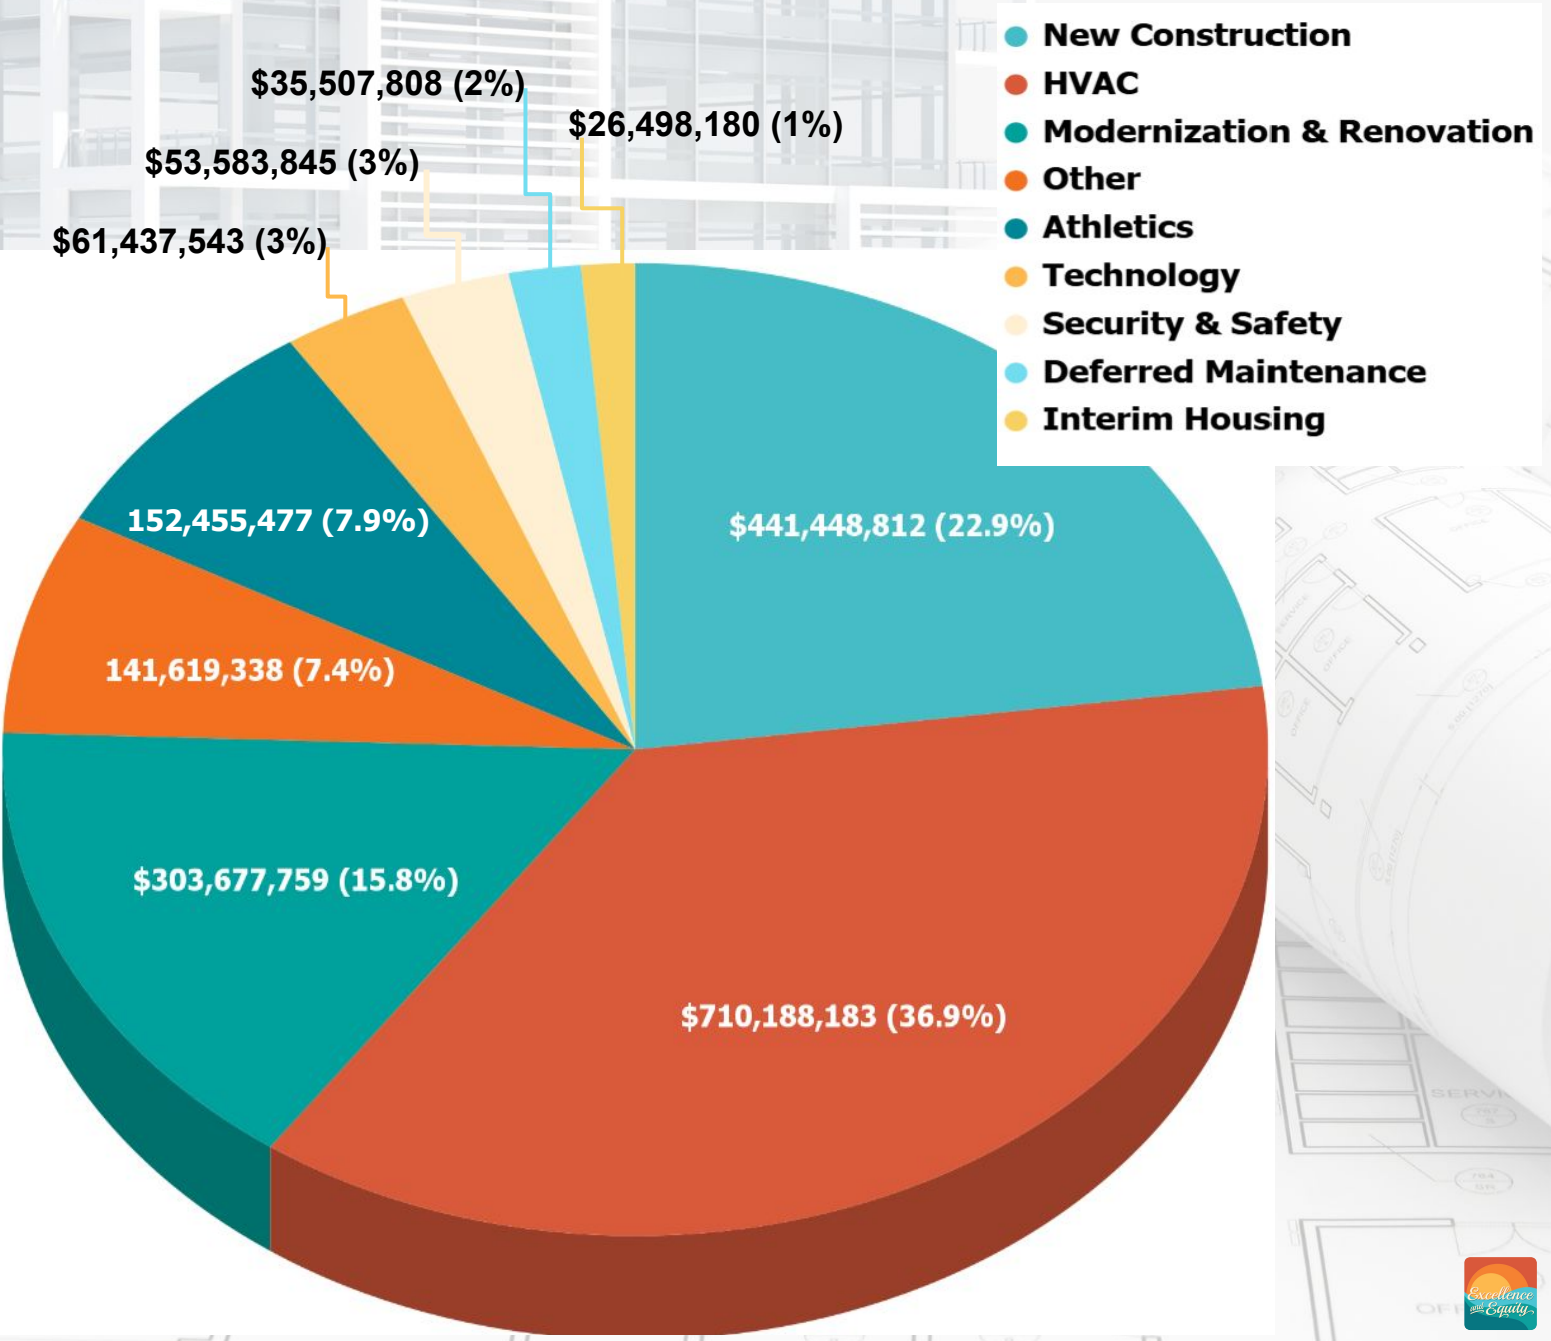

CURRENT & FUTURE EXPENDITURES THROUGH JUNE 30, 2024

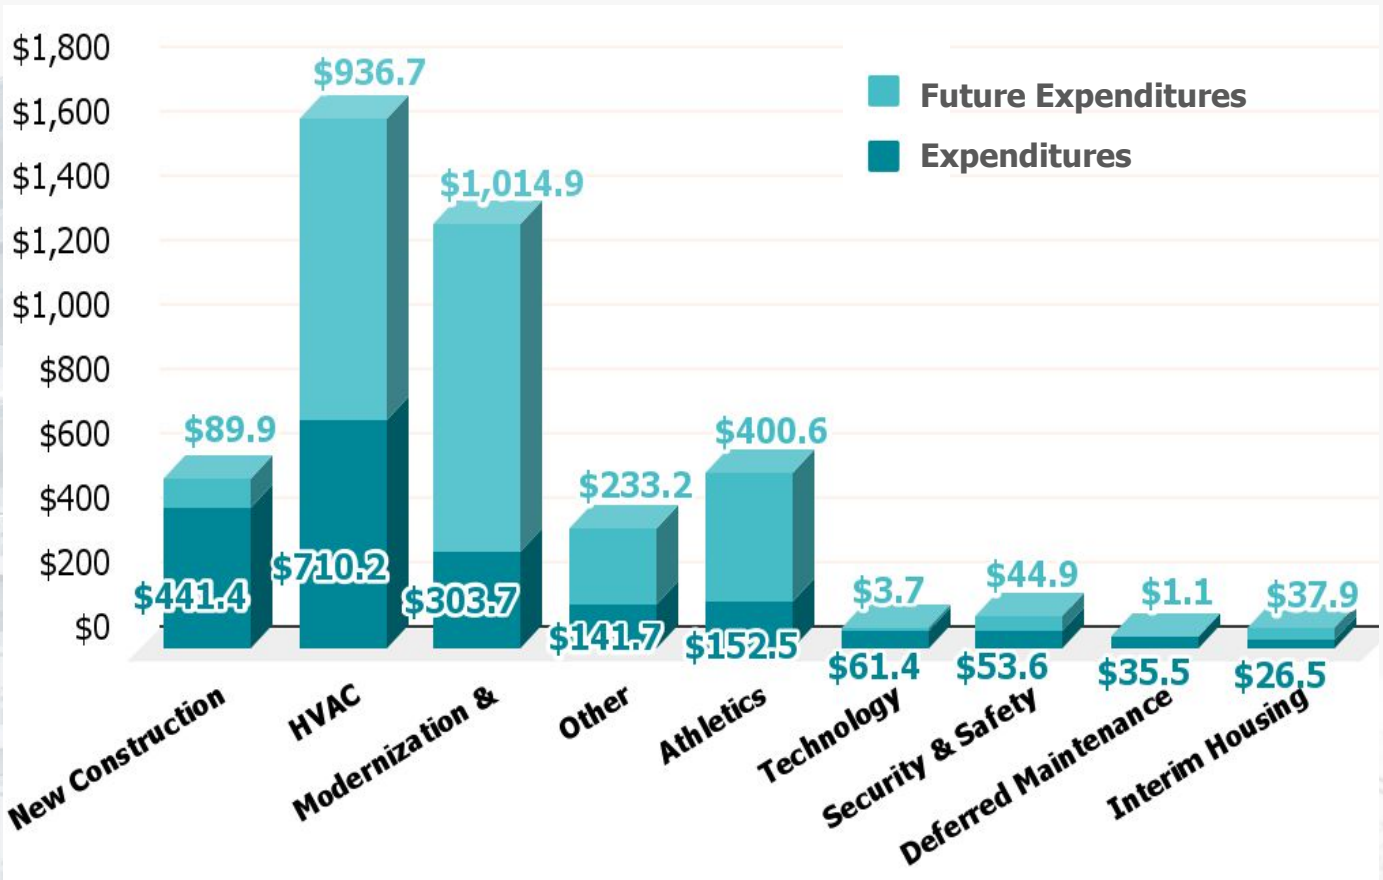

COMPLETED, IN PROGRESS & PLANNED PROJECTS AS OF JUNE 30, 2024

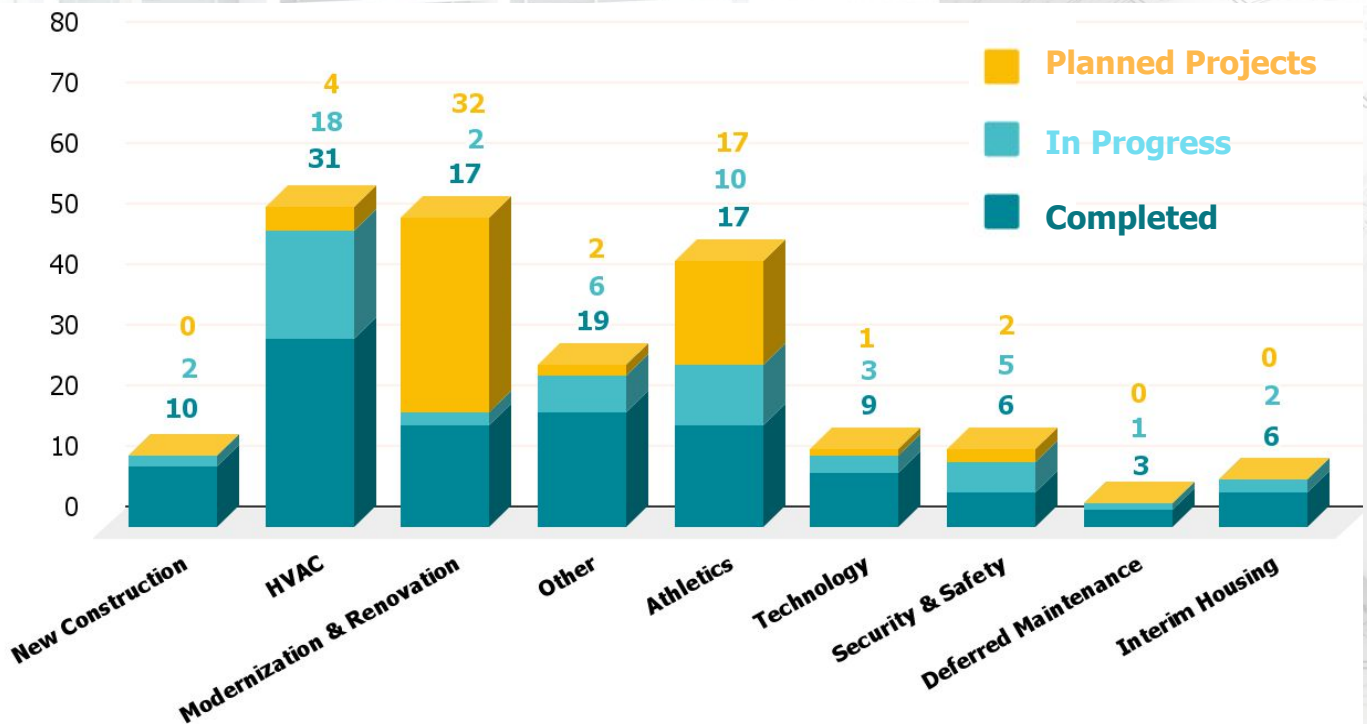

8.0 Audit Findings


After a rigorous review process, an independent audit firm granted the District its highest financial accountability and performance rating for the twelfth consecutive year.

9.0 Conclusion

Based upon the listed activities, the Committee advises the public that the District is in compliance with Article XIII A, Section 1(b)(3) of the California Constitution: Bond proceeds have been expended on projects set forth in ballot measure; further, it was noted that the Measure K, Measure E and Measure Q bond Program funds, were expended for salaries and benefits only to the extent allowable and audits have been performed as prescribed by law.

10.0 Additional Information

Meeting minutes, audits, and other related documents can be accessed on the Long Beach Unified School District Bond Website at lbschoolbonds.net.

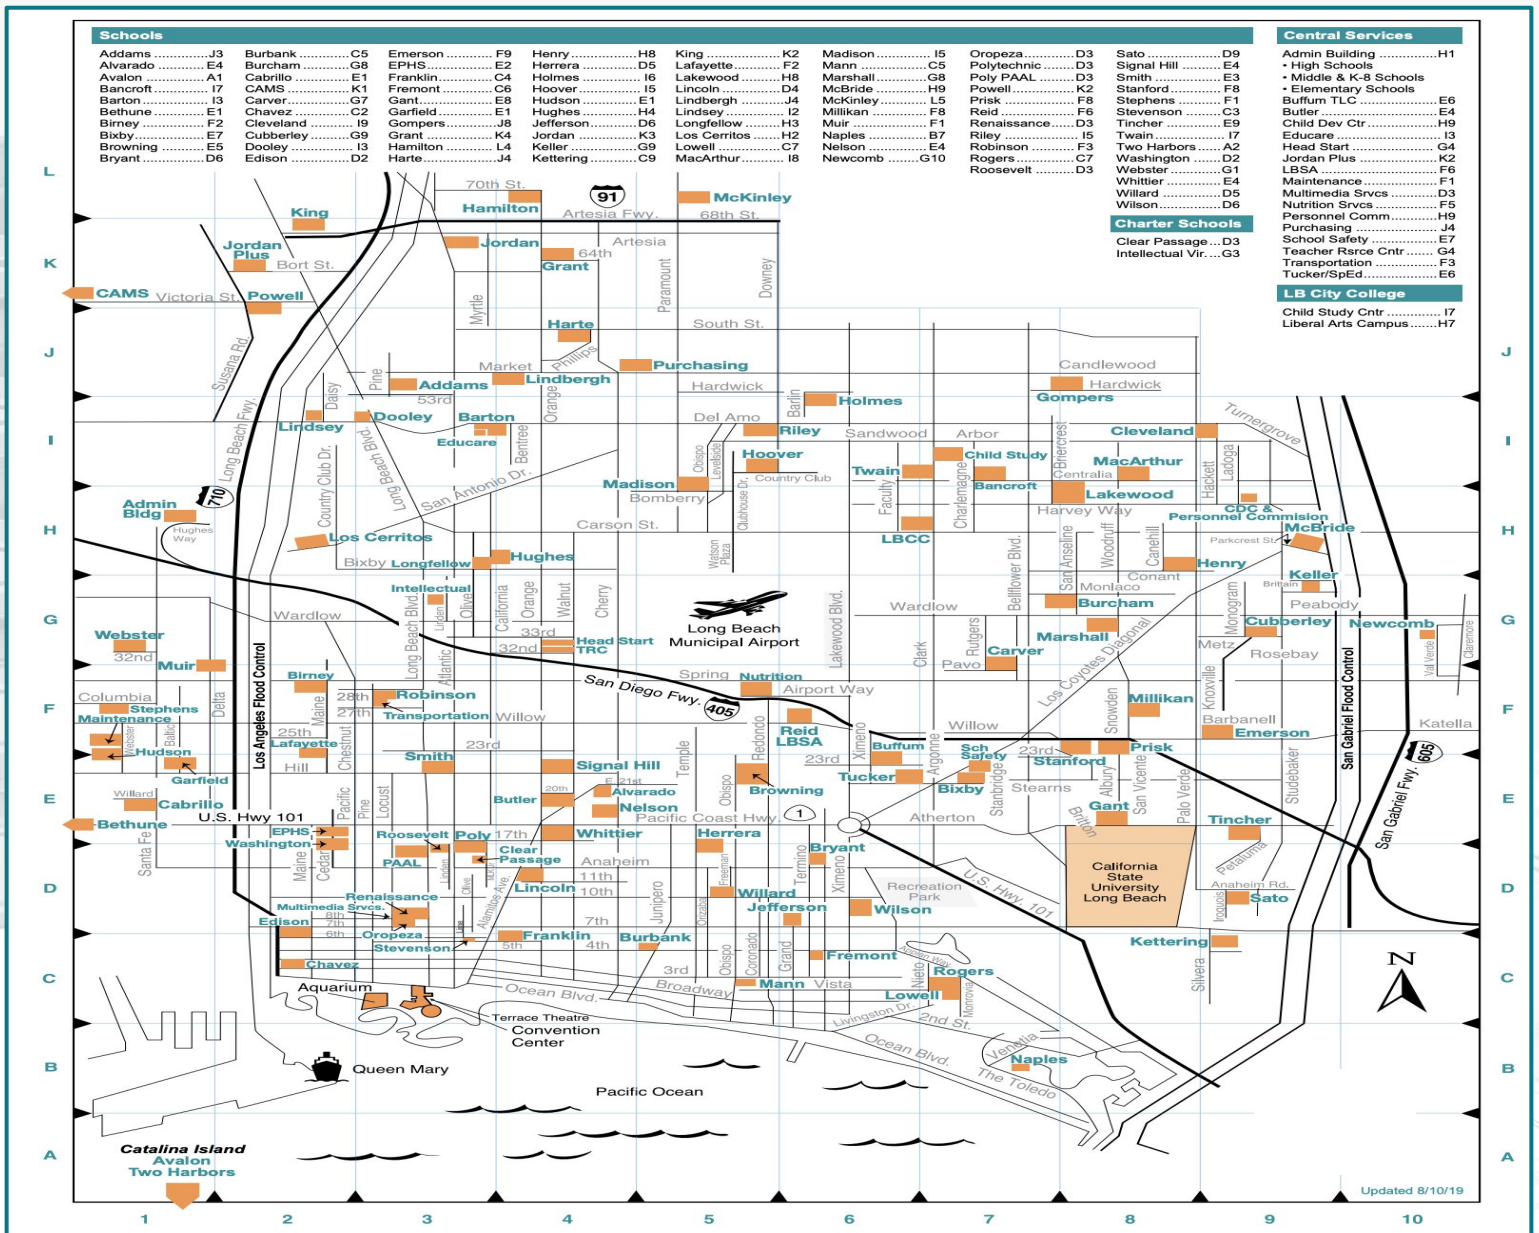

LONG BEACH

UNIFIED • SCHOOL • DISTRICT

Board of Education

Diana Craighead, President ■ Douglas Otto, Vice President
 Juan Benitez, Ph.D., Member ■ Maria Isabel López, Member
 Erik Miller, Member
 Dr. Jill Baker, Superintendent
