




2023 BOND

MAJOR PROJECTS UPDATE

NOVEMBER 2023



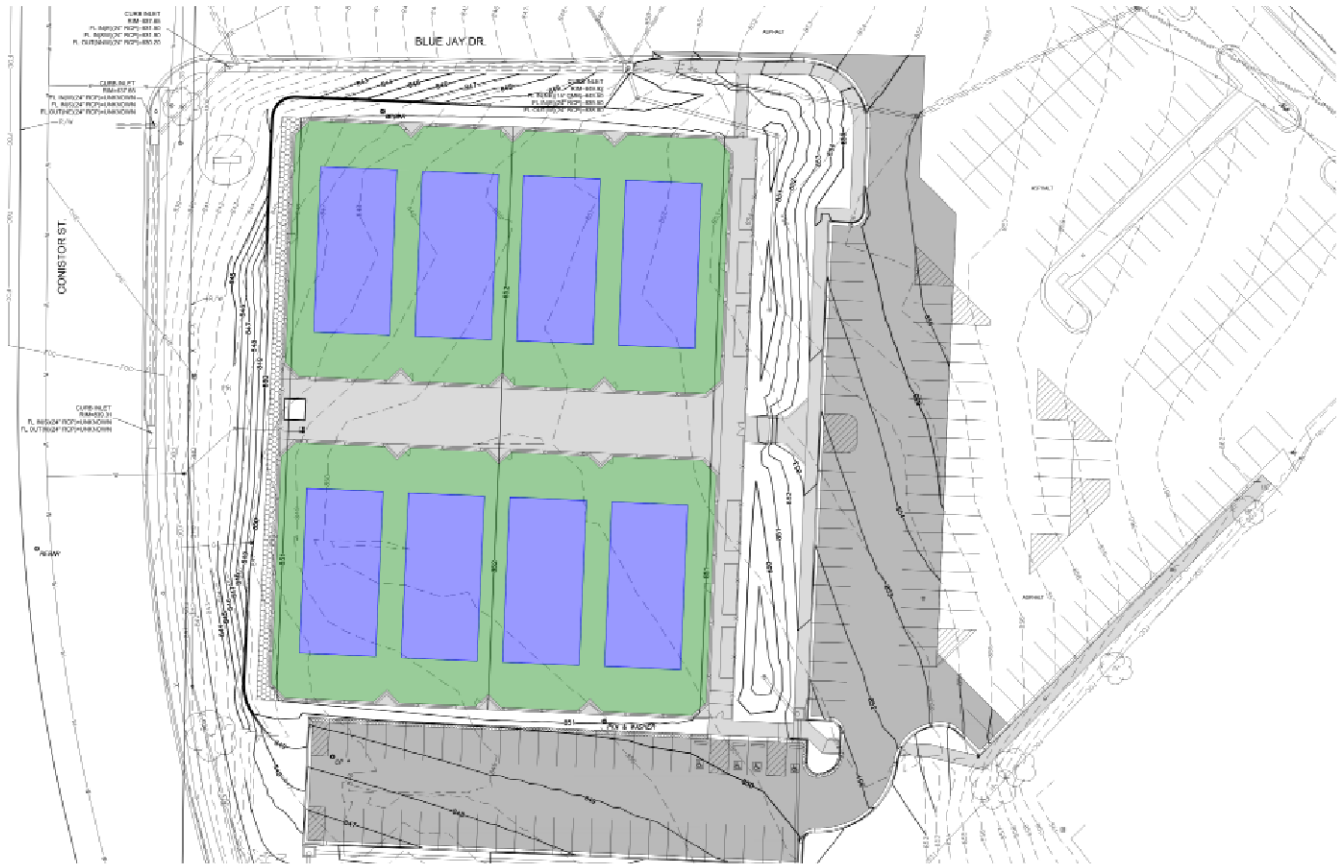

Liberty High School Tennis

- (8) Competition Tennis Courts
- Post-Tensioned Concrete slab with DecoTurf brand acrylic surfacing
- 10'-0" tall perimeter fence with windscreen
- Retaining wall and asphalt parking lot improvements

Construction Start: Spring 2023

Construction Complete: Fall 2023

**WEEKLY
PROGRESS
REPORT**

Tennis Courts 11/13/2023

Liberty Public Schools



PROJECT STATUS

- Courts Substantially Complete
- Turned Over 10/31
- Final Punch List Items Being Completed

UPCOMING

Project Completion October 2023




North Courts Looking West



North Courts Looking Southwest



East Concourse Looking South

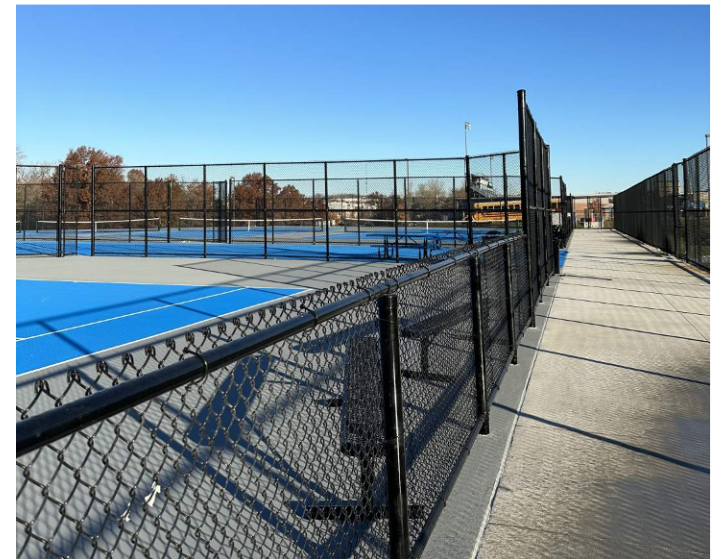

East Concourse Looking North


WEEKLY PROGRESS REPORT



South Courts Looking West



Center Spectator Concourse Looking West

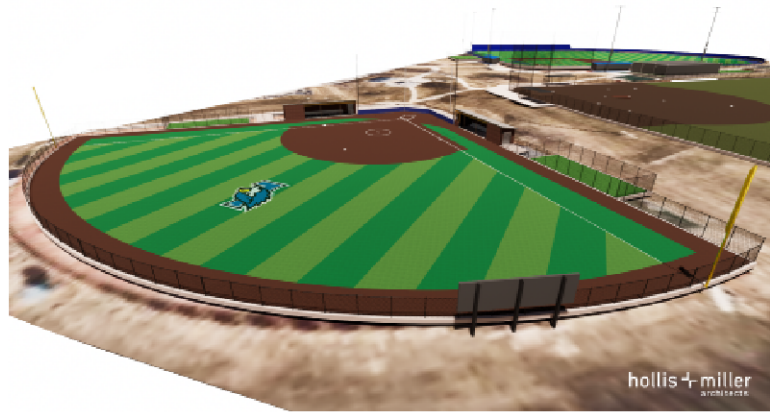

Liberty High School Baseball/Softball Complex

Baseball Field

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Pitching and Batting Practice areas

Softball Field

- New Dugouts
- Reduced Field Dimensions to 210' outfield, 25' Foul Territory, Softball
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

Multi-purpose Field

- Revised grading, perimeter fencing and infield improvements

Construction Start: Fall 2023

Construction Complete: Summer 2024

PROJECT STATUS

- LHS
- Baseball Backstop Footings Complete
 - Baseball Champion Wall Footings Complete
 - Baseball Fence Post & Perimeter Curb Complete
 - Aux Field Grading Ongoing
 - Aux MEP Underground Ongoing
 - Softball Field Demo & Grading Ongoing

UPCOMING

- LHS -
- Baseball Field Drainage / Rock
 - Baseball Turf Subgrade
 - Baseball Backstop Paving
 - Aux Finish Grading
 - Aux Fence Post & Perimeter Curb
 - Aux Irrigation Install
 - Softball Finish Grading
 - Softball MEP Underground
 - Softball Dugout Footings

Project Completion:
Baseball March 2024/Softball May 2024



LHS - Baseball



LHS - Baseball



LHS - Baseball



LHS - Baseball

WEEKLY PROGRESS REPORT



LHS - Multi-Purpose




LHS - Multi-Purpose



LHS - Multi-Purpose



LHS - Softball

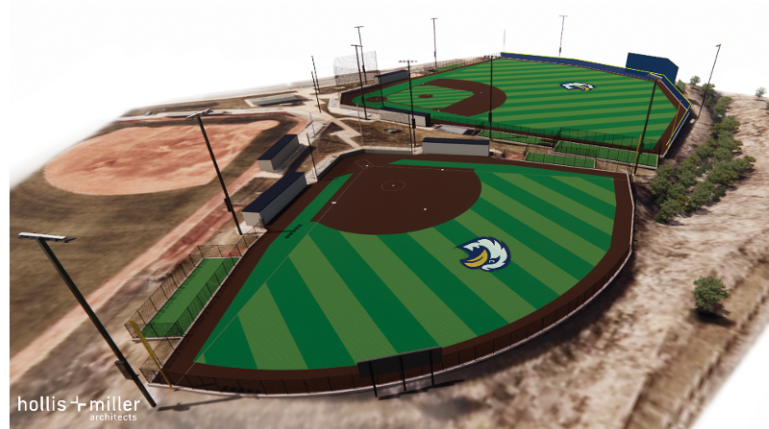

Liberty North High School Baseball/Softball Complex

Baseball Field

- Synthetic Turf Playing Surface & Tension Backstop Netting
- Upgraded Center field Batter's Eye
- Additional Bullpen Space
- ChampionWall PVC Athletic Fence System at Outfield

Softball Field

- Increased Field Dimensions - 194'(L) - 200'(C) - 195'(R)
- Synthetic Turf Playing Surface & Tension Backstop Netting
- Additional Bullpen Space

Construction Start: Fall 2023

Construction Complete: Summer 2024

**WEEKLY
PROGRESS
REPORT**

Baseball Softball 11/13/2023

Liberty Public Schools



PROJECT STATUS

- LNHS
- Baseball Backstop Footings Complete
 - Baseball Field Curb/ Fencing Complete
 - Baseball Turf Subgrade Ongoing
 - Baseball Champion Wall Footings Ongoing
- Softball Field Demo & Grading Complete

UPCOMING

- LNHS-
- Baseball MEP Underground
 - Baseball Backstop Paving
 - Baseball Fence Fabric
- Softball Finish Grading
- Softball Field Drainage
- Softball Fence Post & Perimeter Curb


Project Completion
Baseball March 2024/Softball May 2024



LNHS - Baseball



LNHS - Baseball

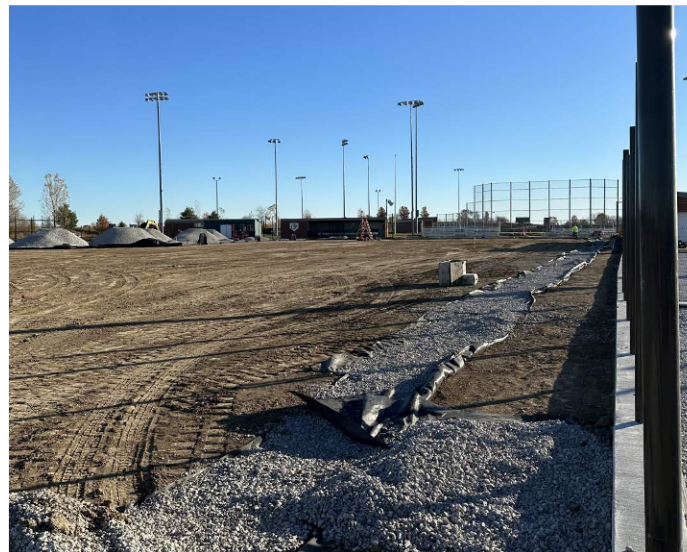

LNHS - Baseball



LNHS - Softball

WEEKLY PROGRESS REPORT



LNHS - Softball



LNHS - Softball



LED Lighting upgrades are planned throughout the District and will be sequenced with other projects as possible between the fall of 2023 through fall of 2026.

PROJECT STATUS

South Valley MS- Upgrades Complete

Discovery MS - Upgrades Complete


EPiC Elementary - Upgrades Complete

LNHS - Upgrades Ongoing


UPCOMING

Energy Inspections All Four Schools
Emergency LED Fixtures

Project Completion
December 2023

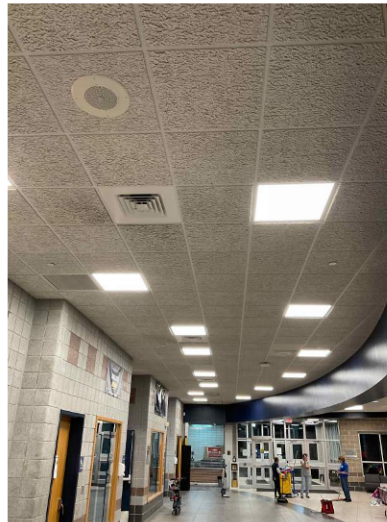


South Valley Middle School

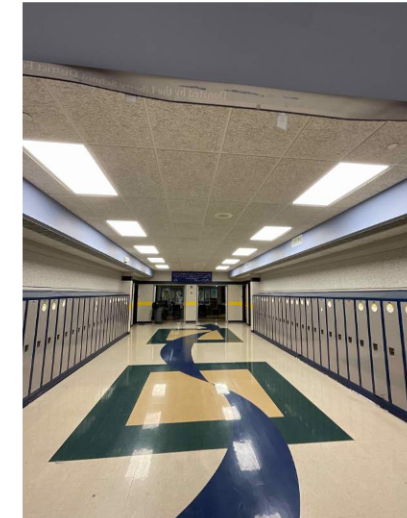

South Valley Middle School



Discovery Middle School

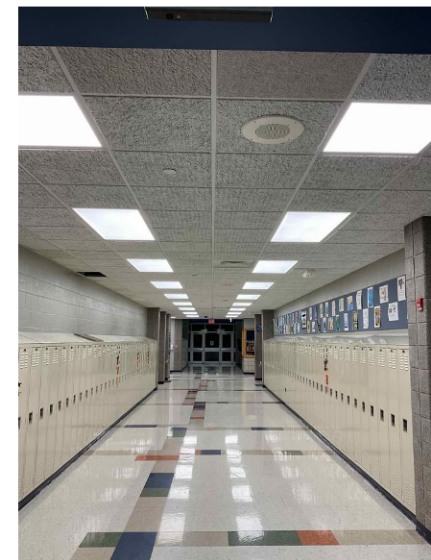

Discovery Middle School

WEEKLY PROGRESS REPORT



Epic Elementary




Epic Elementary



Liberty North High School




Liberty North High School

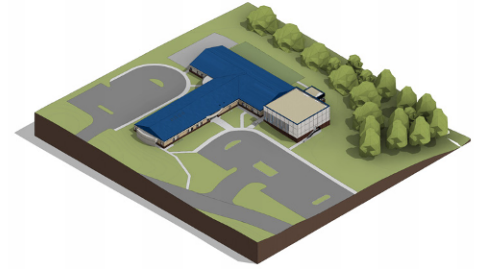


EPiC Elementary Addition

- 8000 Square Foot Building Addition & Renovation
- New Gym & Performance Space
- New Art Classroom
- Renovated Restrooms, Mother's Room and New Walk-in Cooler / Freezer
- Construction Start: Spring 2024
- Construction Complete: Summer 2025

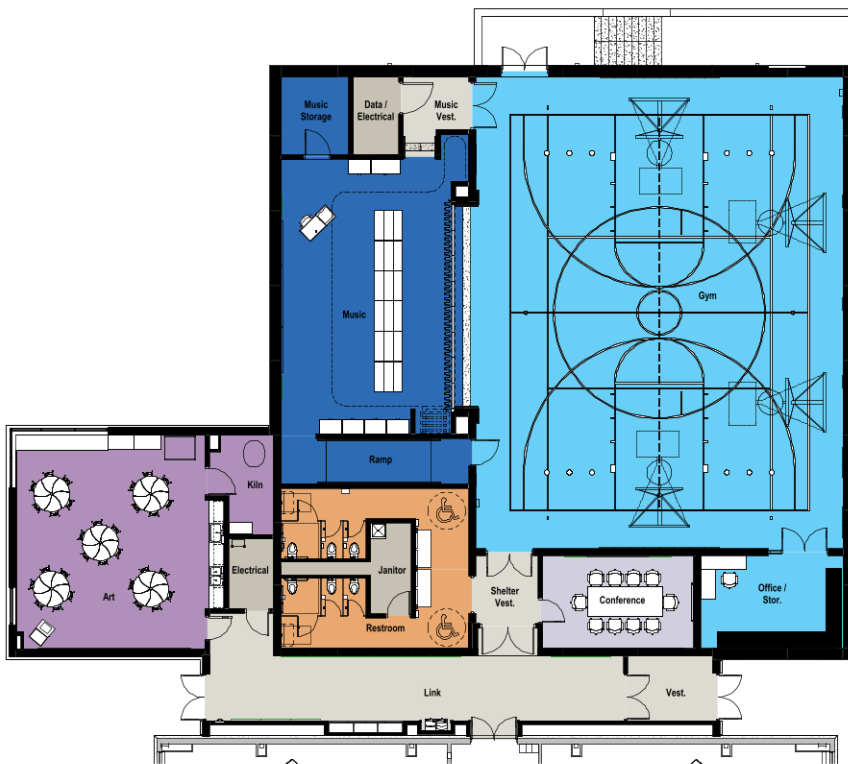

▲ Addition

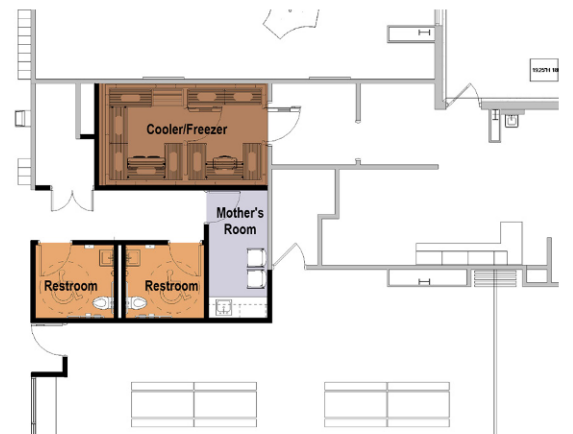



▲ Renovation Area



Discovery Middle School

- 11,000 square foot addition
 - ICC 500 rated shelter
 - Additional PE space
- Raised performance stage
- Theatrical AV and lighting
- Increased audience capacity
 - Additional storage
- Projected Construction Schedule:
Spring 2024–Summer 2025

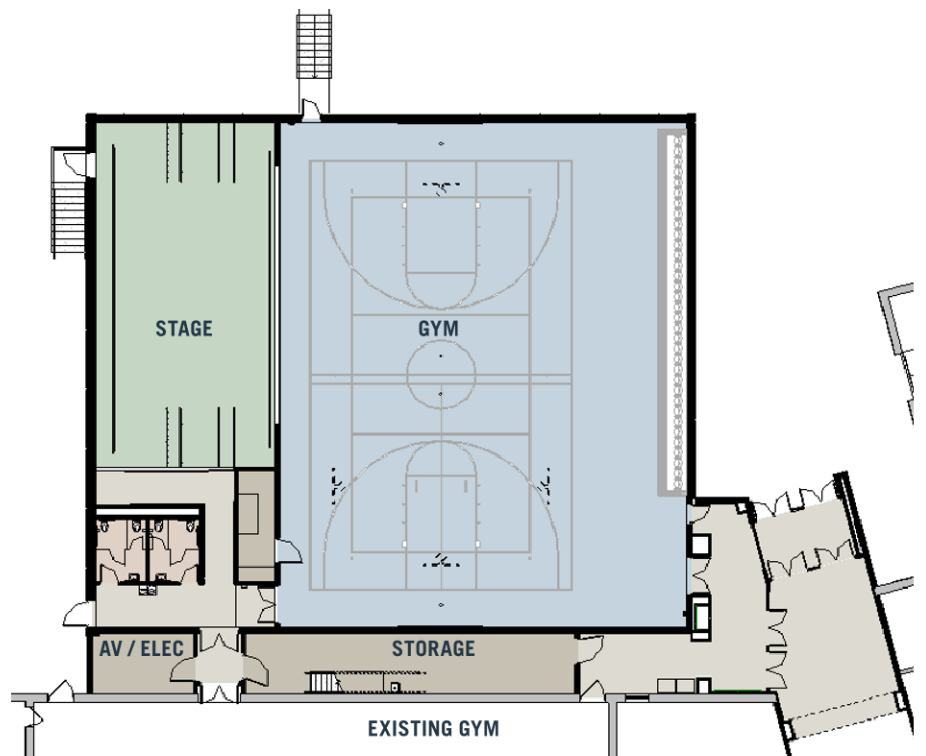

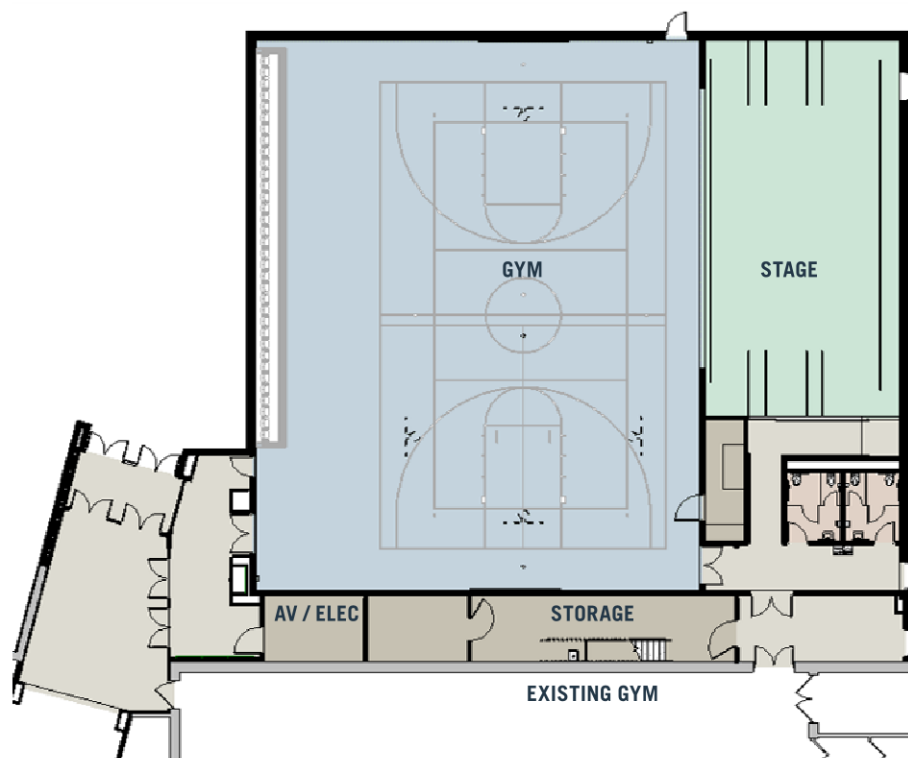

South Valley Middle School

- 11,000 square foot addition
- ICC 500 rated shelter
- Additional PE space
- Raised performance stage
- Theatrical AV and lighting
- Increased audience capacity
- Additional storage
- Projected Construction Schedule: Spring 2024–Summer 2025



hollis + miller



hollis + miller



hollis + miller



hollis + miller

Distribution Center

- 29,000 Square Foot New Building
- Storage Warehouse
- Dry Food Warehouse
- Large Storage Freezer
- New Office Space
- New Copy Center
- Additional Parking
- Projected Construction Schedule: Fall 2023–Spring 2025




Fine Arts
 Kid's Zone
 Technology
 Shared Amenities
 Building Systems
 Future Phase



District Technology Center

- Renovated workspace for District’s Technology, Fine Arts, and Kid’s Zone departments
- Shell space for future growth
- Minor exterior patch + repair improvements
- Projected Construction Schedule: Fall 2023 - Summer 2024

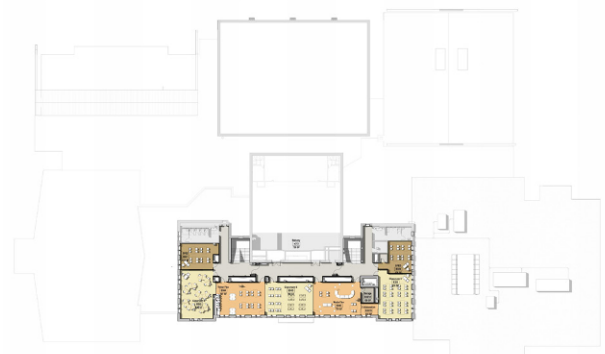

LEVEL 3



LEVEL 2



LEVEL 1



LEVEL 0

Heritage Middle School

- 39,000 square feet academic renovation
- Grade level neighborhoods with flex collaboration spaces
 - Integrated SPED resources
- Renovated cafeteria & scramble
 - Restroom renovations
- Exterior masonry repair & window replacement
 - Elevator replacement
- Projected Construction Schedule:
Spring 2024–Fall 2025
