




Monthly Progress Report

March 2026

Hempstead Union Free School District



Report prepared by Idris Mashriqi





Table of Contents

Section I – Program Summary

Section II – Work Progress **March 2026**

Section III – Work Projected for **April 2026**

Section IV – Progress Photos

Section V – Monthly Workforce Summary



Section I – Program Summary

March 2026

Project List

- **Hempstead UFSD – Phase 1 Infrastructure Upgrades @ HS – Closeout**
 - Staircase railings upgrades.
 - Classroom wall upgrades per code.
 - Install eye wash stations.
 - Install new exhaust fans.
 - Install new kitchen Ansul system valves.
- **Hempstead UFSD – Tennis Courts @ HS – Closeout**
 - Remove old asphalt tennis grounds.
 - Install new tennis courts with bleachers.
 - Install a bridge for students to access the tennis courts.
- **Hempstead UFSD – Window replacement at McNeil and Paterson elementary school – In Progress**
 - Removal of caulking under abatement.
 - Removal of existing windows.
 - Installation of new windows and new caulking.
- **Hempstead UFSD – Boiler replacement at McNeil elementary school – Closeout**
 - Boiler and piping replacement.
- **Hempstead UFSD – IAQ at Various School – In Progress**
 - Indoor air quality and mechanical upgrades.
 - Electrical upgrades.
- **Hempstead UFSD – 2022 Bond Phase 3 – In Progress**

Infrastructure upgrades throughout all schools.



Section II - Work Progress March 2026

Hempstead UFSD – HS Priority Infrastructure Upgrades

- **Total:**
 - Completed training to staff.

Hempstead UFSD – HS Tennis Courts

- **United Paving:**
 - Completed asphalt walkways.

Hempstead UFSD – Window replacement

- **Arrow Steel Windows:**
 - Completed window replacement at Paterson ES.
 - Started storefront door installation.

Hempstead UFSD – IAQ at Various Schools

- **Reliance:**
 - Started CO work on UVs.
 - Working on BMS for McNeil and Paterson.
- **Eldor:**
 - Continued roughing in ceilings and on walls at Paterson ES and McNeil ES.
 - Started swapping out old panels for new panels.
 - Continued roughing in Prospect ES.

Hempstead UFSD – 2022 Bond Phase 3

- **J Cole:**
 - Railing surveying.
 - Delivered conex box for elevator equipment.



Section III - Work Planned April 2026

Hempstead UFSD – HS Priority Infrastructure Upgrades

- **Total:**
 - Closeout

Hempstead UFSD – HS Tennis Courts

- **United Paving**
 - Closeout

Hempstead UFSD – Window replacement

- **Arrow steel windows**
 - Complete storefront doors and window film.

Hempstead UFSD – Boiler replacement

- **Thermotech:**
 - Closeout.

Hempstead UFSD – IAQ at Various Schools

- **Reliance:**
 - Install chiller pad and bollards at Prospect ES.
 - Completed chilled water piping.
 - Complete low voltage wiring.
 - Startup chiller and associated pumps.
- **Eldor:**
 - Complete all electrical upgrades at Paterson ES, McNeil ES, and Prospect ES.
 - Complete all panel swaps and switchovers.
 - Complete new transformer work at Paterson ES.



Section III - Work Planned April 2026

Hempstead UFSD – 2022 Bond Phase 3

- **J Cole:**
 - Power washing at Paterson ES.
 - Door replacements at McNeil Es.
 - Concrete work in courtyard and ramp at McNeil Es.
 - Start brick work at the HS.
- **IPS:**
 - Start sum pump work and grease trap at the HS.
- **RMS:**
 - Survey schools for duct drafting completion.
- **Eldor**
 - Start HS parking lot light pole replacements.




Section IV – Progress Photos



Hempstead IAQ – Paterson Transformer Pad



Section IV – Progress Photos

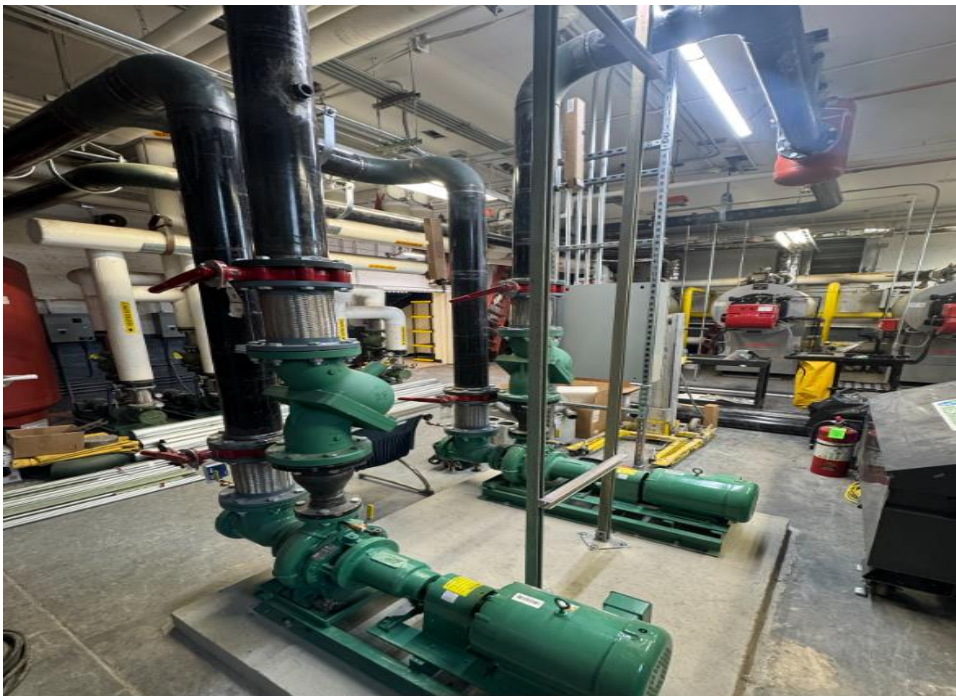

Hempstead IAQ – Prospect ES CHW Piping



Section IV – Progress Photos



Hempstead IAQ – McNeil ES Conduit Runs



Section IV – Progress Photos




Hempstead UFSD – Window Replacements



Section V – Workforce Summary – Company/Hours

March 2026

MANPOWER GRAPH

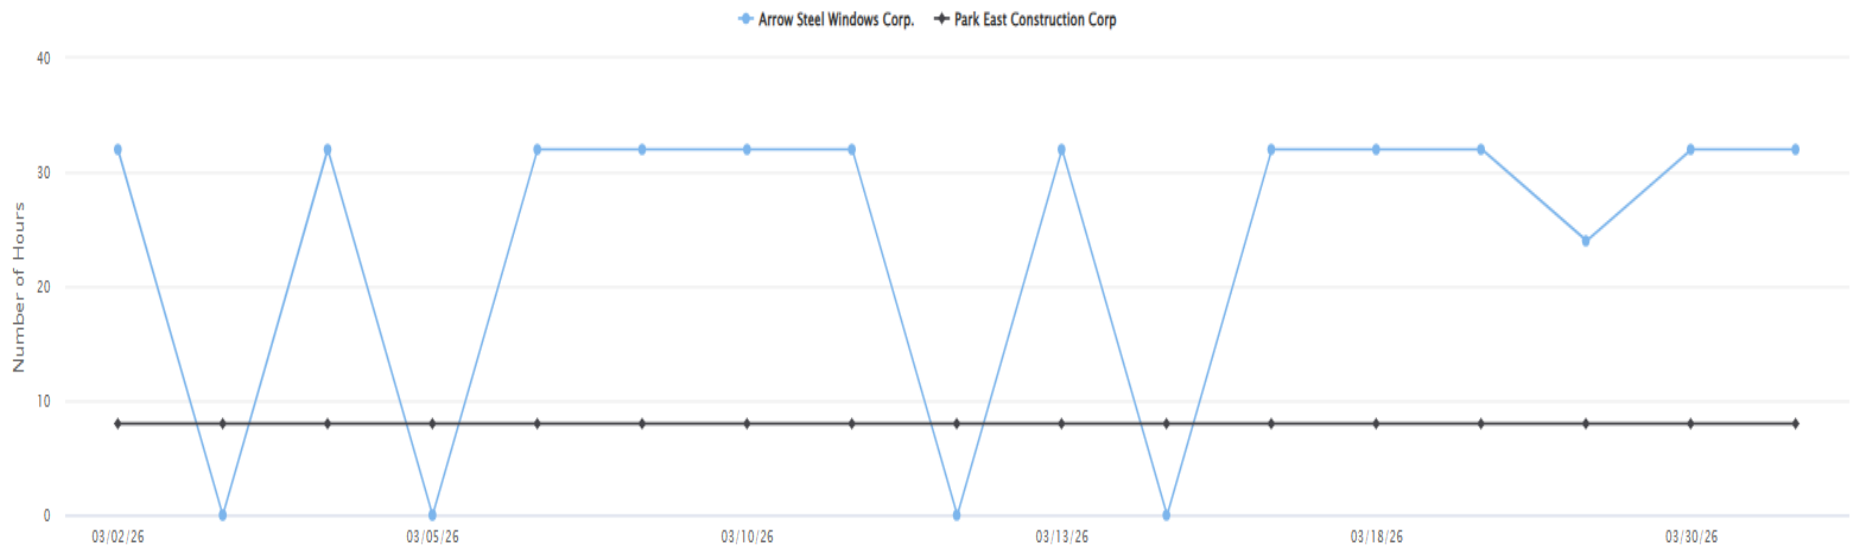


Hempstead UFSD – Window Replacement



Section V – Workforce Summary – Company/Hours

March 2026

MANPOWER GRAPH

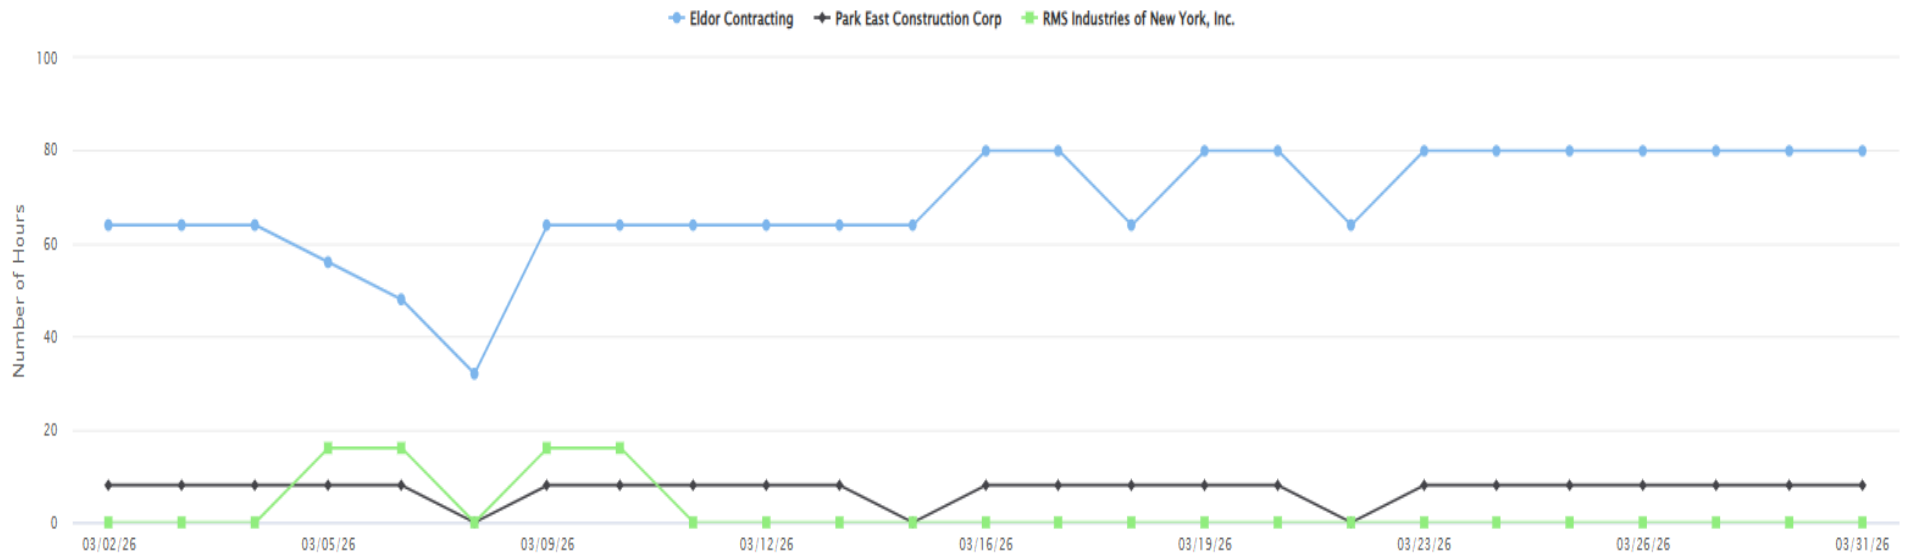


Hempstead UFSD – IAQ at Various Schools



Section V – Workforce Summary – Company/Hours

March 2026

MANPOWER GRAPH

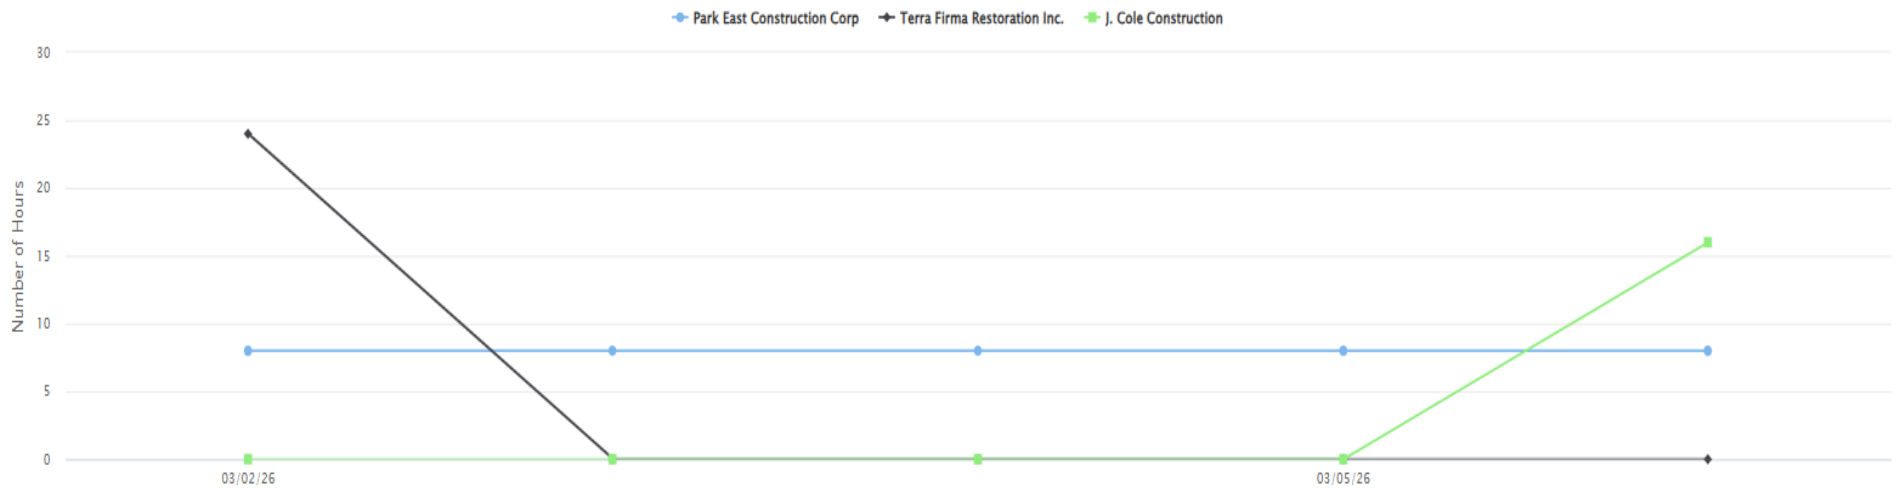

Hempstead UFSD – 2022 Bond Phase 3



Hempstead Union Free School District

March 2026

End of Progress Report
