

Bond Projects Program Update  
Board of Trustees Meeting  
April 9, 2026

Measure BB-2018

**New Laurelwood Elementary School at the Former Patrick Henry Site**

- Interior drywall and finishes are underway
- Parking lot construction is underway.
- PG&E is still working on the new electrical service.
- New sidewalks on Teal Drive are complete.
- The school is on track to open in August 2026.



View above Teal Drive on March 24, 2026. The office is on the right, classroom wings in the middle, and the multipurpose building on the left.



## Campus Modernization Program: Bracher, Briarwood and Westwood Elementary Schools.

- **Bracher Elementary School.**

- The multipurpose building slab is poured.
- Attempts to secure clean soil for the turf field have not yet been successful. Imported material must be tested and accepted as clean by the Department of Toxic Substances Control (DTSC). The quarry that supplied soil for the Agnews Campus is now closed. DTSC is assisting in locating a suitable source.
- A promising source of clean material has been located. Testing is underway.
- The building occupancy dates have changed from August to December.
- The geotextile barrier (the black material covering the field in the photo below) is being installed over native soil in the new turf areas. DTSC has required this material under all landscaped areas on the entire campus.
- Structural steel erection will begin in the next two weeks.



Aerial view looking northwest on March 25, 2026.



Geotechnical Barrier Under Turf



Multipurpose Building Floor Slab

**Briarwood Elementary School**

- The building steel shell is erected. Supports for roof solar panels are visible.
- Interior partition framing is underway.
- Pluming mechanical and electrical rough-in has started.
- Roofing will begin shortly.
- Contracts have been awarded for the Townsend Avenue street improvements.



Aerial View looking northeast on March 25, 2026.



New Classroom

## Westwood Elementary School



- Steel erection will be completed over a three-week period.
- The front parking lot is not available during this time.
- Working hours are being adjusted to accommodate testing days.
- The building occupancy dates have changed from August to December.



Views from the webcam in the rear playground looking toward the front parking lot. April 1, 2026  
This view highlights the difficulty in coordinating construction and school activities.

**New Valley High School Campus / Laurelwood Campus Reconfiguration**

- Schematic design is underway.
- The space program has been finalized.
- Structural and mechanical systems are being selected.
- Environmental and sustainability goals are being established.
- DTSC directed soils samples will be obtained next week.

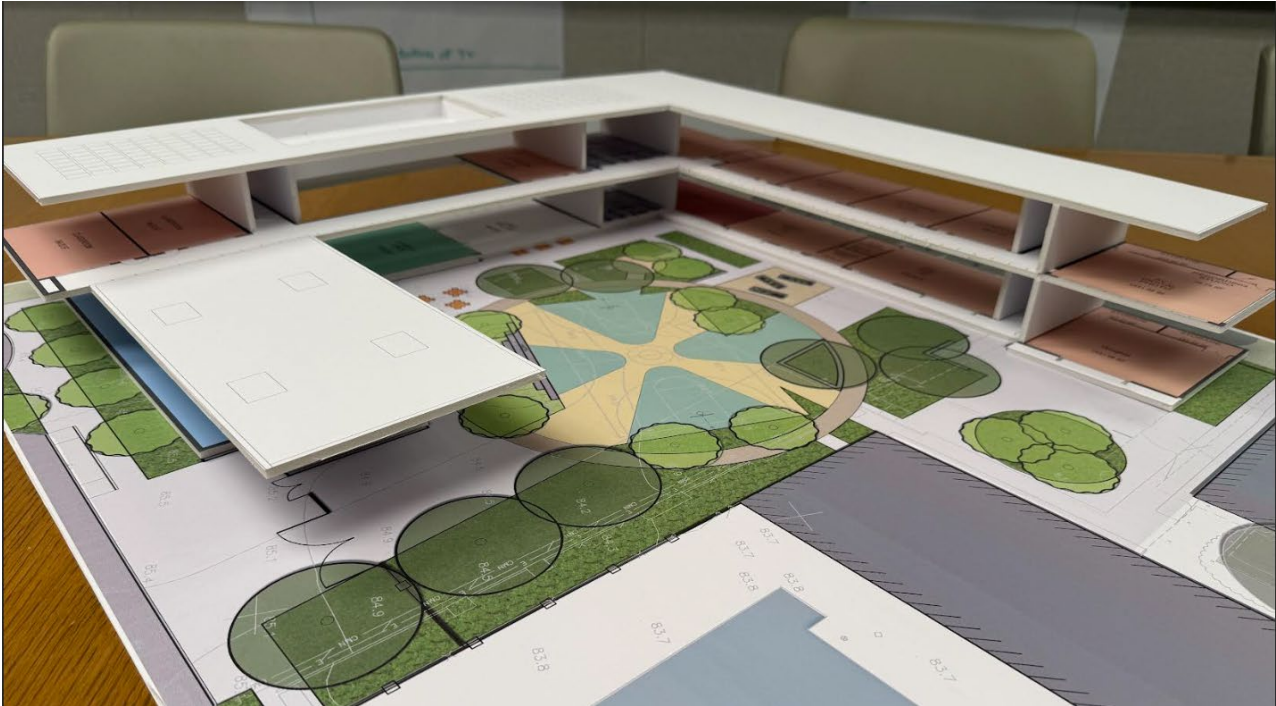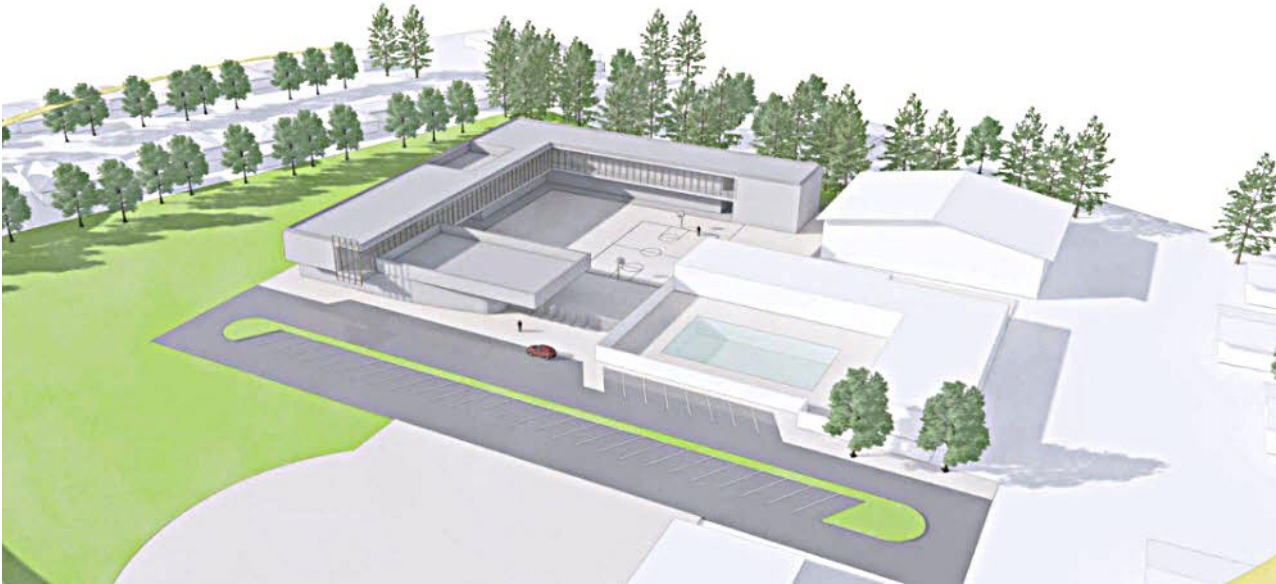

## Peterson Middle School Fields

- A Request for Statement of Qualifications (RFQ) is underway to select a new pool of architects. A request for proposals (RFP) for the project will then be issued.

## Measure H-2014

### Santa Clara High School Pool Modernization

- Underground piping is in progress.
- Significant reinforcing corrosion has been discovered. Repair procedures are being authorized to repair the pool shell
- Project completion will extend into the summer.




New drainage piping. Corroded steel reinforcing can be seen in the pool bottom. The new scoreboard will be installed on the Girl's locker building in the distance.

Corroded reinforcing bars

## Wilcox High School Pool Modernization

- The project has been advertised for bids.
- Work is planned to begin in June.

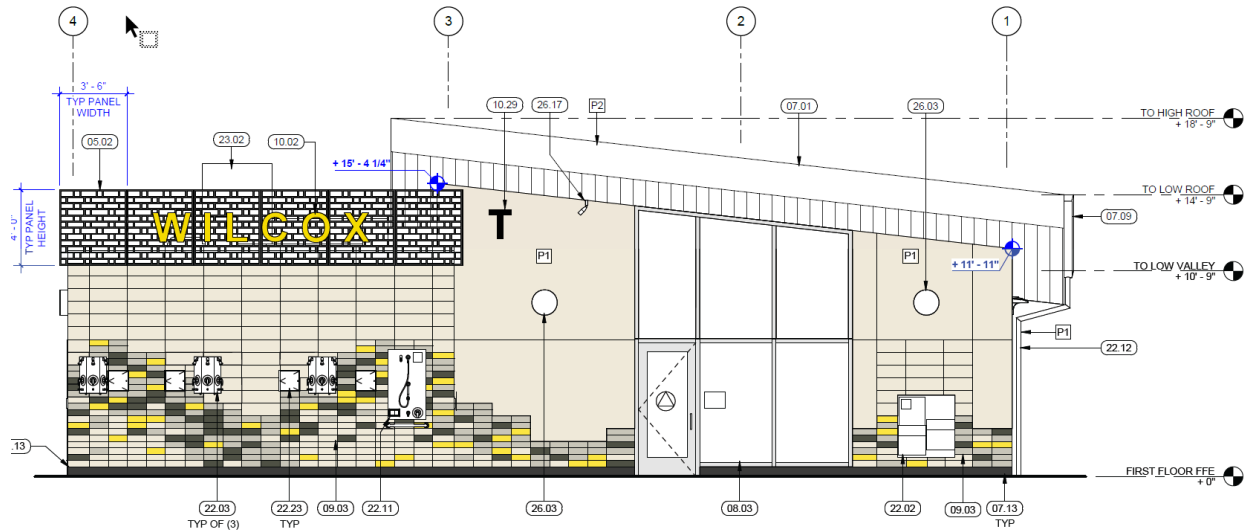

## Wilcox Pedestrian Bridge over Calabazas Creek



- Legal counsel has been retained to assist with negotiations with the Water District on the agreements for the new and existing bridges. The draft agreement requires an annual fee of \$27,900.00 per year, increasing 4% each year, for school use of the existing and new bridges.
- The Santa Clara Valley Water District response has been slow, fragmented, and inconsistent. Efforts to obtain a permit for a replacement bridge are entering a third year.
- The DSA bridge permit will expire next year. A new permit submittal will be required under a new building code edition.

[End]
