



Bond 2024 Oversight Committee Meeting #3

April 29, 2026

Agenda



- Recap of Proposition A
 - NMS Addition Project
- Update on Propositions A (New Elementary School) and C
- Review of Proposition B
 - JHS Kitchen Renovation and Cafeteria Expansion



Bond Construction Website



<https://www.joshuaisd.org/bond2024construction>

The Joshua ISD Bond 2024 construction update website serves as a platform to keep the JISD community informed about ongoing projects.

The website shares important information and provides updates, photos and progress on each project to engage our community.

These pages will be regularly updated.

Recap Proposition A - Nichols Middle School



Recap Proposition A - Nichols Middle School



CATEGORY	ORIGINAL AMOUNT	CHANGE ORDERS	TOTAL AMOUNT	EXPENDITURES as of 04/29/26
Direct Cost of Work	6,793,370	36,801	6,830,171	6,830,171
Professional Services	1,159,595	(101,221)	1,058,374	1,058,374
Furnishings, Technology, Misc.	305,052	987	306,039	306,039
Contingencies	276,426	(276,426)	-	-
TOTAL	8,534,443	(339,859)	8,194,584	8,194,584

SAVINGS
\$339,859

Update Proposition A - New Elementary



March 2026 Update: Despite weather delays, grade beams were formed and subgrade mechanical, electrical and plumbing were installed. Concrete slabs to support the building were poured.




Update Proposition C - JHS CTE Renovation & Expansion



Electrical work, interior framing and duct work have continued on the first level of the new structure, as well as steel erection and decking of the roof and lobby section. These tasks are expected to be completed soon. Waterproofing and brick work is underway. Fire sprinklers on the first floor and electrical on the second level will begin soon.



Update Proposition C - JHS CTE Renovation & Expansion

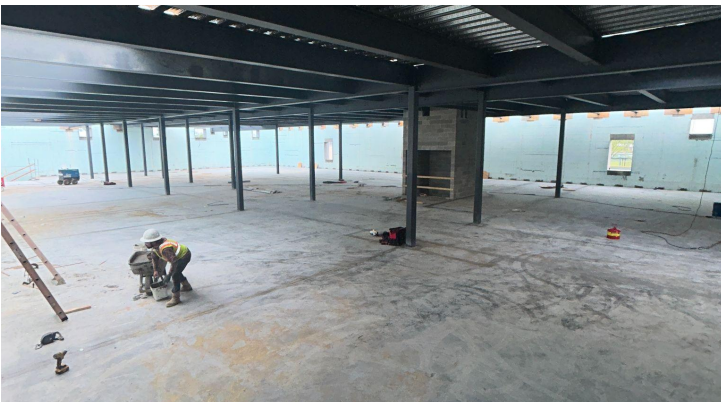

Review Proposition B - JHS Kitchen Renovation & Cafeteria Expansion CTE Site D



CATEGORY	ORIGINAL AMOUNT	CHANGE ORDERS	TOTAL AMOUNT	EXPENDITURES as of 04/29/26	AMOUNT REMAINING
Direct Cost of Work	10,326,596	551,440	10,878,036	10,603,181	274,855
Professional Services	1,434,978	5,054	1,440,032	1,312,736	127,296
Furnishings, Technology, Misc.	390,929	6,530	397,459	151,538	153,515
Contingencies	490,680	(490,680)	-	-	-
TOTAL	12,643,183	72,344	12,715,528	12,217,081	498,447

Review Proposition B - JHS Kitchen Renovation & Cafeteria Expansion

CTE Site D



Direct Cost of Work

BID PACKAGE	DESCRIPTION	AWARDED VENDOR	ORIGINAL PO AMOUNTS	CHANGE ORDERS	TOTAL PURCHASE AMOUNT	Prop C	Prop B, Int	TOTAL EXPENSES as of 04/29/26	AMOUNT REMAINING
						CTE Site D Expenses	Cafeteria / Kitchen Expenses		
01a	General Requirements	Crossland Construction	\$ 289,226	\$ -	\$ 289,226	\$ -	\$ 235,578	\$ 235,578	\$ 53,648
02A	Demolition	SW Construction Services	\$ 132,990	\$ 48,660	\$ 181,650	\$ 31,500	\$ 150,150	\$ 181,650	\$ -
03A	Cast-in-Place Concrete	JDS Contractors	\$ 717,000	\$ 69,801	\$ 786,801	\$ -	\$ 786,801	\$ 786,801	\$ -
03B	Concrete Staining & Polishing	CCC Allowance	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
04A	ICF/ Masonry	GG&S	\$ 241,300	\$ 34,980	\$ 276,280	\$ -	\$ 276,280	\$ 276,280	\$ -
05A	Structural & Miscellaneous Steel	Tippen Steel Services, Inc.	\$ 301,000	\$ 14,760	\$ 315,760	\$ 23,596	\$ 289,035	\$ 312,631	\$ 3,129
06A	Woods and Plastics	NWC Commercial Millwork	\$ 40,895	\$ 2,740	\$ 43,635	\$ 28,500	\$ 15,135	\$ 43,635	\$ -
07A	Roofing	Durolast, Prime Source	\$ 270,133	\$ 80,400	\$ 350,533	\$ -	\$ 349,609	\$ 349,609	\$ 924
07B	Waterproofing - incl w 02A	SW Construction Services	\$ -	\$ -	\$ -	\$ -		\$ -	\$ -
07C	Spray Foam Insulation	Bahl Fireproofing	\$ 33,240	\$ -	\$ 33,240	\$ -	\$ 33,240	\$ 33,240	\$ -
08A	Doors & Hardware	Woodard Builders Supply	\$ 61,450	\$ 26,333	\$ 87,783	\$ 18,300	\$ 69,288	\$ 87,588	\$ 195
08B	Glass & Glazing	Layne Glass Company	\$ 335,907	\$ 6,263	\$ 342,170	\$ 21,099	\$ 321,071	\$ 342,170	\$ -
09A	Drywall & Acoustical	Rice Drywall	\$ 450,600	\$ 82,916	\$ 533,516	\$ 90,700	\$ 384,216	\$ 474,916	\$ 58,600
09B	Flooring (Owner Direct)	Vector	\$ 301,728	\$ -	\$ 301,728	\$ 52,270	\$ 217,882	\$ 270,153	\$ 31,576
09C	Tile	PDL Designs	\$ 152,795	\$ 44,115	\$ 196,910	\$ 26,794	\$ 153,845	\$ 180,640	\$ 16,271
09E	Painting	Ray Noteboom	\$ 95,073	\$ 10,172	\$ 105,245	\$ -	\$ 81,130	\$ 81,130	\$ 24,115
10A	Misc Specialties	Texas Specialties	\$ 21,340	\$ 8,875	\$ 30,215	\$ 12,070	\$ 18,145	\$ 30,215	\$ -
10B	Signage	Pinnacle	\$ 12,550	\$ 2,100	\$ 14,650	\$ -	\$ -	\$ -	\$ 14,650
10C	Pre-Fabricated Canopies	Avadek, Inc.	\$ 54,635	\$ -	\$ 54,635	\$ -	\$ 54,635	\$ 54,635	\$ -
10E	Lockers - incl w 10A	CCC Allowance	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
11A	Food Service Equipment	Oswalt Restaurant Supply	\$ 2,711,246	\$ 5,545	\$ 2,716,791	\$ -	\$ 2,716,791	\$ 2,716,791	\$ -

Review Proposition B - JHS Kitchen Renovation & Cafeteria Expansion

CTE Site D



Direct Cost of Work (continued)

BID PACKAGE	DESCRIPTION	AWARDED VENDOR	ORIGINAL PO AMOUNTS	CHANGE ORDERS	TOTAL PURCHASE AMOUNT	Prop C	Prop B, Int	TOTAL EXPENSES as of 04/29/26	AMOUNT REMAINING
						CTE Site D Expenses	Cafeteria / Kitchen Expenses		
21A	Fire Protection	Highland Fire Protection	\$ 83,925	\$ 9,913	\$ 93,838	\$ 16,211	\$ 77,628	\$ 93,838	\$ -
22A	Plumbing	Witt Plumbing	\$ 561,017	\$ 2,056	\$ 563,073	\$ 63,351	\$ 499,722	\$ 563,073	\$ -
23A	HVAC	Logical Control Services	\$ 668,280	\$ 39,827	\$ 708,107	\$ 104,965	\$ 603,142	\$ 708,107	\$ -
23Aa	HVAC	Texas Air	\$ 663,616	\$ (68,385)	\$ 595,231	\$ 148,620	\$ 446,611	\$ 595,231	\$ -
26A	Electrical	Double Eagle	\$ 1,370,000	\$ 46,623	\$ 1,416,623	\$ 30,835	\$ 1,385,788	\$ 1,416,623	\$ (0)
27A	Communications	TFE Connect	\$ 115,968	\$ 5,052	\$ 121,020	\$ 97,871	\$ 23,149	\$ 121,020	\$ -
27B	Audio/Visual	Master Audio Visual, Inc.	\$ 80,881	\$ -	\$ 80,881	\$ 3,203	\$ 77,678	\$ 80,881	\$ -
27C	Intercom	Lonestar	\$ 23,900	\$ -	\$ 23,900	\$ -	\$ 23,900	\$ 23,900	\$ -
27D	Networking (Owner Direct)	NetSync	\$ 72,833	\$ -	\$ 72,833	\$ -	\$ 64,254	\$ 64,254	\$ 8,579
28A	Fire Alarm	Texas Fire & Cabling	\$ 66,918	\$ 2,500	\$ 69,418	\$ 12,125	\$ 57,293	\$ 69,418	\$ -
28B	Access Control/Security - incl w/ 27A	TFE Connect	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
31A	Earthwork	Select Excavation	\$ 71,579	\$ 13,176	\$ 84,755	\$ -	\$ 84,755	\$ 84,755	\$ -
31B	Erosion Control - incl w/ 31A	Select Excavation	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
31C	Termite Control - through Crossland 01A	CCC Allowance	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
32A	Landscaping & Irrigation - through Crossland 01A	Legacy	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
32E	Pavement Markings - through Crossland 01A	CCC Allowance	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -	\$ -
32F	Fencing	Prime Source	\$ 15,998	\$ 48,500	\$ 64,498	\$ -	\$ -	\$ -	\$ 64,498
33A	Site Utilities	Maverick	\$ 244,133	\$ 14,518	\$ 258,651	\$ -	\$ 258,651	\$ 258,651	\$ -
Construction Manager Agent - Liability Ins		Crossland Construction	\$ 51,521	\$ -	\$ 51,521	\$ 4,044	\$ 47,477	\$ 51,521	\$ -
Construction Manager Agent - Preconstruction Phase		Crossland Construction	\$ 12,919	\$ -	\$ 12,919	\$ -	\$ 12,919	\$ 12,919	\$ -
Construction Manager Agent - Reimbursables		Crossland Construction	\$ -	\$ -	\$ -	\$ -	\$ 1,329	\$ 1,329	\$ (1,329)
SUBTOTAL DIRECT COST OF WORK			\$10,326,596	\$ 551,440	\$ 10,878,036	\$ 786,054	\$ 9,817,127	\$10,603,181	\$ 274,855

Review Proposition B - JHS Kitchen Renovation & Cafeteria Expansion CTE Site D



Professional Services

BID PACKAGE	DESCRIPTION	AWARDED VENDOR	ORIGINAL PO AMOUNTS	CHANGE ORDERS	TOTAL PURCHASE AMOUNT	Prop C	Prop B, Int	TOTAL EXPENSES as of 04/29/26	AMOUNT REMAINING
						CTE Site D Expenses	Cafeteria / Kitchen Expenses		
Construction Manager Agent - 6% of Const Cost		Crossland Construction	\$ 736,019	\$ -	\$ 736,019	\$ -	\$ 620,493	\$ 620,493	\$ 115,526
Architect - 6.5% of Const Cost; Reimbursables		WRA Architects	\$ 609,519	\$ -	\$ 609,519	\$ -	\$ 600,707	\$ 600,707	\$ 8,812
Builders Risk Insurance		USI Insurance Services, IMA	\$ 49,989	\$ 5,054	\$ 55,043	\$ -	\$ 55,043	\$ 55,043	\$ -
Construction Materials Testing		UES Professional Services	\$ 25,000	\$ -	\$ 25,000	\$ -	\$ 22,042	\$ 22,042	\$ 2,958
Asbestos Sampling & Inspection		TASB Facility Services	\$ 3,656		\$ 3,656	\$ -	\$ 3,656	\$ 3,656	\$ -
Permits		City of Joshua, TX Dept of HHS	\$ 10,795	\$ -	\$ 10,795	\$ -	\$ 10,795	\$ 10,795	\$ -
SUBTOTAL PROFESSIONAL SERVICES			\$ 1,434,978	\$ 5,054	\$ 1,440,032	\$ -	\$ 1,312,736	\$ 1,312,736	\$ 127,296

Review Proposition B - JHS Kitchen Renovation & Cafeteria Expansion

CTE Site D (DAEP)



Furnishings, Technology, Contingencies

			Prop C		Prop B, Int				
BID PACKAGE	DESCRIPTION	AWARDED VENDOR	ORIGINAL PO AMOUNTS	CHANGE ORDERS	TOTAL PURCHASE AMOUNT	CTE Site D Expenses	Cafeteria / Kitchen Expenses	TOTAL EXPENSES as of 04/29/26	AMOUNT REMAINING
Furniture		Virco	\$ 381,164	\$ 3,957	\$ 385,121	\$ -	\$ 288,825	\$ 288,825	\$ 96,295
Technology, Small Items		Shi, Various	\$ 9,765	\$ 2,574	\$ 12,339	\$ 329	\$ 12,010	\$ 12,339	\$ -
Contingencies			\$ 490,680	\$ (490,680)	\$ -	\$ -	\$ -	\$ -	\$ -
SUBTOTAL FFE AND CONTINGENCIES			\$ 881,609	\$ (484,149)	\$ 397,459	\$ 329	\$ 300,835	\$ 301,164	\$ 96,295
TOTALS			\$ 12,643,183	\$ 72,344	\$ 12,715,528	\$ 786,383	\$ 11,430,698	\$ 12,217,081	\$ 498,447

Update Proposition B - Kitchen/Cafeteria



April 2026 Update: Started serving students after spring break.





Next Meeting

Late September

Tour of Completed Portion of CTE Renovation



Questions and Tour



Thank you!
