



Report Date	09 / 24 / 2026
Project Name/Number	Group 5 Security Vestibules Project Kelley Lake ES / 23736, Lithonia MS / 31036, Tucker HS / 42136
Facility Name	Kelley Lake ES, Lithonia MS, Tucker HS
Area Superintendent	Damian Bounds
Principal	LaToya Carmichael, Dr. Cornelius Polk, Dr. Eric Parker
School Contact	Principals at All Schools
Project Manager	Joseph King and Jamison Owen
Architect	CROFT Associates
Contractor	Lefko Construction

Scope of Work:

Install security vestibules in each of the following schools. These three schools originally were a part of Security Vestibule Group 1 and got re-bundled into an entirely new "Group 5 Project".

Project Construction Budget: Kelley Lake ES: \$325,268.05, Lithonia MS: \$494,076.83, Tucker HS: \$408,481.56

Project Schedule Milestones:

- Design Completion: December 2025 (Revised Drawings)
- General Contractor Procurement: March 2025
- Construction Start: March 13th, 2026 (KLES) , April 27th, 2026 (LMS) , May 26th, 2026 (THS)
- Construction End: June 10th, 2026 (KLES) , July 7th, 2026 (LMS) , July 9th, 2026 (THS)

Current Project Status:

- Lefko Construction has completed the punch list items at Kelley Lake Elementary School and currently working on collecting all closeout documents.
- The Project Team conducted a Punchlist Meeting at Lithonia Middle School on Tuesday, 07/07, and at Tucker High School on Thursday, 07/09, where substantial completion was achieved and a final punch list was created.
- Lefko Construction has nearly completed all punch list items and has now shifted to night work for the remaining tasks after all front office staff has moved back into their spaces during the work day.


4-Week Look Ahead

- All three projects are currently collecting closeout documentation to be packaged and sent to the A/E for final approval. Both Lithonia Middle School and Tucker High School have been given punch lists to complete; after all tasks have been completed.
-

Project Photographs



Floor at Doorframe at Lithonia Middle School

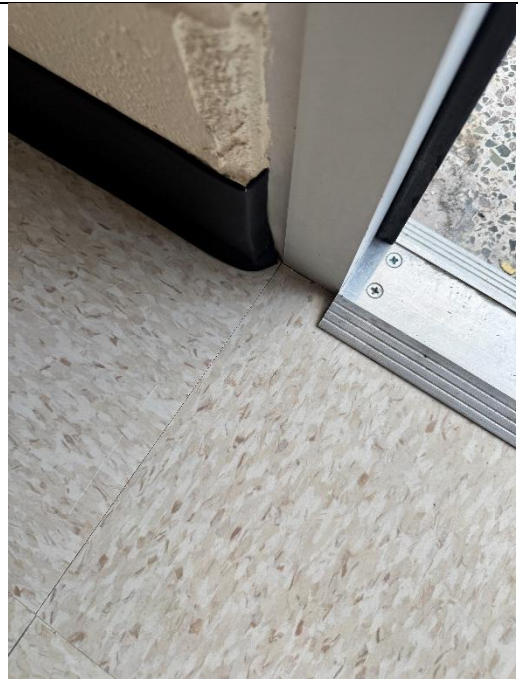

Floor at Doorframe at Lithonia Middle School



Door Closure Hardware at Tucker High School



Door Closure Hardware at Tucker High School
