

Liberty High School Tennis

- (8) Competition Tennis Courts
- Post-Tensioned Concrete slab with DecoTurf brand acrylic surfacing
- 10'-0" tall perimeter fence with windscreen
- Retaining wall and asphalt parking lot improvements

Construction Start: Spring 2023

Construction Complete: Fall 2023

PROJECT STATUS

- Retaining wall complete.
- Site Utilities Complete
- Parking Lots at rough grade
- PT Tennis Courts at final grade.

UPCOMING


- Fence Posts being set
- North and South Court Slabs Pouring this month.
- Site Concrete and Light Pole Bases pouring in the next 3 weeks.



North Court Vapor Barrier for PT Slab



Site Fencing

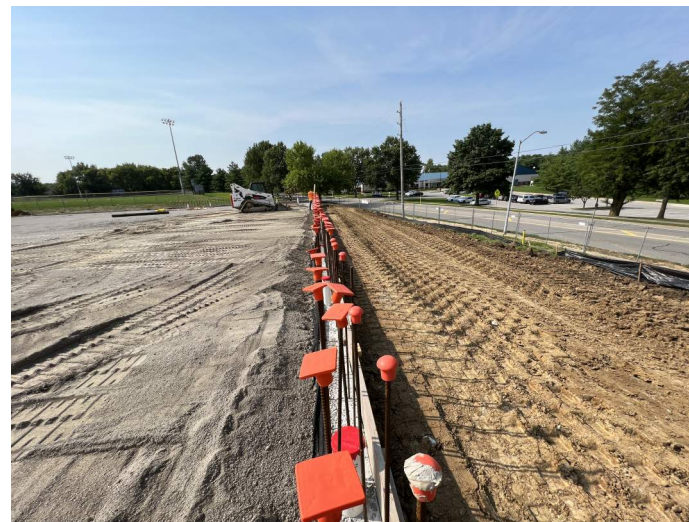

Looking South at Wall



Looking North from South Courts

WEEKLY PROGRESS REPORT



Site Storm Boxes / Drainage



Utility Excavation
