



CONSTRUCT 6'-8' WIDE PATH  
REGRADE, STONE BASE, PAVEMENT  
L = 3950 FEET  
CONSTRUCTION COST = \$200,000 (2008 ONLY)

**PHASE 3**  
**CONSTRUCTION 2024**  
NARROW ROADWAY FOR PATH AS PART OF  
FUTURE ROADWAY RECONSTRUCTION  
L = 3900 FEET  
BID CONSTRUCTION COST = \$939,000

CONSTRUCT 10' WIDE ASPHALT PATH  
REMOVE TREES, REGRADE, STONE BASE, BITUMINOUS SURFACE  
LANDSCAPE, MODIFY I-84 RAMPS AND PROVIDE TRAIL CROSSING  
L = 3030 FEET  
FINAL CONSTRUCTION COST = \$380,708

 EXISTING PAVED TRAIL  
 EXISTING UNPAVED TRAIL  
 TRAIL UNDER CONSTRUCTION  
 PROPOSED TRAIL


BE COORDINATED WITH REDEVELOPMENT  
OF 1800 ASYLUM AVENUE  
L = TBD  
EST. CONSTRUCTION COST TBD

CONSTRUCT 8'-10' WIDE ASPHALT PATH  
L = 700 FEET  
FINAL CONSTRUCTION COST (\$54,291)

**PHASE 6  
COMPLETED 2023**  
CONSTRUCT 10' WIDE ASPHALT PATH  
REGRADE, STONE BASE  
BIT. SURFACE, PLANT TREES  
L = 2890 FEET  
D.E.E.P. EASEMENT OBTAINED  
CONSTRUCTION COST \$1,246,092

**PHASE 5  
COMPLETED 2022**  
CONSTRUCT 10' WIDE ASPHALT PATH  
L = 2990 FEET  
REGRADE, STONE BASE  
BIT. SURFACE, PLANT TREES  
D.E.E.P. EASEMENT OBTAINED  
FINAL CONSTRUCTION COST \$807,212

CONSTRUCT 8' WIDE ASPHALT PATH  
ON TOP OF EXIST. FLOOD CONTROL DIKE  
D.E.E.P. APPROVAL REQUIRED  
L = 2500 FEET  
CONSTRUCTION COST = \$185,000

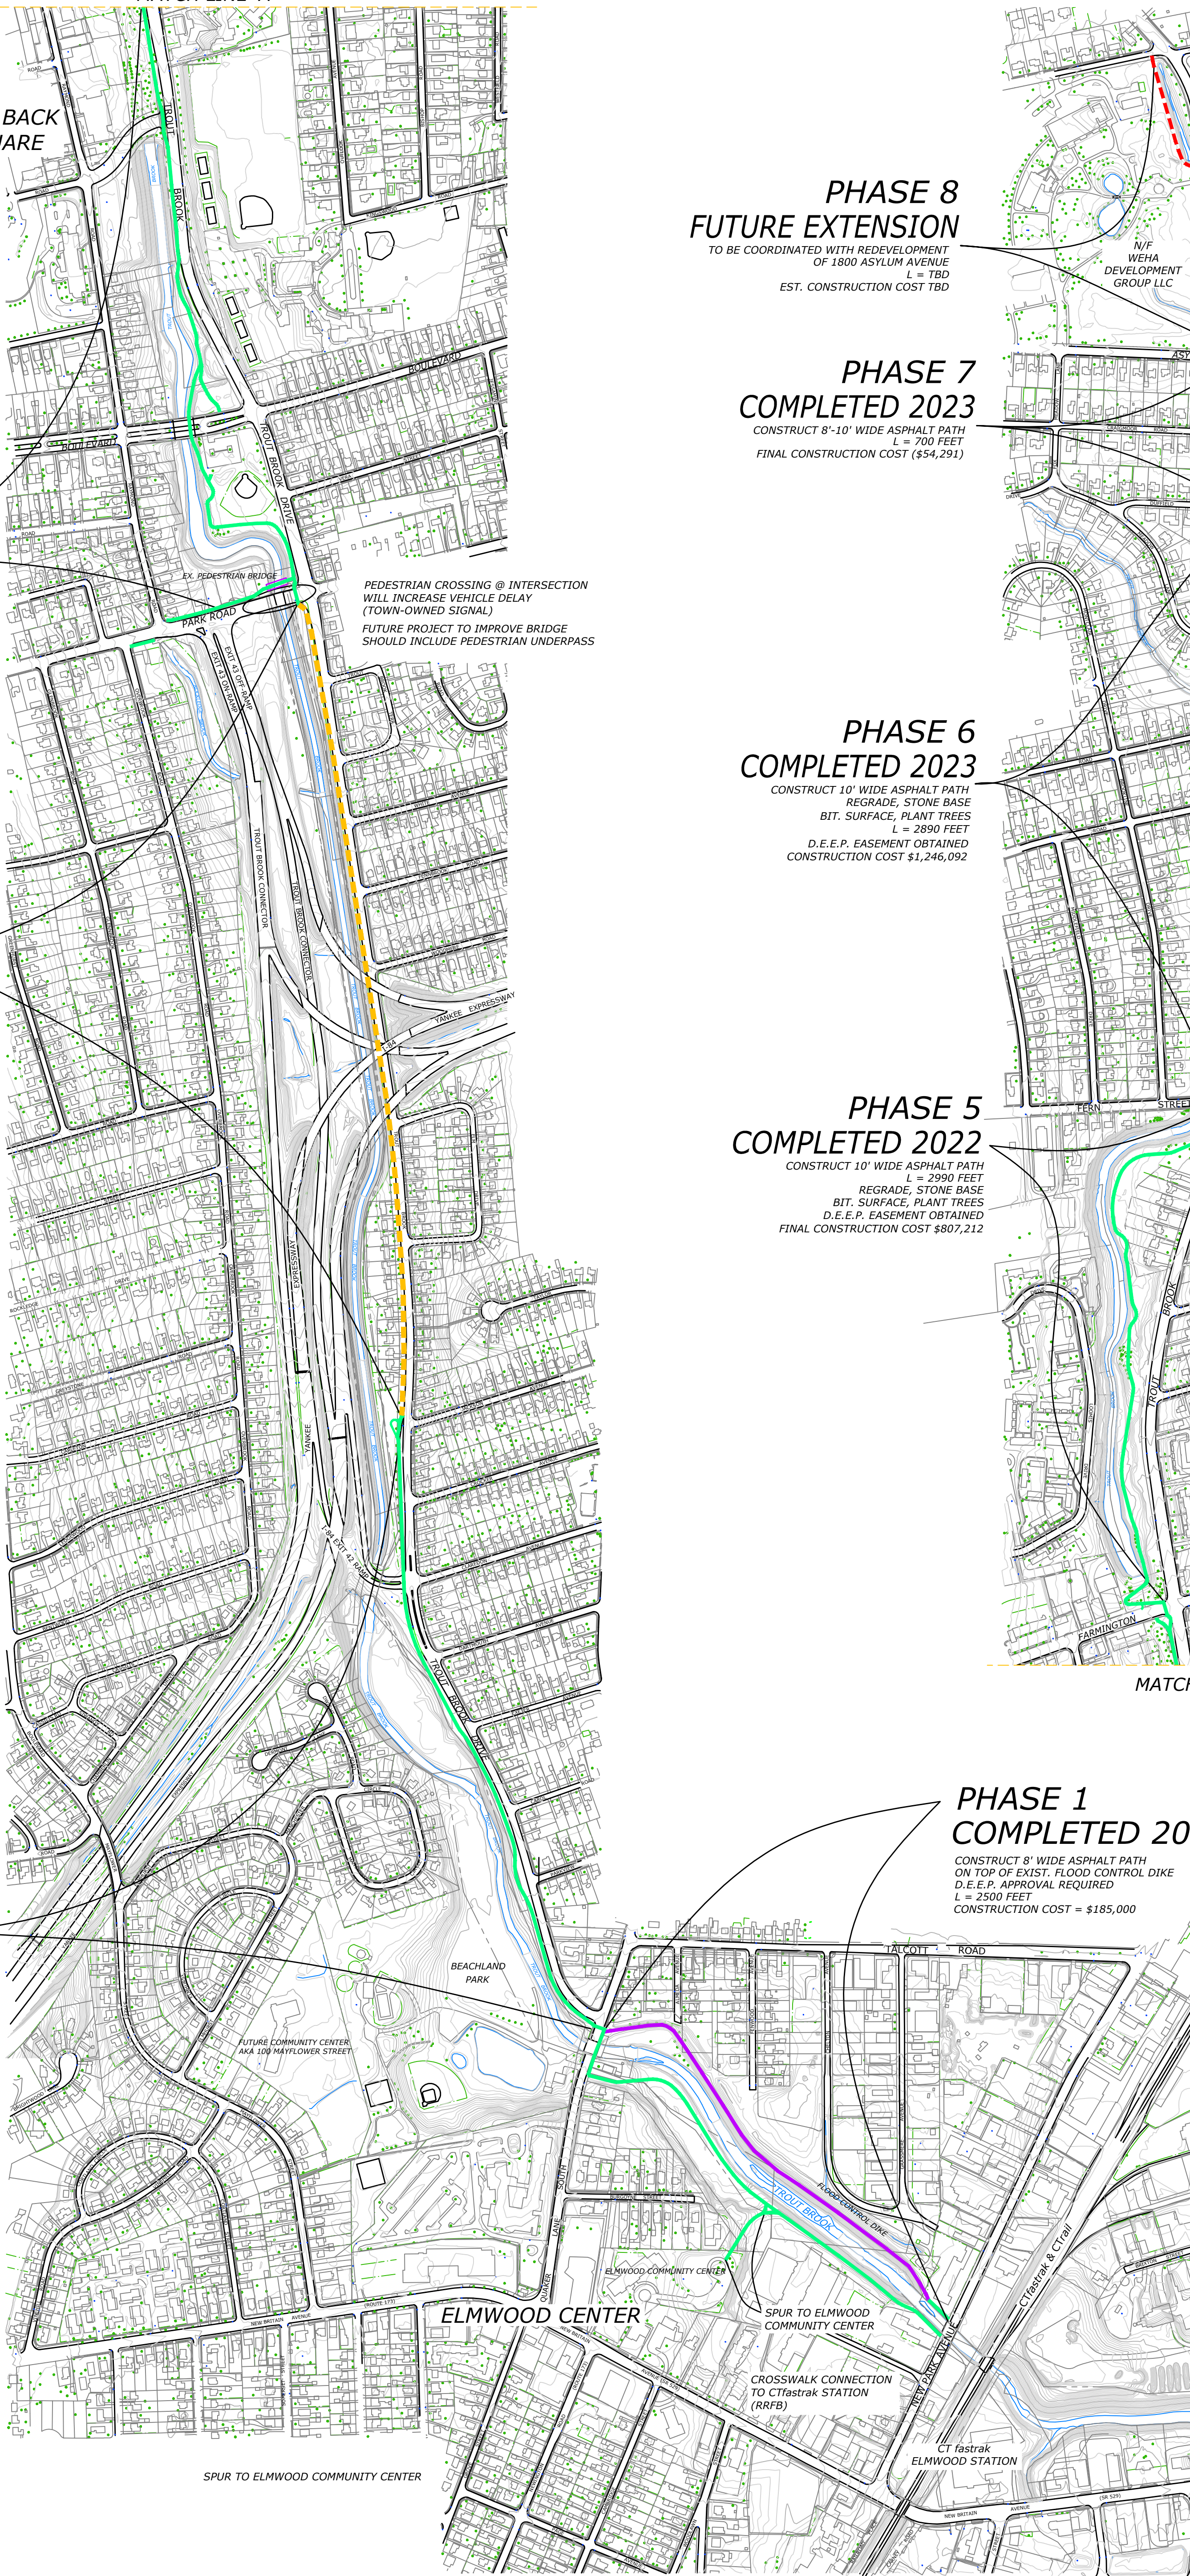

# **TROUT BROOK TRAIL OVERALL PROJECT PLAN**

NEW PARK AVENUE TO ASYLUM AVENUE

**DATE: AUGUST 2024**
