


SEQUENCE A: 05/15/25 - 12/31/26

General Notes:

1. Reference Scope of Work and Special Provisions for responsibility of temporary construction / facilities as shown.
2. Site Work Contractor to install and maintain temporary site fencing and entry/exit gates for the duration of the Middle School renovations. Gate 2 shall be the primary entrance / exit gate for construction use. Include wheels to minimize wearing of existing asphalt surface. Existing gate access to be coordinated with the Owner and CM.
3. General Trades Contractor to provide dumpsters and temporary toilet facilities for the duration of the Middle School renovations. Dumpster locations do not represent quantities. Refer to Special Provisions and Scope of Work for dumpster requirements. Include plywood surfacing for underneath dumpsters for protection of asphalt.

3. General Trades Contractor to provide dumpsters and temporary toilet facilities for the duration of the Middle School renovations. Dumpster locations do not represent quantities. Refer to Special Provisions and Scope of Work for dumpster requirements. Include plywood surfacing for underneath dumpsters for protection of asphalt.

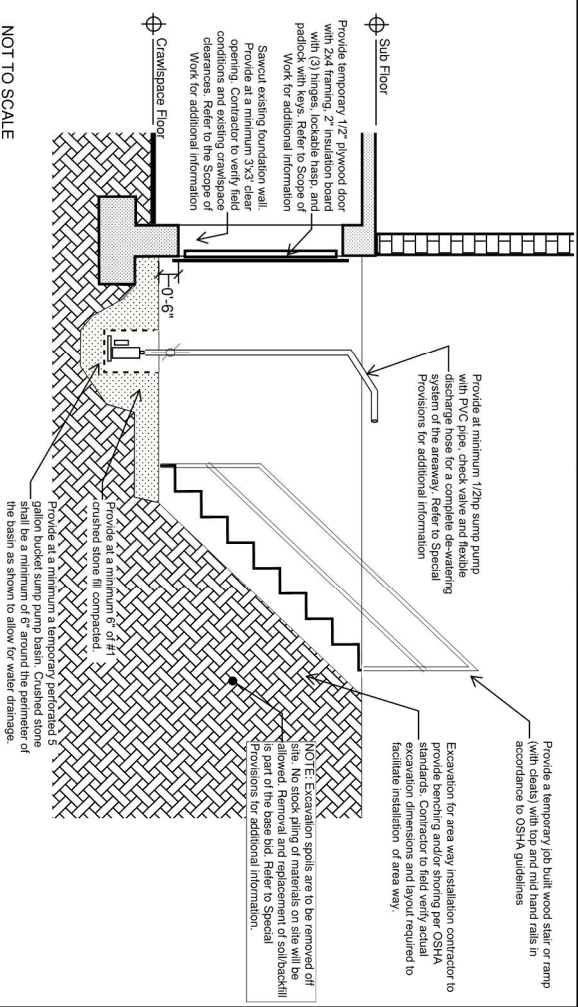

Provide at a minimum a temporary perforated 5 gallon bucket sump pump basin. Crushed stone shall be a minimum of 6" around the perimeter of the basin as shown to allow for water drainage.

IN ADDITION TO THE AREAWAY DETAIL BELOW, CONTRACTOR IS RESPONSIBLE TO PROVIDE THE REQUIREMENTS NOTED IN THE SCOPE OF WORK AND SPECIAL PROVISIONS. CONTRACTOR IS ADVISED CLEARANCES/ELEVATIONS DIFFER IN EACH LOCATION. CONTRACTOR SHALL ASSUME 8'-6" EXCAVATION DEPTH AT A MINIMUM IN THEIR BASE BID. CONTRACTOR TO VERIFY ALL SITE CONDITIONS, CLEARANCES AND ELEVATIONS TO ESTABLISH PROPER DIMENSIONS FOR AREAWAY INSTALLATION.

Exhibit G
2/10/2025
