



Airflow Testing Report

Prepared for

Portland Public Schools

November 2021





9700 SW Capitol Hwy, Suite 110
Portland, OR 97219
ameresco.com

PROJECT OVERVIEW

As part of the continuing process to ensure a safe return to in-person learning, Portland Public Schools has contracted with Ameresco to test the airflow and ventilation of all educational and office spaces in each school. The data is reviewed by both Ameresco and PPS personnel to identify any potential shortcomings in the airflow from the HVAC systems. To accomplish this task, Ameresco has partnered with a local NEBB certified Test-Adjust-Balance (TAB) firm, Neudorfer Engineers, who will measure the airflow to each zone with calibrated measurement equipment in accordance with current testing standards and procedures. As part of this effort, HVAC professionals will review the operation of the HVAC equipment serving every educational and office space in each school.

Ameresco is pleased to have partnered with PPS over the last decade as the district's Energy Services Company (ESCO) on six energy efficiency construction projects, four service projects, and numerous energy audits. Our partnership has resulted in reducing over 3,000 tons of CO₂ and other GHG emissions and over \$1,000,000 in utility cost savings per year. Ameresco appreciates this opportunity to play a small role in the safe reopening of schools.

About Ameresco, Inc.

Founded in 2000, Ameresco, Inc. (NYSE:AMRC) is a leading cleantech integrator and renewable energy asset developer, owner and operator. Our comprehensive portfolio includes energy efficiency, infrastructure upgrades, asset sustainability and renewable energy solutions delivered to clients throughout North America and the United Kingdom. Ameresco's sustainability services in support of clients' pursuit of Net Zero include upgrades to a facility's energy infrastructure and the development, construction, and operation of distributed energy resources. Ameresco has successfully completed energy saving, environmentally responsible projects with Federal, state and local governments, healthcare and educational institutions, housing authorities, and commercial and industrial customers. With its corporate headquarters in Framingham, MA, Ameresco has more than 1,000 employees providing local expertise in the United States, Canada, and the United Kingdom. For more information, visit www.ameresco.com.

Explanation of ASHRAE Total Effective Air Changes per Hour (ACH_e) Calculation

ASHRAE has been updating their Building Readiness document to reflect the most current understanding in the engineering community for how to operate and maintain buildings during the pandemic. Their update on 4/27/2021 provided an explanation of the impact air filters and air cleaning devices have on the air in buildings. They provided the methodology, formulas, and an Excel-based tool for determining the equivalent outside air a space is receiving by having a mix of outside air, filtered recirculated air, and additional air filtration or cleaning devices in the room. Here is the explanation from ASHRAE:

Epidemic Conditions in Place



Equivalent Outdoor Air:

The equivalent outdoor air calculation indicates that the outdoor air can be calculated by using the combination of the actual outdoor air, impact of filtration or air cleaning technologies on recirculated air, and the impact of air cleaning technologies in the space.

This is using the principal of filters in series and the effectiveness at reducing particles. For items in series, the initial item would see the recirculated airflow to clean. The second item in the series would see the “cleaned” air from Item 1 and so the impact of Item 1 must be accounted for in Item 2.

As part of the airflow testing project that Portland Public Schools has partnered with Ameresco to complete, we are including the calculation of the Total Effective Air Changes per Hour (ACH_e) to show the impact of the air filtration that is active in nearly all spaces in the PPS schools. The formula for doing so is:

$$ACH_e = (ACH_{oa} + ACH_f) * E_z + ACH_{ir}$$

where:

- ACH_{oa} = air changes per hour of outside air = outside airflow in cubic feet per minute * 60 minutes per hour / room volume in cubic feet
- ACH_f = air changes per hour of clean air from filtered recirculated air with filters of the specified MERV rating as determined by ASHRAE
- E_z = Zone Air Distribution Effectiveness = how effective the HVAC system is at circulating and mixing the air to distribute the clean air throughout the room
- ACH_{ir} = the air changes per hour of clean air from portable air filters in the room = number of filters * CADR * 60 minutes per hour / room volume in cubic feet
 - CADR = Clear Air Delivery Rate = the CFM of clean air as specified by the manufacturer of the air filter

In order to include these calculations in the airflow testing reports, Ameresco and PPS have made the following assumptions as not all the variables are known:

1. PPS is in process of upgrading the air filters in their HVAC systems to MERV 13 and plans to be complete with that project for the start of the '21-'22 school year. In this report and for the sake of the ACH_e calculation, we are using the filters that are in place at the time of the measurements, so some of them are still MERV 8.
2. ASHRAE has guidelines for what should be used for the Zone Air Distribution Effectiveness (E_z) based on the HVAC system configuration, but they do not provide a value for every HVAC system and room configuration. For the majority of PPS rooms, an E_z of 0.8 – 1.0 would be most appropriate, so we have made the conservative assumption of using 0.8 for every space as that yields the lower ACH_e.
3. The CADR for a given air filter is from manufacturer ratings and is based on certain conditions (fan speed, particulate size, filter cleanliness, etc.) that change with operating conditions.



NEUDORFER ENGINEERS INC.

**TEST REPORT TYPE:
SURVEY REPORT**

Portland Public Schools Airflow Testing Clarendon ES

Job Number: 2021-0297

Project Completion Date: November 2021

Revision Date:

-


Revision Number:

-



SEATTLE

5516 1st Avenue South
Seattle, Washington 98108
Phone (206) 621-1810
Fax (206) 343-9820



PORTLAND

2501 SE Columbia Way, Suite 230
Vancouver, Washington 98661
Phone (503) 235-8924
Fax (503) 235-8925



Neudorfer Engineers, Inc.

Consulting Engineers Seattle, Washington - Portland, Oregon



www.NeudorferEngineers.com

**Portland Public Schools Airflow Testing
Clarendon ES**

TABLE OF CONTENTS

Title Sheet	3
Report Certification	4
Terms	5
Instrument Calibration	6
Report Summary	7
Airflow Survey Report	8
TAB Notes	10
Floor Layout	11



Neudorfer Engineers, Inc.

Consulting Engineers Seattle, Washington - Portland, Oregon



www.NeudorferEngineers.com

REPORT TITLE

CERTIFIED TEST: SURVEY REPORT

Project: Portland Public Schools Airflow Testing
Clarendon ES

NEI Job#: 2021-0297

Mechanical Engineer: NA

Architect: NA

HVAC Contractor: NA

TAB Firm: Neudorfer Engineers Inc
Test Engineer: Zach Mayer



5516 1st Ave South
Seattle, Washington 98108
Phone (206) 621-1810
Fax (206) 343-9820



2501 SE Columbia Way, Suite 230
Vancouver, Washington 98661
Phone (503) 235-8924
Fax (503) 235-8925

CERTIFICATION

Portland Public Schools Airflow Testing

The data presented in this report is a record of system measurements and final adjustments that have been obtained in accordance with the current edition of the NEBB Procedural Standards for Testing, Adjusting, and Balancing of Environmental Systems. Any variances from design quantities, which exceed NEBB tolerances, are noted in the Test-Adjust-Balance Report Project Summary.

Significant / Noteworthy Remarks are noted on the General Remarks and General Field Notes pages. Other remarks are noted on individual test sheets.

Noted deficiencies are not the TAB firms responsibility to repair. Prior to issuance of this report, Deficiency Reports are forwarded to our contracted agent.

Warranty is limited to one year from date of this report. Within that time, any discrepancies, ambiguities, or omissions found in this report will be retested, adjusted, or balanced as needed. A written notification will be required.

Submitted and Certified by:

NEBB TAB Firm: **Neudorfer Engineers Inc**

Certification No: **3414**

Expiration Date: **March 31, 2023**

Certification Date: **March 31, 2021**

(Date completed) Signed and Sealed by:

NEBB Supervisor: **Mike Vawter P.E.**

NEBB Supervisor: **Eric Stotts**





Neudorfer Engineers, Inc.

Consulting Engineers Seattle, Washington - Portland, Oregon



www.NeudorferEngineers.com

TERMS AND ABBREVIATIONS

Project: **Portland Public Schools Airflow Testing**

AC or ACU Air Conditioner or Air Conditioning Unit

AH or AHU Air Handler or Air Handling Unit

ACH Air Changes per Hour

AVG Average

BHP Brake Horsepower

CAV Constant Air Volume

CBV Calibrated Balancing Valve
(Circuit Setter)

CC Cooling Coil

CD Ceiling Diffuser

CFM Cubic Feet per Minute

CH Chiller

CHWS Chilled Water Supply

CHWR Chilled Water Return

CP Circulating Pump

CR Ceiling Register

CRAC Computer Room Air Conditioner

CRU Computer Room Unit

CT Cooling Tower

CU Condenser Unit

CUH Cabinet Unit Heater

CWS Condenser Water Supply

CWR Condenser Water Return

DAT Discharge Air Temperature

DB Dry Bulb

DD Direct Drive

DDC Direct Digital Controls: EMS Control
System for the HVAC

Des. Design

Dia. Diameter

Disch. Discharge

EA Exhaust Air

EAT Entering Air Temperature

Economizer Controls and components that allow an
air handler to logically utilize outdoor air
for cooling as opposed to the use of
mechanical cooling.

EF Exhaust Fan

EG Exhaust Grille

EMCS Energy Management Control System

ERU Energy Recovery Unit

E.S.P. External Static Pressure

HRC Heat Recovery Coil

EWT Entering Water Temperature

FCU Fan Coil Unit

FD Fire Damper

FSD Fire Smoke Damper

FLA Full Load Amperage: Maximum
amperage a motor can draw.

Flow Hood Instrument that captures air and
converts the reading to CFM.

FHT Fume Hood Test

FPB Fan Powered Box

FPM Feet per Minute

FR Field Report

FT Foot, Feet

FTU Fan Terminal Unit

GPM Gallons per Minute

HC Heating Coil

TDH Pressure Difference across the entering
and leaving side of a pump.

HEPA High Efficiency Particulate Absorbing

HP Horsepower

HVAC Heating Ventilation and Air Conditioning

HWS Heating Water Supply

HWR Heating Water Return

HX Heat Exchanger

HZ Hertz, cycle per second

in. inches

in.w.g. inches of water gauge

Kfactor Correction factor to the free area need to
calculate CFM.

KW Kilowatts

LAT Leaving Air Temperature

LBWG Low Wall Grille

LWR Low Wall Register

LWT Leaving Water Temperature

MAU Make-up Air Handling Unit

MBH 1,000 BTUH

N/A Not Applicable

OSA Outside Air

OBD Opposed Blade Damper

ΔP Pressure Drop.

PH Phase

PSI Pounds per Square Inch

RA Return Air

RAT Return Air Temperature

RF Return Fan

RH Relative Humidity

RHC Reheat Coil

RPM Revolutions per Minute

RTU Roof Top Unit

SA Supply Air

SAT Supply Air Temperature

S.F. Service Factor

SF Supply Fan

SFD Smoke/Fire Damper

SP Static Pressure

sq.ft. square feet

Suct. Suction

SWG Sidewall Grille

SWR Sidewall Register

TAB Test; Adjust; and Balance

TSP Total Static Pressure: Difference
between the entering and leaving
static pressure of a fan.

UH Unit Heater

VAV Variable Air Volume; box that
contains a motorized damper that
modulates airflow.

VD Volume Damper

VFD Variable Frequency Drive

Velgrid Instrument that reads used to read
velocity in feet per minute.

VVT Variable Volume Terminal

WC Water Column

W.G. Water Gauge

WB Wet Bulb

INSTRUMENT CALIBRATIONS

Portland Public Schools Airflow Testing

Clarendon ES

Instrument Type	Air Data Meter with Flowhood	Instrument Serial #	M97410
Instrument Manufacturer	Shortridge	Calibration Date	10/4/2021
Instrument Model Number	ADM 860	Calibration Due	10/4/2022
Instrument Type	Differential Pressure Water Meter	Instrument Serial #	W12178
Instrument Manufacturer	Shortridge	Calibration Date	10/4/2021
Instrument Model Number	HDM-250	Calibration Due	10/4/2022
Instrument Type	Psychrometer	Instrument Serial #	181128924
Instrument Manufacturer	Extech	Calibration Date	10/1/2021
Instrument Model Number	RH390	Calibration Due	10/1/2022
Instrument Type	Tachometer	Instrument Serial #	B185B5022P
Instrument Manufacturer	Nidec	Calibration Date	10/1/2021
Instrument Model Number	MT-200	Calibration Due	10/1/2022
Instrument Type	Amp Probe	Instrument Serial #	33380179WS
Instrument Manufacturer	Fluke	Calibration Date	10/1/2021
Instrument Model Number	323 Clamp Meter	Calibration Due	10/1/2022
Instrument Type	Digital Thermometer	Instrument Serial #	45400509WS
Instrument Manufacturer	Fluke	Calibration Date	10/1/2021
Instrument Model Number	52 II	Calibration Due	10/1/2022
Instrument Type	Manometer	Instrument Serial #	M97410
Instrument Manufacturer	Shortridge	Calibration Date	10/4/2021
Instrument Model Number	ADM 860	Calibration Due	10/4/2022
Instrument Type	Thermal Anemometer	Instrument Serial #	AVM440808002
Instrument Manufacturer	Alnor Instruments	Calibration Date	9/22/2021
Instrument Model Number	AVM 440	Calibration Due	9/22/2022
Instrument Type	Ultrasonic Flow Meter	Instrument Serial #	N1F1823T
Instrument Manufacturer	Fuji	Calibration Date	9/20/2021
Instrument Model Number	Portaflow-C	Calibration Due	9/20/2022



PROJECT	Portland Public Schools Airflow Testing
LOCATION	Clarendon ES; 9325 N Van Houten Ave, Portland, OR 97203

REPORT SUMMARY

This project has been surveyed per plans and specifications using the National Environmental Balancing Bureau (NEBB) standards and procedures.

The scope of work for this project was to assess the current airflows for each classroom, office, and special purpose space. Air changes per hour were calculated along with the % of OSA for the spaces and any deficiencies found for each piece of equipment has been noted in the following report.

All ventilation equipment was commanded to run by the BMS system. Ventilation units were measured with a flowhood on the supply outlets. Outside air was recorded with a flowhood on the OSA louvre where accessible. AK factors were calculated from flowhood readings. The remaining OSA values were recorded with a velgrid. AHU supply air was recorded by a summation of the outlets as recorded by flowhood or velgrid when appropriate. Outside air was recorded with a velgrid or airfoil and calculated by the free area method.

The measured airflows in this report represent the performance of the equipment at the time of measurement, which vary over time based on operating conditions. There are factors outside the control of Neudorfer that impact airflow, and variance in those factors is expected and normal. One significant factor is the MERV rating and condition of the air filters on the equipment. During the summer of 2021, PPS began upgrading the filters on all their fan systems to MERV 13. Those upgraded filters are more effective at capturing particles but also impact the amount of airflow from the equipment. These filter changes were occurring while the airflow measurement project was happening, so some schools had the new filters, and some had the old filters at the time of measurement. On the data page included this report, there is a line stating whether or not the upgraded filters were in place at the time of measurement.



AIRFLOW SURVEY REPORT

Project: Portland Public Schools Airflow Testing
Location: Clarendon ES; 9325 N Van Houten Ave, Portland, OR 97203
Filter Status: Upgraded

Room	Equipment Info		Room Dimensions					Airflow Measurements			Calculated ACH					Notes
	Served By	Equipment Type	Room Length	Room Width	Room Area	Room Height	Room Volume	Total CFM Supply	OA CFM Supply	OA %	Air Changes per Hour (supply)	Air Changes per Hour (OA)	# of Portable Filters	Total Effective Air Changes per Hour (ACH_e) with Portable Filter	Total Effective Air Changes per Hour (ACH_e) without Portable Filter	
First Floor																
009	SU-19	AHU	51.9	82.9	4,374	20.4	89,176	3,440	1,445	42%	2.3	1.0	4	2.4	1.7	
009C	-	-	21.2	27.7	357	9.2	3,284	-	-	-	0.0	0.0	0	N/A	0.0	Note #1. This is storage.
009F	-	-	21.2	27.7	357	9.2	3,284	-	-	-	0.0	0.0	0	N/A	0.0	Note #1. This is storage.
009G	SU-19	AHU	11.5	16.5	116	9.2	1,067	80	34	42%	4.5	1.9	1	18.0	3.4	Note #1
Rm 010B	-	-	-	-	-	-	-	-	-	-	0.0	0.0	0	N/A	N/A	This is an outdoor courtyard.
Rm 011F	SU-15	AHU	19.1	38.8	741	8.3	6,197	1,250	188	15%	12.1	1.8	1	11.4	8.9	Note #1
013A	SU-15	AHU	18.4	23.8	333	9.9	3,297	470	71	15%	8.6	1.3	1	11.0	6.3	Note #1
013B	SU-15	AHU	7.4	11.2	83	7.9	655	50	8	15%	4.6	0.7	1	27.2	3.4	Note #1
012A	12A FCU	FCU	10.1	30.7	283	9.2	2,604	-	-	-	0.0	0.0	0	N/A	0.0	This is storage.
Rm 014A	UV	UV	30.0	59.4	1,321	10.8	14,267	570	185	32%	2.4	0.8	1	2.9	1.8	Note #1
Rm 015A	UV	UV	30.0	59.4	1,361	10.8	14,699	520	250	48%	2.1	1.0	1	2.7	1.6	Note #1
Rm 016A	UV	UV	30.0	63.3	1,422	10.8	15,358	460	80	17%	1.8	0.3	1	2.3	1.3	Note #1. OSA damper may be closed.
Rm 017A	UV	UV	30.0	63.3	1,422	10.8	15,358	515	120	23%	2.0	0.5	1	2.5	1.5	Note #1
Conf. Room 019A	SU-15	AHU	10.0	16.3	163	8.0	1,304	185	28	15%	8.5	1.3	1	18.2	6.2	Note #1
019	SU-15	AHU	15.1	35.1	378	7.9	2,982	230	35	15%	4.6	0.7	1	8.6	3.4	This is open to 018.
019B	SU-15	AHU	13.5	22.7	279	7.9	2,208	460	69	15%	12.5	1.9	1	16.2	9.1	Note #1
019E	SU-15	AHU	14.3	16.5	193	8.0	1,544	330	50	15%	12.8	1.9	1	19.5	9.4	Note #1
019G	SU-15	AHU	8.7	9.3	71	8.0	568	105	16	15%	11.1	1.7	1	35.6	8.1	Note #1
001A	UV	UV	22.8	33.9	718	10.6	7,611	425	0	0%	3.4	0.0	1	4.5	2.4	Note #1. OSA damper may be closed.
001B	-	-	-	-	-	-	-	-	-	-	0.0	0.0	0	N/A	0.0	This is storage.
Rm 002A	UV	UV	34.7	61.1	2,107	108.0	227,574	910	200	22%	0.2	0.1	1	0.2	0.2	Note #1
Rm 003A	UV	UV	30.0	63.3	1,422	10.8	15,358	0	0	0%	0.0	0.0	1	1.0	0.0	Note #1. Unit is not running.
Rm 004A	UV	UV	30.0	63.3	1,422	10.8	15,358	400	0	0%	1.6	0.0	1	2.1	1.1	Note #1. OSA damper may be closed.
Rm 005A	UV	UV	30.0	59.4	1,361	10.8	14,699	570	160	28%	2.3	0.7	1	2.8	1.7	Note #1

Date: 11/3/2021

Readings By: Mayer

Some HVAC equipment for this site has not yet been tested. This version of the report is a draft with the information available at this time. Once all data has been collected, a final report will be published.



Page 9 of 11

Project: Portland Public Schools Airflow Testing

Location: Clarendon ES; 9325 N Van Houten Ave, Portland, OR 97203

NOTE #	NOTE DESCRIPTION
1	Non-rectangular room.

CLARENDON: First Floor

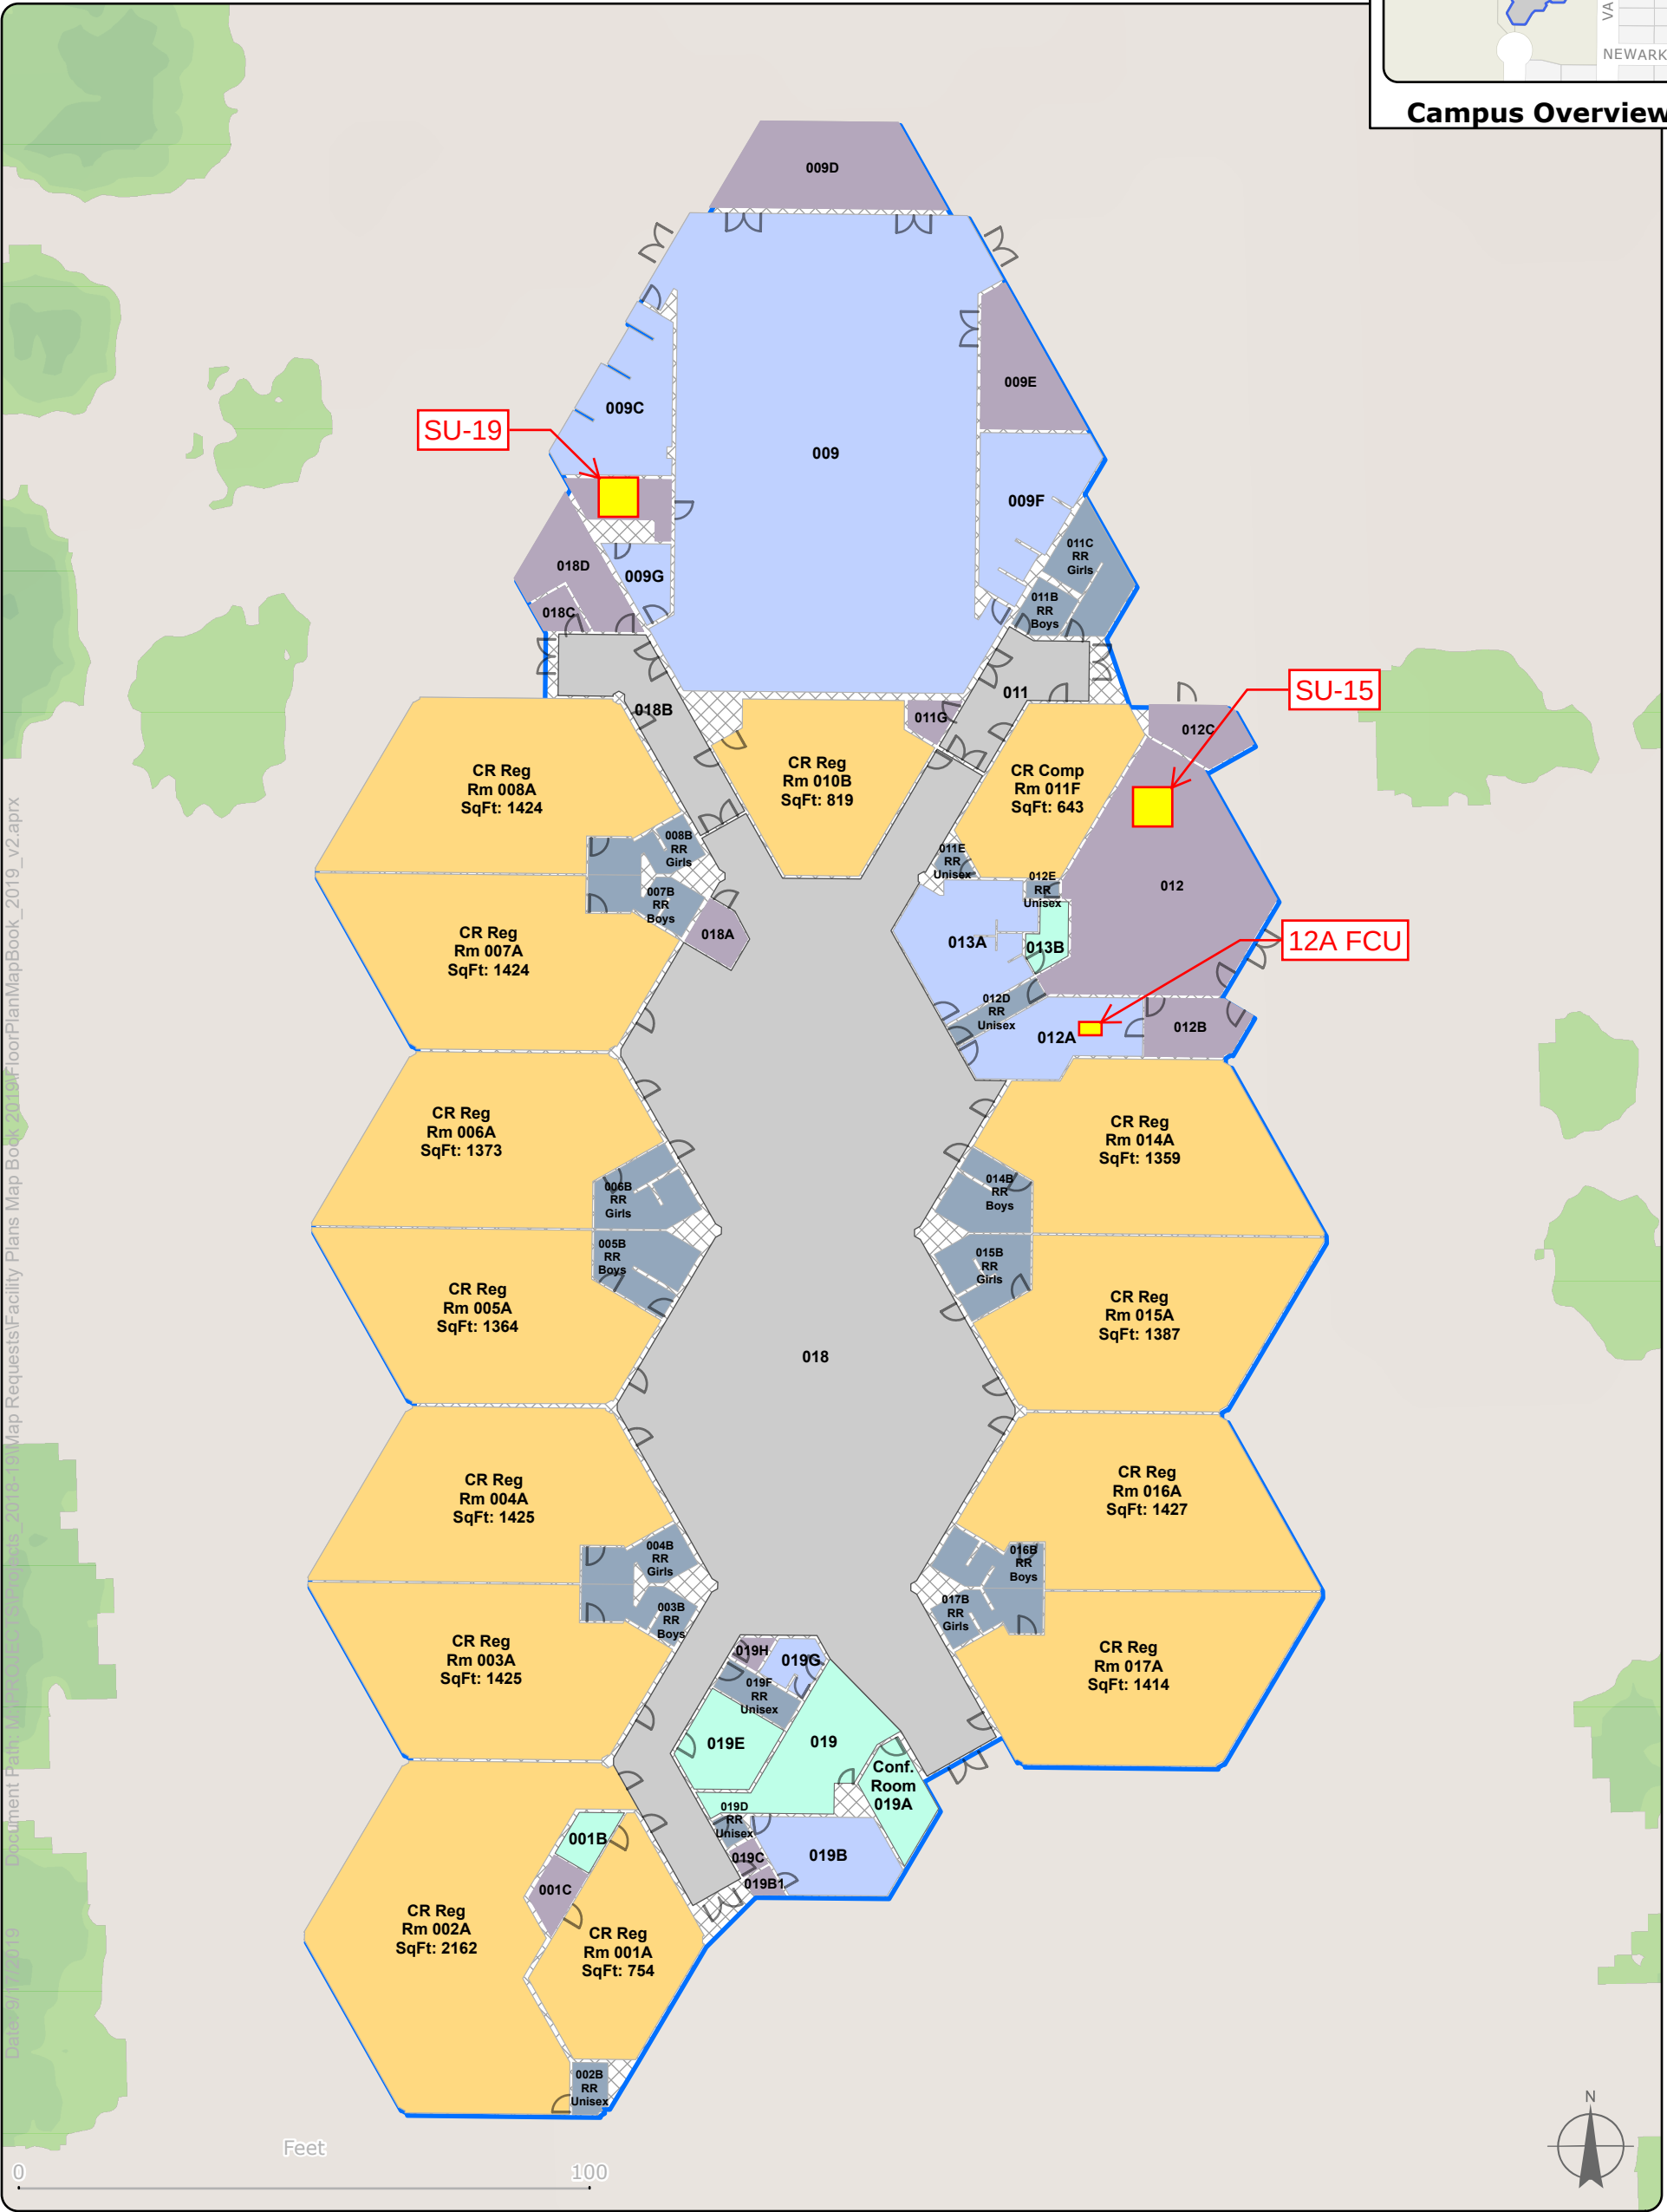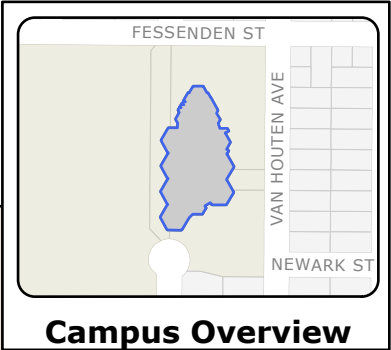

Space Use	School Grounds
 Classroom	 Campus Footprints
 Office	 Athletic Field
 Rest Room	 Playground: Paved
 Special Purpose	 Playground: Unpaved
 Corridor	 Streets
 Other	 Doors
 Stairs/Elevator	

Total Number Of Rooms By Classification

Classrooms: 14	Special Purpose: 8
Office Spaces: 5	Storage: 10
