



Airflow Testing Report

Prepared for

Portland Public Schools

August 2021





9700 SW Capitol Hwy, Suite 110
Portland, OR 97219
ameresco.com

PROJECT OVERVIEW

As part of the continuing process to ensure a safe return to in-person learning, Portland Public Schools has contracted with Ameresco to test the airflow and ventilation of all educational and office spaces in each school. The data is reviewed by both Ameresco and PPS personnel to identify any potential shortcomings in the airflow from the HVAC systems. To accomplish this task, Ameresco has partnered with a local NEBB certified Test-Adjust-Balance (TAB) firm, Neudorfer Engineers, who will measure the airflow to each zone with calibrated measurement equipment in accordance with current testing standards and procedures. As part of this effort, HVAC professionals will review the operation of the HVAC equipment serving every educational and office space in each school.

Ameresco is pleased to have partnered with PPS over the last decade as the district's Energy Services Company (ESCO) on six energy efficiency construction projects, four service projects, and numerous energy audits. Our partnership has resulted in reducing over 3,000 tons of CO₂ and other GHG emissions and over \$1,000,000 in utility cost savings per year. Ameresco appreciates this opportunity to play a small role in the safe reopening of schools.

About Ameresco, Inc.

Founded in 2000, Ameresco, Inc. (NYSE:AMRC) is a leading cleantech integrator and renewable energy asset developer, owner and operator. Our comprehensive portfolio includes energy efficiency, infrastructure upgrades, asset sustainability and renewable energy solutions delivered to clients throughout North America and the United Kingdom. Ameresco's sustainability services in support of clients' pursuit of Net Zero include upgrades to a facility's energy infrastructure and the development, construction, and operation of distributed energy resources. Ameresco has successfully completed energy saving, environmentally responsible projects with Federal, state and local governments, healthcare and educational institutions, housing authorities, and commercial and industrial customers. With its corporate headquarters in Framingham, MA, Ameresco has more than 1,000 employees providing local expertise in the United States, Canada, and the United Kingdom. For more information, visit www.ameresco.com.

Explanation of ASHRAE Total Effective Air Changes per Hour (ACH_e) Calculation

ASHRAE has been updating their Building Readiness document to reflect the most current understanding in the engineering community for how to operate and maintain buildings during the pandemic. Their update on 4/27/2021 provided an explanation of the impact air filters and air cleaning devices have on the air in buildings. They provided the methodology, formulas, and an Excel-based tool for determining the equivalent outside air a space is receiving by having a mix of outside air, filtered recirculated air, and additional air filtration or cleaning devices in the room. Here is the explanation from ASHRAE:

Epidemic Conditions in Place



Equivalent Outdoor Air:

The equivalent outdoor air calculation indicates that the outdoor air can be calculated by using the combination of the actual outdoor air, impact of filtration or air cleaning technologies on recirculated air, and the impact of air cleaning technologies in the space.

This is using the principal of filters in series and the effectiveness at reducing particles. For items in series, the initial item would see the recirculated airflow to clean. The second item in the series would see the “cleaned” air from Item 1 and so the impact of Item 1 must be accounted for in Item 2.

As part of the airflow testing project that Portland Public Schools has partnered with Ameresco to complete, we are including the calculation of the Total Effective Air Changes per Hour (ACH_e) to show the impact of the air filtration that is active in nearly all spaces in the PPS schools. The formula for doing so is:

$$ACH_e = (ACH_{oa} + ACH_f) * E_z + ACH_{ir}$$

where:

- ACH_{oa} = air changes per hour of outside air = outside airflow in cubic feet per minute * 60 minutes per hour / room volume in cubic feet
- ACH_f = air changes per hour of clean air from filtered recirculated air with filters of the specified MERV rating as determined by ASHRAE
- E_z = Zone Air Distribution Effectiveness = how effective the HVAC system is at circulating and mixing the air to distribute the clean air throughout the room
- ACH_{ir} = the air changes per hour of clean air from portable air filters in the room = number of filters * CADR * 60 minutes per hour / room volume in cubic feet
 - CADR = Clear Air Delivery Rate = the CFM of clean air as specified by the manufacturer of the air filter

In order to include these calculations in the airflow testing reports, Ameresco and PPS have made the following assumptions as not all the variables are known:

1. PPS is in process of upgrading the air filters in their HVAC systems to MERV 13 and plans to be complete with that project for the start of the '21-'22 school year. In this report and for the sake of the ACH_e calculation, we are using the filters that are in place at the time of the measurements, so some of them are still MERV 8.
2. ASHRAE has guidelines for what should be used for the Zone Air Distribution Effectiveness (E_z) based on the HVAC system configuration, but they do not provide a value for every HVAC system and room configuration. For the majority of PPS rooms, an E_z of 0.8 – 1.0 would be most appropriate, so we have made the conservative assumption of using 0.8 for every space as that yields the lower ACH_e.
3. The CADR for a given air filter is from manufacturer ratings and is based on certain conditions (fan speed, particulate size, filter cleanliness, etc.) that change with operating conditions.



NEUDORFER ENGINEERS INC.

**TEST REPORT TYPE:
SURVEY REPORT**

Portland Public Schools Airflow Testing King ES

Job Number: 2021-0297


Project Completion Date: January 2022

Revision Date:

-

Revision Number:

-



SEATTLE

5516 1st Avenue South
Seattle, Washington 98108
Phone (206) 621-1810
Fax (206) 343-9820

PORTLAND

2501 SE Columbia Way, Suite 230
Vancouver, Washington 98661
Phone (503) 235-8924
Fax (503) 235-8925



Neudorfer Engineers, Inc.

Consulting Engineers Seattle, Washington - Portland, Oregon



www.NeudorferEngineers.com

**Portland Public Schools Airflow Testing
King ES**

TABLE OF CONTENTS

Title Sheet	3
Report Certification	4
Terms	5
Instrument Calibration	6
Report Summary	7
Airflow Survey Report	8
TAB Notes	12
Floor Layout	13



Neudorfer Engineers, Inc.

Consulting Engineers Seattle, Washington - Portland, Oregon



www.NeudorferEngineers.com

REPORT TITLE

CERTIFIED TEST: SURVEY REPORT

Project: Portland Public Schools Airflow Testing
King ES

NEI Job#: 2021-0297

Mechanical Engineer: NA

Architect: NA

HVAC Contractor: NA

TAB Firm: Neudorfer Engineers Inc
Test Engineer: Justin Davis



5516 1st Ave South
Seattle, Washington 98108
Phone (206) 621-1810
Fax (206) 343-9820



2501 SE Columbia Way, Suite 230
Vancouver, Washington 98661
Phone (503) 235-8924
Fax (503) 235-8925

CERTIFICATION

Portland Public Schools Airflow Testing

The data presented in this report is a record of system measurements and final adjustments that have been obtained in accordance with the current edition of the NEBB Procedural Standards for Testing, Adjusting, and Balancing of Environmental Systems. Any variances from design quantities, which exceed NEBB tolerances, are noted in the Test-Adjust-Balance Report Project Summary.

Significant / Noteworthy Remarks are noted on the General Remarks and General Field Notes pages. Other remarks are noted on individual test sheets.

Noted deficiencies are not the TAB firms responsibility to repair. Prior to issuance of this report, Deficiency Reports are forwarded to our contracted agent.

Warranty is limited to one year from date of this report. Within that time, any discrepancies, ambiguities, or omissions found in this report will be retested, adjusted, or balanced as needed. A written notification will be required.

Submitted and Certified by:

NEBB TAB Firm: **Neudorfer Engineers Inc**

Certification No: **3414**

Expiration Date: **March 31, 2023**

Certification Date: **March 31, 2021**

(Date completed) *Signed and Sealed by:*

NEBB Supervisor: **Mike Vawter P.E.**

NEBB Supervisor: **Eric Stotts**





Neudorfer Engineers, Inc.

Consulting Engineers Seattle, Washington - Portland, Oregon



www.NeudorferEngineers.com

TERMS AND ABBREVIATIONS

Project: **Portland Public Schools Airflow Testing**

AC or ACU Air Conditioner or Air Conditioning Unit

AH or AHU Air Handler or Air Handling Unit

ACH Air Changes per Hour

AVG Average

BHP Brake Horsepower

CAV Constant Air Volume

CBV Calibrated Balancing Valve
(Circuit Setter)

CC Cooling Coil

CD Ceiling Diffuser

CFM Cubic Feet per Minute

CH Chiller

CHWS Chilled Water Supply

CHWR Chilled Water Return

CP Circulating Pump

CR Ceiling Register

CRAC Computer Room Air Conditioner

CRU Computer Room Unit

CT Cooling Tower

CU Condenser Unit

CUH Cabinet Unit Heater

CWS Condenser Water Supply

CWR Condenser Water Return

DAT Discharge Air Temperature

DB Dry Bulb

DD Direct Drive

DDC Direct Digital Controls: EMS Control
System for the HVAC

Des. Design

Dia. Diameter

Disch. Discharge

EA Exhaust Air

EAT Entering Air Temperature

Economizer Controls and components that allow an
air handler to logically utilize outdoor air
for cooling as opposed to the use of
mechanical cooling.

EF Exhaust Fan

EG Exhaust Grille

EMCS Energy Management Control System

ERU Energy Recovery Unit

E.S.P. External Static Pressure

HRC Heat Recovery Coil

EWT Entering Water Temperature

FCU Fan Coil Unit

FD Fire Damper

FSD Fire Smoke Damper

FLA Full Load Amperage: Maximum
amperage a motor can draw.

Flow Hood Instrument that captures air and
converts the reading to CFM.

FHT Fume Hood Test

FPB Fan Powered Box

FPM Feet per Minute

FR Field Report

FT Foot, Feet

FTU Fan Terminal Unit

GPM Gallons per Minute

HC Heating Coil

TDH Pressure Difference across the entering
and leaving side of a pump.

HEPA High Efficiency Particulate Absorbing

HP Horsepower

HVAC Heating Ventilation and Air Conditioning

HWS Heating Water Supply

HWR Heating Water Return

HX Heat Exchanger

HZ Hertz, cycle per second

in. inches

in.w.g. inches of water gauge

Kfactor Correction factor to the free area need to
calculate CFM.

KW Kilowatts

LAT Leaving Air Temperature

LBWG Low Wall Grille

LWR Low Wall Register

LWT Leaving Water Temperature

MAU Make-up Air Handling Unit

MBH 1,000 BTUH

N/A Not Applicable

OSA Outside Air

OBD Opposed Blade Damper

ΔP Pressure Drop.

PH Phase

PSI Pounds per Square Inch

RA Return Air

RAT Return Air Temperature

RF Return Fan

RH Relative Humidity

RHC Reheat Coil

RPM Revolutions per Minute

RTU Roof Top Unit

SA Supply Air

SAT Supply Air Temperature

S.F. Service Factor

SF Supply Fan

SFD Smoke/Fire Damper

SP Static Pressure

sq.ft. square feet

Suct. Suction

SWG Sidewall Grille

SWR Sidewall Register

TAB Test; Adjust; and Balance

TSP Total Static Pressure: Difference
between the entering and leaving
static pressure of a fan.

UH Unit Heater

VAV Variable Air Volume; box that
contains a motorized damper that
modulates airflow.

VD Volume Damper

VFD Variable Frequency Drive

Velgrid Instrument that reads used to read
velocity in feet per minute.

VVT Variable Volume Terminal

WC Water Column

W.G. Water Gauge

WB Wet Bulb

INSTRUMENT CALIBRATIONS

Portland Public Schools Airflow Testing

King ES

Instrument Type	Air Data Meter with Flowhood	Instrument Serial #	M97410
Instrument Manufacturer	Shortridge	Calibration Date	10/4/2021
Instrument Model Number	ADM 860	Calibration Due	10/4/2022
Instrument Type	Differential Pressure Water Meter	Instrument Serial #	W12178
Instrument Manufacturer	Shortridge	Calibration Date	10/4/2021
Instrument Model Number	HDM-250	Calibration Due	10/4/2022
Instrument Type	Psychrometer	Instrument Serial #	181128924
Instrument Manufacturer	Extech	Calibration Date	10/1/2021
Instrument Model Number	RH390	Calibration Due	10/1/2022
Instrument Type	Tachometer	Instrument Serial #	B185B5022P
Instrument Manufacturer	Nidec	Calibration Date	10/1/2021
Instrument Model Number	MT-200	Calibration Due	10/1/2022
Instrument Type	Amp Probe	Instrument Serial #	33380179WS
Instrument Manufacturer	Fluke	Calibration Date	10/1/2021
Instrument Model Number	323 Clamp Meter	Calibration Due	10/1/2022
Instrument Type	Digital Thermometer	Instrument Serial #	45400509WS
Instrument Manufacturer	Fluke	Calibration Date	10/1/2021
Instrument Model Number	52 II	Calibration Due	10/1/2022
Instrument Type	Manometer	Instrument Serial #	M97410
Instrument Manufacturer	Shortridge	Calibration Date	10/4/2021
Instrument Model Number	ADM 860	Calibration Due	10/4/2022
Instrument Type	Thermal Anemometer	Instrument Serial #	AVM440808002
Instrument Manufacturer	Alnor Instruments	Calibration Date	9/22/2021
Instrument Model Number	AVM 440	Calibration Due	9/22/2022
Instrument Type	Ultrasonic Flow Meter	Instrument Serial #	N1F1823T
Instrument Manufacturer	Fuji	Calibration Date	9/20/2021
Instrument Model Number	Portaflow-C	Calibration Due	9/20/2022



PROJECT	Portland Public Schools Airflow Testing
LOCATION	King ES; 4906 NE 6th Ave, Portland, OR 97211

REPORT SUMMARY

This project has been surveyed per plans and specifications using the National Environmental Balancing Bureau (NEBB) standards and procedures.

The scope of work for this project was to assess the current airflows for each classroom, office, and special purpose space. Air changes per hour were calculated along with the % of OSA for the spaces and any deficiencies found for each piece of equipment has been noted in the following report.

All ventilation equipment was commanded to run by the BMS system. Ventilation units were measured with a flowhood on the supply outlets. Outside air was recorded with a flowhood on the OSA louvre where accessible. AK factors were calculated from flowhood readings. The remaining OSA values were recorded with a velgrid. AHU supply air was recorded by a summation of the outlets as recorded by flowhood or velgrid when appropriate. Outside air was recorded with a velgrid or airfoil and calculated by the free area method.

The measured airflows in this report represent the performance of the equipment at the time of measurement, which vary over time based on operating conditions. There are factors outside the control of Neudorfer that impact airflow, and variance in those factors is expected and normal. One significant factor is the MERV rating and condition of the air filters on the equipment. During the summer of 2021, PPS began upgrading the filters on all their fan systems to MERV 13. Those upgraded filters are more effective at capturing particles but also impact the amount of airflow from the equipment. These filter changes were occurring while the airflow measurement project was happening, so some schools had the new filters, and some had the old filters at the time of measurement. On the data page included this report, there is a line stating whether or not the upgraded filters were in place at the time of measurement.



AIRFLOW SURVEY REPORT

Project: Portland Public Schools Airflow Testing
Location: King ES; 4906 NE 6th Ave, Portland, OR 97211
Filter Status: Not Upgraded

Room Floor Plan # (Actual #)	Equipment Info		Room Dimensions					Airflow Measurements			Calculated ACH					Notes
	Served By	Equipment Type	Room Length	Room Width	Room Area	Room Height	Room Volume	Total CFM Supply	OA CFM Supply	OA %	Air Changes per Hour (supply)	Air Changes per Hour (OA)	# of Portable Filters	Total Effective Air Changes per Hour (ACH_e) with Portable Filter	Total Effective Air Changes per Hour (ACH_e) without Portable Filter	
Lower Level 1																
Conf Rm 4	-	-	13.1	17.3	227	8.5	1,926	-	-	-	0.0	0.0	1	8.1	0.0	Ventilation supplied by adjacent spaces.
First Floor																
Rm 109	UV	UV	36.7	29.9	1,097	13.7	15,033	1,125	80	7%	4.5	0.3	1	3.1	2.1	
Rm 120C	UV	UV	29.3	22.1	648	12.2	7,900	1,050	70	7%	8.0	0.5	1	5.7	3.7	
Rm 121	UV	UV	29.9	24.4	730	12.2	8,901	785	75	10%	5.3	0.5	1	4.3	2.5	
Rm 122	UV	UV	29.2	22.0	642	12.2	7,837	1,401	60	4%	10.7	0.5	1	6.9	4.9	
Rm 123	UV	UV	30.1	23.9	719	12.2	8,777	745	360	48%	5.1	2.5	1	4.9	3.1	
Rm 124	UV	UV	29.4	22.3	656	12.2	10,401	580	55	9%	3.3	0.3	1	3.1	1.6	
Rm 130	Classroom Fan	AHU	27.5	31.0	853	12.0	11,050	435	31	7%	2.4	0.2	1	2.5	1.1	Note #2, Boys RR 2nd Flr. Labeled "Classroom Fan".
Rm 131	Classroom Fan	AHU	29.8	30.9	921	12.0	11,050	475	34	7%	2.6	0.2	1	2.6	1.2	Note #2, Boys RR 2nd Flr. Labeled "Classroom Fan".
Rm 132	Classroom Fan	AHU	27.8	30.9	859	12.0	10,308	415	30	7%	2.4	0.2	1	2.6	1.1	Note #2, Boys RR 2nd Flr. Labeled "Classroom Fan".
Rm 134	Classroom Fan	AHU	27.8	30.9	859	12.2	10,480	750	54	7%	4.3	0.3	1	3.5	2.0	Note #2, Boys RR 2nd Flr. Labeled "Classroom Fan".
Rm 140A	UV	UV	29.9	21.9	655	12.2	7,989	241	26	11%	1.8	0.2	1	2.8	0.9	
Rm 140C	UV	UV	30.5	22.4	683	12.2	8,335	1,070	310	29%	7.7	2.2	1	6.1	4.2	
Rm 140D	UV	UV	36.8	29.1	1,071	13.9	14,885	1,370	425	31%	5.5	1.7	1	4.1	3.1	
Rm 141	FCU	FCU	40.3	30.2	1,217	12.0	14,605	530	530	100%	2.2	2.2	1	2.8	1.7	Labeled "Kindergarten/RM 142".
Rm 142	FCU	FCU	39.8	30.2	1,202	12.0	14,424	465	465	100%	1.9	1.9	1	2.6	1.5	Labeled "Kindergarten/RM 142".
Rm 153	UV	UV	22.0	30.4	669	12.1	8,092	755	30	4%	5.6	0.2	1	4.5	2.6	
Office 100	SF#2	AHU	25.7	17.5	450	9.2	4,138	140	11	8%	2.0	0.2	1	4.7	1.0	Labeled "SF#2".
Office 100D	SF#2	AHU	3.1	7.8	24	8.4	203	-	-	-	0.0	0.0	1	76.8	0.0	Ventilation supplied from adjacent space.
Office 102	SF#2	AHU	11.1	10.9	121	11.4	1,379	50	4	8%	2.2	0.2	1	12.3	1.0	
Office 103	SF#2	AHU	10.5	10.6	111	10.2	1,135	70	5	8%	3.7	0.3	1	15.5	1.7	
Office 104	SF#2	AHU	11.1	10.9	121	11.4	1,379	70	5	8%	3.0	0.2	1	12.7	1.4	
Office 105	SF#2	AHU	17.5	10.3	180	12.3	2,217	780	59	8%	21.1	1.6	1	17.0	9.9	

Date: 5/7/2021

Readings By: Mayer & Davis



AIRFLOW SURVEY REPORT

Project: Portland Public Schools Airflow Testing
Location: King ES; 4906 NE 6th Ave, Portland, OR 97211
Filter Status: Not Upgraded

Room Floor Plan # (Actual #)	Equipment Info		Room Dimensions					Airflow Measurements			Calculated ACH					Notes
	Served By	Equipment Type	Room Length	Room Width	Room Area	Room Height	Room Volume	Total CFM Supply	OA CFM Supply	OA %	Air Changes per Hour (supply)	Air Changes per Hour (OA)	# of Portable Filters	Total Effective Air Changes per Hour (ACH_e) with Portable Filter	Total Effective Air Changes per Hour (ACH_e) without Portable Filter	
First Floor																
Office 106	SF#2	AHU	9.3	13.2	123	10.7	1,314	20	2	8%	0.9	0.1	1	12.3	0.4	
Office 107	SF#2	AHU	13.3	9.3	124	9.0	1,113	20	2	8%	1.1	0.1	1	14.5	0.5	Door labeled "106".
Conf Rm 108	SF#2	AHU	13.3	15.2	202	11.1	2,244	40	3	8%	1.1	0.1	1	7.5	0.5	
Office 111	Classroom Fan	AHU	9.5	9.7	92	7.8	719	35	3	7%	2.9	0.2	1	23.1	1.4	Note #2, Boys RR 2nd Flr. Labeled "Classroom Fan".
Office 116	Classroom Fan	AHU	16.4	6.2	102	8.7	885	230	16	7%	15.6	1.1	1	25.0	7.3	Note #2, Open and shared with rooms PRAC-1&2.
Office 138	-	-	13.5	14.0	189	11.5	2,174	-	-	-	0.0	0.0	1	7.2	0.0	Ventilation supplied from hallway.
Office 139	Classroom Fan	AHU	26.8	13.4	359	12.3	4,417	613	242	39%	7.2	2.9	1	7.3	4.2	
139B	-	-	7.7	7.1	55	12.3	672	-	-	-						
Office 148D	FCU	FCU	15.3	8.0	122	7.6	930	75	0	0%	4.8	0.0	1	18.9	2.2	Kitchenette open to Office 139 OSA damper may be closed.
Office 158	-	-	13.6	13.9	189	11.5	2,174	-	-	-	0.0	0.0	1	7.2	0.0	Ventilation provided from gym.
Office 159	-	-	21.1	14.2	300	12.1	3,625	-	-	-	0.0	0.0	1	4.3	0.0	Ventilation provided from gym.
Office 160	-	-	10.0	10.6	106	13.0	1,378	-	-	-	0.0	0.0	1	11.3	0.0	Ventilation provided from gym.
Entry 101	AHU-1	AHU	21.9	19.3	423	7.9	3,339	550	39	7%	9.9	0.7	1	9.3	4.6	
Conf Rm 130A	-	-	19.2	19.4	372	7.9	2,943	-	-	-	0.0	0.0	1	5.3	0.0	Ventilation supplied from adjacent space.
Conf. Rm. 106	AHU-1	AHU	19.5	17.9	349	7.8	2,723	185	13	7%	4.1	0.3	1	7.6	1.9	
Office 115	AHU-1	AHU	89.3	28.5	2,545	12.2	31,050	835	60	7%	1.6	0.1	1	1.3	0.8	
Office 120	AHU-1	AHU	39.5	29.4	1,161	17.9	20,787	390	28	7%	1.1	0.1	1	1.3	0.5	
Office 120A	-	-	9.6	9.6	92	14.4	1,327	-	-	-	0.0	0.0	1	11.8	0.0	Ventilation supplied from adjacent space 120.
Office 120B	AHU-1	AHU	9.6	9.6	92	14.4	1,325	50	75	7%	2.3	3.4	1	14.0	2.2	
Office 120C	AHU-1	AHU	9.6	9.6	92	14.4	1,327	60	4	7%	2.7	0.2	1	13.0	1.3	
Conf Rm 123	AHU-1	AHU	29.4	28.3	832	17.5	14,560	770	55	7%	3.2	0.2	1	2.6	1.5	
Office 125	AHU-1	AHU	84.8	19.4	1,645	13.4	22,045	675	49	7%	1.8	0.1	1	1.6	0.9	
Office 125A	AHU-1	AHU	12.0	9.6	115	11.5	1,325	275	20	7%	12.5	0.9	1	17.6	5.9	
Office 125B	AHU-1	AHU	12.0	11.1	133	11.5	1,532	190	14	7%	7.4	0.5	1	13.7	3.5	

Date: 5/7/2021

Readings By: Mayer & Davis



AIRFLOW SURVEY REPORT

Project: Portland Public Schools Airflow Testing
Location: King ES; 4906 NE 6th Ave, Portland, OR 97211
Filter Status: Not Upgraded

Room Floor Plan # (Actual #)	Equipment Info		Room Dimensions					Airflow Measurements			Calculated ACH						Notes
	Served By	Equipment Type	Room Length	Room Width	Room Area	Room Height	Room Volume	Total CFM Supply	OA CFM Supply	OA %	Air Changes per Hour (supply)	Air Changes per Hour (OA)	# of Portable Filters	Total Effective Air Changes per Hour (ACH_e) with Portable Filter	Total Effective Air Changes per Hour (ACH_e) without Portable Filter		
First Floor																	
Office 130	-	-	-	-	-	-	-	-	-	-	0.0	0.0	0	N/A	0.0	All closet space, ventilation supplied from adjacent. Rm 130A & 130B are the same space.	
Offices 130A & 130B	AHU-1	AHU	23.5	7.5	176	8.6	1,516	35	3	7%	1.4	0.1	1	10.9	0.7		
Offices C7 & C8	AHU-1	AHU	19.4	9.4	182	11.3	2,061	105	8	7%	3.1	0.2	1	9.0	1.4	Served by AHU. There is no center wall, all one room. Copy 110 used for storage.	
Office C9	AHU-1	AHU	9.6	9.5	91	7.8	711	25	2	7%	2.1	0.2	0	N/A	1.0		
Office C10 (111)	AHU-1	AHU	9.5	9.7	92	7.8	719	35	3	7%	2.9	0.2	1	23.1	1.4		
Library 101	AHU-1	AHU	59.7	49.9	2,979	24.9	74,178	8,810	617	7%	7.1	0.5	1	3.6	3.3		
120B	UV	UV	29.5	21.9	646	12.1	7,817	725	50	7%	5.6	0.4	1	4.6	2.6		
111	-	-	2.5	5.1	13	7.6	97	-	-	-	0.0	0.0	0	N/A	0.0	Electrical Closet.	
140B	UV	UV	29.4	23.6	694	12.2	8,465	1,335	125	9%	9.5	0.9	1	6.4	4.5		
143	-	-	20.0	18.5	370	11.9	4,403	-	-	-	0.0	0.0	1	3.5	0.0	Ventilation supplied by Cafeteria.	
144	-	-	53.3	30.3	1,615	12.0	19,380	-	-	-	0.0	0.0	1	0.8	0.0	Ventilation supplied by Cafeteria.	
144A	-	-	-	-	-	-	-	-	-	-	0.0	0.0	0	N/A	0.0	No access. This is the walk-in cooler.	
Cafeteria 146	SF2	AHU	73.9	60.0	4,434	18.9	83,803	4,920	4,920	100%	3.5	3.5	1	3.0	2.8	Note #3 , Unit in Boys RR 2nd Flr. Labeled café	
146A	-	-	17.8	39.8	708	14.8	10,485	-	-	-	0.0	0.0	1	1.5	0.0	Ventilation supplied by Cafeteria.	
Gym 148	SF#2	AHU	59.9	81.2	4,864	22.2	107,978	2,400	180	8%	1.3	0.1	1	0.8	0.6		
148C	-	-	13.5	14.0	189	11.5	2,174	-	-	-	0.0	0.0	1	7.2	0.0	Ventilation supplied by Gym.	
151	UV	UV	29.9	22.1	661	12.2	8,062	755	50	7%	5.6	0.4	1	4.6	2.6		
152	UV	UV	29.6	22.2	657	12.2	8,017	890	65	7%	6.7	0.5	1	5.1	3.1		
160A	-	-	13.3	14.1	188	14.0	2,625	-	-	-	0.0	0.0	1	5.9	0.0	Ventilation supplied by hallway.	
109A	-	-	5.5	6.9	38	7.6	288	-	-	-	0.0	0.0	1	54.1	0.0	Ventilation supplied by hallway.	
Second Floor																	
Rm 201	UV	UV	30.0	22.0	660	12.3	8,118	715	45	6%	5.3	0.3	1	4.4	2.5		
Rm 202	UV	UV	30.0	21.9	657	12.3	8,081	685	45	7%	5.1	0.3	1	4.3	2.4		
Rm 203	UV	UV	30.0	21.9	657	12.3	8,081	590	60	10%	4.4	0.4	1	4.0	2.1		

Date: 5/7/2021

Readings By: Mayer & Davis



AIRFLOW SURVEY REPORT

Project: Portland Public Schools Airflow Testing
Location: King ES; 4906 NE 6th Ave, Portland, OR 97211
Filter Status: Not Upgraded

Room Floor Plan # (Actual #)	Equipment Info		Room Dimensions					Airflow Measurements			Calculated ACH					Notes
	Served By	Equipment Type	Room Length	Room Width	Room Area	Room Height	Room Volume	Total CFM Supply	OA CFM Supply	OA %	Air Changes per Hour (supply)	Air Changes per Hour (OA)	# of Portable Filters	Total Effective Air Changes per Hour (ACH_e) with Portable Filter	Total Effective Air Changes per Hour (ACH_e) without Portable Filter	
Second Floor																
Rm 204	UV	UV	30.0	21.9	657	12.3	8,081	835	370	44%	6.2	2.7	1	5.7	3.7	
Rm 205	UV	UV	30.0	21.9	657	12.3	8,081	820	60	7%	6.1	0.4	1	4.8	2.9	
Rm 206	UV	UV	30.0	22.0	660	12.3	8,118	860	40	5%	6.4	0.3	1	4.9	2.9	
Rm 210	Classroom Fan	AHU	30.6	28.2	863	12.1	10,441	235	17	7%	1.4	0.1	1	2.1	0.6	Note #2, Boys RR 2nd Flr. Labeled "Classroom Fan"
Rm 211	Classroom Fan	AHU	30.0	27.6	828	12.2	10,102	420	30	7%	2.5	0.2	1	2.7	1.2	Note #2, Boys RR 2nd Flr. Labeled "Classroom Fan"
Rm 212	Classroom Fan	AHU	30.9	27.8	859	12.2	10,480	450	32	7%	2.6	0.2	1	2.7	1.2	Note #2, Boys RR 2nd Flr. Labeled "Classroom Fan"
Rm 213	Classroom Fan	AHU	30.9	27.8	859	12.2	10,480	790	57	7%	4.5	0.3	1	3.6	2.1	Note #2, Boys RR 2nd Flr. Labeled "Classroom Fan"
Rm 223	UV	UV	30.0	21.9	657	12.3	8,081	690	50	7%	5.1	0.4	1	4.3	2.4	
Rm 224	UV	UV	30.0	21.9	657	12.2	8,015	730	35	5%	5.5	0.3	1	4.5	2.5	
Rm 228	UV	UV	29.9	21.9	655	12.3	8,054	682	100	15%	5.1	0.7	1	4.5	2.5	
Rm 229	UV	UV	29.9	21.9	655	12.2	7,989	665	75	11%	5.0	0.6	1	4.4	2.4	
Rm 230	UV	UV	29.9	21.8	652	12.2	7,952	670	450	67%	5.1	3.4	1	5.4	3.5	
Rm 233	UV	UV	30.0	22.1	663	12.2	8,089	715	45	6%	5.3	0.3	1	4.4	2.5	
Rm 234	UV	UV	30.0	24.3	729	12.2	8,894	870	105	12%	5.9	0.7	1	4.6	2.9	
Rm 235	UV	UV	30.0	21.9	657	12.3	8,081	550	45	8%	4.1	0.3	1	3.9	1.9	
Office 201A	-	-	16.9	12.7	215	9.3	1,996	-	-	-	0.0	0.0	1	7.8	0.0	Open air to the hallway.
Office 207	-	-	14.9	18.0	268	12.2	3,272	-	-	-	0.0	0.0	1	4.8	0.0	Ventilation is supplied from adjacent spaces.
Conf Rm 218	Classroom Fan	AHU	13.0	10.0	130	8.7	1,131	88	6	7%	4.7	0.3	1	16.0	2.2	
Office 239	SF#2	AHU	17.5	12.3	215	12.3	2,648	90	7	8%	2.0	0.2	1	6.9	1.0	
208	-	-	11.2	12.2	137	12.2	1,667	-	-	-	0.0	0.0	1	9.4	0.0	Ventilation is supplied from adjacent spaces.
220	-	-	50.6	16.0	810	15.5	12,549	-	-	-	0.0	0.0	1	1.2	0.0	Ventilation is supplied from adjacent spaces.
251	SF#2	AHU	18.6	16.9	314	12.3	3,866	30	2	8%	0.5	0.0	1	4.3	0.2	

Date: 5/7/2021



Readings By: Mayer & Davis



Location: King ES; 4906 NE 6th Ave, Portland, OR 97211

Page 12 of 15

KING: Lower Level 1

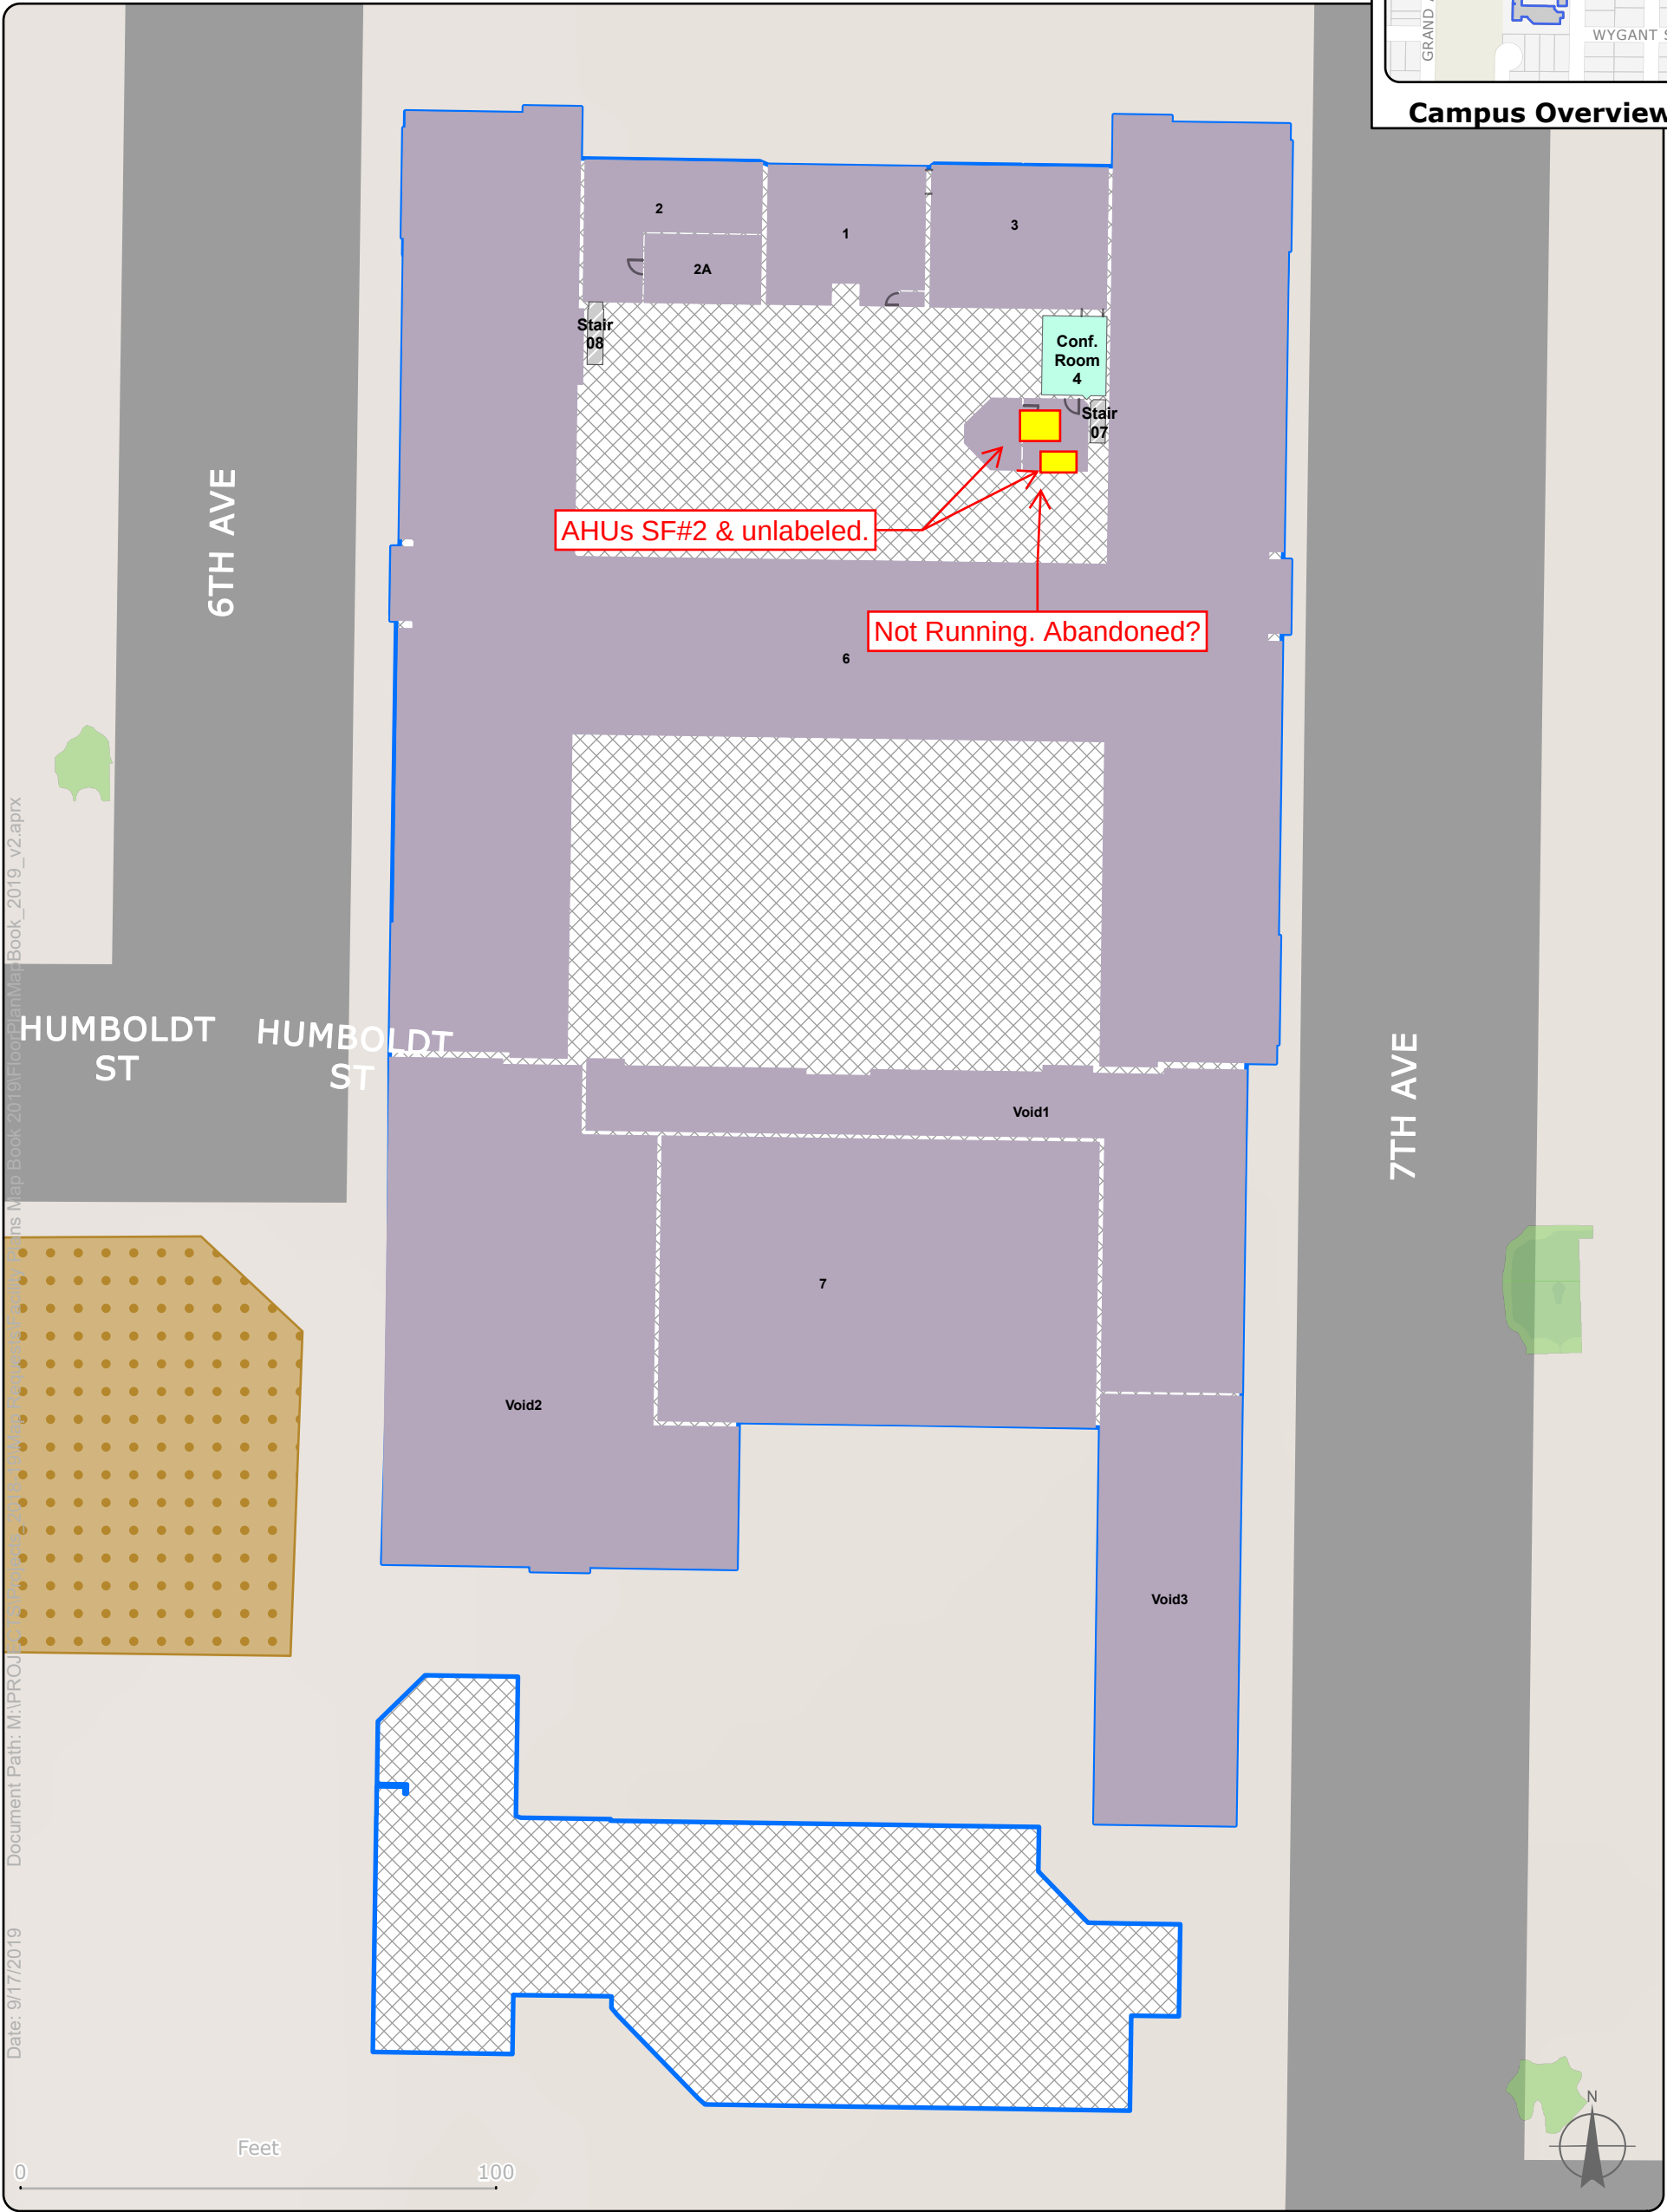
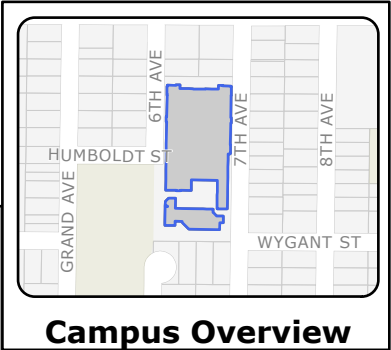


Space Use		School Grounds	
	Classroom		Campus Footprints
	Office		Athletic Field
	Rest Room		Playground: Paved
	Special Purpose		Playground: Unpaved
	Corridor		Streets
	Other		Doors
	Stairs/Elevator		

Total Number Of Rooms By Classification

Classrooms: 0	Special Purpose: 0
Office Spaces: 1	Storage: 3



KING: First Floor

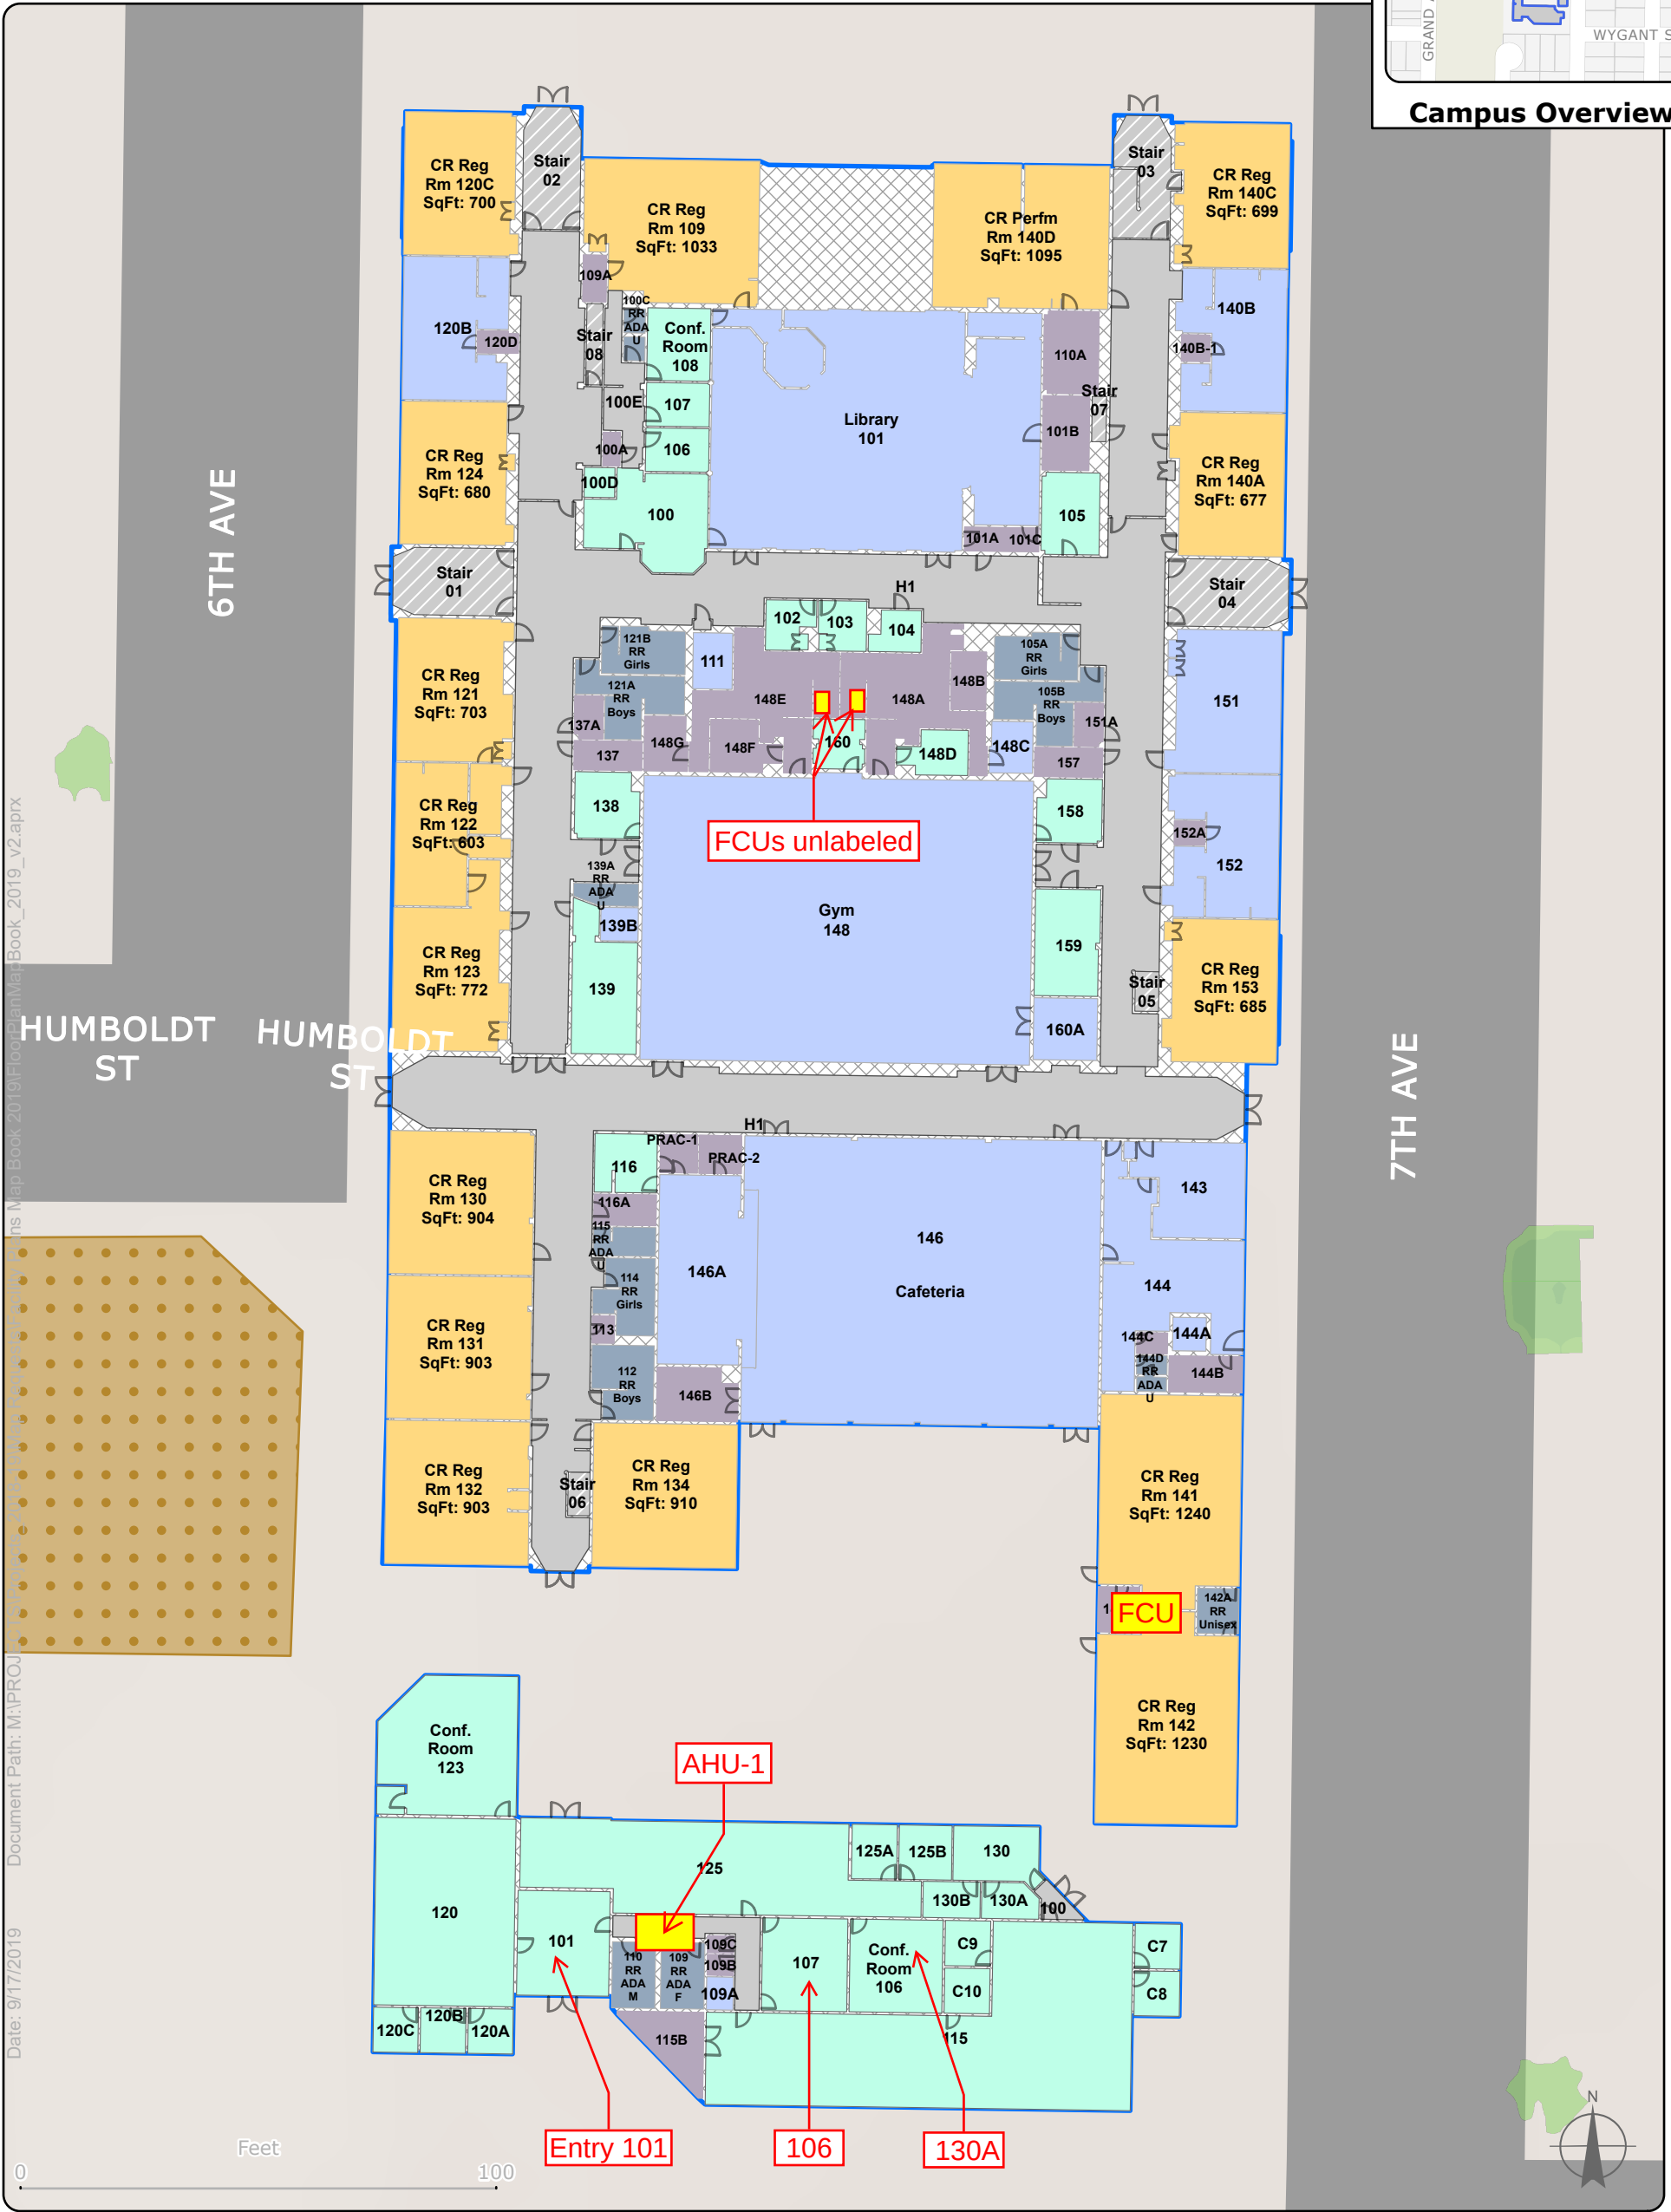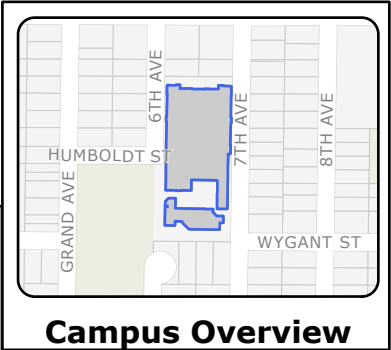

Space Use		School Grounds	
	Classroom		Campus Footprints
	Office		Athletic Field
	Rest Room		Playground: Paved
	Special Purpose		Playground: Unpaved
	Corridor		Streets
	Other		Doors
	Stairs/Elevator		

Total Number Of Rooms By Classification			
Classrooms: 16		Special Purpose: 16	
Office Spaces: 35		Storage: 25	

KING: Second Floor

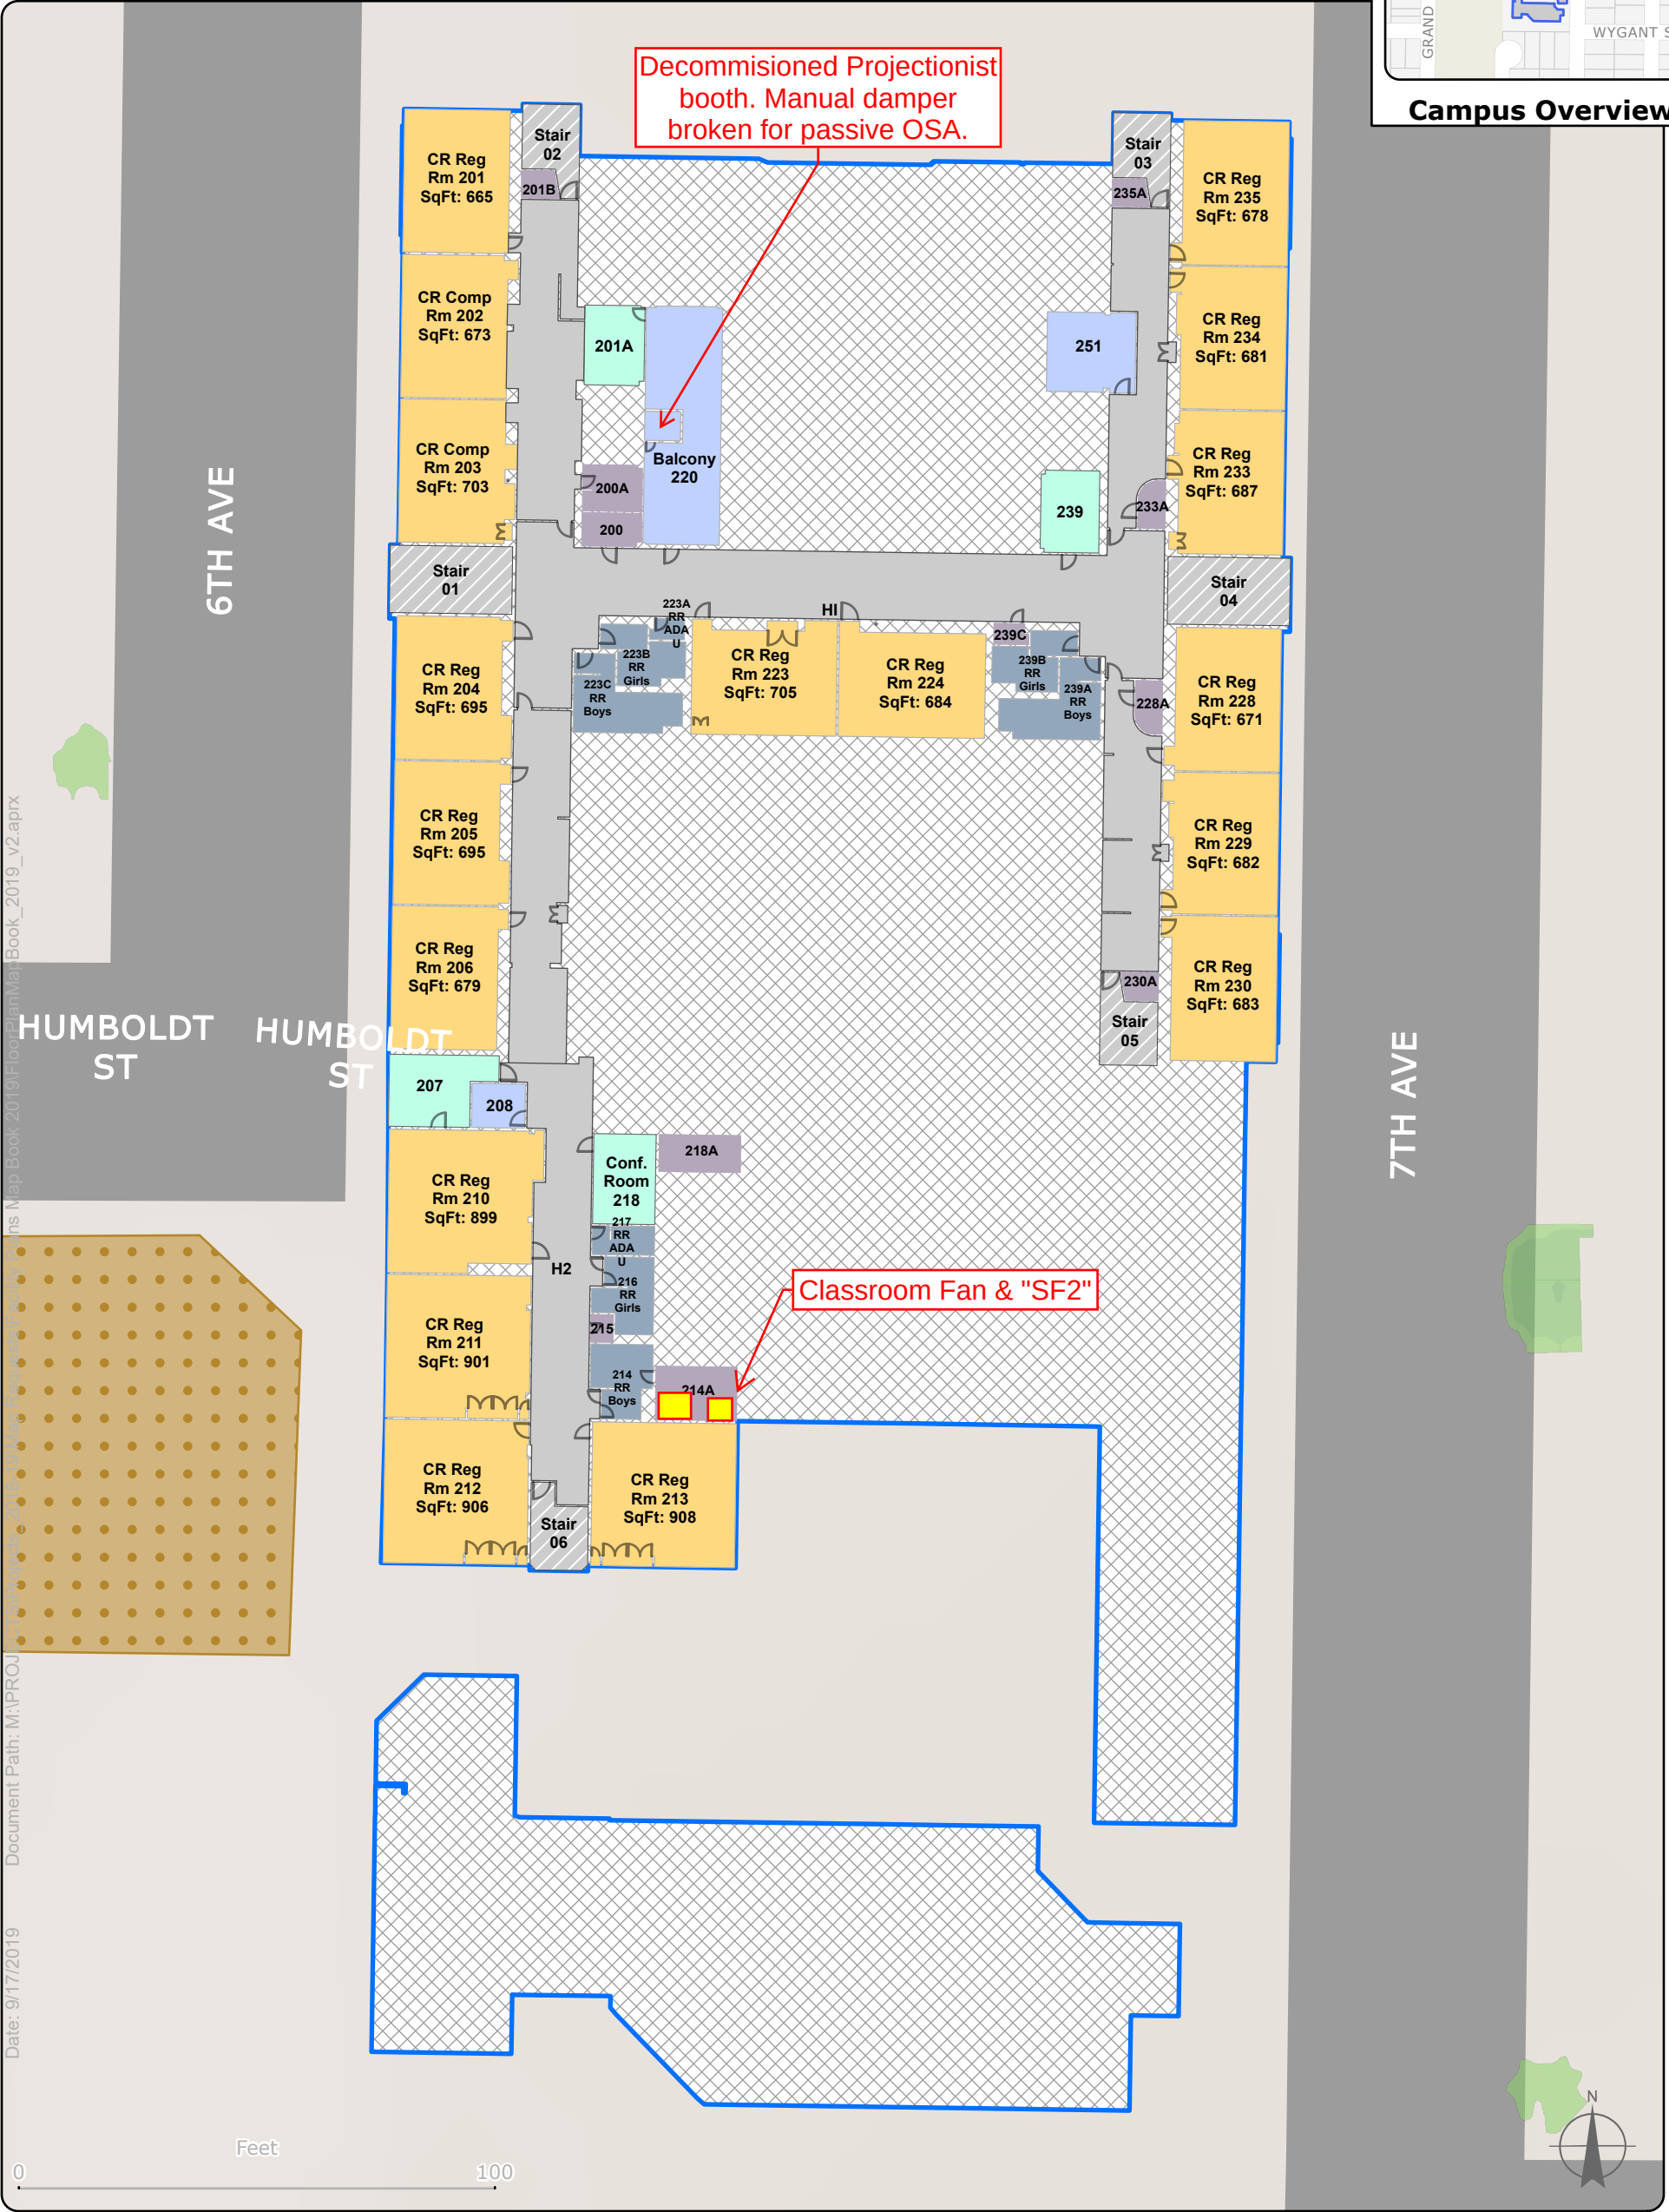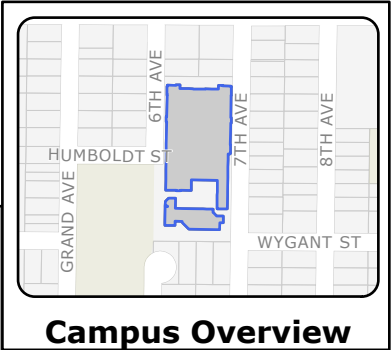

Space Use		School Grounds	
	Classroom		Campus Footprints
	Office		Athletic Field
	Rest Room		Playground: Paved
	Special Purpose		Playground: Unpaved
	Corridor		Streets
	Other		Doors
	Stairs/Elevator		

Total Number Of Rooms By Classification

Classrooms: 18	Special Purpose: 4
Office Spaces: 4	Storage: 8
