



Airflow Testing Report

Prepared for

Portland Public Schools

August 2021





9700 SW Capitol Hwy, Suite 110
Portland, OR 97219
ameresco.com

PROJECT OVERVIEW

As part of the continuing process to ensure a safe return to in-person learning, Portland Public Schools has contracted with Ameresco to test the airflow and ventilation of all educational and office spaces in each school. The data is reviewed by both Ameresco and PPS personnel to identify any potential shortcomings in the airflow from the HVAC systems. To accomplish this task, Ameresco has partnered with a local NEBB certified Test-Adjust-Balance (TAB) firm, Neudorfer Engineers, who will measure the airflow to each zone with calibrated measurement equipment in accordance with current testing standards and procedures. As part of this effort, HVAC professionals will review the operation of the HVAC equipment serving every educational and office space in each school.

Ameresco is pleased to have partnered with PPS over the last decade as the district's Energy Services Company (ESCO) on six energy efficiency construction projects, four service projects, and numerous energy audits. Our partnership has resulted in reducing over 3,000 tons of CO₂ and other GHG emissions and over \$1,000,000 in utility cost savings per year. Ameresco appreciates this opportunity to play a small role in the safe reopening of schools.

About Ameresco, Inc.

Founded in 2000, Ameresco, Inc. (NYSE:AMRC) is a leading cleantech integrator and renewable energy asset developer, owner and operator. Our comprehensive portfolio includes energy efficiency, infrastructure upgrades, asset sustainability and renewable energy solutions delivered to clients throughout North America and the United Kingdom. Ameresco's sustainability services in support of clients' pursuit of Net Zero include upgrades to a facility's energy infrastructure and the development, construction, and operation of distributed energy resources. Ameresco has successfully completed energy saving, environmentally responsible projects with Federal, state and local governments, healthcare and educational institutions, housing authorities, and commercial and industrial customers. With its corporate headquarters in Framingham, MA, Ameresco has more than 1,000 employees providing local expertise in the United States, Canada, and the United Kingdom. For more information, visit www.ameresco.com.

Explanation of ASHRAE Total Effective Air Changes per Hour (ACH_e) Calculation

ASHRAE has been updating their Building Readiness document to reflect the most current understanding in the engineering community for how to operate and maintain buildings during the pandemic. Their update on 4/27/2021 provided an explanation of the impact air filters and air cleaning devices have on the air in buildings. They provided the methodology, formulas, and an Excel-based tool for determining the equivalent outside air a space is receiving by having a mix of outside air, filtered recirculated air, and additional air filtration or cleaning devices in the room. Here is the explanation from ASHRAE:

Epidemic Conditions in Place



Equivalent Outdoor Air:

The equivalent outdoor air calculation indicates that the outdoor air can be calculated by using the combination of the actual outdoor air, impact of filtration or air cleaning technologies on recirculated air, and the impact of air cleaning technologies in the space.

This is using the principal of filters in series and the effectiveness at reducing particles. For items in series, the initial item would see the recirculated airflow to clean. The second item in the series would see the “cleaned” air from Item 1 and so the impact of Item 1 must be accounted for in Item 2.

As part of the airflow testing project that Portland Public Schools has partnered with Ameresco to complete, we are including the calculation of the Total Effective Air Changes per Hour (ACH_e) to show the impact of the air filtration that is active in nearly all spaces in the PPS schools. The formula for doing so is:

$$ACH_e = (ACH_{oa} + ACH_f) * E_z + ACH_{ir}$$

where:

- ACH_{oa} = air changes per hour of outside air = outside airflow in cubic feet per minute * 60 minutes per hour / room volume in cubic feet
- ACH_f = air changes per hour of clean air from filtered recirculated air with filters of the specified MERV rating as determined by ASHRAE
- E_z = Zone Air Distribution Effectiveness = how effective the HVAC system is at circulating and mixing the air to distribute the clean air throughout the room
- ACH_{ir} = the air changes per hour of clean air from portable air filters in the room = number of filters * CADR * 60 minutes per hour / room volume in cubic feet
 - CADR = Clear Air Delivery Rate = the CFM of clean air as specified by the manufacturer of the air filter

In order to include these calculations in the airflow testing reports, Ameresco and PPS have made the following assumptions as not all the variables are known:

1. PPS is in process of upgrading the air filters in their HVAC systems to MERV 13 and plans to be complete with that project for the start of the '21-'22 school year. In this report and for the sake of the ACH_e calculation, we are using the filters that are in place at the time of the measurements, so some of them are still MERV 8.
2. ASHRAE has guidelines for what should be used for the Zone Air Distribution Effectiveness (E_z) based on the HVAC system configuration, but they do not provide a value for every HVAC system and room configuration. For the majority of PPS rooms, an E_z of 0.8 – 1.0 would be most appropriate, so we have made the conservative assumption of using 0.8 for every space as that yields the lower ACH_e.
3. The CADR for a given air filter is from manufacturer ratings and is based on certain conditions (fan speed, particulate size, filter cleanliness, etc.) that change with operating conditions.



NEUDORFER ENGINEERS INC.

**TEST REPORT TYPE:
SURVEY REPORT**

Portland Public Schools Airflow Testing Roseway Heights MS

Job Number: 2021-0297

Project Completion Date: November 2021

Revision Date:

-


Revision Number:

-



SEATTLE

5516 1st Avenue South
Seattle, Washington 98108
Phone (206) 621-1810
Fax (206) 343-9820



PORTLAND

2501 SE Columbia Way, Suite 230
Vancouver, Washington 98661
Phone (503) 235-8924
Fax (503) 235-8925



Neudorfer Engineers, Inc.

Consulting Engineers Seattle, Washington - Portland, Oregon



www.NeudorferEngineers.com

**Portland Public Schools Airflow Testing
Roseway Heights MS**

TABLE OF CONTENTS

Title Sheet	3
Report Certification	4
Terms	5
Instrument Calibration	6
Report Summary	7
Airflow Survey Report	8
TAB Notes	12
Floor Layout	13



Neudorfer Engineers, Inc.

Consulting Engineers Seattle, Washington - Portland, Oregon



www.NeudorferEngineers.com

REPORT TITLE

CERTIFIED TEST: SURVEY REPORT

Project: Portland Public Schools Airflow Testing
Roseway Heights MS

NEI Job#: 2021-0297

Mechanical Engineer: NA

Architect: NA

HVAC Contractor: NA

TAB Firm: Neudorfer Engineers Inc
Test Engineer: Zach Mayer



5516 1st Ave South
Seattle, Washington 98108
Phone (206) 621-1810
Fax (206) 343-9820



2501 SE Columbia Way, Suite 230
Vancouver, Washington 98661
Phone (503) 235-8924
Fax (503) 235-8925

CERTIFICATION

Portland Public Schools Airflow Testing

The data presented in this report is a record of system measurements and final adjustments that have been obtained in accordance with the current edition of the NEBB Procedural Standards for Testing, Adjusting, and Balancing of Environmental Systems. Any variances from design quantities, which exceed NEBB tolerances, are noted in the Test-Adjust-Balance Report Project Summary.

Significant / Noteworthy Remarks are noted on the General Remarks and General Field Notes pages. Other remarks are noted on individual test sheets.

Noted deficiencies are not the TAB firms responsibility to repair. Prior to issuance of this report, Deficiency Reports are forwarded to our contracted agent.

Warranty is limited to one year from date of this report. Within that time, any discrepancies, ambiguities, or omissions found in this report will be retested, adjusted, or balanced as needed. A written notification will be required.

Submitted and Certified by:

NEBB TAB Firm: **Neudorfer Engineers Inc**

Certification No: **3414**

Expiration Date: **March 31, 2023**

Certification Date: **March 31, 2021**

(Date completed) Signed and Sealed by:

NEBB Supervisor: **Mike Vawter P.E.**

NEBB Supervisor: **Eric Stotts**





Neudorfer Engineers, Inc.

Consulting Engineers Seattle, Washington - Portland, Oregon



www.NeudorferEngineers.com

TERMS AND ABBREVIATIONS

Project: **Portland Public Schools Airflow Testing**

AC or ACU Air Conditioner or Air Conditioning Unit

AH or AHU Air Handler or Air Handling Unit

ACH Air Changes per Hour

AVG Average

BHP Brake Horsepower

CAV Constant Air Volume

CBV Calibrated Balancing Valve
(Circuit Setter)

CC Cooling Coil

CD Ceiling Diffuser

CFM Cubic Feet per Minute

CH Chiller

CHWS Chilled Water Supply

CHWR Chilled Water Return

CP Circulating Pump

CR Ceiling Register

CRAC Computer Room Air Conditioner

CRU Computer Room Unit

CT Cooling Tower

CU Condenser Unit

CUH Cabinet Unit Heater

CWS Condenser Water Supply

CWR Condenser Water Return

DAT Discharge Air Temperature

DB Dry Bulb

DD Direct Drive

DDC Direct Digital Controls: EMS Control
System for the HVAC

Des. Design

Dia. Diameter

Disch. Discharge

EA Exhaust Air

EAT Entering Air Temperature

Economizer Controls and components that allow an
air handler to logically utilize outdoor air
for cooling as opposed to the use of
mechanical cooling.

EF Exhaust Fan

EG Exhaust Grille

EMCS Energy Management Control System

ERU Energy Recovery Unit

E.S.P. External Static Pressure

HRC Heat Recovery Coil

EWT Entering Water Temperature

FCU Fan Coil Unit

FD Fire Damper

FSD Fire Smoke Damper

FLA Full Load Amperage: Maximum
amperage a motor can draw.

Flow Hood Instrument that captures air and
converts the reading to CFM.

FHT Fume Hood Test

FPB Fan Powered Box

FPM Feet per Minute

FR Field Report

FT Foot, Feet

FTU Fan Terminal Unit

GPM Gallons per Minute

HC Heating Coil

TDH Pressure Difference across the entering
and leaving side of a pump.

HEPA High Efficiency Particulate Absorbing

HP Horsepower

HVAC Heating Ventilation and Air Conditioning

HWS Heating Water Supply

HWR Heating Water Return

HX Heat Exchanger

HZ Hertz, cycle per second

in. inches

in.w.g. inches of water gauge

Kfactor Correction factor to the free area need to
calculate CFM.

KW Kilowatts

LAT Leaving Air Temperature

LBWG Low Wall Grille

LWR Low Wall Register

LWT Leaving Water Temperature

MAU Make-up Air Handling Unit

MBH 1,000 BTUH

N/A Not Applicable

OSA Outside Air

OBD Opposed Blade Damper

ΔP Pressure Drop.

PH Phase

PSI Pounds per Square Inch

RA Return Air

RAT Return Air Temperature

RF Return Fan

RH Relative Humidity

RHC Reheat Coil

RPM Revolutions per Minute

RTU Roof Top Unit

SA Supply Air

SAT Supply Air Temperature

S.F. Service Factor

SF Supply Fan

SFD Smoke/Fire Damper

SP Static Pressure

sq.ft. square feet

Suct. Suction

SWG Sidewall Grille

SWR Sidewall Register

TAB Test; Adjust; and Balance

TSP Total Static Pressure: Difference
between the entering and leaving
static pressure of a fan.

UH Unit Heater

VAV Variable Air Volume; box that
contains a motorized damper that
modulates airflow.

VD Volume Damper

VFD Variable Frequency Drive

Velgrid Instrument that reads used to read
velocity in feet per minute.

VVT Variable Volume Terminal

WC Water Column

W.G. Water Gauge

WB Wet Bulb

INSTRUMENT CALIBRATIONS

Portland Public Schools Airflow Testing

Roseway Heights MS

Instrument Type	Air Data Meter with Flowhood	Instrument Serial #	M97410
Instrument Manufacturer	Shortridge	Calibration Date	10/4/2021
Instrument Model Number	ADM 860	Calibration Due	10/4/2022
Instrument Type	Differential Pressure Water Meter	Instrument Serial #	W12178
Instrument Manufacturer	Shortridge	Calibration Date	10/4/2021
Instrument Model Number	HDM-250	Calibration Due	10/4/2022
Instrument Type	Psychrometer	Instrument Serial #	181128924
Instrument Manufacturer	Extech	Calibration Date	10/1/2021
Instrument Model Number	RH390	Calibration Due	10/1/2022
Instrument Type	Tachometer	Instrument Serial #	B185B5022P
Instrument Manufacturer	Nidec	Calibration Date	10/1/2021
Instrument Model Number	MT-200	Calibration Due	10/1/2022
Instrument Type	Amp Probe	Instrument Serial #	33380179WS
Instrument Manufacturer	Fluke	Calibration Date	10/1/2021
Instrument Model Number	323 Clamp Meter	Calibration Due	10/1/2022
Instrument Type	Digital Thermometer	Instrument Serial #	45400509WS
Instrument Manufacturer	Fluke	Calibration Date	10/1/2021
Instrument Model Number	52 II	Calibration Due	10/1/2022
Instrument Type	Manometer	Instrument Serial #	M97410
Instrument Manufacturer	Shortridge	Calibration Date	10/4/2021
Instrument Model Number	ADM 860	Calibration Due	10/4/2022
Instrument Type	Thermal Anemometer	Instrument Serial #	AVM440808002
Instrument Manufacturer	Alnor Instruments	Calibration Date	9/22/2021
Instrument Model Number	AVM 440	Calibration Due	9/22/2022
Instrument Type	Ultrasonic Flow Meter	Instrument Serial #	N1F1823T
Instrument Manufacturer	Fuji	Calibration Date	9/20/2021
Instrument Model Number	Portaflow-C	Calibration Due	9/20/2022



PROJECT	Portland Public Schools Airflow Testing
LOCATION	Roseway Heights MS; 7334 NE Siskiyou St, Portland, OR 97213

REPORT SUMMARY

This project has been surveyed per plans and specifications using the National Environmental Balancing Bureau (NEBB) standards and procedures.

The scope of work for this project was to assess the current airflows for each classroom, office, and special purpose space. Air changes per hour were calculated along with the % of OSA for the spaces and any deficiencies found for each piece of equipment has been noted in the following report.

All ventilation equipment was commanded to run by the BMS system. Ventilation units were measured with a flowhood on the supply outlets. Outside air was recorded with a flowhood on the OSA louvre where accessible. AK factors were calculated from flowhood readings. The remaining OSA values were recorded with a velgrid. AHU supply air was recorded by a summation of the outlets as recorded by flowhood or velgrid when appropriate. Outside air was recorded with a velgrid or airfoil and calculated by the free area method.

The measured airflows in this report represent the performance of the equipment at the time of measurement, which vary over time based on operating conditions. There are factors outside the control of Neudorfer that impact airflow, and variance in those factors is expected and normal. One significant factor is the MERV rating and condition of the air filters on the equipment. During the summer of 2021, PPS began upgrading the filters on all their fan systems to MERV 13. Those upgraded filters are more effective at capturing particles but also impact the amount of airflow from the equipment. These filter changes were occurring while the airflow measurement project was happening, so some schools had the new filters, and some had the old filters at the time of measurement. On the data page included this report, there is a line stating whether or not the upgraded filters were in place at the time of measurement.



AIRFLOW SURVEY REPORT

Project: Portland Public Schools Airflow Testing
Location: Roseway Heights MS; 7334 NE Siskiyou St, Portland, OR 97213
Filter Status: Upgraded

Room	Equipment Info		Room Dimensions					Airflow Measurements			Calculated ACH					Notes
	Served By	Equipment Type	Room Length	Room Width	Room Area	Room Height	Room Volume	Total CFM Supply	OA CFM Supply	OA %	Air Changes per Hour (supply)	Air Changes per Hour (OA)	# of Portable Filters	Total Effective Air Changes per Hour (ACH_e) with Portable Filter	Total Effective Air Changes per Hour (ACH_e) without Portable Filter	
Lower Level 1																
003	-	-	9.1	13.0	118	8.3	982	-	-	-	0.0	0.0	0	N/A	0.0	Electrical panel room.
006	HVU-8	AHU	23.5	30.0	705	10.1	7,121	850	850	100%	7.2	7.2	1	7.9	5.7	Note #1
007	HVU-8	AHU	39.6	37.6	1,146	10.2	11,685	485	485	100%	2.5	2.5	1	3.3	2.0	Note #1. Non-rectangular room.
First floor																
Conf. Room 101	FCU-11	AHU	24.8	28.2	700	11.3	7,910	1,115	468	42%	8.5	3.6	1	8.3	6.4	
146	FCU-11	FCU	10.4	9.0	94	8.8	824	350	147	42%	25.5	10.7	1	38.1	19.2	Open to adjacent space.
102	FCU-10	FCU	15.8	16.1	254	10.0	2,544	330	76	23%	7.8	1.8	1	11.9	5.7	
102A	FCU-10	FCU	8.0	6.3	50	9.0	454	155	36	23%	20.5	4.7	1	49.5	15.1	
102B	FCU-10	FCU	6.2	7.7	48	8.9	425	80	18	23%	11.3	2.6	1	45.1	8.3	
103	FCU-12	FCU	8.3	9.8	81	9.0	732	115	36	31%	9.4	2.9	1	28.3	7.0	
105	FCU-12	FCU	9.0	13.0	117	11.2	1,310	105	33	31%	4.8	1.5	1	15.5	3.6	
107	FCU-12	FCU	12.0	23.8	286	11.2	3,199	195	60	31%	3.7	1.1	1	7.6	2.7	
Rm 109	FCU-13	FCU	23.4	29.0	679	11.5	7,804	1,105	235	21%	8.5	1.8	1	8.3	6.3	
Rm 112	FCU-14	FCU	23.4	29.2	683	11.5	7,858	860	615	72%	6.6	4.7	2	9.1	5.1	
Rm 117	AH-6	AHU	19.8	31.3	620	11.0	6,817	460	460	100%	4.0	4.0	2	7.8	3.2	
Rm 121	AH-6	AHU	20.8	30.1	626	11.1	6,949	870	870	100%	7.5	7.5	1	8.3	6.0	
122	AH-5	AHU	23.4	30.8	721	10.0	7,207	850	306	36%	7.1	2.5	1	7.5	5.3	
Rm 123	AH-6	AHU	32.1	50.1	1,292	10.3	13,310	1,285	1,285	100%	5.8	5.8	1	5.8	4.6	Non-rectangular room.
123A	AH-6	AHU	10.2	11.7	119	10.3	1,229	165	165	100%	8.1	8.1	1	19.1	6.4	
123B	AH-6	AHU	12.0	19.6	235	10.1	2,376	300	300	100%	7.6	7.6	1	12.6	6.1	
124	HV-1	FCU	30.4	41.1	659	8.7	5,737	855	23	3%	8.9	0.2	1	9.2	6.5	Non-rectangular room.
Rm 129	HV-2	FCU	39.9	53.8	2,147	15.8	33,917	2,060	1,140	55%	3.6	2.0	1	3.2	2.8	
Rm 125	AH-6	AHU	32.6	32.7	881	10.7	9,427	1,030	1,030	100%	6.6	6.6	2	8.6	5.2	Non-rectangular room.
129A	AH-6	AHU	9.4	10.7	101	9.0	905	180	180	100%	11.9	11.9	1	26.8	9.5	

Date: 10/28/2021

Readings By: Mayer



AIRFLOW SURVEY REPORT

Project: Portland Public Schools Airflow Testing
Location: Roseway Heights MS; 7334 NE Siskiyou St, Portland, OR 97213
Filter Status: Upgraded

Room	Equipment Info		Room Dimensions					Airflow Measurements			Calculated ACH					Notes
	Served By	Equipment Type	Room Length	Room Width	Room Area	Room Height	Room Volume	Total CFM Supply	OA CFM Supply	OA %	Air Changes per Hour (supply)	Air Changes per Hour (OA)	# of Portable Filters	Total Effective Air Changes per Hour (ACH_e) with Portable Filter	Total Effective Air Changes per Hour (ACH_e) without Portable Filter	
First Floor																
130	-	-	-	-	-	-	-	-	-	-	-	-	0	-	-	This is part of the boiler room.
135	FCU-16	FCU	7.7	9.6	74	9.0	665	155	17	11%	14.0	1.5	1	33.6	10.2	
140	HV-4	FCU	7.1	13.8	98	8.9	872	120	35	29%	8.3	2.4	1	24.0	6.1	
Gym 142	HV-5	FCU	41.0	61.4	2,517	18.5	46,572	2,258	2,132	94%	2.9	2.7	1	2.6	2.3	
142A	HV-6	FCU	12.1	17.5	212	10.0	2,118	255	232	91%	7.2	6.6	1	13.1	5.7	
142B	HV-6	FCU	7.1	12.6	89	9.1	814	80	73	91%	5.9	5.4	1	23.8	4.7	
142D	-	-	10.1	19.6	198	13.9	2,752	-	-	-	0.0	0.0	0	N/A	0.0	This is storage.
145	AH-2B	AHU	16.9	34.1	576	9.9	5,705	2,520	1,915	76%	26.5	20.1	1	23.4	20.7	
145A	AH-2B	AHU	10.1	9.1	92	8.0	735	195	148	76%	15.9	12.1	1	33.6	12.4	
145C	-	-	9.0	24.7	222	8.6	1,912	-	-	-	0.0	0.0	0	N/A	0.0	This is a shower.
152	-	-	7.4	18.7	138	9.0	1,245	-	-	-	0.0	0.0	1	12.5	0.0	Ventilation provided by adjacent spaces.
154	AH-2A	AHU	43.4	17.0	738	10.0	7,378	2,005	241	12%	16.3	2.0	1	14.0	11.9	
155	-	-	12.0	7.2	86	9.0	778	-	-	-	0.0	0.0	1	20.1	0.0	Open to adjacent space.
155A	AH-2A	AHU	6.0	8.7	52	9.0	470	195	23	12%	24.9	3.0	1	51.4	18.2	
155B	-	-	9.0	10.0	90	8.0	720	-	-	-	0.0	0.0	1	21.7	0.0	Ventilation provided by adjacent spaces.
155D	-	-	12.1	6.7	81	9.0	730	-	-	-	0.0	0.0	1	21.4	0.0	Open to adjacent space.
Gym 159	AH-1	AHU	104.2	76.0	7,923	32.8	259,886	21,360	10,830	51%	4.9	2.5	1	3.8	3.7	
161	AH-3	AHU	14.0	23.2	325	10.0	3,248	520	42	8%	9.6	0.8	1	11.8	7.0	
Conf. Room 161C	AH-3	AHU	10.0	13.9	139	9.0	1,251	105	8	8%	5.0	0.4	1	16.1	3.7	
Conf. Room 161D	AH-3	AHU	9.0	13.9	125	9.0	1,126	130	10	8%	6.9	0.6	1	18.9	5.0	
161E	AH-3	AHU	9.0	13.9	125	9.0	1,126	205	16	8%	10.9	0.9	1	21.8	7.9	
Rm 167	AH-8	AHU	28.7	29.3	841	11.6	9,755	1,490	655	44%	9.2	4.0	1	8.5	6.9	
169	AH-3	AHU	11.6	19.6	227	9.9	2,251	150	12	8%	4.0	0.3	1	9.8	2.9	
171	AH-3	AHU	9.2	9.3	86	10.1	864	170	14	8%	11.8	0.9	1	26.6	8.6	

Date: 10/28/2021

Readings By: Mayer



AIRFLOW SURVEY REPORT

Project: Portland Public Schools Airflow Testing
Location: Roseway Heights MS; 7334 NE Siskiyou St, Portland, OR 97213
Filter Status: Upgraded

Room	Equipment Info		Room Dimensions					Airflow Measurements			Calculated ACH					Notes
	Served By	Equipment Type	Room Length	Room Width	Room Area	Room Height	Room Volume	Total CFM Supply	OA CFM Supply	OA %	Air Changes per Hour (supply)	Air Changes per Hour (OA)	# of Portable Filters	Total Effective Air Changes per Hour (ACH_e) with Portable Filter	Total Effective Air Changes per Hour (ACH_e) without Portable Filter	
First Floor																
Rm 175	AH-3	AHU	28.2	28.9	815	11.8	9,617	970	78	8%	6.1	0.5	1	6.0	4.4	
Rm 177	AH-3	AHU	27.5	28.1	773	11.9	9,196	1,085	87	8%	7.1	0.6	1	6.8	5.1	
Rm 181	AH-3	AHU	27.2	28.1	764	11.8	9,019	890	71	8%	5.9	0.5	1	6.0	4.3	
Rm 170	AH-3	AHU	29.0	36.4	1,056	11.8	12,456	945	76	8%	4.6	0.4	1	4.6	3.3	
170A	AH-3	AHU	14.7	26.6	391	11.8	4,614	205	16	8%	2.7	0.2	1	5.3	1.9	
Rm 168	AH-3	AHU	29.0	36.4	1,056	11.8	12,456	1,030	82	8%	5.0	0.4	1	4.9	3.6	
Rm 166	AH-3	AHU	26.6	34.3	912	11.7	10,675	1,015	81	8%	5.7	0.5	1	5.6	4.1	
Rm 182A	FCU-1	FCU	22.3	29.9	667	11.4	7,601	780	710	91%	6.2	5.6	1	6.9	4.9	
Rm 182	FCU-2	FCU	38.6	62.9	2,428	11.5	27,921	650	320	49%	1.4	0.7	1	1.6	1.1	
Rm 184	FCU-5	FCU	23.8	29.0	690	11.5	7,937	750	275	37%	5.7	2.1	1	6.2	4.2	
Rm 185	FCU-3&4	FCU	33.7	49.7	1,675	10.6	17,754	1,890	870	46%	6.4	2.9	1	5.7	4.8	
185A	-	-	4.9	11.8	58	9.6	555	-	-	-	0.0	0.0	0	N/A	0.0	This is storage.
185B	FCU-3	FCU	5.9	11.8	70	9.5	661	135	15	11%	12.2	1.4	1	32.5	8.9	
185C	FCU-3	FCU	9.7	11.8	114	9.5	1,087	110	12	11%	6.1	0.7	1	18.8	4.4	
Rm 187	FCU-6	FCU	23.9	29.2	698	11.5	8,026	990	115	12%	7.4	0.9	1	7.3	5.4	
Rm 189	FCU-7	FCU	23.9	29.2	698	11.5	8,026	1,100	242	22%	8.2	1.8	1	8.0	6.1	
189A	-	-	23.5	8.4	197	12.0	2,369	-	-	-	0.0	0.0	1	6.6	0.0	Ventilation provided by adjacent spaces.
190	FCU-8	FCU	14.8	16.0	237	8.9	2,108	135	135	39%	3.8	3.9	1	10.5	3.1	
191	FCU-8	FCU	11.6	14.7	171	9.0	1,535	90	90	39%	3.5	3.5	1	13.0	2.8	
193	FCU-8	FCU	14.5	14.6	212	9.0	1,905	95	95	39%	3.0	3.0	1	10.6	2.4	
Auditorium 196	HV-3&4	FCU	58.8	66.7	3,922	19.1	74,909	1,935	561	29%	1.5	0.4	2	1.6	1.2	
196A	HV-3	FCU	33.8	15.6	527	16.0	8,436	171	50	29%	1.2	0.4	1	2.8	0.9	Stage area
197	AH-5	AHU	26.2	62.4	1,635	10.3	16,839	2,060	742	36%	7.3	2.6	1	6.4	5.5	
176	HV-7	FCU	19.4	43.9	852	8.8	7,495	435	435	100%	3.5	3.5	1	4.9	2.8	Return damper closed.

Date: 10/28/2021

Readings By: Mayer



AIRFLOW SURVEY REPORT

Project: Portland Public Schools Airflow Testing
Location: Roseway Heights MS; 7334 NE Siskiyou St, Portland, OR 97213
Filter Status: Upgraded



Room	Equipment Info		Room Dimensions					Airflow Measurements			Calculated ACH					Notes
	Served By	Equipment Type	Room Length	Room Width	Room Area	Room Height	Room Volume	Total CFM Supply	OA CFM Supply	OA %	Air Changes per Hour (supply)	Air Changes per Hour (OA)	# of Portable Filters	Total Effective Air Changes per Hour (ACH_e) with Portable Filter	Total Effective Air Changes per Hour (ACH_e) without Portable Filter	
Second Floor																
Rm 202	FCU-30	FCU	23.8	29.0	690	11.7	8,075	775	103	13%	5.8	0.8	1	6.1	4.2	
Rm 201	FCU-31	FCU	23.7	28.9	685	11.5	7,877	685	96	14%	5.2	0.7	1	5.8	3.8	
204	FCU-29	FCU	16.6	21.6	359	11.3	4,052	110	15	14%	1.6	0.2	1	5.0	1.2	
Library 208	FCU-24,26,27&29	FCU	60.2	94.8	4,811	10.6	50,996	400	205	51%	0.5	0.2	3	1.3	0.4	
Conf room 212	FCU-25	FCU	11.4	14.1	161	9.0	1,447	96	12	13%	4.0	0.5	1	13.7	2.9	This is open to library.
213	FCU-25	FCU	5.9	10.4	61	8.9	546	54	7	13%	5.9	0.8	1	32.9	4.3	
214	FCU-22	FCU	10.0	23.8	238	11.5	2,737	100	12	12%	2.2	0.3	1	7.3	1.6	
Rm 216	FCU-22	FCU	23.5	29.1	684	11.6	7,933	792	95	12%	6.0	0.7	1	6.3	4.4	
Rm 219	FCU-23	FCU	26.3	29.0	763	11.7	8,924	460	65	14%	3.1	0.4	1	4.0	2.3	
Rm 222	FCU-18	FCU	23.2	37.5	870	11.6	10,092	1,295	945	73%	7.7	5.6	1	7.5	6.0	
Rm 225	FCU-21	FCU	25.3	29.7	751	11.6	8,716	620	220	35%	4.3	1.5	1	5.0	3.2	
Rm 226	FCU-19	FCU	22.3	31.5	702	11.5	8,078	495	0	0%	3.7	0.0	1	4.6	2.6	OSA damper may be closed.
Rm 227	FCU-20	FCU	22.3	29.9	667	11.5	7,668	480	173	36%	3.8	1.4	3	8.9	2.8	
231	FCU-20	FCU	7.8	11.6	90	10.0	905	85	31	36%	5.6	2.0	1	21.5	4.2	
Rm 234	AH-4	AHU	26.6	32.8	872	11.2	9,772	355	46	13%	2.2	0.3	1	3.2	1.6	
Rm 235	AH-4	AHU	21.5	25.9	557	11.4	6,348	325	42	13%	3.1	0.4	1	4.7	2.2	
Rm 236	AH-4	AHU	27.3	29.0	792	11.2	8,867	455	59	13%	3.1	0.4	1	4.0	2.2	
Rm 237	AH-4	AHU	28.2	28.6	863	11.3	9,746	480	62	13%	3.0	0.4	1	3.8	2.2	
Rm 238	AH-4	AHU	27.3	28.8	786	11.2	8,806	505	66	13%	3.4	0.4	1	4.3	2.5	
Rm 239	AH-4	AHU	26.4	29.5	779	11.3	8,800	610	79	13%	4.2	0.5	1	4.8	3.0	
Rm 240	AH-4	AHU	29.0	30.3	879	11.2	9,841	280	36	13%	1.7	0.2	1	2.8	1.2	
Rm 247	AH-4	AHU	27.3	29.0	792	11.3	8,946	585	76	13%	3.9	0.5	1	4.6	2.9	
Rm 253	AH-4	AHU	27.4	28.2	773	11.2	8,654	590	77	13%	4.1	0.5	1	4.8	3.0	

Date: 10/28/2021

Readings By: Mayer



ROSEWAY HEIGHTS: Lower Level 1

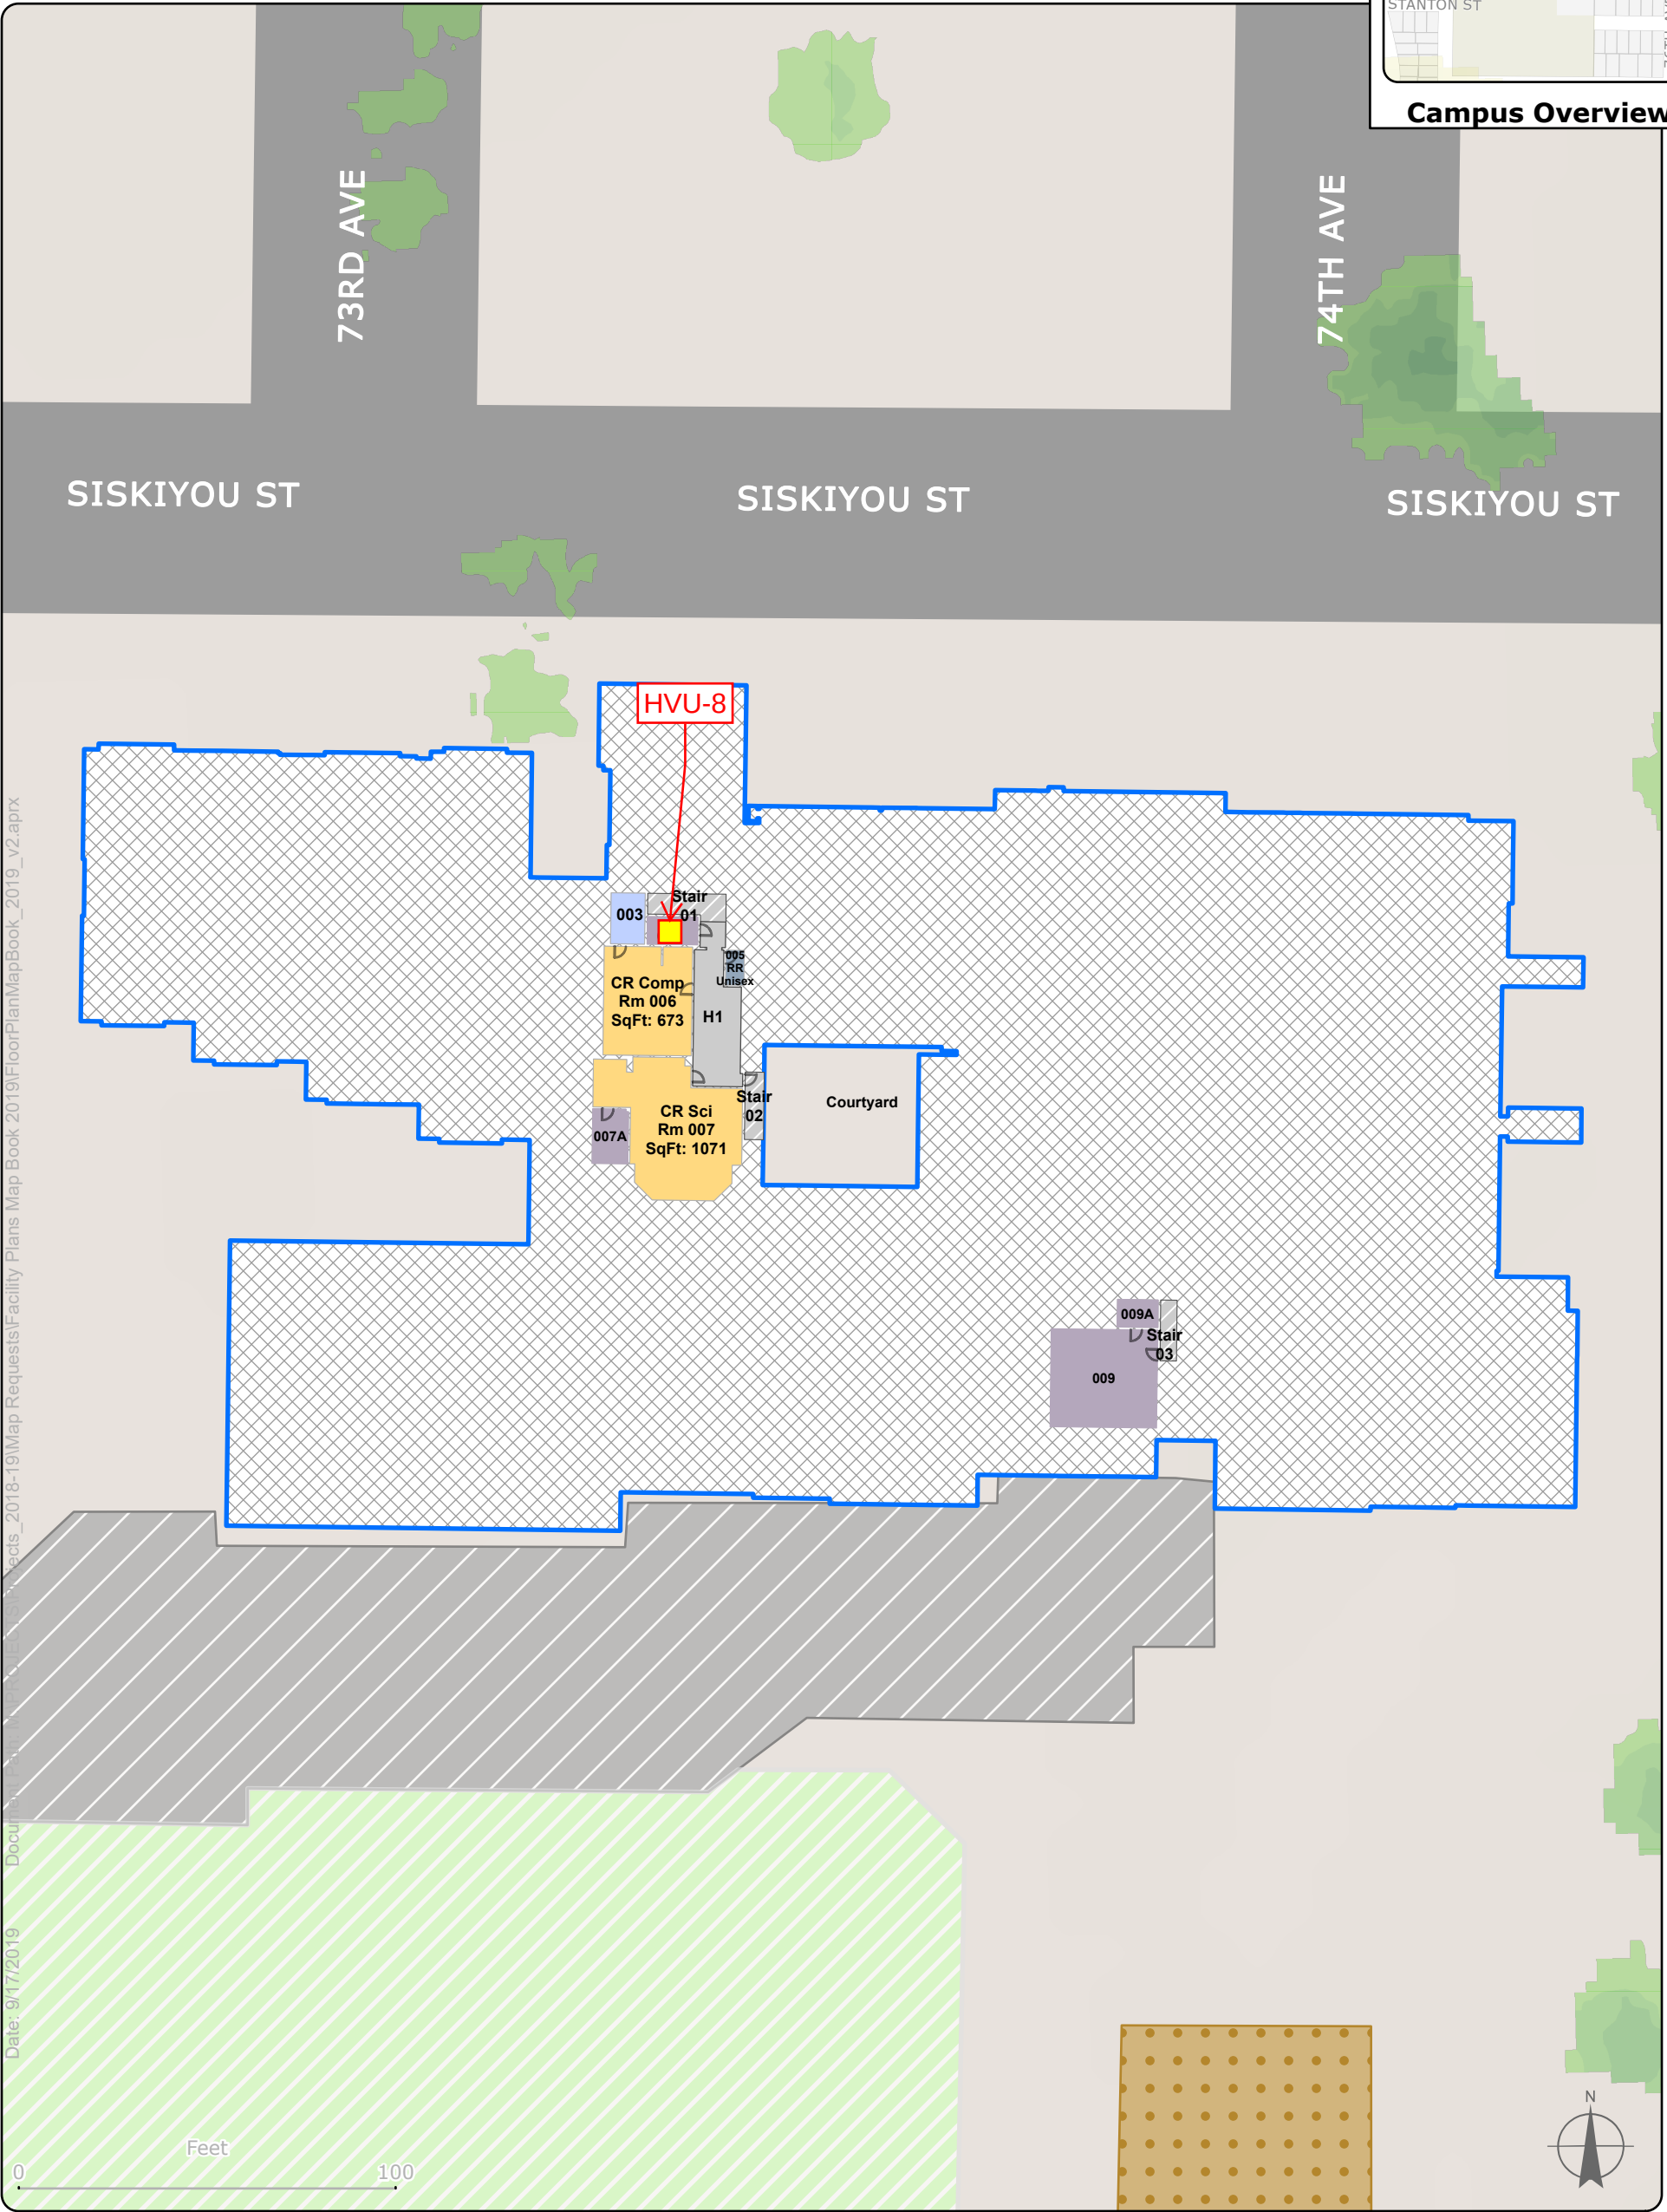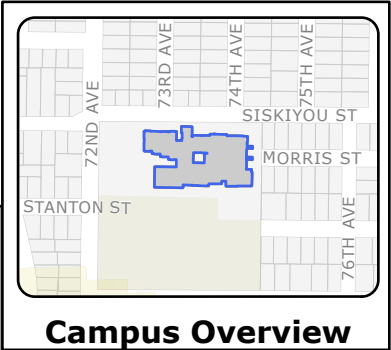

Space Use

Classroom

Office

Rest Room

Special Purpose

Corridor

Other

Stairs/Elevator

School Grounds

Campus Footprints

Athletic Field

Playground: Paved

Playground: Unpaved



Streets

Doors

Total Number Of Rooms By Classification			
Classrooms: 2		Special Purpose: 1	
Office Spaces: 0		Storage: 3	

Page 13 of 15

ROSEWAY HEIGHTS: First Floor

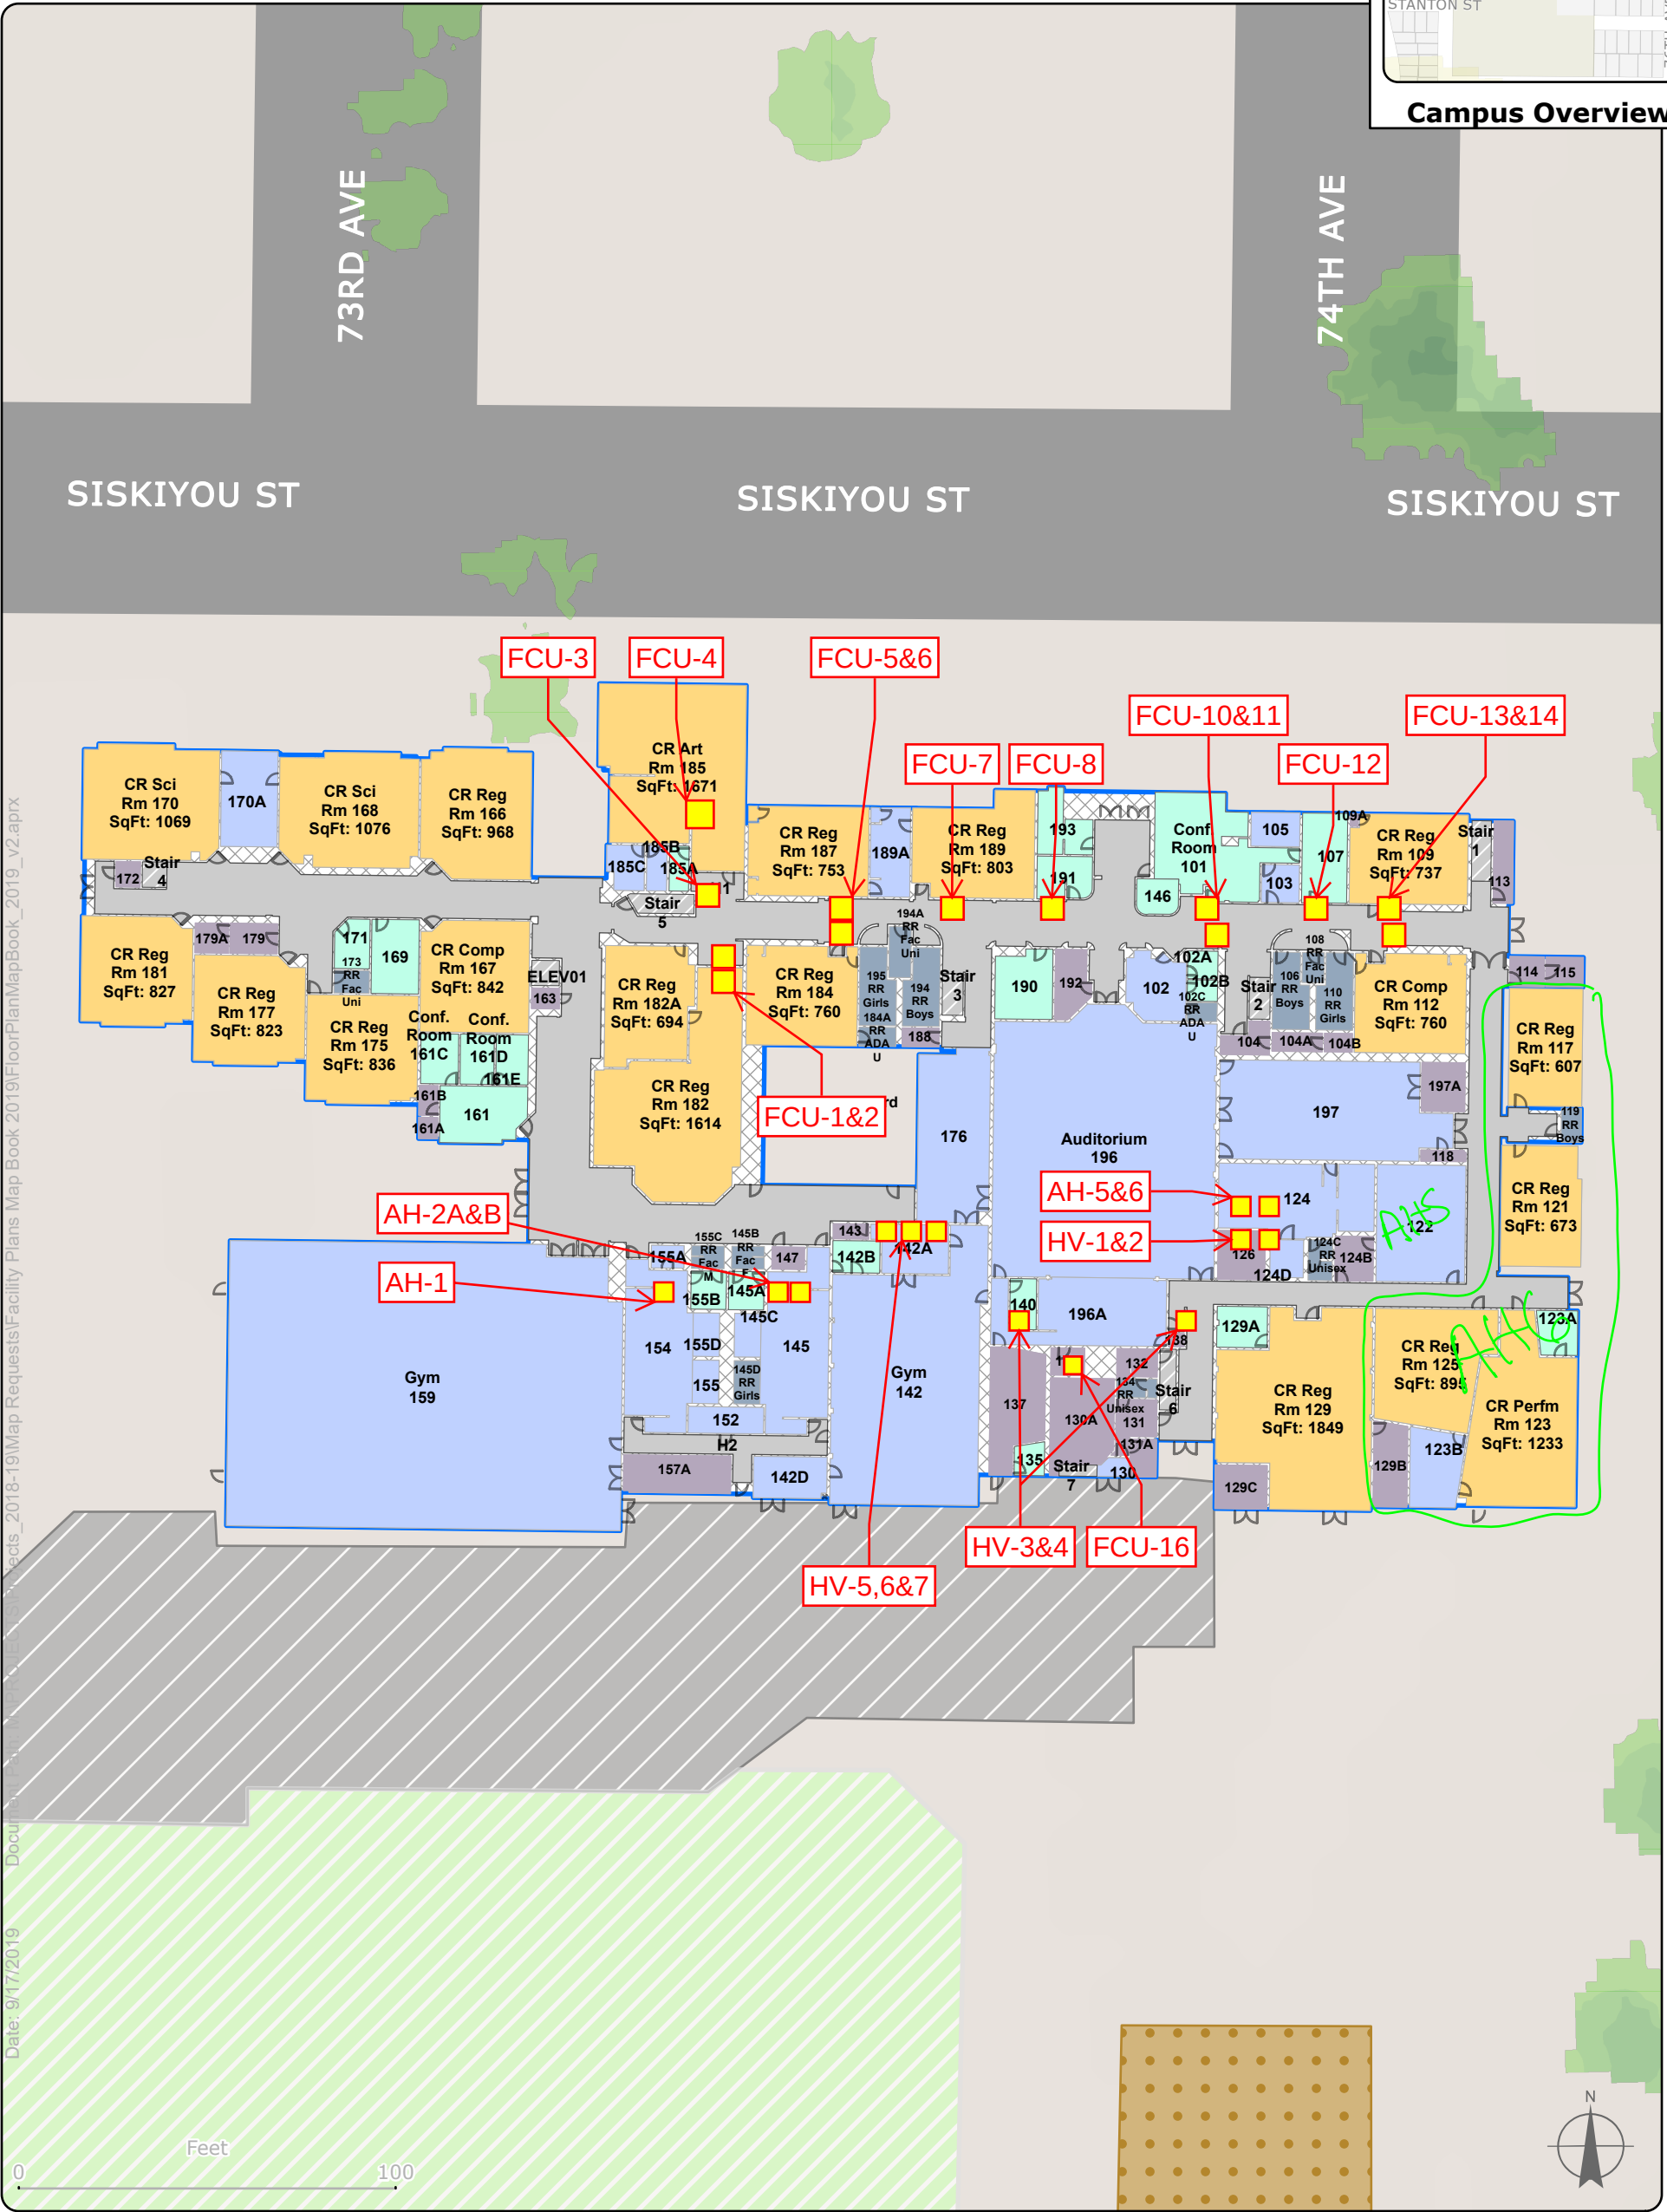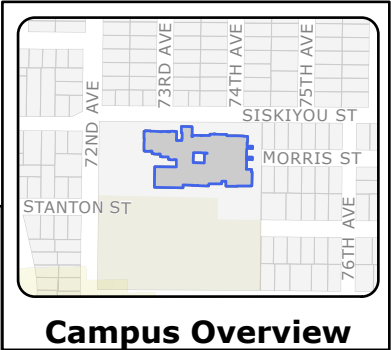

Space Use

- Classroom
- Office
- Rest Room
- Special Purpose
- Corridor
- Other
- Stairs/Elevator

School Grounds

- Campus Footprints
- Athletic Field
- Playground: Paved
- Playground: Unpaved
- Streets
- Doors

Total Number Of Rooms By Classification



Classrooms: 20

Special Purpose: 27

Office Spaces: 22

Storage: 22

ROSEWAY HEIGHTS: Second Floor

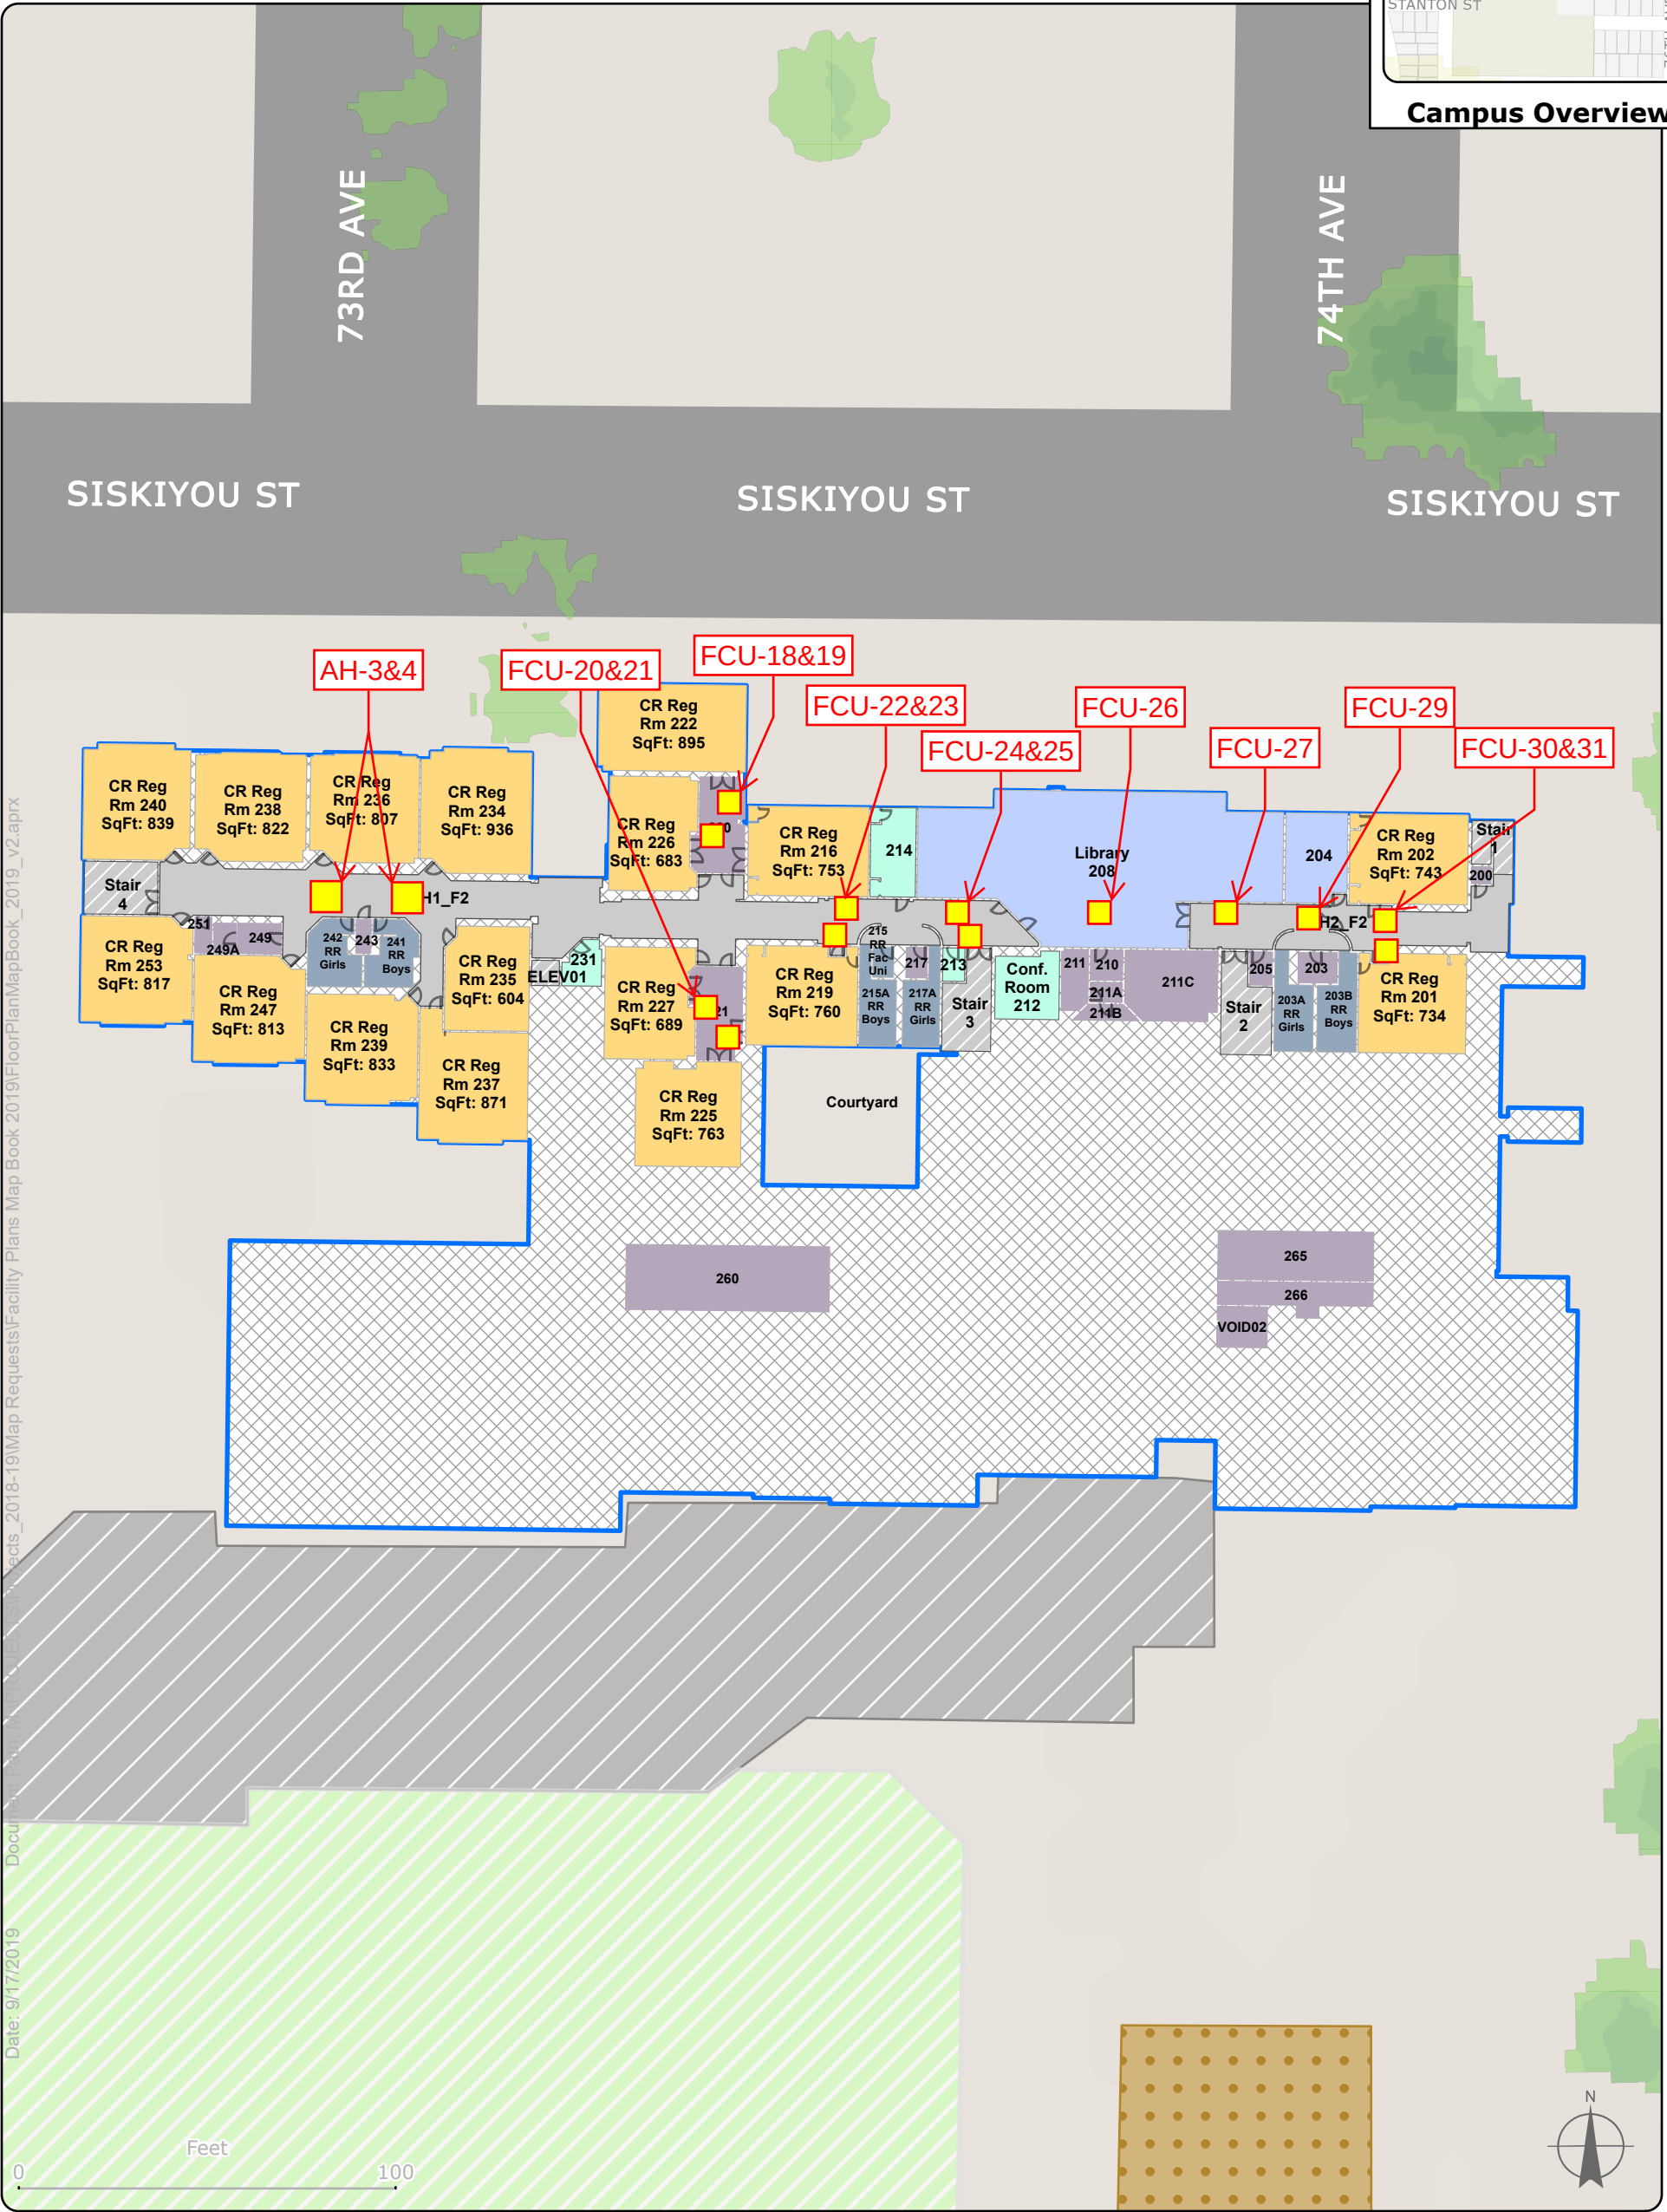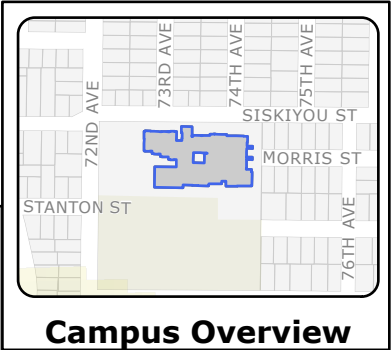

Space Use

- Classroom
- Office
- Rest Room
- Special Purpose
- Corridor
- Other
- Stairs/Elevator

School Grounds

- Campus Footprints
- Athletic Field
- Playground: Paved
- Playground: Unpaved
- Streets
- Doors

Total Number Of Rooms By Classification

Classrooms: 17	Special Purpose: 2
Office Spaces: 4	Storage: 11
