

# Measure BB Bond

21st Century Classroom Improvements

July 17, 2025




CUMMING  
GROUP

//////////////////// BUILDING VALUE THROUGH EXPERTISE



# HLPUSD MEASURE BB - SUMMARY

## SCHOOLS IN PROGRESS

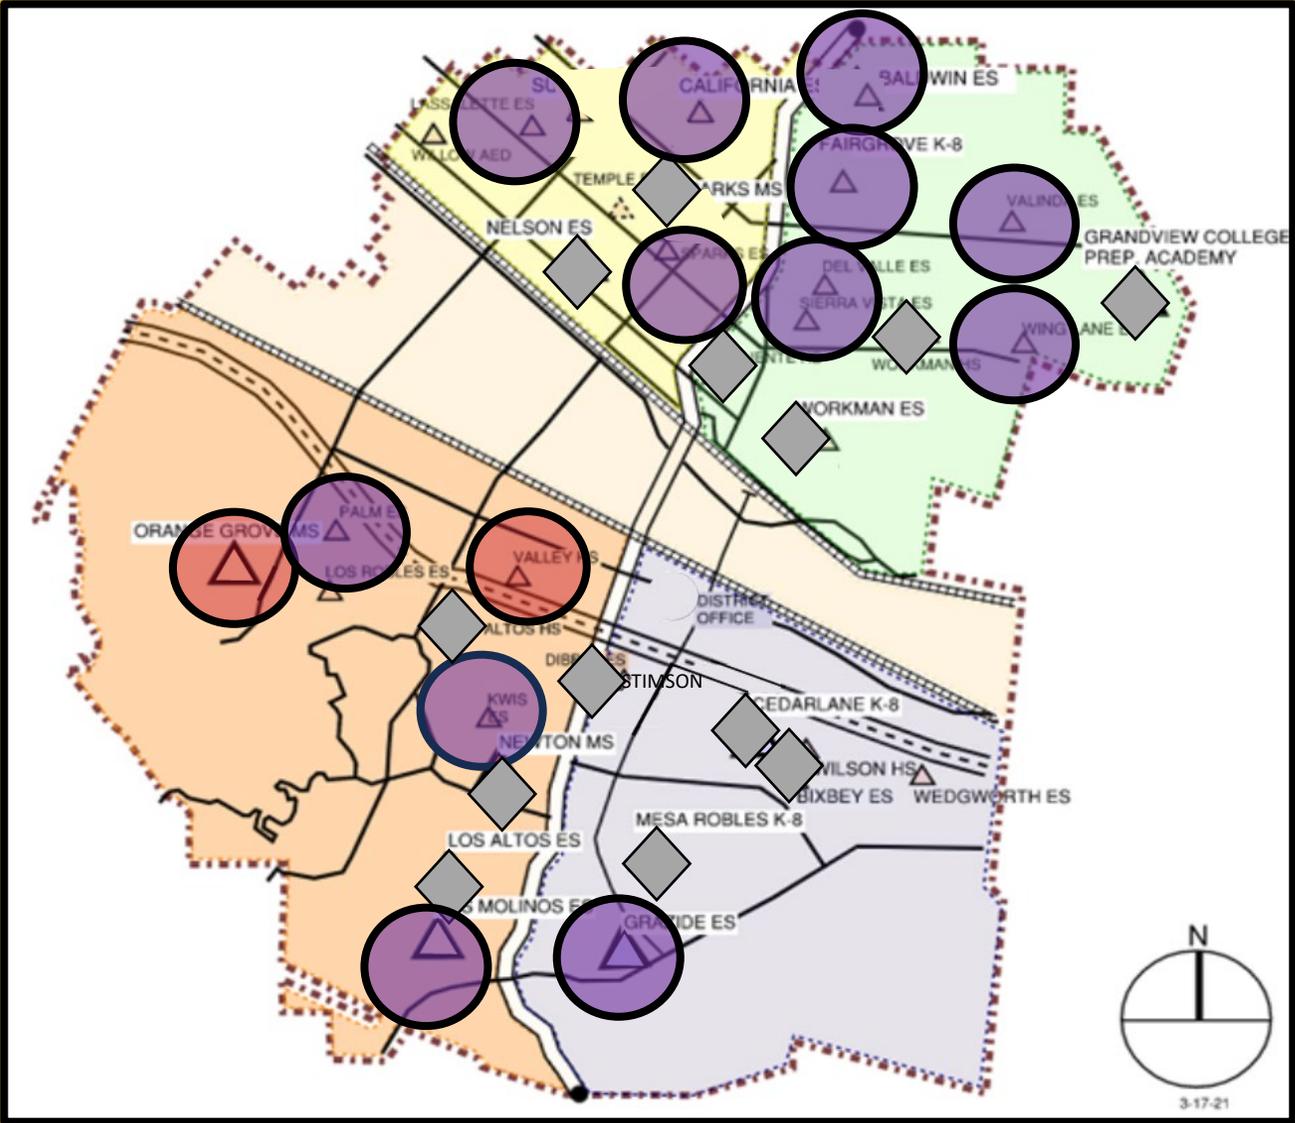

**IN PROGRESS CONSTRUCTION**

- California ES
- Baldwin ES
- Los Molinos ES
- Grazide ES
- Kwis ES
- Fairgrove K-8
- Lassalette ES
- Sierra Vista MS
- Palm ES
- Valinda ES
- Sparks ES
- Wing Lane ES



**DSA PLAN REVIEW**

- Valley Alternative School

**IN DESIGN**

- Orange Grove MS




**COMPLETED**

- Nelson ES
- Los Altos ES
- Workman ES
- Mesa Robles K-8
- Cedarlane K-8
- Sparks MS
- Grandview MS
- Newton MS
- Stimson EC
- Workman HS
- La Puente HS
- Wilson HS
- Los Altos HS

# PHASE B PROGRESS

	PROJECT STARTS	CONSTRUCTION DOCUMENTS TO DSA	DSA PLAN REVIEWS COMPLETED	PROJECTS BID	CONSTRUCTION STARTS (COMPLETED*)
Baldwin ES	●	●	●	●	●
California ES	●	●	●	●	●
Grazide ES	●	●	●	●	●
Los Molinos	●	●	●	●	●
Kwis ES	●	●	●	●	●
Lassalette ES	●	●	●	●	●
Fairgrove Academy	●	●	●	●	●
Sierra Vista MS	●	●	●	●	●
Sparks ES	●	●	●	●	●
Palm ES	●	●	●	●	○
Valinda ES	●	●	●	●	●
Wing Lane ES	●	●	●	●	●
Valley Alternative School	●	●	·	·	·
Orange Grove	●	·	·	·	·

Measure BB 21<sup>st</sup> Century  
Classroom Improvements  
California Elementary School  
Phases B3 & B4

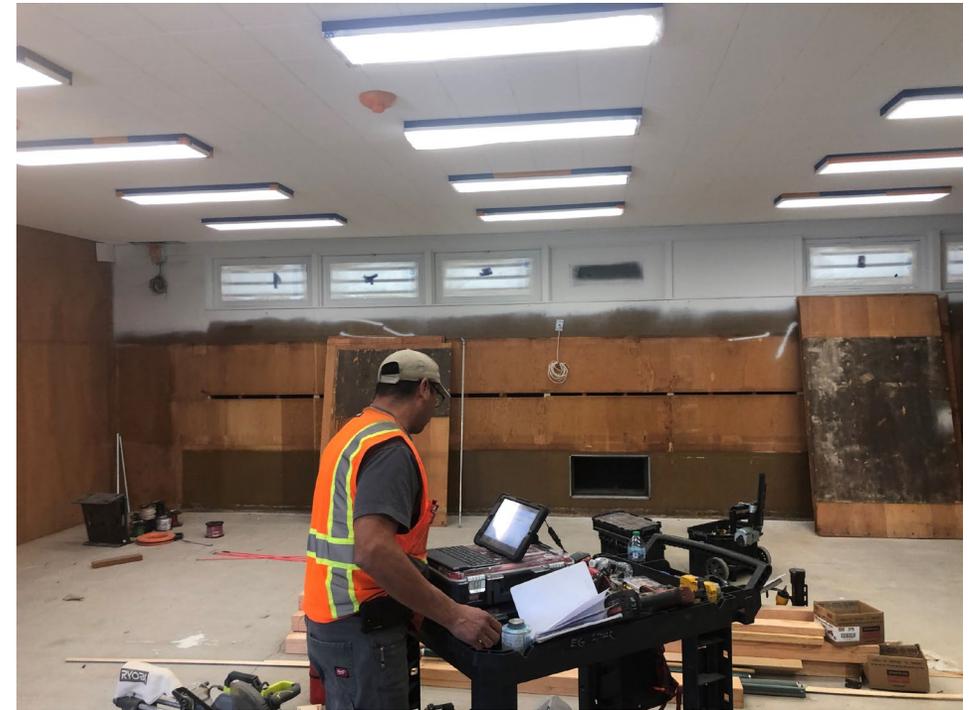

ESTIMATED COMPLETION AUGUST 20, 2025

Measure BB 21<sup>st</sup> Century  
Classroom Improvements  
Baldwin Academy School  
Phase B3



ESTIMATED PROJECT COMPLETION JULY 30, 2025

Measure BB 21<sup>st</sup> Century  
Classroom Improvements  
Los Molinos Elementary Phase B3



ESTIMATED COMPLETION JULY 30, 2025

Measure BB 21<sup>st</sup> Century  
Classroom Improvements  
Grazide Elementary Phase B1



ESTIMATED COMPLETION JANUARY 23, 2026

Measure BB 21<sup>st</sup> Century  
Classroom Improvements  
Kwis Elementary Phase B1 & Phase B2



ESTIMATED COMPLETION OCTOBER 2025

Measure BB 21<sup>st</sup> Century  
Classroom Improvements  
Lassalette Elementary Phase B1



ESTIMATED COMPLETION OCTOBER 2025

Measure BB 21<sup>st</sup> Century  
Classroom Improvements  
Sierra Vista Middle School Phase B1




ESTIMATED COMPLETION OCTOBER 2025

# Measure BB 21<sup>st</sup> Century Classroom Improvements Fairgrove K-8 Phase B1



**BEFORE**

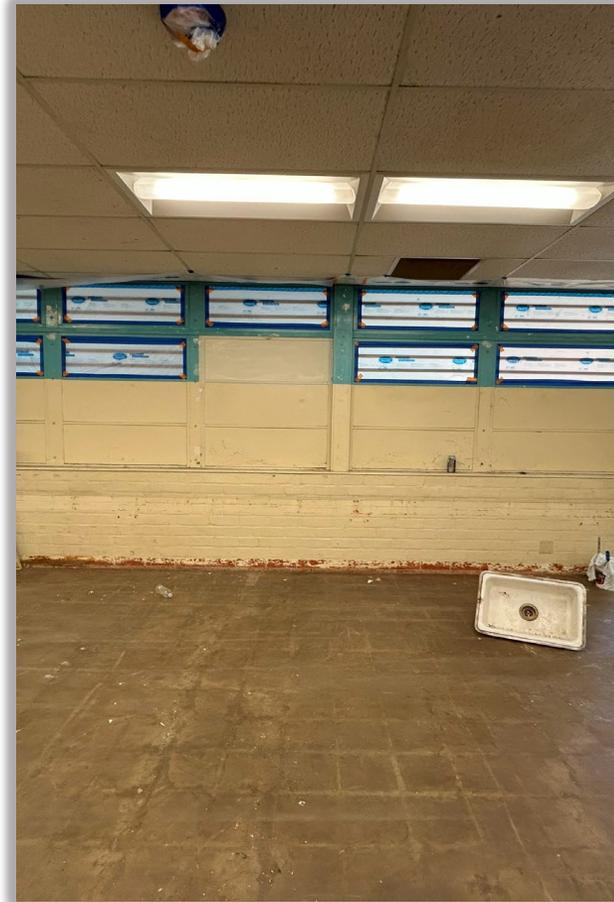

**ESTIMATED COMPLETION DECEMBER 2025**

# Measure BB 21<sup>st</sup> Century Classroom Improvements

## Palm, Valinda, Wing Lane, Sparks ES

(on hold)





QUESTIONS
