

New Elementary School on Greendale Road



➤ **Completed Work:**

- The site was covered in snow and ice. Not all site items could be observed.
- Laying of interior CMU masonry is in progress in Womens 169 and Mens 170. The area has been tented to keep heat.
- A few locations of CMU appear to have been damaged from the cold temperature. The CM was advised for replacement of the damage CMU.
- Installation of above grade MEP is in progress.
- The retention pond is frozen over but appears to be operating properly. Water was not observed in the lower pond.
- Temporary electric is connected to the building.

➤ **Upcoming Work / Look Ahead:**

- Continue setting and filling the ICF forms.
- Continue placing concrete floor slabs.
- Continue laying of masonry in the kitchen area.
- Continue placement of the hollow core planks.

New Elementary School on Greendale Road



Snow Covered Site at the Geothermal




Week Ending February 6, 2026

New Elementary School on Greendale Road



Laying of Interior CMU at Womens 169

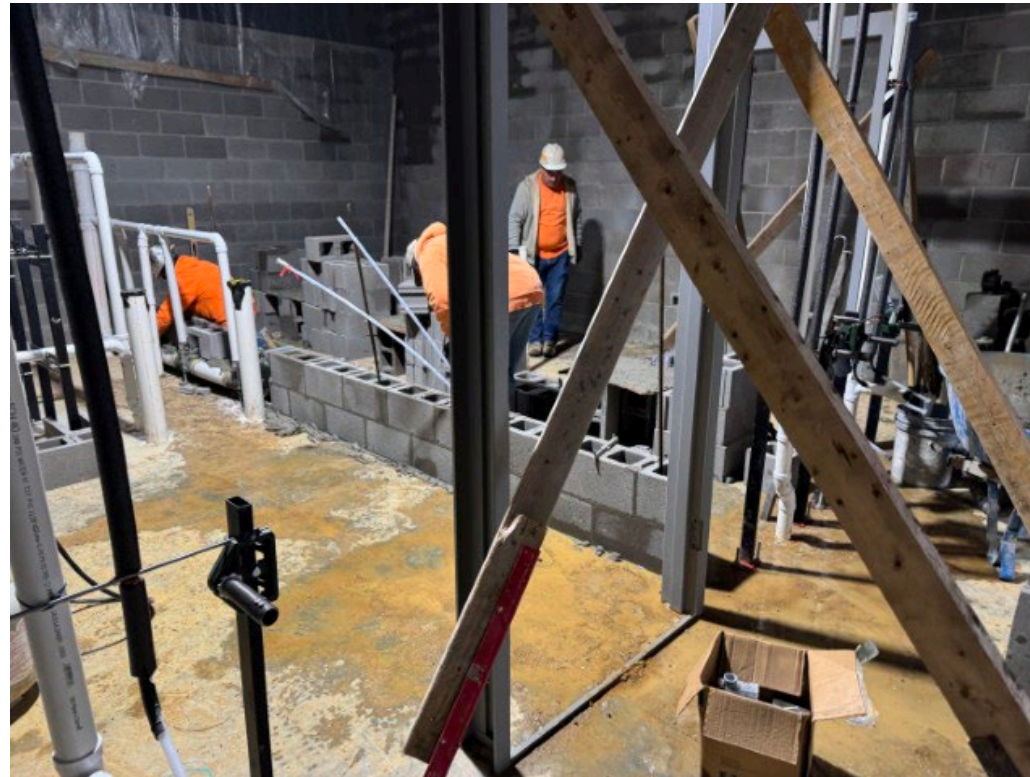


Week Ending February 6, 2026

New Elementary School on Greendale Road



Copper Piping Installation at Corridor C02

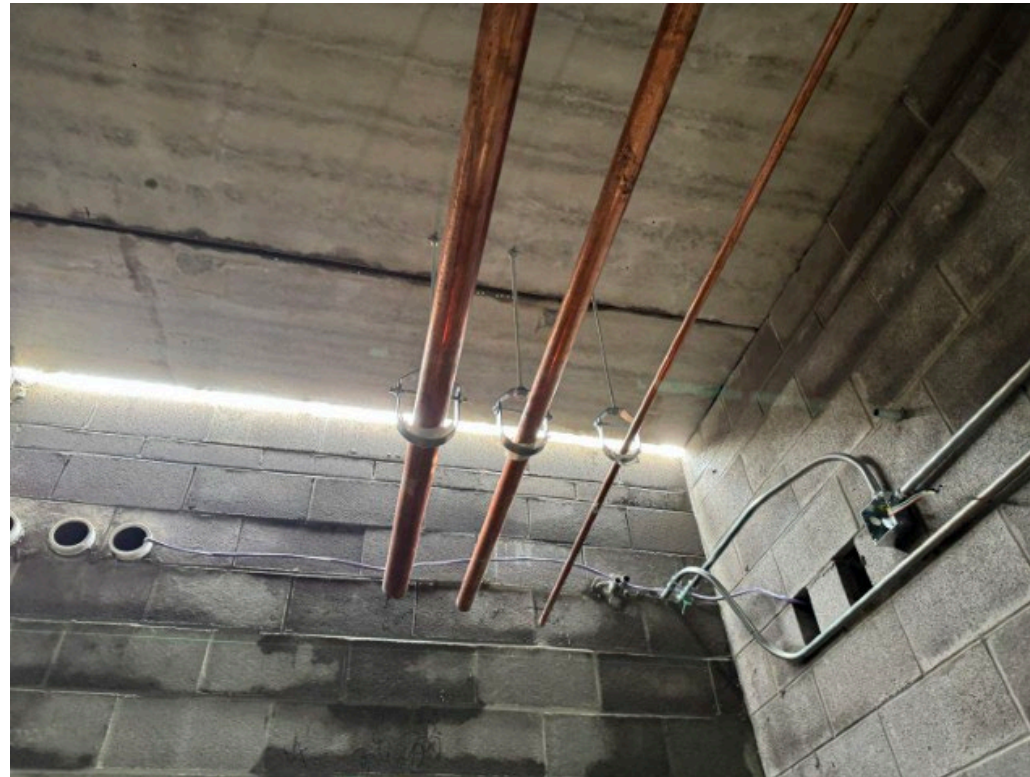

Week Ending February 6, 2026

New Elementary School on Greendale Road



Plumbing Stub Ups in Restroom 170A




Week Ending February 6, 2026

New Elementary School on Greendale Road



Duct Openings are installed in the CMU Corridor Wall (C02)

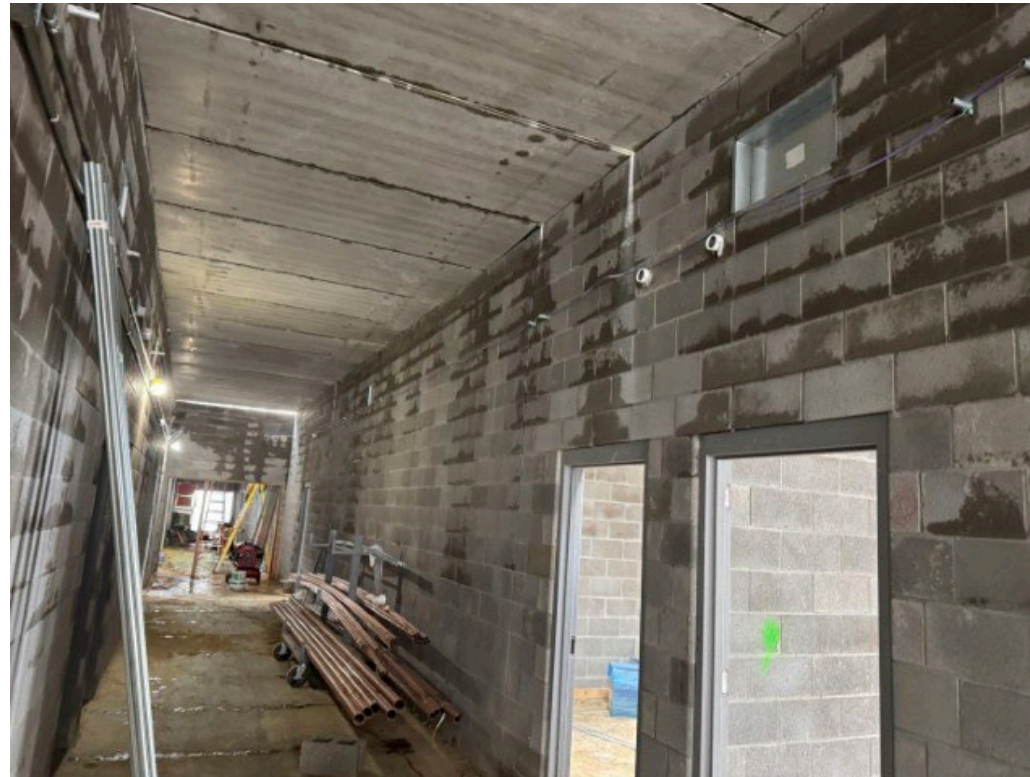

Week Ending February 6, 2026

New Elementary School on Greendale Road



Upper Retention Pond



Week Ending February 6, 2026

New Elementary School on Greendale Road



Lower Retention Pond



Week Ending February 6, 2026

New Elementary School on Greendale Road



Apparent CMU Damage from the Cold Weather



Week Ending February 6, 2026
