Agenda Request Form

Meeting Date	Agenda Item Number
September 17, 2020	F-1

Title

Monthly Update on Capital Outlay Projects

Requested Action

School Board Consideration of Superintendent's Recommendation for Approval of the Monthly Update on Capital Outlay Projects

Summary Explanation and Background

See the attached report from the Chief Support Services Officer regarding the status of the current Capital Outlay Projects.

Priority Area

Organizational and Operational Effectiveness

Financial Impact

N/A

Exhibits: (List)

See Attachment

Source of Additional Information

William J. Sebring	770.479.1871
Steve Werner	770.479.1871

Cherokee County School District

DATE: 04 September 2020

TO: Dr. Brian V. Hightower
Superintendent of Schools

FROM: William J. Sebring
Chief Support Services Officer

SUBJECT: Construction Status Reports

Capital Improvements staff has reviewed the architect's monthly status report on the current construction projects. A summary of the progress for each project is shown below:

Bus Shop I – New Fuel Island

- Long lead items (i.e. fuel tanks, fueling equipment and canopies) have been released for fabrication.
- General Contractor plans to mobilize mid-September.
- This project is scheduled for completion March 2021.

Creekview HS Agri-Science Lab

- Architect/Engineer punch list inspections are taking place.
- Overhead inspections are complete.
- Canopy and sidewalk installations are finished.
- This project is scheduled for completion December 2020.

Etowah HS Athletic Facility Improvements

- Underground utility installation is progressing at the baseball field.
- Grading for MSE wall at the visitor's fieldhouse continues.
- Curb and gutter work are scheduled to begin within the next week.
- This project is scheduled for completion August 2021.

Woodstock MS Classroom Addition

- Rock removal is complete.
- Concrete foundations and masonry are underway.
- Retaining wall construction is in progress.
- This project is scheduled for completion August 2021.

1205 Bluffs Parkway
Canton, Georgia 30114
770.479.1871
www.cherokeek12.net

Woodstock HS Auxiliary Gym


- Building footing and pad grading is underway.
- Access drive and parking area grading is in progress.
- Curb and gutter are in place.
- Underground utilities are roughed in.
- This project is scheduled for completion August 2021.




WJS

WJS/SW:mm
Attachments

Creekview High School Agri-Science Lab

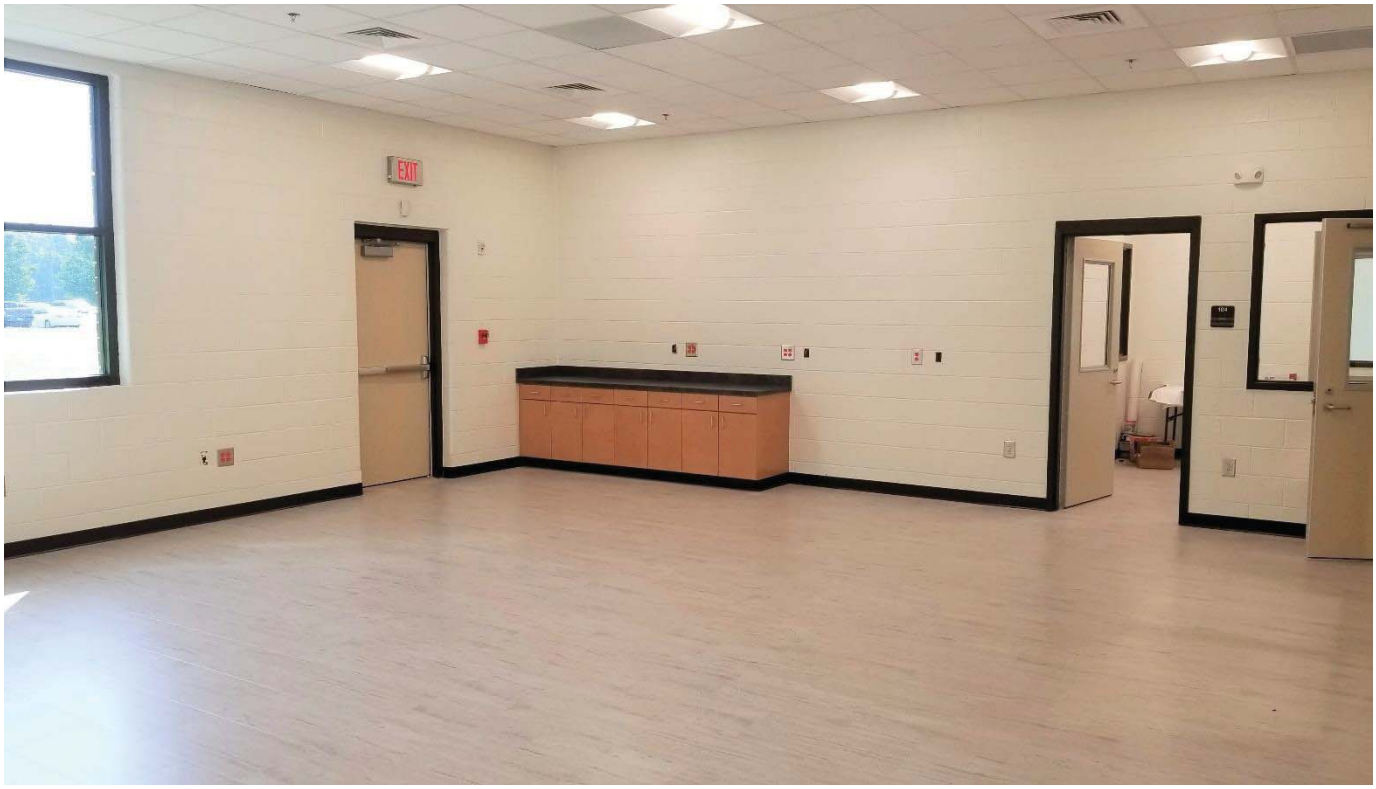

Interior View – Classroom

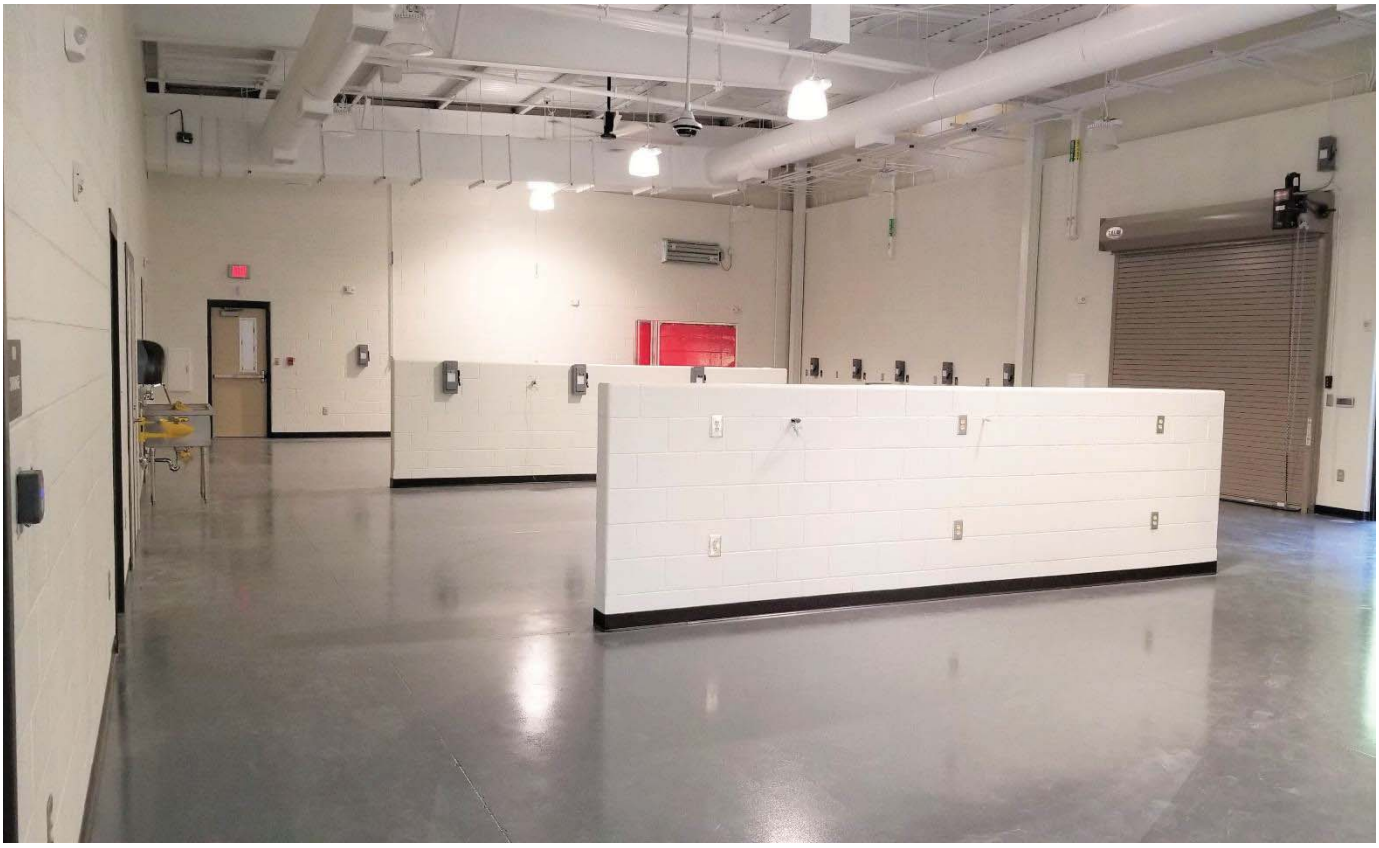

Interior View - Lab

Etowah High School Athletic Facility Improvements



Aerial View – Baseball Field



Aerial View – Softball Field

Woodstock High School Auxiliary Gym



Aerial View

Woodstock Middle School Classroom Addition



Aerial View
