Cherokee County School District

Agenda Request Form

Meeting Date	Agenda Item Number
November 19, 2020	F-1

Title

Monthly Update on Capital Outlay Projects

Requested Action

School Board Consideration of Superintendent's Recommendation for Approval of the Monthly Update on Capital Outlay Projects

Summary Explanation and Background

See the attached report from the Chief Support Services Officer regarding the status of the current Capital Outlay Projects.

Priority Area

Organizational and Operational Effectiveness

Financial Impact

N/A

Exhibits: (List)

See Attachment

Source of Additional Information

William J. Sebring	770.479.1871
Steve Werner	770.479.1871

Cherokee County School District

DATE: 09 Novemer 2020

TO: Dr. Brian V. Hightower
Superintendent of Schools

FROM: William J. Sebring
Chief Support Services Officer

SUBJECT: Construction Status Reports

Capital Improvements staff has reviewed the architect's monthly status report on the current construction projects. A summary of the progress for each project is shown below:

Bus Shop I – New Fuel Island

- Installation of the fuel tanks and associated piping are underway.
- Rough grading for concrete paving has begun.
- Data conduit to connect to existing Bus Shop 1 is progressing.
- This project is scheduled for completion March 2021.

Creekview HS Agri-Science Lab

- Architect/Engineer punch list repairs have been finalized.
- All Cherokee County inspections have been completed.
- Anticipate receipt of the Certificate of Occupancy within the next week.
- Storage shelving installation is complete.
- Delivery of lab equipment is expected within 4-6 weeks.
- This project is scheduled for completion December 2020.

Etowah HS Athletic Facility Improvements

- Metal roof trusses at the baseball concessions are underway.
- Rough ins for plumbing and electrical continue at the baseball concessions.
- Sanitary sewer lift station and piping installation are ongoing.
- Modular wall construction at the visitor's fieldhouse has begun.
- Curb and gutter installation at the visitor's field house is complete.
- This project is scheduled for completion August 2021.

Woodstock MS Classroom Addition

- Classroom addition concrete slabs are in place.
- Structural steel erection is commencing.
- This project is scheduled for completion August 2021.

1205 Bluffs Parkway
Canton, Georgia 30114
770.479.1871
www.cherokeek12.net

Woodstock HS Auxiliary Gym

- Pre-engineered metal building frame is in place.
- Installation of decking is underway.
- Under slab utilities for locker room area are complete.
- This project is scheduled for completion August 2021.

WJS

WJS/SW:mm
Attachments

Bus Shop I – Replacement Fuel Island



Aerial View

Etowah High School Athletic Facility Improvements




Aerial View – Visitor Field House




Aerial View – Baseball Concessions

Woodstock High School Auxiliary Gym

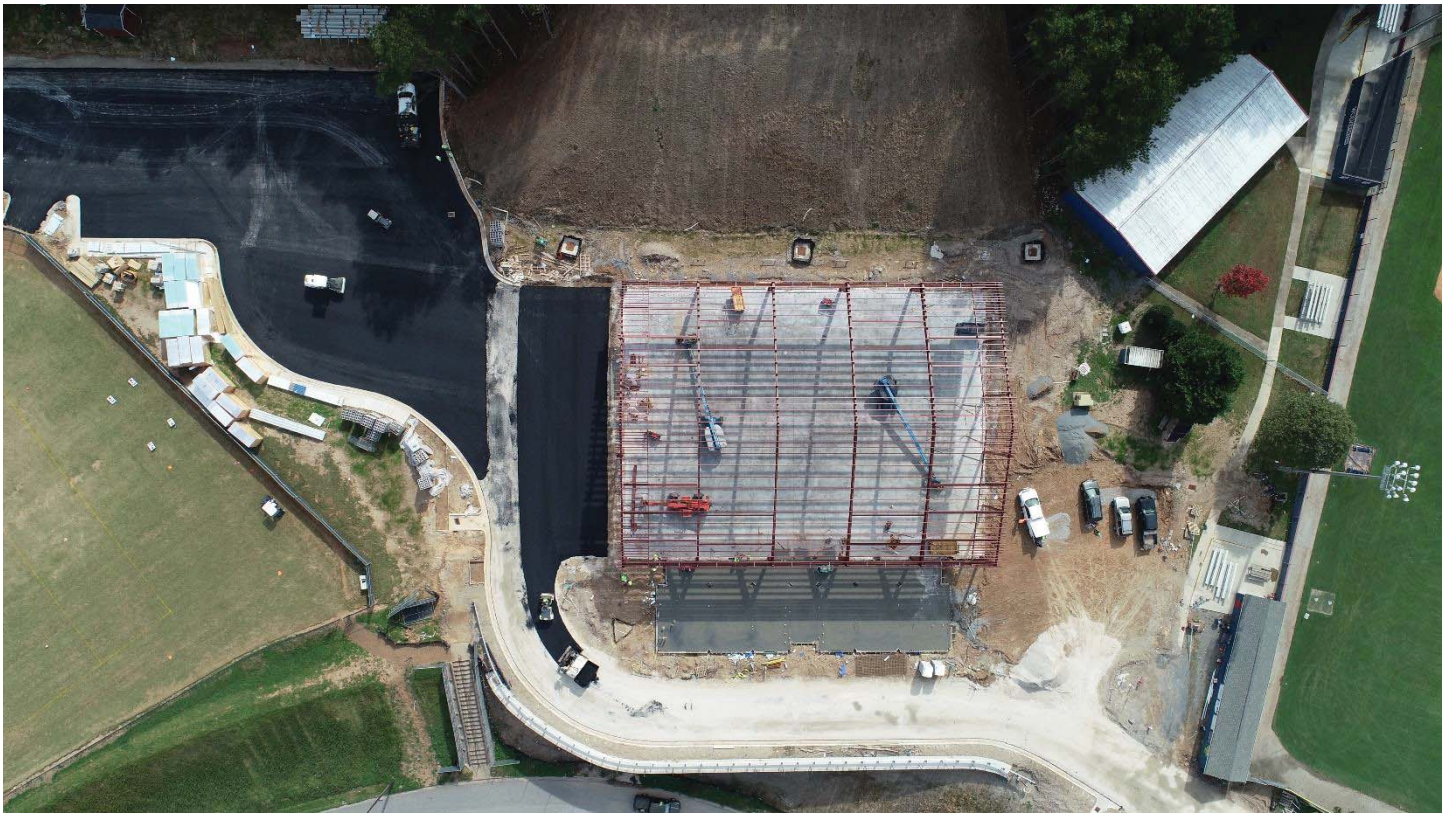

Aerial View

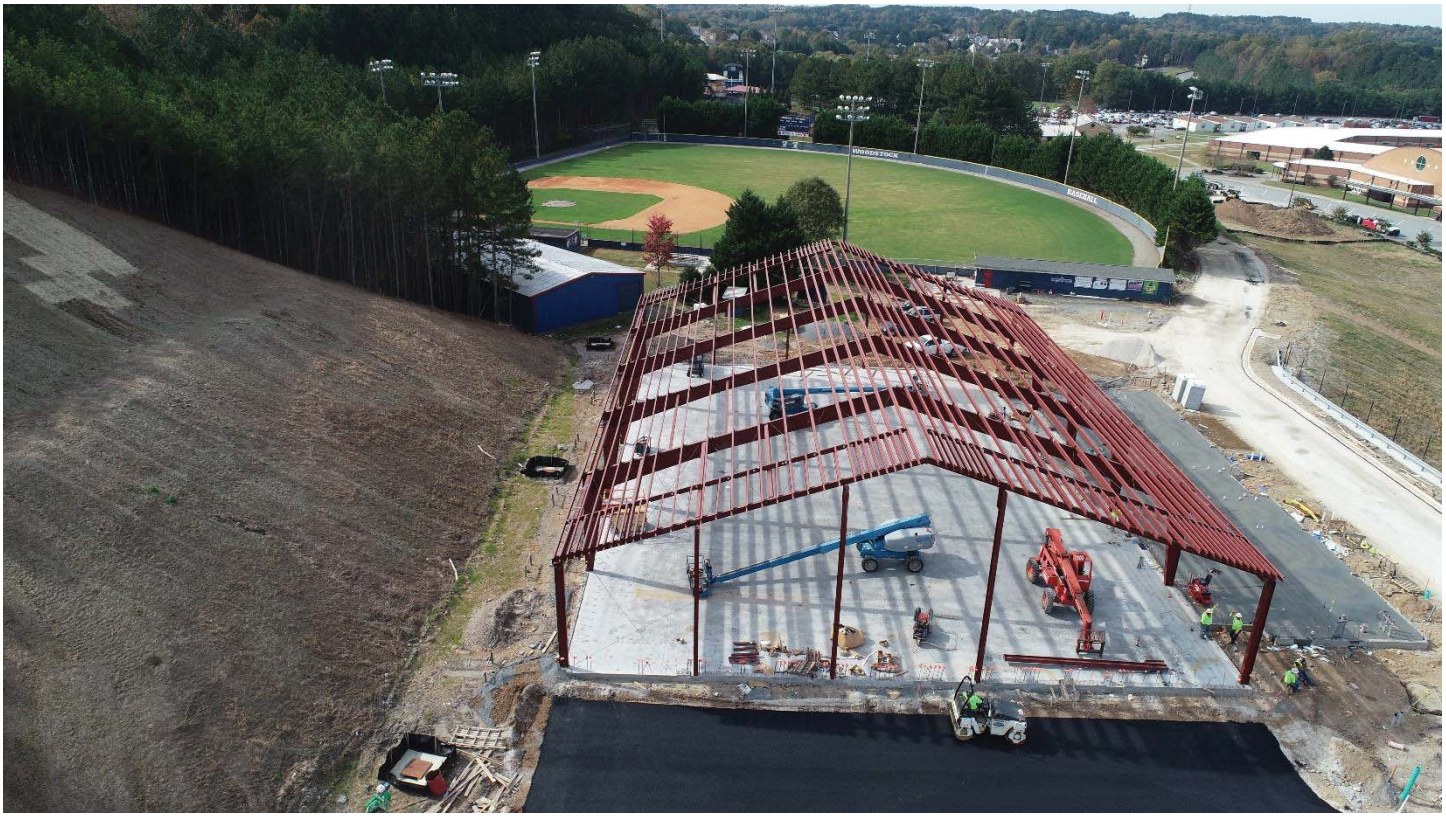

Side View

Woodstock Middle School Classroom Addition



Aerial View



Aerial View
