Cherokee County School District

Agenda Request Form

Meeting Date	Agenda Item Number
November 18, 2021	F-1

Title

Monthly Update on Capital Outlay Projects

Requested Action

School Board Consideration of Superintendent's Recommendation for Approval of the Monthly Update on Capital Outlay Projects

Summary Explanation and Background

See the attached report from the Chief Support Services Officer regarding the status of the current Capital Outlay Projects.

Priority Area

Organizational and Operational Effectiveness

Financial Impact

N/A

Exhibits: (List)

See Attachment

Source of Additional Information

William J. Sebring	770.479.1871
Steve Werner	770.479.1871

Cherokee County School District

DATE: 09 November 2021

TO: Dr. Brian V. Hightower
Superintendent of Schools

FROM: William J. Sebring
Chief Support Services Officer

SUBJECT: Construction Status Reports

Capital Improvements staff has reviewed the architect's monthly status report on the current construction projects. A summary of the progress for each project is shown below:

Etowah HS Athletic Facility Improvements

- Due to supply chain delivery delays, final roof installation is anticipated to begin in mid-December.
- The completion date for this project has been adjusted to December 2021.

Woodstock HS Auxiliary Gym

- Completion of final punch list items is underway.
- Gym floor installation has begun.
- The completion date for this project has been adjusted to December 2021.

WJS

WJS/SW:mm
Attachments


1205 Bluffs Parkway
Canton, Georgia 30114
770.479.1871
www.cherokeek12.net

Etowah High School Athletic Facility Improvements



Exterior View – Softball Concessions Building

Woodstock High School Auxiliary Gym

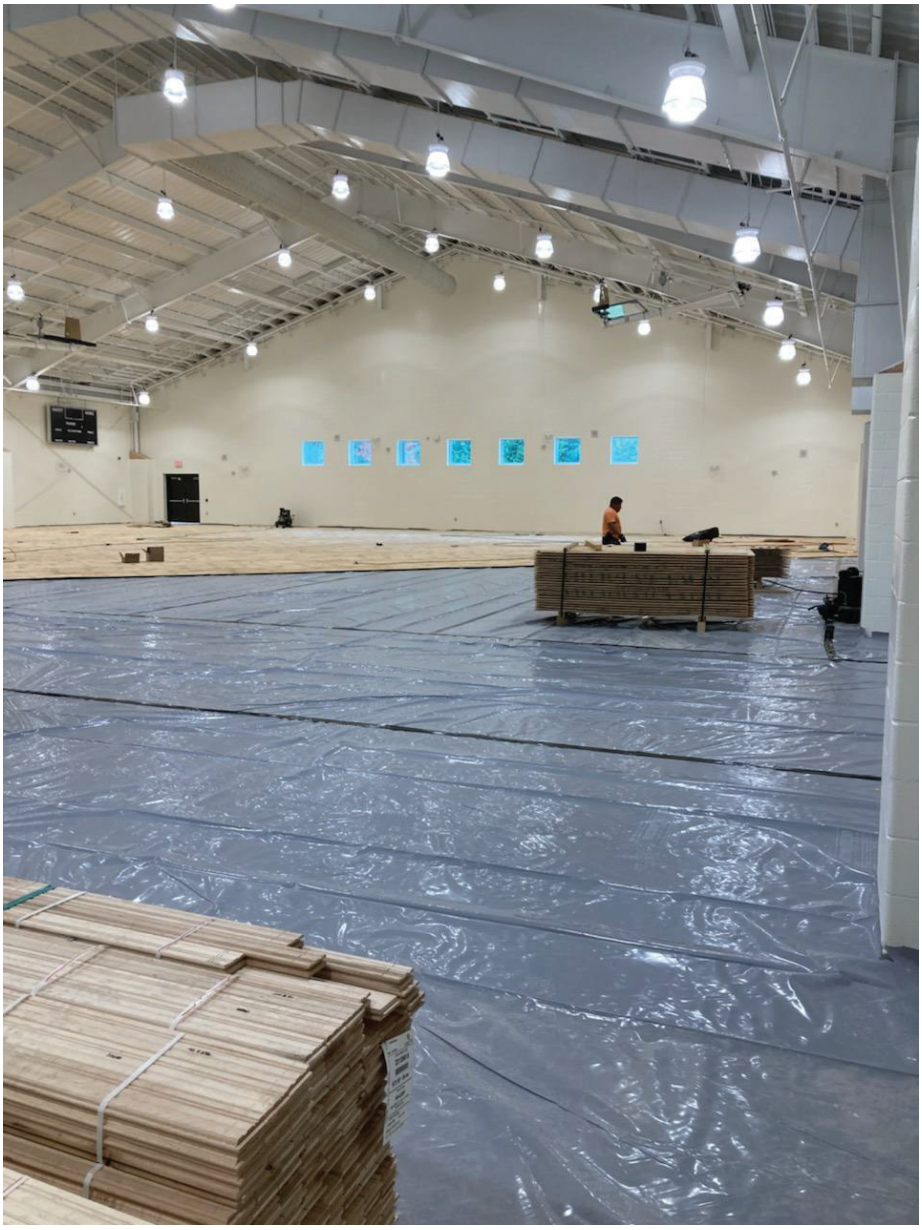

Interior View
