Hanover Community School Corporation
Construction Projects

Board Report
October 26, 2021



SKILLMAN

GIBRALTAR DESIGN

Hanover Community School Corporation
Construction Projects

Board Report
October 26, 2021

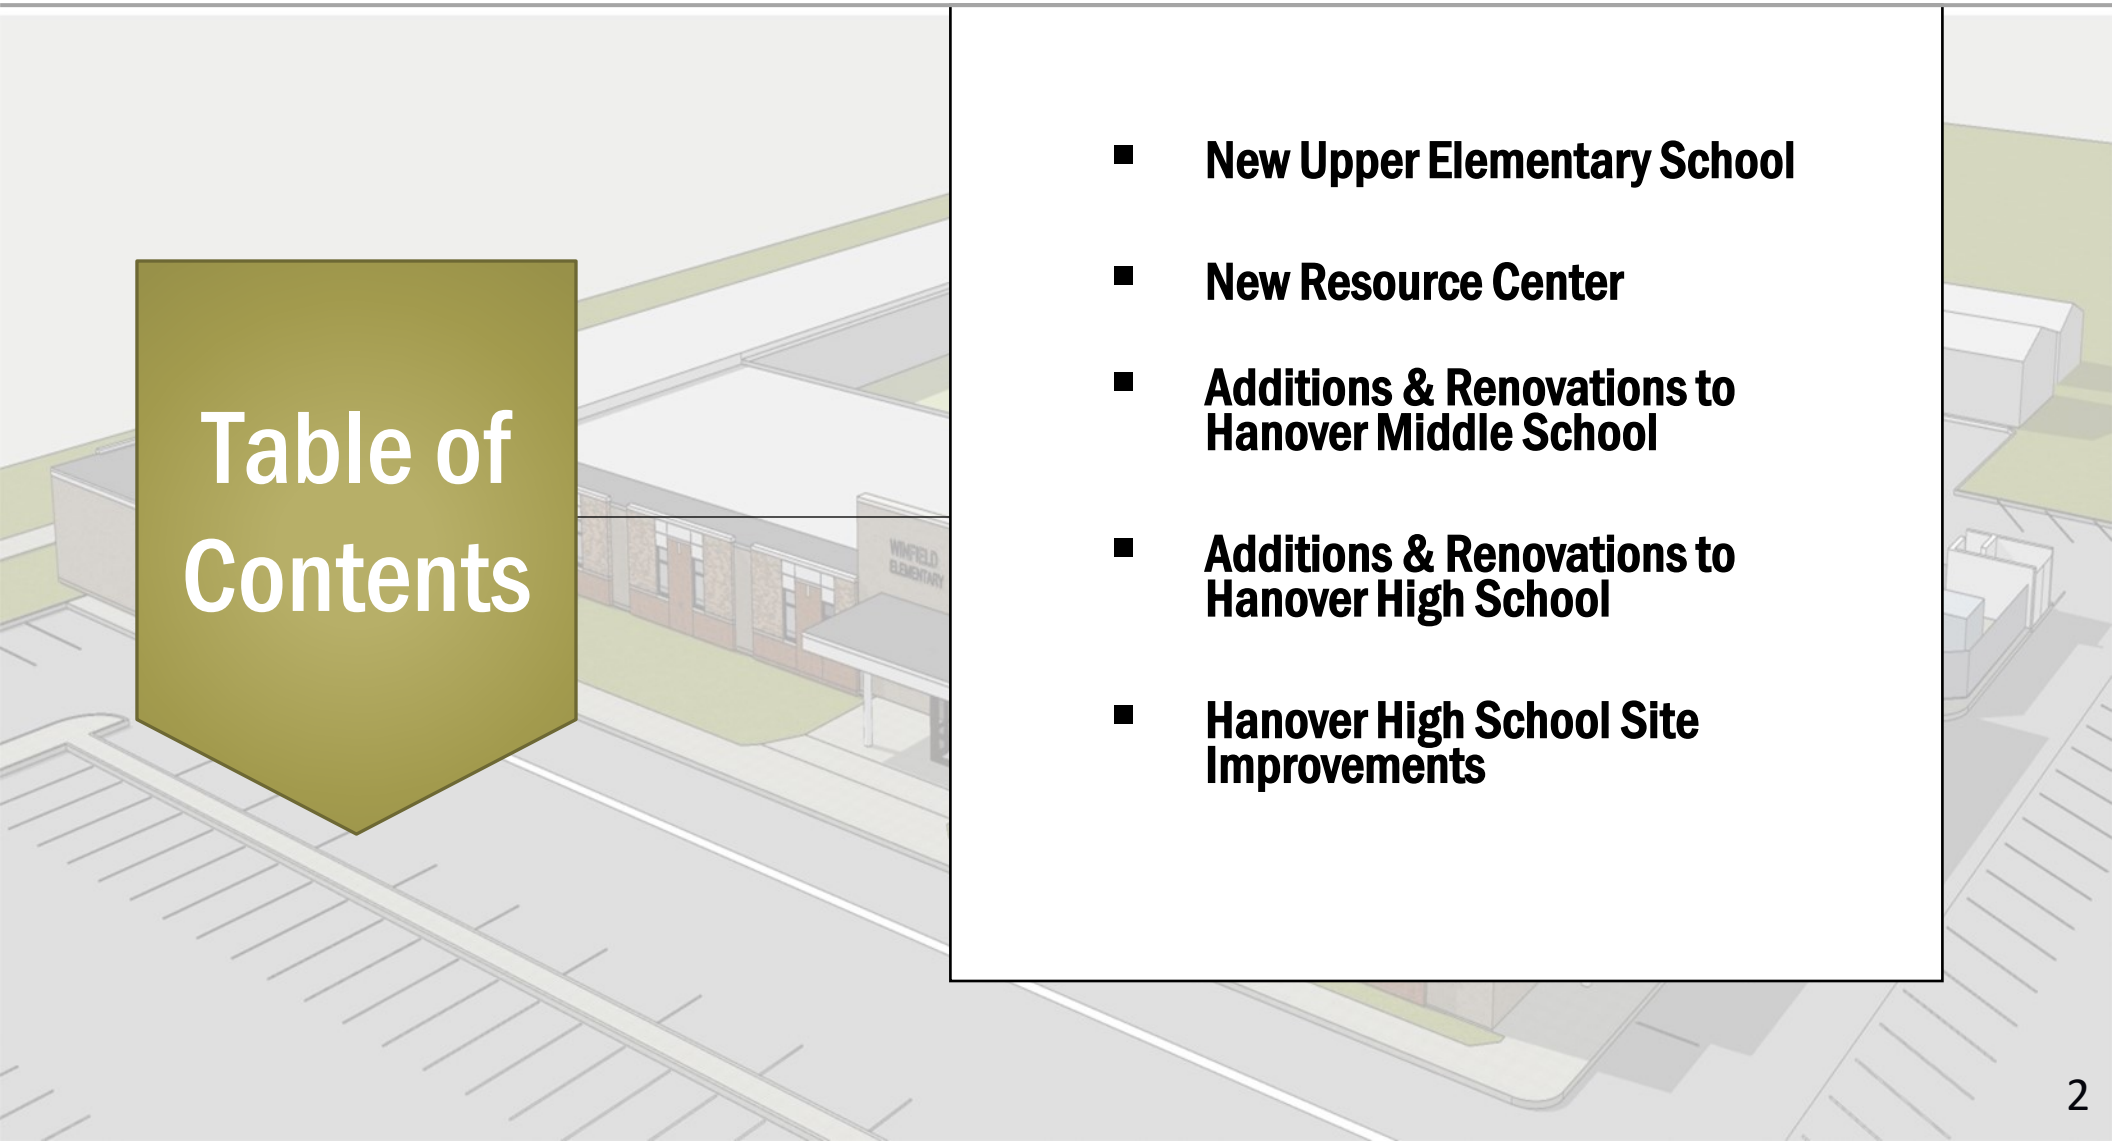


Table of Contents

- New Upper Elementary School
- New Resource Center
- Additions & Renovations to Hanover Middle School
- Additions & Renovations to Hanover High School
- Hanover High School Site Improvements

Progress Photographs



Northeast Corner of Upper Elementary

New Upper Elementary:

- Completed roof joists and deck in Academic Areas and Cafeteria
- Built out exterior walls and masonry at west Courtyard
- Continued buildout of exterior walls and masonry at east Courtyard
- Began roofing installation
- Set Mechanical Air Handling Units in second floor Mezzanines.
- Continued exterior sheathing around Academics
- Continued interior stud walls and MEP rough-ins

Progress Photographs



West Entrance Near Administration

New Upper Elementary:

Next Four Weeks

- Complete roofing installation
- Complete buildout of exterior walls and masonry at east Courtyard
- Complete exterior metal stud and sheathing around perimeter of the building
- Continue ductwork installation inside the building
- Continue interior metal stud walls and MEP rough-ins at Academic Areas
- Continue masonry brick around perimeter of the building

Progress Photographs



Resource Center –
Admin and Bus Garage Foundations

New Resource Center:

- Completed pouring perimeter foundation walls in Admin Building
- Began excavating for perimeter foundation walls in the Bus Garage Building

Next Four Weeks

- Complete pouring perimeter foundation walls in the Bus Garage Building
- Begin excavating for perimeter foundation walls in the Mechanics and Maintenance Buildings
- Begin underground utilities for Admin and Bus Garage Buildings

Progress Photographs



Main Corridor of Classroom Addition

Middle School Additions & Renovations:

- Completed interior metal studs for Gymnasium/Classroom Addition
- Completed exterior cavity insulation and brick at Cafeteria Addition
- Installed new roofing at Cafeteria and Classroom Addition
- Continued mechanical and electrical rough-ins in Classroom Addition
- Continued exterior cavity insulation and brick at Classroom Addition

Progress Photographs



Middle School Cafeteria & Classroom Addition

Middle School Additions & Renovations:

Next Four Weeks

- Complete roofing installation at the Music Addition
- Complete mechanical and electrical rough-ins in Classroom Addition
- Complete exterior cavity insulation and brick at Classroom and Music Additions
- Begin asphalt paving of Parking Lots
- Begin drywall installation in Classroom Addition

Progress Photographs



Classroom Addition

High School Additions & Renovations:

- Completed steel roof joists for Admin and Classroom Additions
- Completed painting in Classroom Renovations
- Began roofing installation at Classroom and Admin Additions
- Began exterior stud walls and sheathing at Classroom and Admin Additions
- Began interior metal stud walls in Classroom Addition
- Began ceiling installation in Renovation Classrooms

Progress Photographs



Classroom Addition Main Corridor

High School Additions & Renovations:

Next Four Weeks

- Complete exterior stud walls and sheathing for Classroom and Admin Additions
- Complete installing roofing materials for Classroom and Admin Additions
- Complete ceilings in Classroom Renovations
- Begin casework install in Classroom Renovations
- Begin flooring install in Classroom Renovations

Progress Photographs



Locker Room/Concession Stand

High School Site Improvements:

- Completed final grades of practice Fields
- Completed roofing install at Locker Room
- Began drywall ceilings in Locker Room
- Began ductwork in Locker Room

Progress Photographs



Locker Room Concession/Supply Room

High School Site Improvements:

Next Four Weeks

- Complete drywall ceilings in Locker Room
- Complete ductwork in Locker Room
- Begin painting in Locker Room
- Begin casework, lockers, and benches
- Begin tile installation in showers
