# Hanover Community School Corporation
# Construction Projects

# Board Report
January 25, 2022



# Hanover Community School Corporation
# Construction Projects

## Board Report
January 25, 2022

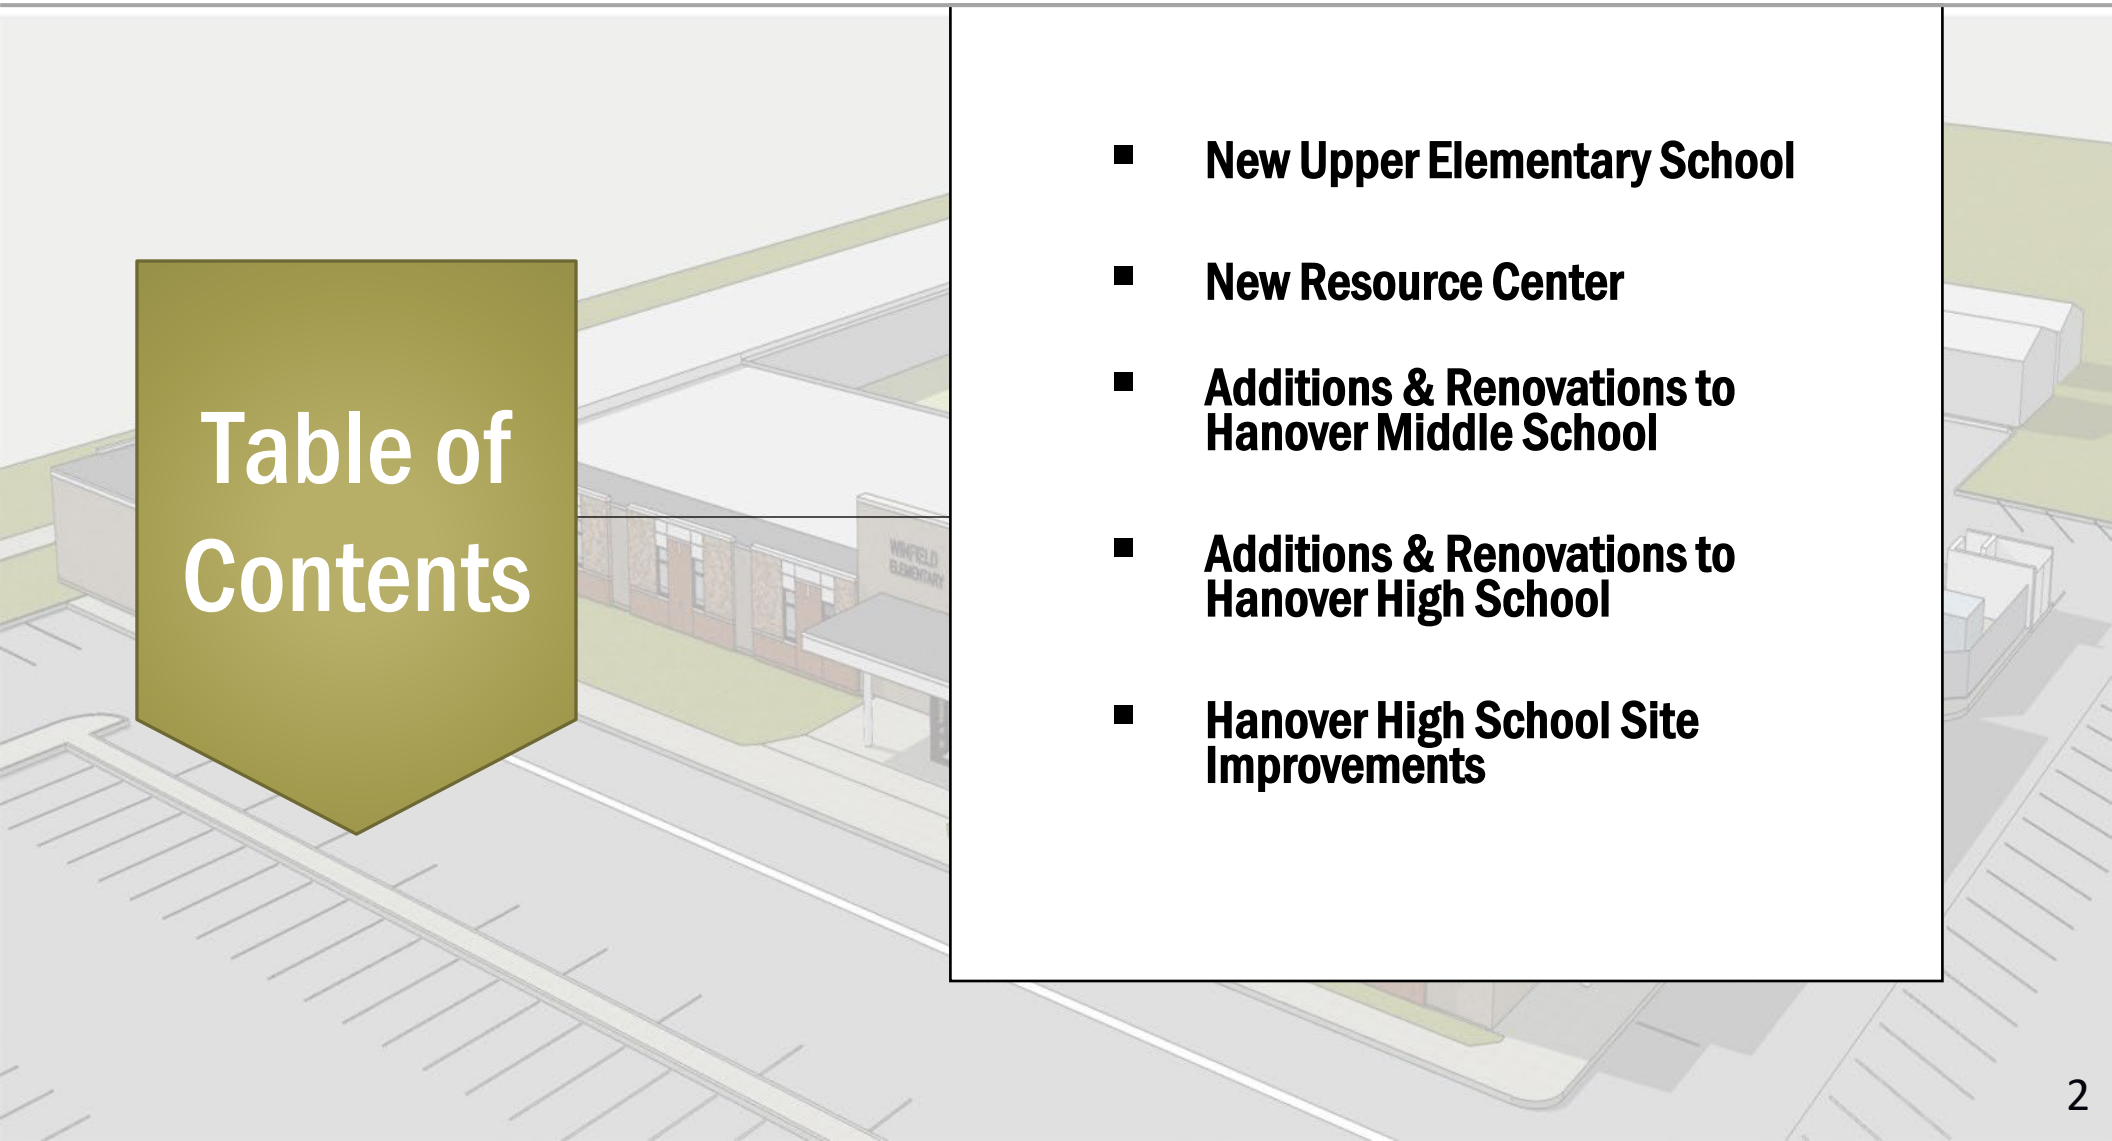


Table of Contents


- New Upper Elementary School
- New Resource Center
- Additions & Renovations to Hanover Middle School
- Additions & Renovations to Hanover High School
- Hanover High School Site Improvements

# Progress Photographs



**Northwest Corner of Upper Elementary**

**New Upper Elementary:**

- Continued roofing installation
- Started temporary heat
- Continued installing windows
- Started drywall install only where roof is complete
- Continued ductwork installation inside the building
- Continued interior block walls for Restrooms
- Completed interior metal stud walls and MEP rough-ins at Academic Areas

# Progress Photographs



Unit C Restrooms

## New Upper Elementary:

**Next Four Weeks**

- Complete roofing
- Continue masonry walls for Restrooms
- Continue hanging drywall where roofing is installed
- Begin taping and finishing drywall in Administration offices
- Continue piping rough-ins for fire sprinkler system
- Continue overhead conduit runs for lighting

# Progress Photographs



Resource Center

**New Resource Center:**

- Began erecting new Administration building
- Completed remaining footings for all four buildings
- Completed underground utilities in Admin Building

**Next Four Weeks**

- Continue underground utilities for Bus Garage, Maintenance and Mechanics Buildings
- Begin erecting Mechanics Building
- Begin exterior metal stud walls for new Administration Building
- Begin masonry walls for Mechanics Building

# Progress Photographs




Cafeteria Addition

**Middle School Additions & Renovations:**

- Completed finishes in Cafeteria Addition
- Began locker install in new Classroom Addition Corridors
- Completed painting in Gymnasium and Classrooms
- Began installing Athletic Equipment in new Gymnasium
- Installed casework in new Classrooms

# Progress Photographs



New Classroom Addition Corridor

## Middle School Additions & Renovations:

### Next Four Weeks

- Complete ceiling tile installation in new Classroom Addition
- Complete locker installation
- Complete athletic equipment in new Gymnasium
- Complete installation of light fixtures in new Classroom addition
- Complete painting in Music Addition
- Install ceilings in Music Addition
- Install music casework in Music Addition

# Progress Photographs



Admin Addition

**High School Additions & Renovations:**

- Turned over Math Classrooms
- Turned over first set of Science Classrooms
- Completed tile in Athletic Restrooms
- Completed painting in Classroom Addition
- Continued exterior masonry brick at Administration Addition
- Completed exterior masonry brick at Classroom Addition
- Began demolition in second set of Science Classrooms
- Began Demolition of second set of classrooms East of the Admin Addition

# Progress Photographs



Math Classroom Corridor

## High School Additions & Renovations:

### Next Four Weeks

- Complete and turn over Athletic Restrooms
- Begin piping and conduit for electric and water in second set of Science Classrooms
- Begin framing new walls for second set of Classroom renovations
- Continue drywall installation in Admin Addition
- Begin ceiling install in Classroom Addition
- Continue tile install in Classroom Addition restrooms

# Progress Photographs




Locker Room

## High School Site Improvements:

- Completed finishes in Locker Room
- Continued installing lockers and benches

**Remaining items**

- Touchup and trim work in Locker Room
- Install fire alarm panel once delivered
- Complete locker and bench installation
- Complete restroom partitions and fixtures
- Complete remaining field work once weather allows
