Hanover Community School Corporation
Construction Projects

Board Report
February 22, 2022



SKILLMAN

GIBRALTAR DESIGN

Hanover Community School Corporation
Construction Projects

Board Report
February 22, 2022

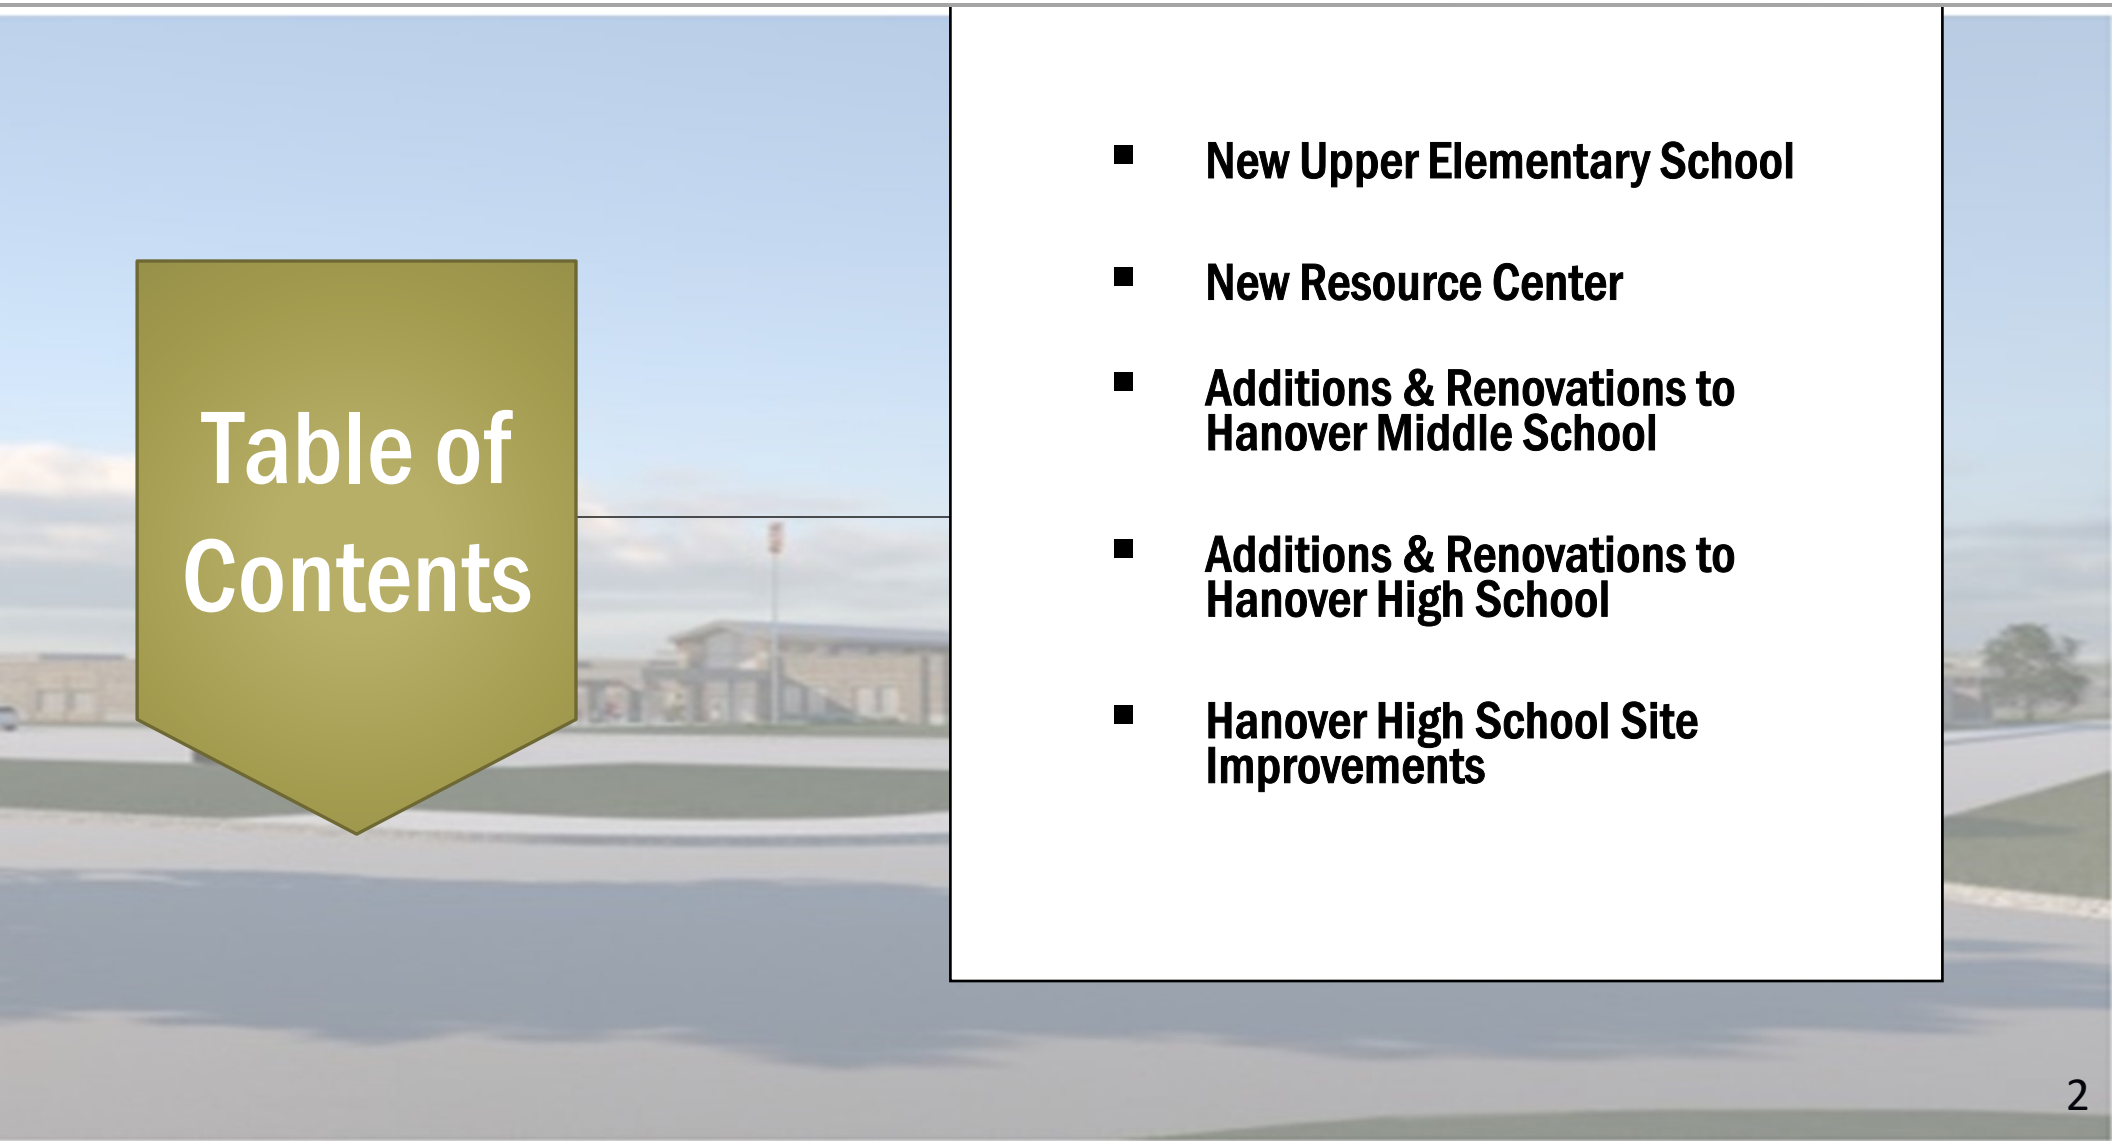


Table of Contents

- New Upper Elementary School
- New Resource Center
- Additions & Renovations to Hanover Middle School
- Additions & Renovations to Hanover High School
- Hanover High School Site Improvements

Progress Photographs



Aerial of Upper Elementary

New Upper Elementary:

- Continued roofing installation
- Continued drywall install only where roof is complete
- Began finishing drywall in Admin areas
- Continued interior block walls for Restrooms
- Continued sprinkler lines and water lines
- Began painting in gymnasium

Progress Photographs




Main Corridor between Cafeteria and Administration

New Upper Elementary:

Next Four Weeks

- Complete roofing
- Complete masonry walls for Restrooms
- Complete remaining Facebrick
- Continue hanging drywall where roofing is installed
- Continue finishing drywall in Administration offices and into academic areas
- Begin installing exterior storefronts
- Continue overhead conduit runs for lighting
- Continue painting in gymnasium and cafeteria masonry walls

Progress Photographs

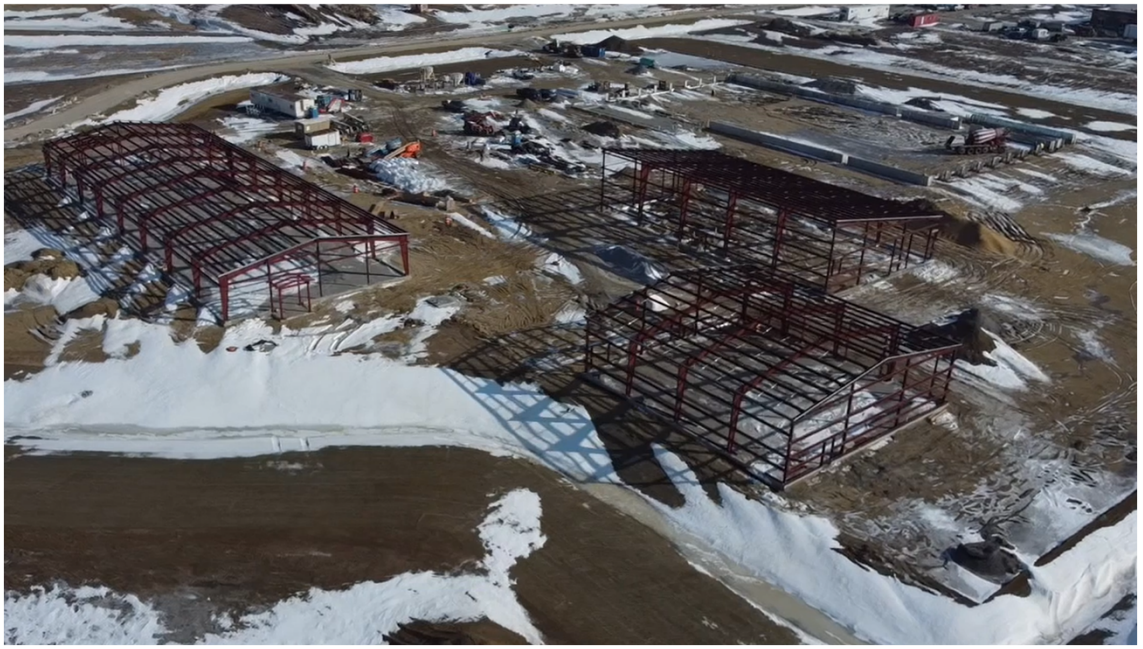

Resource Center

New Resource Center:

- Continued framing of mechanics and maintenance buildings
- Continued underground electrical rough-ins

Next Four Weeks

- Complete erecting Mechanics and Maintenance Buildings
- Begin erecting Bus Garage Building
- Begin exterior metal stud walls for new Administration Building

Progress Photographs



Music Addition

Middle School Additions & Renovations:

- Completed ceiling install in Music Addition
- Completed acoustical sound panels in Music Addition and Cafeteria
- Continued Toilet accessories and fixtures in new gym addition restrooms
- Began installing exterior doors in gymnasium addition

Progress Photographs



Gymnasium

Middle School Additions & Renovations:

Next Four Weeks

- Complete all new exterior doors
- Complete remaining flooring installation in rooms around the gymnasium
- Complete restrooms in Gym Addition
- Began Casework for Music Addition
- Began Gym floor installation

Progress Photographs



Classroom Addition

High School Additions & Renovations:

- Turned over Athletic Restrooms
- Begin piping and conduit for electric and water in second set of Science Classrooms
- Begin framing new walls for second set of Classroom renovations
- Continued drywall installation in Admin Addition
- Begin ceiling install in Classroom Addition
- Continued tile install in Classroom Addition restrooms

Progress Photographs



Pre-School Addition Restrooms

High School Additions & Renovations:

Next Four Weeks

- Complete framing new walls for second set of Classroom renovations
- Complete ceiling install in Classroom Addition
- Continue piping and conduit for electric and water in second set of Science Classrooms
- Continue drywall installation in Admin Addition
- Continue tile install in Classroom Addition restrooms
- Begin Unit Ventilator Installation

Progress Photographs



Locker Room

High School Site Improvements:

- Complete locker and bench installation
- Complete restroom partitions and fixtures

Remaining items

- Touchup and trim work in Locker Room
- Install fire alarm panel once delivered
- Complete remaining field work once weather allows
